



**JOB No.: TCS00881/18 & TCS00944/18**

**SITE FORMATION AND ASSOCIATED INFRASTRUCTURAL  
WORKS FOR DEVELOPMENT OF COLUMBARIUM,  
CREMATORIUM AND RELATED FACILITIES AT SANDY  
RIDGE CEMETERY**

**MONTHLY ENVIRONMENTAL MONITORING AND AUDIT  
REPORT (No.6) – JANUARY 2019**

**PREPARED FOR  
HSIN CHONG TSUN YIP JOINT VENTURE &  
SANG HING CIVIL CONTRACTORS CO., LTD**

Date	Reference No.	Prepared By	Certified By
14 February 2019	TCS00881/18/600/R0243v2		
		Nicola Hon (Environmental Consultant)	Tam Tak Wing (Environmental Team Leader)

Version	Date	Remarks
1	11 February 2019	First Submission
2	14 February 2019	Amended according to the IEC's comments on 13 February 2019

Our Ref: TCS00881/18/300/L0245

**Civil Engineering and Development Department**  
2/F, Civil Engineering and Development Building,  
101 Princess Margaret Rd,  
Homantin, Kowloon

**Attn: Mr. Joseph Wong**

**14 February 2019**  
By e-mail

Dear Sirs,

**Re: Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery  
Monthly Environmental Monitoring & Audit Report (No.6) – January 2019**

---

We confirmed that the captioned report has complied with the requirement set out in the EM&A Manual, we hereby certify the captioned report pursuant to Specific Condition 3.4 of the Environmental Permit No. FEP-01/534/2017/A and EP-534/2017/A.

Should you have any queries, please feel free to contact the undersigned at Tel: 2959-6059 or Fax: 2959-6079 or Email: [twtam@fordbusiness.com](mailto:twtam@fordbusiness.com).

Yours sincerely,  
For and on Behalf of  
**Action-United Environmental Services & Consulting (AUES)**

T. W. Tam  
Environmental Team Leader  
TW/nh

cc	ARUP (RE of Contract 1)	Mr. Steven Tang	by e-mail
	ARUP (RE of Contract 2)	Mr. Anthony Lau	by e-mail
	HCTY-JV (Contractor of Contract 1)	Mr. Ho Man To	by e-mail
	Sang Hing (Contractor of Contract 2)	Mr. Elvin Lam	by e-mail
	Acuity (IEC)	Mr. Jacky Leung	by e-mail





**ACUITY**  
SUSTAINABILITY  
CONSULTING LIMITED



Website: [www.acuityhk.com](http://www.acuityhk.com)



Unit 1908, iPlace,  
Nos. 301-305 Castle Peak Road,  
Kwai Chung, New Territories



Tel. : (852) 2698 6833  
Fax.: (852) 2698 9383

Our ref: CJO4068

Hsin Chong Tsun Yip Joint Venture (CV/2016/10)  
Hsin Chong Centre  
107-109 Wai Yip Street  
Kwun Tong, Kowloon  
Hong Kong

Attention: Mr. HO Man-to

14 February 2019

Dear Sir,

**Site formation and Associated Infrastructural Works for Development of Columbarium at  
Sandy Ridge Cemetery  
Monthly Environmental Monitoring and Audit Report (No.6) January 2019**

I refer to the email of ET regarding the captioned Monthly Report. We have no further comment on the Monthly Environmental Monitoring and Audit Report (No.6) January 2019 (Version 2) dated 14 February 2019 with reference No. TCS00881/18/600/R0243v2 after verification.

Yours faithfully,

*CH Leung*

Ir Leung CH Jacky  
Independent Environmental Checker

cc. CEDD-DPTL/Land Works – Mr. SHUM Steven  
ARUP – Mr. LEE Davis  
ET Leader – Mr. TAM

## EXECUTIVE SUMMARY

- ES.01. Civil Engineering and Development Department (hereafter referred as “CEDD”) is the Project Proponent for the Project “*Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery*” (hereafter referred as “the Project”). The Project is a Designated Project to be implemented under Environmental Permit No. EP-534/2017 and FEP-01/534/2017. On 24 December 2018 EPD issued Environmental Permit No. EP-534/2017/A and FEP-01/534/2017/A for the Project. To facilitate the Project management, the Project works were separated into three different Contracts and they are listed below.
- CEDD Contract No. CV/2016/10 - *Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery* (hereafter referred as “**Contract 1**”)
  - CEDD Contract No. CV/2017/02 - *Infrastructural Works at Man Kam To Road and Lin Ma Hang Road for Development of Columbarium at Sandy Ridge Cemetery* (hereafter referred as “**Contract 2**”)
  - Other CEDD’s Contract as related Development of Columbarium at Sandy Ridge Cemetery (hereafter referred as “**Contract 3**”)
- ES.02. Action-United Environmental Services & Consulting (hereinafter referred as “AUES”) has been commissioned by the Contractors as an Environmental Team (hereinafter referred as “the ET”) to implement the Environmental Monitoring & Audit (EM&A) programme in accordance with the approved EM&A Manual as well as the associated duties.
- ES.03. The Construction works of Contract CV/2016/01 - Contract 1 implemented under FEP-01/534/2017 was commenced on 16 August 2018 and construction phase impact monitoring has been started on 16 August 2018. Furthermore, EPD issued Environmental Permit No. FEP-01/534/2017/A on 24 December 2018. The construction works of Contract CV/2017/02 - Contract 2 implemented under EP-534-2017 was commenced on 5 November 2018 and construction phase impact monitoring has been started on 5 November 2018. Furthermore, EPD issued Environmental Permit No. EP-534/2017/A on 24 December 2018.
- ES.04. This is the 6<sup>th</sup> monthly Environmental Monitoring and Audit Report reporting the monitoring results and inspection findings under the Project for the period from 1 to 31 January 2019 (the Reporting Month).

## ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

- ES.05. In the Reporting Month, the major construction works under the Project included Contract 1 and Contract 2. Environmental monitoring activities under the EM&A programme in this Reporting Month are summarized in the following table.

Issues	Environmental Monitoring Parameters / Inspection	Monitoring Locations		Total Occasions
		CV/2016/10	CV/2017/12	
Air Quality	1-hour TSP	ASR-1	ASR-2	45
	24-hour TSP		ASR-3	15
Construction Noise	Leq (30min) Daytime	CN-1 CN-2	CN-3 CN-4	20
Water Quality	In-situ measurement and Water sampling	M3	M1, M2 and M4	13
Ecology	Monthly Monitoring	Transect within site area of CV/2016/10	Transect within site area of CV/2017/12	1
Landscape & Visual	Site Inspection	Site area of CV/2016/10	Site area of CV/2017/12	1
Inspection & Audit	ET Regular Environmental Site Inspection	Site area of CV/2016/10	Site area of CV/2017/12	4
	IEC Monthly Environmental Site Audit			3

### BREACH OF ACTION AND LIMIT (A/L) LEVELS

- ES.06. No exceedance of air quality, construction noise and water quality monitoring was recorded in this Reporting Month. No Notification of Exceedance (NOE) of water quality was issued. The statistics of environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

**Table ES-5 Breach of Action and Limit (A/L) Levels in the Reporting Period**

Environmental Issues	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation findings	Corrective Actions
Air Quality	1-hour TSP	0	0	0	-	-
	24-hour TSP	0	0	0	-	-
Construction Noise	Leq <sub>30min</sub> Daytime	0	0	0	-	-
Water Quality	DO	0	0	0	-	-
	Turbidity	0	0	0	-	-
	SS	0	0	0	-	-

Note: NOE – Notification of Exceedance

### ENVIRONMENTAL COMPLAINT

- ES.07. No environmental complaint was recorded or received in this Reporting Month. The statistics of environmental complaint are summarized in the following table.

**Table ES-6 Environmental Complaint Summaries in the Reporting Month**

Reporting Period		Environmental Complaint Statistics		
		Frequency	Cumulative	Complaint Nature
1 – 31 Jan 2019	Contract 1	0	0	NA
1 – 31 Jan 2019	Contract 2	0	0	NA

- ES.08. In addition, no complaints and emergency events relating to violation of environmental legislation for illegal dumping and landfilling was received.

### NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

- ES.09. No environmental summons or successful prosecution was recorded in this Reporting Month. The statistics of summons or successful prosecutions are summarized in the following tables.

**Table ES-7 Environmental Summons Summaries in the Reporting Month**

Reporting Period		Environmental Complaint Statistics		
		Frequency	Cumulative	Summons Nature
1 – 31 Jan 2019	Contract 1	0	0	NA
1 – 31 Jan 2019	Contract 2	0	0	NA

**Table ES-8 Environmental Prosecution Summaries in the Reporting Month**

Reporting Period		Environmental Complaint Statistics		
		Frequency	Cumulative	Prosecution Nature
1 – 31 Jan 2019	Contract 1	0	0	NA
1 – 31 Jan 2019	Contract 2	0	0	NA

### REPORTING CHANGE

- ES.010. No reporting change was made in the Reporting Month.

### SITE INSPECTION

- ES.011. In this Reporting Month, joint site inspections to evaluate the site environmental performance at **Contract 1** have been carried out by the RE, ET and the Contractor on **3<sup>rd</sup>, 10<sup>th</sup>, 17<sup>th</sup>, 24<sup>th</sup> and 31<sup>st</sup> January 2019** and IEC attended joint site inspection on **24<sup>th</sup> January 2019**. No non-compliance was noted.

ES.012. In the Reporting Period, joint site inspections to evaluate the site environmental performance at ***Contract 2*** have been carried out by the RE, ET and the Contractor on ***3<sup>rd</sup>, 10<sup>th</sup>, 17<sup>th</sup>, 24<sup>th</sup> and 31<sup>st</sup> January 2019*** and IEC attended joint site inspection on ***24<sup>th</sup> January 2019***. No non-compliance was noted.

#### **FUTURE KEY ISSUES**

- ES.013. The Contractors should pay special attention on water quality mitigation measures and fully implement according to the ISEMM of the EM&A Manual, in particular to prevent surface runoff with high SS content and other pollutants from flowing to local stream and Conservation Area (CA).
- ES.014. Moreover, air quality and construction noise are the major environmental issues as under the Project Works. Air quality mitigation measures such as wheel wash facilities, watering of haul roads and covering of dusty materials with tarpaulin sheet should be implemented as far as practicable. Construction noise mitigation measures such as use of movable noise barriers and Quality Powered Mechanical Equipment (QPME) should be properly provided to reduce construction noise impact.
- ES.015. Furthermore, daily cleaning and weekly tidiness shall be properly performed and maintained. In addition, mosquito control should be performed to prevent mosquito breeding on site.

## Table of Contents

<b>1</b>	<b>INTRODUCTION</b>	<b>1</b>
1.1	PROJECT BACKGROUND	1
1.2	REPORT STRUCTURE	2
<b>2</b>	<b>PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS</b>	<b>4</b>
2.1	CONSTRUCTION CONTRACT PACKAGING	4
2.2	CONSTRUCTION PROGRESS	4
2.3	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	4
2.4	SUMMARY OF SUBMISSION UNDER THE ENVIRONMENTAL PERMIT REQUIREMENTS	5
<b>3</b>	<b>SUMMARY OF IMPACT MONITORING REQUIREMENT</b>	<b>7</b>
3.1	GENERAL	7
3.2	MONITORING PARAMETERS	7
3.3	MONITORING LOCATIONS	7
3.4	MONITORING FREQUENCY AND PERIOD	9
3.5	MONITORING EQUIPMENT	10
3.6	EQUIPMENT CALIBRATION	12
3.7	DATA MANAGEMENT AND DATA QA/QC CONTROL	13
3.8	DETERMINATION OF ACTION/LIMIT (A/L) LEVELS	13
<b>4</b>	<b>AIR QUALITY</b>	<b>15</b>
4.1	MONITORING RESULTS	15
4.2	AIR MONITORING EXCEEDANCE	15
<b>5</b>	<b>CONSTRUCTION NOISE</b>	<b>17</b>
5.1	MONITORING RESULTS	17
5.2	NOISE MONITORING EXCEEDANCE	17
<b>6</b>	<b>WATER QUALITY</b>	<b>18</b>
6.1	MONITORING RESULTS	18
6.2	WATER QUALITY MONITORING EXCEEDANCE	19
<b>7</b>	<b>ECOLOGY MONITORING</b>	<b>20</b>
7.1	REQUIREMENT	20
7.2	METHODOLOGY	20
7.3	ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 1)	21
7.4	ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 2)	23
<b>8</b>	<b>LANDSCAPE AND VISUAL</b>	<b>26</b>
8.1	REQUIREMENT	26
8.2	FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH	26
<b>9</b>	<b>WASTE MANAGEMENT</b>	<b>27</b>
9.1	GENERAL WASTE MANAGEMENT	27
9.2	RECORDS OF WASTE QUANTITIES	27
<b>10</b>	<b>SITE INSPECTION</b>	<b>28</b>
10.1	REQUIREMENT	28
10.2	FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH	28
<b>11</b>	<b>ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE</b>	<b>30</b>
11.1	ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	30
<b>12</b>	<b>IMPLEMENTATION STATUS OF MITIGATION MEASURES</b>	<b>31</b>
12.1	GENERAL REQUIREMENTS	31
12.2	TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH	31
12.3	KEY ISSUES FOR THE COMING MONTH	32
<b>13</b>	<b>CONCLUSIONS AND RECOMMENDATIONS</b>	<b>33</b>
13.1	CONCLUSIONS	33
13.2	RECOMMENDATIONS	33

## **LIST OF TABLES**

TABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS FOR CONTRACT 1
TABLE 2-2	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS FOR CONTRACT 2
TABLE 2-3	STATUS OF SUBMISSION AS UNDER FEP FOR CONTRACT 1
TABLE 2-4	STATUS OF SUBMISSION AS UNDER FEP FOR CONTRACT 2
TABLE 3-1	SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2	DESIGNATED AIR QUALITY MONITORING LOCATION UNDER THE PROJECT
TABLE 3-3	DESIGNATED CONSTRUCTION NOISE MONITORING LOCATION UNDER THE PROJECT
TABLE 3-4	DESIGNATED WATER QUALITY MONITORING STATIONS UNDER THE PROJECT
TABLE 3-5	AIR QUALITY MONITORING EQUIPMENT
TABLE 3-6	NOISE MONITORING EQUIPMENT
TABLE 3-7	WATER QUALITY MONITORING EQUIPMENT
TABLE 3-8	ACTION AND LIMIT LEVELS FOR AIR QUALITY MONITORING
TABLE 3-9	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 3-10	ACTION AND LIMIT LEVELS FOR WATER QUALITY
TABLE 4-1	SUMMARY OF AIR QUALITY MONITORING RESULTS AT ASR-1 UNDER CONTRACT 1
TABLE 4-2	SUMMARY OF AIR QUALITY MONITORING RESULTS AT ASR-2 UNDER CONTRACT 2
TABLE 4-3	SUMMARY OF AIR QUALITY MONITORING RESULTS AT ASR-3A UNDER CONTRACT 2
TABLE 5-1	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS UNDER CONTRACT 1
TABLE 5-2	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS UNDER CONTRACT 2
TABLE 6-1	SUMMARY OF WATER QUALITY MONITORING RESULTS – M3 UNDER CONTRACT 1
TABLE 6-2	SUMMARY OF WATER QUALITY MONITORING RESULTS (M1, M2 AND M4) UNDER CONTRACT 2
TABLE 6-3	SUMMARY OF FIELD MEASUREMENTS FOR WATER QUALITY
TABLE 6-4	ACTION AND LIMIT (A/L) LEVELS EXCEEDANCE RECORD
TABLE 6-5	SUMMARY OF INVESTIGATION OF WATER QUALITY EXCEEDANCE IN THE REPORTING PERIOD
TABLE 7-1	ACTION AND LIMIT LEVELS FOR WET WOODLAND HABITATS MONITORING
TABLE 7-2	ACTION AND LIMIT LEVELS FOR NON-WET WOODLAND HABITATS MONITORING
TABLE 7-3	SCHEDULE OF FAUNAL SURVEYS IN EACH YEAR DURING CONSTRUCTION PHASE
TABLE 7-4	RESULT OF AVIFAUNA SURVEY UNDER CONTRACT 1
TABLE 7-5	RESULT OF REPTILE SURVEY UNDER CONTRACT 1
TABLE 7-6	RESULT OF AMPHIBIAN SURVEY UNDER CONTRACT 1
TABLE 7-7	RESULT OF BUTTERFLY SURVEY UNDER CONTRACT 1
TABLE 7-8	RESULT OF ODONATE SURVEY UNDER CONTRACT 1
TABLE 7-9	RESULT OF FRESHWATER COMMUNITIES SURVEY UNDER CONTRACT 1
TABLE 7-10	RESULT OF AVIFAUNA SURVEY UNDER CONTRACT 2
TABLE 7-11	RESULT OF REPTILE SURVEY UNDER CONTRACT 2
TABLE 7-12	RESULT OF AMPHIBIAN SURVEY UNDER CONTRACT 2
TABLE 7-13	RESULT OF BUTTERFLY SURVEY UNDER CONTRACT 2
TABLE 7-14	RESULT OF ODONATE SURVEY UNDER CONTRACT 2
TABLE 7-15	RESULT OF FRESHWATER COMMUNITIES SURVEY UNDER CONTRACT 2
TABLE 8-1	LANDSCAPE & VISUAL INSPECTION FINDING FOR CONTRACT 1
TABLE 8-2	LANDSCAPE & VISUAL INSPECTION FINDING FOR CONTRACT 2
TABLE 9-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 9-2	SUMMARY OF QUANTITIES OF C&D WASTES



TABLE 10-1	SITE OBSERVATIONS FOR THE WORKS OF CONTRACT-1
TABLE 11-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 11-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 11-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 12-1	ENVIRONMENTAL MITIGATION MEASURES

**LIST OF APPENDICES**

APPENDIX A	LAYOUT PLAN OF THE PROJECT
APPENDIX B	ORGANIZATION STRUCTURE AND CONTACT DETAILS OF RELEVANT PARTIES
APPENDIX C	THREE MONTHS ROLLING PROGRAMME
APPENDIX D	DESIGNATED MONITORING LOCATIONS
APPENDIX E	CALIBRATION CERTIFICATES OF MONITORING EQUIPMENT AND LABORATORY CERTIFICATE
APPENDIX F	EVENT AND ACTION PLAN OF AIR QUALITY, NOISE AND WATER QUALITY
APPENDIX G	MONITORING SCHEDULES OF THE REPORTING MONTH AND COMING MONTH
APPENDIX H	MONITORING DATA OF 24-HOUR TSP AIR QUALITY, NOISE AND WATER QUALITY
APPENDIX I	GRAPHICAL PLOTS OF AIR QUALITY, NOISE AND WATER QUALITY
APPENDIX J	METEOROLOGICAL DATA OF THE REPORTING PERIOD
APPENDIX K	ECOLOGY SURVEY REPORT
APPENDIX L	LANDSCAPE & VISUAL INSPECTION CHECKLIST
APPENDIX M	MONTHLY SUMMARY WASTE FLOW TABLE
APPENDIX N	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM)

## **1 INTRODUCTION**

### **1.1 PROJECT BACKGROUND**

- 1.1.1 Civil Engineering and Development Department is the Project Proponent for the Project “*Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery*”. The Project is a Designated Project to be implemented under Environmental Permit No. EP-534/2017/A and FEP-01/534/2017/A. The layout plan of the Project is shown in [Appendix A](#). Major works to be executed under the Project shall include to the following:

#### *A Designated Works under EP-534/2017/A*

- (i) Site formation of about 8 hectares of land and associated drainage, sewerage and landscape works for development of Columbarium and Crematorium facilities at the Sandy Ridge Cemetery;
- (ii) Construction of a new road (about 600m) including a section of viaduct connecting the platform for Crematorium and Man Kam To Road and the pick-up/drop-off point at Man Kam To Road.;
- (iii) Widening of about 900m of the existing Sha Ling Road;
- (iv) Widening of about 1.4km of the existing Lin Ma Hang Road; and
- (v) Improvement works to the existing bargaining point at Siu Lam

#### *Non-Designated Works*

- (i) Construction of a sewage detention tank complete with odour and septicity control mechanism;
- (ii) Construction of noise barriers along Sha Ling Road;
- (iii) Construction of a new Refuse Collection Point (RCP) near the junction between Man Kam To Road and Sha Ling Road;
- (iv) Landscaping works (including both hard and soft landscape works);
- (v) Associated tree felling, transplanting and compensatory planting works;
- (vi) Associated street lighting, street furniture and road marking, etc.; and
- (vii) Other works which are specified in PS of the Contract.

- 1.1.2 To facilitate the Project management, the Project works were separated into three different Contracts which are described below sub-sections.

- 1.1.3 *Contract No. CV/2016/10 - Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery:-*

- Site formation of about 1.77 ha of land for the proposed pick-up and drop-off area for shuttle bus operation;
- Upgrading of a section of 900m existing Sha Ling Road from 3m wide carriageway to 7.3m wide carriageway with footpath at both sides;
- Construction of one EVA with a total length of about 160m;
- Construction of noise barriers along Sha Ling Road;
- Modification of junction between Man Kam To Road and Sha Ling Road;
- Construction of a new pick up / drop off point at Man Kam To Road;
- Relocation and construction of a new refuse collection point near junction between Man Kam To Road and Sha Ling Road;
- Associated geotechnical works including cut and fill slopes, soil nailing works and retaining structures;
- Associated drainage, sewerage and waterworks along Sha Ling Road; and
- Associated landscaping works.

- 1.1.4 *Contract No. CV/2017/02 - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road for Development of Columbarium at Sandy Ridge Cemetery:-*

- Construction of a new road connecting Columbarium site to Crematorium site;
- Construction of one EVA with a total length of about 300m;
- Widening of a section of 1.4 km long Lin Ma Hang Road (between Man Kam To Road and Ping Yuen River) from 6m wide carriageway to 7.3m with 2m width footpath on both sides;
- Provision of a pair of lay-by at Lin Ma Hang Road;
- Construction of a new vehicular access connecting the Sheung Shui Landmark North PTI and Lung Sum Avenue;
- Construction of covered walkway along Fanling Station Road;
- Removal of planters and central divider along Fanling Station Road and San Wan Road;
- Associated drainage, sewerage, waterworks and utility works along Man Kam To Road and Lin Ma Hang Road;
- Associated geotechnical works including cut and fill slopes, soil nailing works and retaining structures; and
- Associated landscaping works.

1.1.5 *CEDD Contract No. (to be advised):-*

- Site Formation for the platform of the columbarium site;
- Construction of two 2 at-grade access roads;
- Construction of road junction between Man Kam To Road and the new access road;
- Associated drainage, sewerage and waterworks along the two new access roads;
- Associated geotechnical works including cut and fill slopes, soil nailing works and retaining structures; and
- Associated landscaping works

1.1.6 Hsin Chong Tsun Yip Joint Venture (hereafter referred as “HCTYJV”) has been awarded Contract 1 on 5 December 2017. According to the Contract requirement, HCTYJV shall take over the responsibility for part of the Environmental Permit No. EP-534/2017 for ease of management, therefore application for Further Environmental Permit was submitted by HCTYJV to EPD on 26 January 2018 and Further Environmental Permit No. FEP-01/534/2017 was granted to HCTYJV by EPD on 23 February 2018. Furthermore, EPD issued Environmental Permit No. FEP-01/534/2017/A on 24 December 2018.

1.1.7 Sang Hing Civil Contractors Company Limited (hereinafter referred as “Sang Hing”) was awarded Contract 2 on 23 May 2018. The Contract Works is a Designated Project as under Environmental Permit (EP) No. EP-534/2017. Furthermore, EPD issued Environmental Permit No. EP-534/2017/A on 24 December 2018.

1.1.8 Action-United Environmental Services & Consulting has been commissioned by the Contractors as an Environmental Team to implement the EM&A programme in accordance with the approved EM&A Manual as well as the associated duties. As part of the EM&A programme, baseline monitoring to determine the ambient environmental conditions was completed before construction work commencement. The Baseline Monitoring Report (air, noise and water) certified by ET Leader (ETL) and verified by Independent Environmental Checker (IEC) was submitted to Environmental Protection Department (EPD) and it was approved by EPD on 25 October 2018.

1.1.9 This is the 6<sup>th</sup> monthly Environmental Monitoring and Audit Report to reporting the monitoring results and inspection findings for the period from 1 to 31 January 2019.

## 1.2 REPORT STRUCTURE

1.2.1 The Monthly Environmental Monitoring and Audit (EM&A) Report is structured into the following sections:-

<b>Section 1</b>	<i>Introduction</i>
<b>Section 2</b>	<i>Project Organization and Construction Progress</i>
<b>Section 3</b>	<i>Summary of Monitoring Requirements</i>
<b>Section 4</b>	<i>Air Quality Monitoring Results</i>
<b>Section 5</b>	<i>Noise Monitoring Results</i>
<b>Section 6</b>	<i>Water Quality Monitoring Results</i>
<b>Section 7</b>	<i>Ecology Monitoring Results</i>
<b>Section 8</b>	<i>Landscape &amp; Visual</i>
<b>Section 9</b>	<i>Waste Management</i>
<b>Section 10</b>	<i>Site Inspections</i>
<b>Section 11</b>	<i>Environmental Complaints and Non-Compliance</i>
<b>Section 12</b>	<i>Implementation Status of Mitigation Measures</i>
<b>Section 13</b>	<i>Conclusions and Recommendation</i>

## 2 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

### 2.1 CONSTRUCTION CONTRACT PACKAGING

2.1.1 To facilitate the project management and implementation, the Project would be divided by the following contracts:

- Contract 1 (Contract No. CV/2016/10)
- Contract 2 (Contract No. CV/2017/02)
- Contract 3 (Contract No. TBA)

2.1.2 Organization structure and contact details of relevant parties with respect to on-site environmental management are shown in [Appendix B](#).

### 2.2 CONSTRUCTION PROGRESS

2.1.3 The three-month rolling construction programme for Contract 1 and Contract 2 are enclosed in [Appendix C](#). The construction activities undertaken in this Reporting Month are listed below:-

#### Contract 1 (CV/2016/10)

2.1.4 Contract 1 was awarded in December 2017 and major construction work was commenced on 16 August 2018. The construction activities undertaken in this Reporting Month is listed below:

- General site clearance
- Bulk Excavation
- Construction of Cut Slope, installation of soil nailing and construction of surface channel.
- Construction of retaining wall
- Construction of fill slope

#### Contract 2 (CV/2017/12)

2.1.5 Contract 2 was awarded in May 2018 and construction work was tentatively commenced on 5 November 2018. The construction activities undertaken in this Reporting Month is listed below:

- Site preparation of PM's Office
- Trial pit excavation along Lin Ma Hang Road and Man Kam To Road.
- Construction of Manhole, gullies, drainage pipe at Lin Ma Hang Road between CH280-340 & CH1015-1075 Northbound.
- Construction of step channel of CS22 at Part A1

### 2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

2.1.6 Summary of the relevant permits, licences, and/or notifications on environmental protection for this Project in this Reporting Month is presented in [Tables 2-1 and 2-2](#).

**Table 2-1 Status of Environmental Licenses and Permits for Contract 1**

Item	Description	License/ Permit ref no.	License/ Permit Status
1	Air Pollution Control (Construction Dust) Regulation	Ref. no. 428909 Acknowledged by EPD on 20/12/2017	Valid
2	Chemical waste Producer Registration	WPN: 5231-641-H3937-01 Issued by EPD on 27/03/2018	Valid
3	Water Pollution Control Ordinance	License no. WT00030795-2018 Issued date: 9/5/2018 Expire Date: 31/5/2023	Valid
4	Billing Account for Disposal of	Account no.: 7029769	Valid



Item	Description	License/ Permit ref no.	License/ Permit Status
	Construction Waste		

**Table 2-2 Status of Environmental Licenses and Permits for Contract 2**

Item	Description	License/ Permit ref no.	License/ Permit Status
1	Chemical waste Producer Registration	Pending approval from EPD	
2	Water Pollution Control Ordinance	License no: WT00032936-2018 Issued date: 16/01/2019 Expire Date: 31/01/2024	Valid
3	Billing Account for Disposal of Construction Waste	Account no.: 7031098	Valid

## 2.4 SUMMARY OF SUBMISSION UNDER THE ENVIRONMENTAL PERMIT REQUIREMENTS

2.1.7 **Tables 2-3 to 2-4** summarized the submission status under the EP and/or FEP stipulation in the Reporting Month.

**Table 2-3 Status of Submission as under FEP for Contract 1**

Item	EP and / or FEP Stipulation	Description	Status
1	Condition 2.10 of FEP	Management organization of : i) the main construction companies; ii) ET; and iii) IEC and the supporting team	Submitted on 11 April 2018
2	Condition 2.11 of FEP	i) Detailed phasing programme of all construction works; and ii) Location plan of all construction works	Submitted on 12 April 2018
3	Condition 2.12 of FEP	Contamination Assessment Plan (CAP)	Submitted on 11 October 2018
4	Condition 2.13 of FEP	Grassland Reinstatement Plan	Submitted on 28 May 2018
5	Condition 2.14 of FEP	Vegetation Survey Report for Contract 1	Approved by EPD on 12 October 2018
6	Condition 2.15 of FEP	Vegetation Transplantation Proposal Contract 1	Approved by EPD on 12 October 2018
7	Condition 2.17 of FEP	Woodland Compensation Plan	Submitted on 15 May 2018
8	Condition 2.18 of FEP	Monitoring and Survey Plan for Golden-headed Cisticola Contract 1	Submitted on 9 May 2018
9	Condition 2.20 of FEP	Landscape & Visual Mitigation and Tree Preservation Plan(s) Contract 1	Submitted on 18 May 2018
10	Condition 2.22 of FEP	Traffic Noise Mitigation Plan Contract 1	Submitted on 17 July 2018
11	Condition 3.3 of the FEP	Baseline Monitoring Report (Air, Noise and Water)	Approved by EPD on 25 October 2018
12	Condition 4.2 of the FEP	The Contract Internet website	Internet website address has notified EPD on 15 Jun 2018

**Table 2-3 Status of Submission as under EP for Contract 2**

Item	EP and / or FEP Stipulation	Description	Status
1a	Condition 2.10 of EP	Management organization of : i) the main construction companies; ii) ET; and iii) IEC and the supporting team	Submitted on 24 September 2018

Item	EP and / or FEP Stipulation	Description	Status
2a	Condition 2.11 of EP	i) Detailed phasing programme of all construction works; and ii) Location plan of all construction works	Submitted on 26 September 2018
3	Condition 2.13 of EP	Contamination Assessment Plan (CAP)	Submitted on 11 October 2018
4	Condition 2.14 of EP	Grassland Reinstatement Plan	Submitted on 28 May 2018
5	Condition 2.15 of EP and	Vegetation Survey Report Contract 2	Submitted on 28 September 2018
6	Condition 2.16 of EP	Vegetation Transplantation Proposal Contract 2	Submitted on 28 September 2018
7	Condition 2.18 of EP	Woodland Compensation Plan	Submitted on 15 May 2018
8	Condition 2.19 of EP	Monitoring and Survey Plan for Golden-headed Cisticola Contract 2	Submitted on 4 October 2018
9	Condition 2.22 of EP	Landscape & Visual Mitigation and Tree Preservation Plan(s) Contract 2	Submitted on 5 October 2018
10	Condition 2.24 of EP	Traffic Noise Mitigation Plan Contract 2	Submitted on 4 October 2018
11	Condition 3.3 of the EP	Baseline Monitoring Report (Air, Noise and Water)	Approved by EPD on 25 October 2018
12	Condition 4.2 of the EP	The Contract Internet website	Internet website address has notified EPD on 15 June 2018

### 3 SUMMARY OF IMPACT MONITORING REQUIREMENT

#### 3.1 GENERAL

3.1.1 The Environmental Monitoring and Audit requirements are set out in the Approved EM&A Manual. Environmental issues such as air quality, construction noise, water quality and ecology were identified as the key issues during the construction phase of the Project.

3.1.2 A summary of construction phase EM&A requirements are presented in the sub-sections below.

#### 3.2 MONITORING PARAMETERS

3.2.1 The EM&A impact monitoring shall cover the following environmental aspect:

- Air quality;
- Construction noise;
- Water quality; and
- Ecology

3.2.2 A summary of the monitoring parameters is presented in *Table 3-1* below

**Table 3-1 Summary of EM&A Requirements**

Environmental Issue	Parameters
Air Quality	<ul style="list-style-type: none"> <li>• 1-hour TSP;</li> <li>• 24-hour TSP</li> </ul>
Noise	<ul style="list-style-type: none"> <li>• <math>Leq_{(30min)}</math> during normal working hours.; and</li> <li>• <math>Leq_{(15min)}</math> during the construction works is undertaken in Restricted Hours</li> </ul>
Water Quality	<b>In-situ Measurements</b> <ul style="list-style-type: none"> <li>• Dissolved Oxygen Concentration (mg/L) &amp; Saturation (%) ;</li> <li>• Temperature (°C);</li> <li>• Turbidity (NTU);</li> <li>• Salinity (ppm)</li> <li>• pH unit;</li> <li>• Water depth (m); and</li> <li>• Stream Flow Velocity (m/sec).</li> </ul>
	<b>Laboratory Analysis</b> <ul style="list-style-type: none"> <li>• Suspended Solids (mg/L)</li> </ul>
Ecology	Ecologically sensitive habitats (wetland habitats and non-wetland habitats)

#### 3.3 MONITORING LOCATIONS

3.3.1 According to the Approved EM&A Manual of the Project - *Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery*, the designated monitoring locations for air quality, noise, water quality and ecology under the monitoring programme, is shown in [Appendix D](#).

3.3.2 Since the Project was divided into three Works Contracts and all Contracts will be commenced at different time, the construction phase impact monitoring will only be performed at the Contract-related monitoring stations upon commencement of each Contract Works.

##### Air Quality

3.3.3 There were three (3) designated air quality monitoring stations recommended in the Approved EM&A Manual Section 5.6.1.1. There was proposed relocation of air quality monitoring location ASR-3 in October 2018 since the landlord refused to set up the HVS at his premises and nearby area

due to noise nuisance and Muk Wu Nga Yiu House No. 2A was proposed as alternative location ASR-3a. The proposal dated on 9 November 2018 which verified by IEC was submitted to EPD for approval. Based on rationale in Section 3.3.2, the Contract-related air quality monitoring location for construction phase were summarized in **Table 3-2** and illustrated in [Appendix D](#).

**Table 3-2 Designated Air Quality Monitoring Location under the Project**

Location ID	Description in EM&A Manual	Location	Related Work Contract
ASR-1	Village House along Man Kam To Road	Sha Ling Village House No.6	Contract 1
ASR-2	Village House at San Uk Ling	San Uk Ling Village House No.1	Contract 2
ASR-3	Village House at Muk Wu Nga Yiu	Muk Wu Nga Yiu House No.28	Contract 2
ASR-3a (#)	Village House at Muk Wu Nga Yiu	Muk Wu Nga Yiu House No.2A	Contract 2

*Remark: (#)*

*There was proposed relocation of air quality monitoring location ASR-3 in October 2018. The proposal dated on 9 November 2018 after verified by IEC was submitted to EPD for approval.*

3.3.4 If the designated monitoring location is required to relocate, alternative monitoring location shall agree with IEC and seek for EPD approval which shall meet the following criteria:

- i) Be at the site boundary or such locations close to the major dust emission source;
- ii) Close to the sensitive receptors;
- iii) Take into account the prevailing meteorological conditions;
- iv) For monitoring location located in the vicinity of the ASRs, care shall be taken to cause minimal disturbance to the occupants during monitoring.
- v) When positioning the HVS, the following points shall be noted:
  - a. a horizontal platform with appropriate support to secure the samples against gusty wind shall be provided;
  - b. no two samplers shall be placed less than 2m apart;
  - c. the distance between the HVS and an obstacle, such as buildings, must be at least twice the height that the obstacle protrudes above the HVS;
  - d. a minimum of 2 m separation from walls, parapets and penthouses is required for HVS at the rooftop;
  - e. a minimum of 2 m separation from any supporting structure, measures horizontally is required;
  - f. no furnace or incinerator flue is nearby;
  - g. airflow around the sampler is unrestricted;
  - h. the HVS is more than 20 m from the dripline;
  - i. any wire fence and gate to protect the HVS, shall not cause any obstruction during monitoring;
  - j. permission must be obtained to set up the HVS and to obtain access to the monitoring stations; and
  - k. a secured supply of electricity is needed to operate the HVS.

### **Construction Noise**

3.3.5 There were four (4) designated noise monitoring locations recommended in the Approved EM&A Manual Section 6.5.1.1. Based on rationale in Section 3.3.2, the Contract-related noise quality monitoring location for construction phase were summarized in **Table 3-3** and illustrated in [Appendix D](#).

**Table 3-3 Designated Construction Noise Monitoring Location under the Project**

Location ID	Description in EM&A Manual	Location	Related Work Contract
CN-1	Village house to the west of Sha Ling Road	Village house to the west of Sha Ling Road (free field condition)	Contract 1
CN-2	Village house to the north of Man Kam To Road	Sha Ling Village House No. 25 (free field condition)	Contract 1 & 3
CN-3	Village house near San Uk Ling	San Uk Ling Village House No. 18 (free field condition)	Contract 2
CN-4	Village house of Muk Wu	Muk Wu Village House No. 267 (1m façade from the building)	Contract 2

### Water Quality

- 3.3.6 There were four (4) water quality monitoring locations recommended in the Approved EM&A Manual Section 7.6.1.2. The locations and coordinates of water quality monitoring were listed in **Table 3-4**. Based on rationale in Section 3.3.2, the Contract-related noise quality monitoring location for construction phase were summarized in **Table 3-4** and illustrated in [Appendix D](#).

**Table 3-4 Designated Water Quality Monitoring Stations under the Project**

Proposed Location ID	Co-ordinates		Description	Related Work Contract
	North	East		
M1	843 431	831 308	Midstream of Nam Hang Stream	Contract 2
M2	843 840	831 101	Downstream of Nam Hang Stream	Contract 2
M3	843 509	830 040	Wetland in the Conservation Area (CA) near Yuen Leng Chai	Contract 1
M4	843 997	831 783	Watercourse across Lin Ma Hang Road, running from east of San Uk Ling to Man Kam To Boundary Control Point	Contract 2

### **3.4 MONITORING FREQUENCY AND PERIOD**

- 3.4.1 The requirements of impact monitoring were stipulated in *Sections 5.8.1.1, 6.7.1.1 and 7.8.1.4* of the approved *EM&A Manual* and presented as follows.

#### Air Quality Monitoring

- 3.4.2 Monitoring frequency for air quality impact monitoring is as follows:

- 1-Hour TSP 3 sets of 1-hour TSP monitoring shall be carried out once every six days during construction periods
- 24-Hour TSP 24-hour TSP monitoring shall be carried out every six days during construction periods

#### Noise Monitoring

- 3.4.3 Noise impact monitoring shall be carried out once per week during construction periods. The noise measurement for the time period between 0700 and 1900 hours shall be measured in terms of  $L_{eq}$  (30 minutes) or 6 sets of  $L_{eq}$  (5mins).

#### Water Quality Monitoring

- 3.4.4 The monitoring frequency shall be 3 days per week during construction phase and the interval between two sets of monitoring shall not be less than 36 hours.

### 3.5 MONITORING EQUIPMENT

- 3.5.1 The monitoring equipment using for the EM&A program as proposed by the ET shall be verified by the IEC.

#### **Air Quality Monitoring**

- 3.5.2 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. If ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to IEC for approval.
- 3.5.3 The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.
- 3.5.4 All equipment used by ET for air quality monitoring is listed in **Table 3-5**.

**Table 3-5 Air Quality Monitoring Equipment**

Equipment	Model
<b><i>24-hour TSP</i></b>	
High Volume Air Sampler (HVAS)	TISCH High Volume Air Sampler, HVS Model TE-5170
Calibration Kit	TISCH Model TE-5025A
<b><i>1-Hour TSP</i></b>	
Portable Dust Meter	Sibata LD-3 Laser Dust monitor Particle Mass Profiler & Counter

#### **Wind Data Monitoring Equipment**

- 3.5.5 According to the approved EM&A Manual, wind data monitoring equipment shall also be provided and set up for logging wind speed and wind direction near the dust monitoring locations. The equipment installation location shall be proposed by the ET and agreed with the IEC. For installation and operation of wind data monitoring equipment, the following points shall be observed:
- 1) The wind sensors should be installed 10 m above ground so that they are clear of obstructions or turbulence caused by buildings.
  - 2) The wind data should be captured by a data logger. The data shall be downloaded for analysis at least once a month.
  - 3) The wind data monitoring equipment should be re-calibrated at least once every six months.
  - 4) Wind direction should be divided into 16 sectors of 22.5 degrees each.
- 3.5.6 ET has liaised with the premises owners/ landlords to grant the permission for the HVS installation. However, they rejected to set up wind data monitoring equipment installation in their premises.
- 3.5.7 Under this situation, the ET proposed to obtain representative wind data from the Hong Kong Observatory Ta Kwu Ling Weather Station. Ta Kwu Ling Station is located near the Project site which situated at the sea level above 15mPD and the wind data monitoring equipment is installed 10 m above the existing ground.

#### **Noise Monitoring**

- 3.5.8 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in  $\text{ms}^{-1}$



before each noise monitoring event. Noise measurements should not be made in fog, rain, wind with a steady speed exceeding  $5 \text{ m s}^{-1}$  or wind with gusts exceeding  $10 \text{ m s}^{-1}$ .

3.5.9 Noise monitoring equipment used for impact monitoring is listed in *Table 3-6*.

**Table 3-6 Noise Monitoring Equipment**

Equipment	Model
Integrating Sound Level Meter	B&K Type 2238
Calibrator	B&K Type 4231
Portable Wind Speed Indicator	Testo Anemometer

3.5.10 Sound level meters listed above comply with the *International Electrotechnical Commission Publications 651: 1979 (Type 1)* and *804: 1985 (Type 1)* specifications, as recommended in TM issued under the NCO.

#### **Water Quality Monitoring**

3.5.11 Water quality parameters include dissolved oxygen, water temperature & depth, turbidity, salinity, pH and stream flow velocity shall be measured *in-situ*, and suspended solids shall be analyzed by a HOKLAS-accredited testing laboratory.

#### **Dissolved Oxygen and Temperature Measurement**

3.5.12 The dissolved oxygen (DO) measuring instruments should be portable and weatherproof. The equipment should also complete with cable and sensor, and DC power source. It should be capable of measuring:

- A DO level in the range of 0 – 20 mg/L and 0 – 200% saturation; and
- A temperature of 0 – 45 degree Celsius.

3.5.13 The equipment should have a membrane electrode with automatic temperature compensation complete with a cable.

3.5.14 Should salinity compensation not be built-in to the DO equipment, in-situ salinity should be measured to calibrate the DO measuring instruments prior to each measurement.

#### **Turbidity Measurement**

3.5.15 The turbidity measuring instruments should be a portable and weatherproof with DC power source. It should have a photoelectric sensor capable of measuring turbidity level between 0–1000 NTU (for example, Hach model 2100Q or an approved similar instrument).

#### **Salinity Measurement**

3.5.16 A portable salinometer capable of measuring salinity in the range of 0–40 parts per thousand (ppt) should be provided for measuring salinity of the water at each monitoring location.

#### **pH Measurement**

3.5.17 A portable pH meter capable of measuring a range between 0.0 and 14.0 should be provided to measure pH under the specified conditions accordingly to the APHA Standard Methods.

#### **Water Depth Measurement**

3.5.18 A portable, battery-operated echo sounder or an approved similar instrument should be used for water depths determination at each designated monitoring station.

Stream Flow Velocity Equipment

- 3.5.19 Since the EM&A Manuals do not specified instrument to use stream flow velocity measurement, the monitoring of stream flow velocity is therefore proposed to be conducted by using a flow probe which is a digital water velocity meter.

Water Sampling Equipment

- 3.5.20 A water sampler is required for suspended solid (SS) monitoring. A water sampler e.g. Kahlsico Water Sampler, which is a transparent PVC cylinder with capacity not less than 2 litres, will be used for water sampling if water depth over than 0.5m.
- 3.5.21 For sampling from very shallow water depths e.g. <0.5 m, water sample will be collected from water surface below 100mm using plastic bottle to avoid inclusion of bottom sediment or humus. Moreover, Teflon/stainless steel bailer or self-made sampling buckets maybe used for water sampling. The equipment used for sampling will be depended the sampling location and depth situations.

Sample Containers and Storage

- 3.5.22 Water samples for suspended solid should be stored in high density polythene bottles with no preservative added, packed in ice (cooled to 4°C without being frozen) and delivered to the laboratory within 24 hours of collection and be analyzed as soon as possible after collection.
- 3.5.23 Analysis of suspended solids should be carried out in a HOKLAS or other accredited laboratory. Water samples of about 1L should be collected at the monitoring stations for carrying out the laboratory suspended solids determination. The SS determination work should start within 24 hours after collection of the water samples. The SS analyses should follow the *APHA Standard Methods 2540D* with Limit of Reporting of 2 mg/L.
- 3.5.24 Details of the equipment used for water quality monitoring are listed in **Table 3-7** below.

**Table 3-7 Water Quality Monitoring Equipment**

Equipment	Model
Water Depth Detector	Tape measures
Water Sampler	A 2-litre transparent PVC cylinder with latex cups at both ends or teflon/stainless steel bailer or self-made sampling bucket
Thermometer & DO meter	YSI 550A / YSI Pro 20
pH meter	AZ8685 pH meter
Turbidimeter	Hach 2100Q
Salinometer	Atago refractometer Atago S Salinity Meter / AZ8371 Salinity Mete
Stream Flow Velocity	FP211 Global Flow Probe
Sample Container	High density polythene bottles (provided by laboratory)
Storage Container	'Willow' 33-litter plastic cool box with Ice pad

- 3.5.25 Furthermore, Suspended solids (SS) analysis was carried out by *ALS Technichem (HK) Pty Ltd.* which is one a local HOKLAS-accredited laboratory

### 3.6 EQUIPMENT CALIBRATION

- 3.6.1 The HVAS is operated and calibrated on a regular basis in accordance with the manufacturer's instruction using Tisch Calibration Kit Model TE-5025A. Calibration would carry out in two month interval. The calibration data are properly documented and the records are maintained by ET for future reference. Furthermore, Tisch Calibration Kit will be calibrated by the manufacturer

in yearly basis.

- 3.6.2 The 1-hour TSP meter calibrated by a local HOKLAS-accredited laboratory would be undertaken in yearly basis. Zero response of the equipment was checked before and after each monitoring event.
- 3.6.3 The sound level meter and acoustic calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis.
- 3.6.4 The multi-parameter Water Quality Monitoring System is calibrated by HOKLAS accredited laboratory of three month intervals.
- 3.6.5 All updated calibration certificates of the monitoring equipment used for the impact monitoring program in this Reporting Month are attached in [Appendix E](#).

### 3.7 DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.7.1 The impact monitoring data are handled by the ET's systematic data recording and management, which complies with in-house Quality Management System. Standard Field Data Sheets (FDS) are used in the impact monitoring program.
- 3.7.2 The monitoring data recorded in the equipment e.g. 1-hour TSP meter, noise meter and Multi-parameter Water Quality Monitoring System are downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data are input into a computerized database properly maintained by the ET. The laboratory results are input directly into the computerized database and QA/QC checked by personnel other than those who input the data. For monitoring activities require laboratory analysis, the local laboratory follows the QA/QC requirements as set out under the HOKLAS scheme for all laboratory testing.

### 3.8 DETERMINATION OF ACTION/LIMIT (A/L) LEVELS

- 3.8.1 The baseline monitoring results form the basis for determining the environmental acceptance criteria for the impact monitoring. the air quality, construction noise and water quality criteria, namely Action and Limit levels were established according to Approved EM&A Manual, and they are listed in **Tables 3-8, 3-9** and **3-10** below.

**Table 3-8 Action and Limit Levels for Air Quality Monitoring**

Monitoring Station	Action Level ( $\mu\text{g}/\text{m}^3$ )		Limit Level ( $\mu\text{g}/\text{m}^3$ )	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
ASR-1	331	181	500	260
ASR-2	316	165	500	260
ASR-3	307	160	500	260

**Table 3-9 Action and Limit Levels for Construction Noise**

Monitoring Location	Action Level	Limit Level in dB(A)
	Time Period: 0700-1900 hours on normal weekdays	
CN-1,CN-2, CN-3, CN-4	When one or more documented complaints are received	75 dB(A)

Note: \* Reduces to 70 dB(A) for schools and 65 dB(A) during the school examination periods.

**Table 3-10 Action and Limit Levels for Water Quality**

Parameter	Performance criteria	Monitoring Location			
		M1	M2	M3	M4
<b>DO (mg/L)</b>	Action Level	3.03	4.99	4.58	3.62
	Limit Level	2.97	4.90	4.49	3.52
<b>Turbidity (NTU)</b>	Action Level	7.1	39.7	5.6	5.4
	Limit Level	7.6	42.2	5.9	5.9
<b>SS (mg/L)</b>	Action Level	8.5	29.0	9.3	4.8
	Limit Level	10.1	31.0	9.5	5.0
<b>Notes:</b> <ul style="list-style-type: none"> <li>For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits</li> <li>For turbidity and SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.</li> </ul>					

3.8.2 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan enclosed in [Appendix F](#).

## 4 AIR QUALITY

### 4.1 MONITORING RESULTS

- 4.1.1 In the Reporting Month, construction works under the project have been commenced in Contract 1 and Contract 2. Air quality monitoring was performed at all designated locations. Air quality impact monitoring schedule was submitted to all relevant parties which shown in [Appendix G](#).
- 4.1.2 In this Reporting Month, **15** occasions of 24-hour TSP and **45** occasions of 1-hour TSP were undertaken for air quality monitoring. The air quality monitoring results including 24-hour and 1-hour TSP are summarized in **Tables 4-1 to 4-3**. The database of 24-hour TSP is shown in [Appendix H](#) and the graphical plots of 24-hour and 1-hour TSP result are shown in [Appendix I](#).

**Table 4-1 Summary of Air Quality Monitoring Results at ASR-1 under Contract 1**

Date	24-hour TSP ( $\mu\text{g}/\text{m}^3$ )	1-hour TSP ( $\mu\text{g}/\text{m}^3$ )				
		Date	Start Time	1 <sup>st</sup> hour measured	2 <sup>nd</sup> hour measured	3 <sup>rd</sup> hour measured
3-Jan-19	116	4-Jan-19	9:16	34	36	38
9-Jan-19	138	10-Jan-19	9:31	67	69	72
15-Jan-19	77	16-Jan-19	9:10	76	75	76
21-Jan-19	150	22-Jan-19	9:25	93	92	88
26-Jan-19	174	28-Jan-19	9:18	80	84	87
Average (Range)	<b>131</b> (77 - 174)	Average (Range)		<b>71</b> (34 – 93)		

**Table 4-2 Summary of Air Quality Monitoring Results at ASR-2 under Contract 2**

Date	24-hour TSP ( $\mu\text{g}/\text{m}^3$ )	1-hour TSP ( $\mu\text{g}/\text{m}^3$ )				
		Date	Start Time	1 <sup>st</sup> hour measured	2 <sup>nd</sup> hour measured	3 <sup>rd</sup> hour measured
3-Jan-19	42	4-Jan-19	9:21	31	35	36
9-Jan-19	79	10-Jan-19	9:25	64	67	69
15-Jan-19	61	16-Jan-19	9:19	77	72	73
21-Jan-19	72	22-Jan-19	9:33	89	91	87
26-Jan-19	100	28-Jan-19	9:23	81	83	88
Average (Range)	<b>71</b> (42 - 100)	Average (Range)		<b>70</b> (31 – 91)		

**Table 4-3 Summary of Air Quality Monitoring Results at ASR-3a under Contract 2**

Date	24-hour TSP ( $\mu\text{g}/\text{m}^3$ )	1-hour TSP ( $\mu\text{g}/\text{m}^3$ )				
		Date	Start Time	1 <sup>st</sup> hour measured	2 <sup>nd</sup> hour measured	3 <sup>rd</sup> hour measured
3-Jan-19	35	4-Jan-19	9:24	27	31	33
9-Jan-19	63	10-Jan-19	9:22	61	64	67
15-Jan-19	55	16-Jan-19	13:21	75	75	70
21-Jan-19	92	22-Jan-19	9:45	89	92	91
26-Jan-19	119	28-Jan-19	9:27	83	84	88
Average (Range)	<b>73</b> (35 - 119)	Average (Range)		<b>69</b> (27 – 92)		

### 4.2 AIR MONITORING EXCEEDANCE

- 4.2.1 As shown in **Tables 4-1 to 4-3**, the monitoring results of 24-hour and 1-hour TSP monitoring in the

Reporting Month were well below the Action Level. No Notification of Exceedance (NOE) of air quality monitoring criteria was issued and therefore corrective action was not required. The meteorological data during the impact monitoring days are summarized in [Appendix J](#).



## 5 CONSTRUCTION NOISE

### 5.1 MONITORING RESULTS

5.1.1 In the Reporting Month, construction works under the project have been commenced in Contract 1 and Contract 2. It is foreseen that construction works of Contract 1 will be in touch of 300m from monitoring station CN-2, noise monitoring was performed at that location in this Reporting Month. Noise quality monitoring was performed at all designated locations. Noise impact monitoring schedule was submitted to all relevant parties which shown in [Appendix G](#).

5.1.2 In this Reporting Month, **20** occasions of noise monitoring were undertaken at designated noise monitoring location. The sound level were set in a free field situation for CN1, CN2 and CN3 and therefore a façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines. The monitoring result of noise monitoring is show in **Tables 5-1 and 5-2** and the graphical plots are shown in [Appendix I](#).

**Table 5-1 Summary of Construction Noise Monitoring Results under Contract 1**

Construction Noise Level ( $L_{eq30min}$ ), dB(A)				
Date	Start Time	CN1(*)	Start Time	CN2(*)
4-Jan-19	9:54	68	11:30	65
10-Jan-19	9:34	65	11:25	64
16-Jan-19	9:14	70	11:24	67
22-Jan-19	9:45	71	10:27	64
28-Jan-19	13:49	65	14:25	67
<b>Limit Level</b>		<b>75 dB(A)</b>		

(\*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

**Table 5-2 Summary of Construction Noise Monitoring Results under Contract 2**

Construction Noise Level ( $L_{eq30min}$ ), dB(A)				
Date	Start Time	CN3(*)	Start Time	CN4
4-Jan-19	10:07	61	9:28	58
10-Jan-19	11:10	58	10:34	64
16-Jan-19	9:52	58	10:31	63
22-Jan-19	11:04	60	13:00	58
28-Jan-19	15:04	57	15:41	60
<b>Limit Level</b>		<b>75 dB(A)</b>		

(\*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

5.1.3 Prior and after noise monitoring, the accuracy of the sound level meter has been checked by an acoustic calibrator to ensure the measurement within acceptance range of  $\pm 0.5$ dB. Moreover, wind speed checked by portable wind speed meter has been performed before noise monitoring. No noise measurement was performed in fog, rain, wind with a steady speed exceeding  $5 \text{ m s}^{-1}$  or wind with gusts exceeding  $10 \text{ m s}^{-1}$ .

### 5.2 NOISE MONITORING EXCEEDANCE

5.2.1 As shown in [Tables 5-1 and 5-2](#), no noise monitoring results exceeded the Limit Level in the Reporting Month. No Notification of Exceedance (NOE) of construction noise criterion was issued and no corrective action was therefore required.

## 6 WATER QUALITY

### 6.1 MONITORING RESULTS

6.1.1 Water quality impact monitoring schedule was submitted to all relevant parties which shown in [Appendix G](#).

6.1.2 In the Reporting Month, a total of **13** monitoring days were carried out for water quality impact monitoring. The monitoring result of key parameters including Dissolved Oxygen, Turbidity and Suspended Solids are summarized in [Tables 6-1](#) and [6-2](#). Detailed monitoring results including in-situ measurements and laboratory analysis data are shown in [Appendix H](#) and graphical plots for monitoring result are shown in [Appendix I](#).

**Table 6-1 Summary of Water Quality Monitoring Results – M3 under Contract 1**

Date	Parameters		
	DO (Averaged) (mg/L)	Turbidity (Averaged) (NTU)	Suspended Solids (Averaged) (mg/L)
3-Jan-19	8.95	2.6	<2
5-Jan-19	8.78	3.1	2.0
8-Jan-19	8.72	2.3	2.5
10-Jan-19	7.63	2.8	3.0
12-Jan-19	6.75	2.4	3.0
15-Jan-19	4.39	2.6	<2
17-Jan-19	5.80	3.2	2.5
19-Jan-19	7.17	1.9	2.0
22-Jan-19	8.92	5.6	6.5
24-Jan-19	9.27	4.6	9.0
26-Jan-19	7.75	4.0	4.5
29-Jan-19	7.87	4.6	4.5
31-Jan-19	8.75	3.1	TBA

**Table 6-2 Summary of Water Quality Monitoring Results (M1, M2 and M4) under Contract 2**

Date	Parameters								
	DO (Averaged) (mg/L)			Turbidity (Averaged) (NTU)			Suspended Solids (Averaged) (mg/L)		
	M1	M2	M4	M1	M2	M4	M1	M2	M4
3-Jan-19	9.28	#	9.15	2.7	#	1.3	4.5	#	<2
5-Jan-19	8.74	#	9.52	1.6	#	1.1	3.0	#	<2
8-Jan-19	8.75	#	8.93	1.7	#	0.7	<2	#	<2
10-Jan-19	8.35	#	7.99	1.7	#	1.5	6.5	#	3.5
12-Jan-19	7.81	#	7.33	1.4	#	1.0	2.0	#	2.0
15-Jan-19	6.62	6.27	3.80	3.7	5.5	2.0	3.0	5.5	<2
17-Jan-19	4.45	#	6.28	2.3	#	1.8	<2	#	<2
19-Jan-19	8.17	#	7.44	1.8	#	1.1	4.0	#	<2
22-Jan-19	10.01	8.93	11.92	2.7	7.8	1.4	4.0	13.0	<2
24-Jan-19	9.59	9.29	10.22	2.0	2.6	1.6	7.5	10.5	<2
26-Jan-19	9.47	#	10.07	1.7	#	3.2	4.0	#	<2
29-Jan-19	9.04	#	9.44	2.0	#	1.2	2.0	#	<2
31-Jan-19	9.13	#	9.13	1.7	#	1.5	TBA	#	TBA

Remarks: (#) During the water monitoring, the channel of M2 was observed dried up and water sampling was unable be carried out.

- 6.1.3 During the Reporting Month, field measurements including temperature of stream water, salinity concentrations, pH values and the stream flow velocity for all monitoring locations are summarized in [Table 6-3](#).

**Table 6-3 Summary of Field Measurements for Water Quality**

Monitoring Location	Parameters of field measurements							
	pH (unit)		Salinity (ppt)		Temp (°C)		Water Flow (m/s)	
	min	max	min	max	min	max	min	max
M1	6.5	8.6	0.02	0.06	18.5	20.3	<0.1	<0.1
M2	6.9	7.9	0.07	0.10	14.6	19.3	<0.1	<0.1
M3	6.8	8.7	0.0	0.02	16.6	20.4	<0.1	<0.1
M4	6.6	8.5	0.03	0.07	16.6	21.5	<0.1	<0.1

## 6.2 WATER QUALITY MONITORING EXCEEDANCE

- 6.2.1 In this Reporting Period, no exceedance was triggered for water quality monitoring. The non-compliance of water quality performance is summarized in [Table 6-4](#). The investigation of exceedance is summarized in [Table 6-5](#).

**Table 6-4 Action and Limit (A/L) Levels Exceedance Record**

Station	DO		Turbidity		SS		Total Exceedance		Project Related exceedance	
	Action	Limit	Action	Limit	Action	Limit	Action	Limit	Action	Limit
M1	0	0	0	0	0	0	0	0	0	0
M2	0	0	0	0	0	0	0	0	0	0
M3	0	0	0	0	0	0	0	0	0	0
M4	0	0	0	0	0	0	0	0	0	0

**Table 6-5 Summary of Investigation of Water Quality Exceedance in the Reporting Period**

Date of Exceedance	Exceeded Location	Exceeded Parameter	Cause of Water Quality Exceedance In Brief
--	--	--	--

## 7 ECOLOGY MONITORING

### 7.1 REQUIREMENT

7.1.1 According to approved EIA report (AEIAR-198/2016), habitat types within project boundary comprise of watercourse, grassland, upland grassland, plantation, woodland and developed area. Natural habitats were of moderate ecological value in terms of species diversity, species rarity, species abundance, ecological linkage as well as nursery. Moreover, 0.3ha of wet woodland on the northern side of Sandy Ridge was deemed habitat with high ecological value. Four types of habitats were regarded as ecologically sensitive habitats, namely wet woodland, watercourses, upland grassland and woodland. Considering human disturbance in upcoming construction and operation phases, ecologically sensitive habitats shall be monitored in accordance with EM&A Manual.

7.1.2 The objective of ecologically sensitive habitats monitoring is to evaluate the effectiveness of measures to minimize impacts on concerned habitats from disturbance and pollution. In order to monitor the effectiveness of the measures to the minimize impact on ecologically sensitive habitats from disturbance and pollution, monthly monitoring during construction and operation phases is required as specified in EM&A Manual. Standard faunal transect and sampling surveys cover both wetland habitats (*wet woodland and watercourse*) and non-wetland habitats (*upland grassland and woodland*).

### 7.2 METHODOLOGY

7.2.1 Wetland habitats include wet woodland and watercourses. Monitoring surveys using standardized quantitative methodology will conduct at fixed points. For seasonal watercourse, the survey will be conducted whenever the habitat appears. Measures to respond to decreases in numbers of aquatic fauna using the wetland habitats and Action/Limit levels to trigger these measures are detailed in **Table 7-1**.

**Table 7-1 Action and Limit Levels for Wet Woodland Habitats Monitoring**

Action Level	Response	Limit Level	Response
Reduction in taxa diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in taxa diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

*Remarks: Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna*

7.2.2 Non-wetland habitats consist of upland grassland and woodland. Monthly quantitative surveys of non-aquatic fauna will be conducted using standard route transect counts. Measures to respond to decreases in numbers of non-aquatic fauna using the non-wetland habitats and Action/Limit levels to trigger these measures are detailed in **Table 7-2**.

**Table 7-2 Action and Limit Levels for Non-Wet Woodland Habitats Monitoring**

Action Level	Response	Limit Level	Response
Reduction in species diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in species diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

*Remarks: Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna*

- 7.2.3 The ecological survey includes all taxa being investigated in accordance with EIA report. Schedule of faunal surveys in each year during construction phase is presented in **Table 7-3**.

**Table 7-3 Schedule of Faunal Surveys in each year During Construction Phase**

Month	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Mammals	√	√	√	√	√	√	√	√	√	√	√	√
Birds (day)	√	√	√	√	√	√	√	√	√	√	√	√
Birds (night)				√	√	√	√	√	√	√		
Herpetofauna				√	√	√	√	√	√	√		
Dragonflies			√	√	√	√	√	√	√	√		
Butterflies			√	√	√	√	√	√	√	√		
Aquatic fauna	√	√	√	√	√	√	√	√	√	√	√	√

Mammal Survey

- 7.2.4 Mammal surveys will be conducted along the proposed transects (shown in Appendix D of the survey report) during both daytime and night time periods. Along with direct observations, other field signs, such as scats and tracks, will be searched and recorded if present.

Bird Survey

- 7.2.5 Bird surveys will be conducted along the transects (shown in Appendix D of the survey report) during the surveys, species and their vocalizing individuals recorded will be enumerated and recorded according to the habitat(s) they are utilizing.

Herpetofauna Survey

- 7.2.6 Reptile and amphibian surveys will be conducted along transects (shown in Appendix D of the survey report) during surveys careful searches of appropriate microhabitats and refugia for reptiles and their vocalizing individuals will be undertaken and all reptiles observed will be identified and counted.

Dragonfly and Butterfly Survey

- 7.2.7 Dragonfly and Butterfly surveys will be conducted along transects (shown in Appendix D of the survey report) during surveys all dragonflies and Butterflies seen will be identified and counted as accurately as possible.

Aquatic Fauna Survey

- 7.2.8 Freshwater fishes and macro-invertebrates will be recorded by direct observation. All species trapped/recorded will be enumerated and identified (to the lowest taxonomic level possible), and the species of conservation importance photographed.
- 7.2.9 After each ecological monitoring survey, a monthly report of the survey result and data collected will be provided with reference to EM&A Manual. An annual analysis of data will be carried out in order to study if there is any significant reduction in taxa diversity and abundance.

**7.3 ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 1)**

- 7.3.1 In the Reporting Month, ecological monitoring was undertaken on **29<sup>th</sup> January 2019** at work area of Contract 1. The weather of monitoring day was fine. The day survey covering wetland and non-wetland areas. The survey was conducted by transect and fixed points. All species seen will be identified and counted as accurately as possible. Results of the monitoring survey are presented

below:

**Monitoring Result for Contract 1**

**Mammal**

7.3.2 There was no mammal recorded in the monitoring area

**Birds**

7.3.3 There were total of 28 bird individuals from 11 species recorded during the survey. One specie of conservation interests was recorded in the monitoring area: *Milvus migrans*, Black Kite(黑鳶)

**Herpetofauna**

7.3.4 There were no reptiles recorded in the monitoring area. There was no amphibian recorded in the monitoring area.

**Dragonfly**

7.3.5 There was one odonate individual in the monitoring area.

**Butterfly**

7.3.6 There were 5 butterfly individuals from 4 species recorded during the survey.

**Aquatic Fauna Survey (Freshwater communities)**

7.3.7 There were no freshwater community recorded in the monitoring area.

7.3.8 The summaries of faunal survey result are shown in [Tables 7-4, 7-5, 7-6, 7-8](#) and [7-9](#).

**Table 7-4 Result of Avifauna Survey under Contract 1**

Scientific Name	English Name	Chinese Name	Conservation Status	Non-wetland	Wetland
<i>Milvus migrans</i>	Black Kite	黑鳶	Fellowes et al. (2002): RC; Appendix 2 of CITES		2
<i>Spilopelia chinensis</i>	Dove	珠頸斑鳩			1
<i>Lanius schach</i>	Shrike	棕背伯勞			1
<i>Parus cinereus</i>	Cinereous Tit	蒼背山雀			1
<i>Pycnonotus jocosus</i>	Red-whiskered Bulbul	紅耳鵯		2	4
<i>Pycnonotus sinensis</i>	Chinese Bulbul	白頭鵯		4	
<i>Pycnonotus aurigaster</i>	Sooty-headed Bulbul	白喉紅臀鵯			2
<i>Hirundo rustica</i>	Barn Swallow	家燕			1
<i>Phylloscopus fuscatus</i>	Dusky Warbler	褐柳鶯			1
<i>Prinia flaviventris</i>	Yellow-bellied Prinia	黃腹鷦鶯			2
<i>Zosterops japonicus</i>	Japanese White-eye	暗綠繡眼鳥			7

**Table 7-5 Result of Reptile Survey under Contract 1**

Scientific Name	Common Name	Chinese Name	Non-wetland	Wetland
--	--	--	--	--

**Table 7-6 Result of Amphibian Survey under Contract 1**

Scientific Name	Common Name	Chinese Name	Conservation Status	Non-wetland	Wetland
--	--	--	--	--	--

**Table 7-7 Result of Butterfly Survey under Contract 1**

Scientific Name	Common Name	Chinese Name	Non-wetland	Wetland
<i>Abisara echerius</i>	Plum Judy	蛇目褐蛱蝶		2
<i>Neptis hylas</i>	Common Sailer	中環蛱蝶		1
<i>Mycalesis mineus</i>	Dark Brand Bush Brown,	小眉眼蝶	1	
<i>Eurema hecabe</i>	Common Grass Yellow	寬邊黃粉蝶	1	

**Table 7-8 Result of Odonate Survey under Contract 1**

Scientific Name	Common Name	Chinese Name	Conservation Status	Non-wetland	Wetland
<i>Pantala flavescens</i>	Wandering Glider	黃蜻	--	1	--

**Table 7-9 Result of Freshwater Communities Survey under Contract 1**

Scientific Name	Common Name	Chinese Name	Conservation Status	29-Jan-19
--	--	--	--	--

#### **7.4 ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 2)**

7.4.1 In the Reporting Month, ecological monitoring was undertaken on **15<sup>th</sup> January 2019** at work area of Contract 2. A rainy day. The day survey covering wetland and non-wetland areas. The survey was conducted by transect and fixed points. All species seen will be identified and counted as accurately as possible. Results of the monitoring survey are presented below:

##### **Monitoring Result for Contract 2**

##### **Mammal**

7.4.2 There was no mammal recorded in the monitoring area

##### **Birds**

7.4.3 There were a total of 32 bird individuals from 15 species recorded during the survey.

##### **Herpetofauna**

7.4.4 There were no reptiles recorded in the monitoring area. There was no amphibian recorded in the monitoring area.

##### **Dragonfly**

7.4.5 There was a total of 1 odonate individual from 1 specie.



Butterfly

7.4.6 There was no butterfly recorded in the monitoring area.

Aquatic Fauna Survey (Freshwater communities)

7.4.7 There were two species of freshwater fish were recorded.

7.4.8 The summaries of faunal survey result are shown in [Tables 7-10, 7-11, 7-12, 7-13](#) and [7-14](#).

**Table 7-10 Result of Avifauna Survey under Contract 2**

Scientific Name	English Name	Chinese Name	Conservation Status	Non-wetland	Wetland
<i>Spilopelia chinensis</i>	Spotted Dove	珠頸斑鳩		1	3
<i>Pericrocotus speciosus</i>	Scarlet Minivet	赤紅山椒鳥			1
<i>Parus cinereus</i>	Cinereous Tit	蒼背山雀		3	
<i>Pycnonotus jocosus</i>	Red-whiskered Bulbul	紅耳鵯		2	
<i>Pycnonotus sinensis</i>	Chinese Bulbul	白頭鵯		2	
<i>Phylloscopus inornatus</i>	Yellow-browed Warbler	黃眉柳鶯		1	
<i>Prinia flaviventris</i>	Yellow-bellied Prinia	黃腹鷦鶯		1	1
<i>Prinia inornata</i>	Plain Prinia	純色鷦鶯			1
<i>Orthotomus sutorius</i>	Common Tailorbird	長尾縫葉鶯		1	
<i>Garrulax perspicillatus</i>	Masked Laughingthrush	黑臉噪鵲		4	4
<i>Zosterops japonicus</i>	Japanese White-eye	暗綠繡眼鳥		3	
<i>Myophonus caeruleus</i>	Blue Whistling Thrush	紫嘯鵯		1	
<i>Phoenicurus auroreus</i>	Daurian Redstart	北紅尾鴝		1	
<i>Saxicola stejnegeri</i>	Stejneger's Stonechat	黑喉石(即鳥)			1
<i>Anthus godlewskii</i>	Olive-backed Pipit	樹鵲		1	

**Table 7-11 Result of Reptile Survey under Contract 2**

Scientific Name	Common Name	Chinese Name	Non-wetland	Wetland
--	--	--	--	--

**Table 7-12 Result of Amphibian Survey under Contract 2**

Scientific Name	Common Name	Chinese Name	Conservation Status	Non-wetland	Wetland
--	--	--	--	--	--

**Table 7-13 Result of Butterfly Survey under Contract 2**

Scientific Name	Common Name	Chinese Name	Non-wetland	Wetland
--	--	--	--	--

**Table 7-14 Result of Odonate Survey under Contract 2**

Scientific Name	Common Name	Chinese Name	Conservation Status	Non-wetland	Wetland
<i>Copera marginipes</i>	Yellow Featherlegs	黃狹扇螳			1

**Table 7-15 Result of Freshwater Communities Survey under Contract 2**

Scientific Name	Common Name	Chinese Name	Conservation Status	15-Jan-19
<i>Gambusia affinis</i>	Mosquito fish	食蚊魚		+
<i>Puntius semifasciolatus</i>	Chinese Barb	五線無鬚魮		+

+: Species appeared but uncountable.

7.4.9 The detailed survey report is attached in [Appendix K](#).

7.4.10 The tentative ecology inspection and monitoring in the next reporting period (February 2019) is scheduled on 21<sup>st</sup> February 2019.

## **8 LANDSCAPE AND VISUAL**

### **8.1 REQUIREMENT**

- 8.1.1 The EIA has recommended EM&A for landscape and visual resources to be undertaken during the design, construction and operational stages of the project. The design, implementation and maintenance of landscape mitigation measures is a key aspect of this and should be checked to ensure that they are fully realized and that potential conflicts between the proposed landscape measures and any other project works let its are resolved at the earliest possible date and without compromise to the intention of the mitigation measures. In addition, implementation of the mitigation measures recommended by the EIA will be monitored through the site audit programme.
- 8.1.2 A number of mitigation measures to ameliorate the landscape and visual impacts of the Project implementation is summarized in the EMIS of **Appendix 13.1** of the EIA Report.
- 8.1.3 The landscape and visual mitigation measures proposed should be incorporated in the landscape and engineering design. Mitigation measures to be implemented during construction should be adopted from the start of construction and be in place throughout the entire construction period. Mitigation measures to be implemented during operation should be integrated into the detailed design and built as part of the construction works so that they are in place on commissioning of the Project. Tree transplantation and compensatory planting should be carried out as early as possible in the Project with transplantation carried out prior to construction starting in any particular area.
- 8.1.4 During construction phase, Landscape & Visual Monitoring of the contractor's operations should be conducted monthly and reported by ET, and countersigned by IEC.

### **8.2 FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH**

- 8.2.1 In the Reporting Period, landscape & Visual inspection was carried out by the Registered Landscape Architect (RLA) for works area of Contract 1 and Contract 2 on **25<sup>th</sup> January 2019**. The findings / reminders recorded during the inspection are presented in **Tables 8-1 and 8-2**.

**Table 8-1 Landscape & Visual Inspection Finding for Contract 1**

<b>Date</b>	<b>Findings and Reminder</b>
25 <sup>th</sup> January 2019	<ol style="list-style-type: none"> <li>1. The Contractor was reminded to prevent the construction material pile within Tree Protection Zone (TPZ) and ensure no works is allowed within the TPZ.</li> <li>2. The Contractor was reminded to provide proper maintenance for transplanted tree (T2928) according to the approved method statement.</li> </ol>

**Table 8-2 Landscape & Visual Inspection Finding for Contract 2**

<b>Date</b>	<b>Findings and Reminder</b>
25 <sup>th</sup> January 2019	No adverse observation.

- 8.2.2 Inspection checklist of Landscape & Visual signed by RLA is attached in **Appendix L**.

## 9 WASTE MANAGEMENT

### 9.1 GENERAL WASTE MANAGEMENT

9.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time in accordance with the Waste Management Plan (WMP).

### 9.2 RECORDS OF WASTE QUANTITIES

9.2.1 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

9.2.2 The quantities of waste for disposal in this Reporting Period are summarized in [Table 9-1](#) and [9-2](#) and the Monthly Summary Waste Flow Table is shown in [Appendix M](#). Whenever possible, materials were reused on-site as far as practicable.

**Table 9-1 Summary of Quantities of Inert C&D Materials**

Type of Waste	Contract 1		Contract 2	
	Quantity	Disposal Location	Quantity	Disposal Location
C&D Materials (Inert) ('000m <sup>3</sup> )	0	--	0	--
Reused in this Contract (Inert) ('000m <sup>3</sup> )	10.431	Within Contract area	0	--
Reused in other Projects (Inert) ('000m <sup>3</sup> )	0	--	0	--
Disposal as Public Fill (Inert) ('000m <sup>3</sup> )	34.013	Tuen Mun Area 38	0	--

**Table 9-2 Summary of Quantities of C&D Wastes**

Type of Waste	Contract 1		Contract 2	
	Quantity	Disposal Location	Quantity	Disposal Location
Recycled Metal ('000kg)	0	--	0	--
Recycled Paper / Cardboard Packing ('000kg)	0	--	0	--
Recycled Plastic ('000kg)	0	--	0	--
Chemical Wastes ('000kg)	0.332	Licensed collector	0	--
General Refuses ('000m <sup>3</sup> )	0.088	NENT Landfill	0	--

9.2.3 Since canteen and/or kitchen are not allowed setting on the Project site, no domestic wastewater was generated from the Project.

## 10 SITE INSPECTION

### 10.1 REQUIREMENT

- 10.1.1 According to the approved Environmental Monitoring and Audit Manual, environmental site inspection should be led by RE and attended by the Contractor and ET at least once per week. Regular environmental site inspections shall be carried out to assess the environmental performance.

### 10.2 FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH

#### Contract 1

In the Reporting Period, joint site inspections for Contract 1 to evaluate the site environmental performance carried out by the RE, ET and the Contractor was on *3<sup>rd</sup>, 10<sup>th</sup>, 17<sup>th</sup>, 24<sup>th</sup> and 31<sup>st</sup> January 2019*. Moreover, IEC attended a joint site inspection on *24<sup>th</sup> January 2019*. No non-compliance was noted.

- 10.2.1 The findings / deficiencies that observed during the weekly site inspection are listed in *Table 10-1*.

**Table 10-1 Site Observations for the Works of Contract-1**

Date	Findings / Deficiencies	Follow-Up Status
27 <sup>th</sup> December 2018 (last reporting month)	<ul style="list-style-type: none"> <li>Chemical containers without drip tray were observed. The Contractor should place the containers into drip tray to avoid leakage on ground.</li> </ul>	<ul style="list-style-type: none"> <li>The chemical container at CS15 was removed and stored at the chemical storage area on site.</li> </ul>
3 <sup>rd</sup> January 2019	<ul style="list-style-type: none"> <li>Proper shelter for grout mixer was not observed at CS15. The Contractor should provide three sides and a top shelter for mixer during the mixing process.</li> </ul>	<ul style="list-style-type: none"> <li>Proper shelter for grout mixer was provided.</li> </ul>
10 <sup>th</sup> January 2019	<ul style="list-style-type: none"> <li>The Contractor was reminded to maintain good housekeeping on site.</li> <li>The Contractor was reminded to implement dust mitigation measures during slop drilling work at CS15/16.</li> </ul>	<ul style="list-style-type: none"> <li>Reminder only.</li> <li>Reminder only.</li> </ul>
17 <sup>th</sup> January 2019	<ul style="list-style-type: none"> <li>The Contractor was reminded to provide water spraying near Retaining Wall 1 regularly.</li> </ul>	<ul style="list-style-type: none"> <li>Reminder only.</li> </ul>
24 <sup>th</sup> January 2019	<ul style="list-style-type: none"> <li>The Contractor was reminded to place the free-standing chemical containers into drip tray at RW1.</li> <li>The Contractor was reminded to cover the stockpile of cement bag properly on site.</li> <li>The Contractor was reminded to ensure dust mitigation measure was implemented during excavation work.</li> <li>The Contractor was reminded to enhance the shelter for cement-mixing plant.</li> </ul>	<ul style="list-style-type: none"> <li>Reminder only.</li> <li>Reminder only.</li> <li>Reminder only.</li> <li>Reminder only.</li> </ul>
31 <sup>st</sup> January 2019	<ul style="list-style-type: none"> <li>Cement mixing without sufficient dust control measures was observed, the Contractor should provide an area sheltered on the tops and 3 sides for the mixing work.</li> </ul>	<ul style="list-style-type: none"> <li>To be followed.</li> </ul>

	<ul style="list-style-type: none"> <li>The Contractor was reminded to provide adequate dust suppressive measures in particular dry season.</li> </ul>	<ul style="list-style-type: none"> <li>Reminder only.</li> </ul>
--	---	--

**Contract 2**

10.2.2 In the Reporting Period, joint site inspections for Contract 2 to evaluate the site environmental performance carried out by the RE, ET and the Contractor was on **3<sup>rd</sup>, 10<sup>th</sup>, 17<sup>th</sup>, 24<sup>th</sup> and 31<sup>st</sup> January 2019**. Moreover, IEC attended a joint site inspection on **24<sup>th</sup> January 2019**. No non-compliance was noted.

10.2.3 The findings / deficiencies that observed during the weekly site inspection are listed in **Table 10-2**.

**Table 10-2 Site Observations for the Works of Contract-1**

<b>Date</b>	<b>Findings / Deficiencies</b>	<b>Follow-Up Status</b>
3 <sup>rd</sup> January 2019	<ul style="list-style-type: none"> <li>No adverse environmental issue was observed.</li> </ul>	<ul style="list-style-type: none"> <li>NA</li> </ul>
10 <sup>th</sup> January 2019	<ul style="list-style-type: none"> <li>No adverse environmental issue was observed.</li> </ul>	<ul style="list-style-type: none"> <li>NA</li> </ul>
17 <sup>th</sup> January 2019	<ul style="list-style-type: none"> <li>NRMM label for the roller at TTA1 was not observed. The Contractor should check and display the NRMM label in accordance to the NRMM regulation.</li> </ul>	<ul style="list-style-type: none"> <li>NRMM label for the roller at TTA1 was displayed properly.</li> </ul>
24 <sup>th</sup> January 2019	<ul style="list-style-type: none"> <li>The Contractor was reminded to ensure the sandbag bund at work area boundary of TTA1 is well adjoined to avoid any site runoff discharge from site without proper treatment</li> <li>The Contractor was reminded to block the existing gully with sand bag at TTA2 to avoid any site runoff direct discharge to the existing drainage.</li> </ul>	<ul style="list-style-type: none"> <li>Reminder only.</li> </ul>
31 <sup>st</sup> January 2019	<ul style="list-style-type: none"> <li>The Contractor was reminded to fully cover the stockpile store on-site to minimize dust impact.</li> </ul>	<ul style="list-style-type: none"> <li>Reminder only.</li> </ul>

## 11 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

### 11.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

11.1.1 In the Reporting Month, no environmental complaint was received for the Project. No summons and prosecution was lodged for the Contract. The statistical summary table of the environmental complaint, summons and prosecution are presented in [Tables 11-1, 11-2](#) and [11-3](#).

**Table 11-1 Statistical Summary of Environmental Complaints**

Reporting Period		Environmental Complaint Statistics		
		Frequency	Cumulative	Complaint Nature
1 – 31 Jan 2019	Contract 1	0	0	NA
1 – 31 Jan 2019	Contract 2	0	0	NA

**Table 11-2 Statistical Summary of Environmental Summons**

Reporting Period		Environmental Summons Statistics		
		Frequency	Cumulative	Complaint Nature
1 – 31 Jan 2019	Contract 1	0	0	NA
1 – 31 Jan 2019	Contract 2	0	0	NA

**Table 11-3 Statistical Summary of Environmental Prosecution**

Reporting Period		Environmental Prosecution Statistics		
		Frequency	Cumulative	Complaint Nature
1 – 31 Jan 2019	Contract 1	0	0	NA
1 – 31 Jan 2019	Contract 2	0	0	NA

11.1.2 In addition, no complaints received and emergency events relating to violation of environmental legislation for illegal dumping and landfilling were received.



## 12 IMPLEMENTATION STATUS OF MITIGATION MEASURES

### 12.1 GENERAL REQUIREMENTS

12.1.1 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the approved EM&A Manual covered the issues of dust, noise, water and waste and they are summarized presented in [Appendix N](#).

12.1.2 The Works of Contract 1 and Contract 2 under the Project shall be implementing the required environmental mitigation measures according to the approved EM&A Manual subject to the site condition. Environmental mitigation measures implemented in this Reporting Month is summarized in **Table 12-1**.

**Table 12-1 Environmental Mitigation Measures**

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> <li>• Provided efficient silt removal facilities to reduce SS level before effluent discharge.</li> <li>• Provided ditches, earth bunds or sand bag barriers to minimize polluted runoff.</li> <li>• Temporary drainage was provided to prevent runoff going through site surface and minimize polluted runoff.</li> <li>• Provided perimeter cut-off drains at site boundaries to intercept storm runoff from crossing the site.</li> <li>• Exposed slopes surface were compacted and covered with tarpaulin or similar means</li> <li>• Provided portable chemical toilets on site.</li> </ul>
Air Quality	<ul style="list-style-type: none"> <li>• Maintain damp / wet surface on access road.</li> <li>• Maintain low vehicular speed within the works areas.</li> <li>• Provided vehicle wheel washing facilities at each construction site exit;</li> <li>• Provided water spraying for all active works area.</li> <li>• Stockpiles of dusty material were covered with impervious sheeting.</li> <li>• Provided workers to clear dusty materials at the vehicle entrance or exit regularly.</li> <li>• Stockpile more than 20 bags of cement or dry pulverized fuel ash (PFA) has been covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.</li> </ul>
Noise	<ul style="list-style-type: none"> <li>• Restricted operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday.</li> <li>• Keep good maintenance of plants</li> <li>• Placed noisy plants away from residence and school</li> <li>• Provided noise barriers or hoarding to enclose the noisy plants or works</li> <li>• Shut down the plants when not in used.</li> </ul>
Waste and Chemical Management	<ul style="list-style-type: none"> <li>• Provided on-site sorting prior to disposal</li> <li>• Followed requirements and procedures of the “Trip-ticket System”</li> <li>• Predicted required quantity of concrete accurately</li> <li>• Collected the unused fresh concrete at designated locations in the sites for subsequent disposal</li> </ul>
General	<ul style="list-style-type: none"> <li>• The site was generally kept tidy and clean.</li> </ul>

### 12.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

12.2.1 According to the information provided by HCTYJV, the forthcoming construction activities for Contract 1 are listed below:

- (i) General Site Clearance
- (ii) Bulk Excavation

- (iii) Construction of Cut Slope, installation of soil nailing and construction of surface channel.
- (iv) Construction of retaining wall
- (v) Construction of fill slope

12.2.2 According to the information provided by Sang Hing, the forthcoming construction activities for Contract 2 are listed below:

- Site preparation of PM's Office
- Utilities Detection and trial pit excavation along Man Kam To Road.
- Liaison with Contract 1 Contractor regarding the access road
- Construction of Manhole, gullies, drainage pipe at Lin Ma Hang Road between CH280-340 & CH1015-1075 Southbound.
- Construction of soil nail at slope CS22 (Part A1)

### **12.3 KEY ISSUES FOR THE COMING MONTH**

12.3.1 Key issues to be considered in the coming month for the works of Contract 1 include:

- Implementation of control measures for rainstorm;
- Regular clearance of stagnant water during wet season;
- Implementation of dust suppression measures at all times;
- Potential wastewater quality impact due to surface runoff;
- Potential fugitive dust quality impact due from the dry/loose/exposure soil surface/dusty material;
- Ensure dust suppression measures are implemented properly;
- Sediment catch-pits and silt removal facilities should be regularly maintained;
- Discharge of site effluent to the nearby wetland is prohibited;
- Nearby wetland prohibited stockpiling and/or disposal of materials;
- Follow-up of improvement on general waste management issues; and
- Implementation of construction noise preventative control measures.

### **13 CONCLUSIONS AND RECOMMENTATIONS**

#### **13.1 CONCLUSIONS**


- 13.1.1 This is the **6<sup>th</sup>** monthly Environmental Monitoring and Audit Report presenting the monitoring results and inspection findings for the period of **1** to **31 January 2019**.
- 13.1.2 No 24-hour or 1-hour TSP monitoring result that triggered the Action or Limit Levels was recorded. No NOEs or the associated corrective action was therefore required.
- 13.1.3 No noise complaint (which is an Action Level exceedance) was received and no construction noise measurement result that exceeded the Limit Level was recorded in this Reporting Month. No NOEs or the associated corrective actions were therefore issued.
- 13.1.4 For water quality monitoring, no exceedance was triggered in the Reporting Month.
- 13.1.5 Monthly ecological monitoring for sensitive habitat for area of Contract 1 and Contract 2 were undertaken on **29<sup>th</sup> January 2019 and 15<sup>th</sup> January 2019** respectively. Moreover, Landscape and visual inspection at both Contracts were undertaken by the RLA on **25<sup>th</sup> January 2019**.
- 13.1.6 In the Reporting Period, no environmental complaint, summons and prosecution was received. In addition, no complaints received and emergency events relating to violation of environmental legislation for illegal dumping and landfilling were received.
- 13.1.7 In the Reporting Period, joint site inspections for Contract 1 to evaluate the site environmental performance were carried out by the RE, ET and the Contractor on **3<sup>rd</sup>, 10<sup>th</sup>, 17<sup>th</sup>, 24<sup>th</sup> and 31<sup>st</sup> January 2019** and IEC attended joint site inspection on **24<sup>th</sup> January 2019**. No non-compliance was noted.
- 13.1.8 Joint site inspections for Contract 2 to evaluate the site environmental performance carried out by the RE, ET and the Contractor was on **3<sup>rd</sup>, 10<sup>th</sup>, 17<sup>th</sup>, 24<sup>th</sup> and 31<sup>st</sup> January 2019** and IEC attended joint site inspection on **24<sup>th</sup> January 2019**. No non-compliance was noted.

#### **13.2 RECOMMENDATIONS**

- 13.2.1 The Contractors should pay special attention on water quality mitigation measures and fully implement according to the ISEMM of the EM&A Manual, in particular to prevent surface runoff with high SS content and other pollutants from flowing to local stream and Conservation Area (CA).
- 13.2.2 Construction noise would be a key environmental issue during construction phase of the Project. Noise mitigation measures such as using quiet plants and mobile noise barriers should be implemented in accordance with the EM&A requirement.
- 13.2.3 Since construction site under the Works of Contract 1 of the Project is located near villages, HCTYJV should fully implement air quality mitigation measures to reduce construction dust emission.
- 13.2.4 Furthermore, daily cleaning and weekly tidiness shall be properly performed and maintained. In addition, mosquito control should be performed to prevent mosquito breeding on site.

## **Appendix A**

### **Layout Plan of the Project**

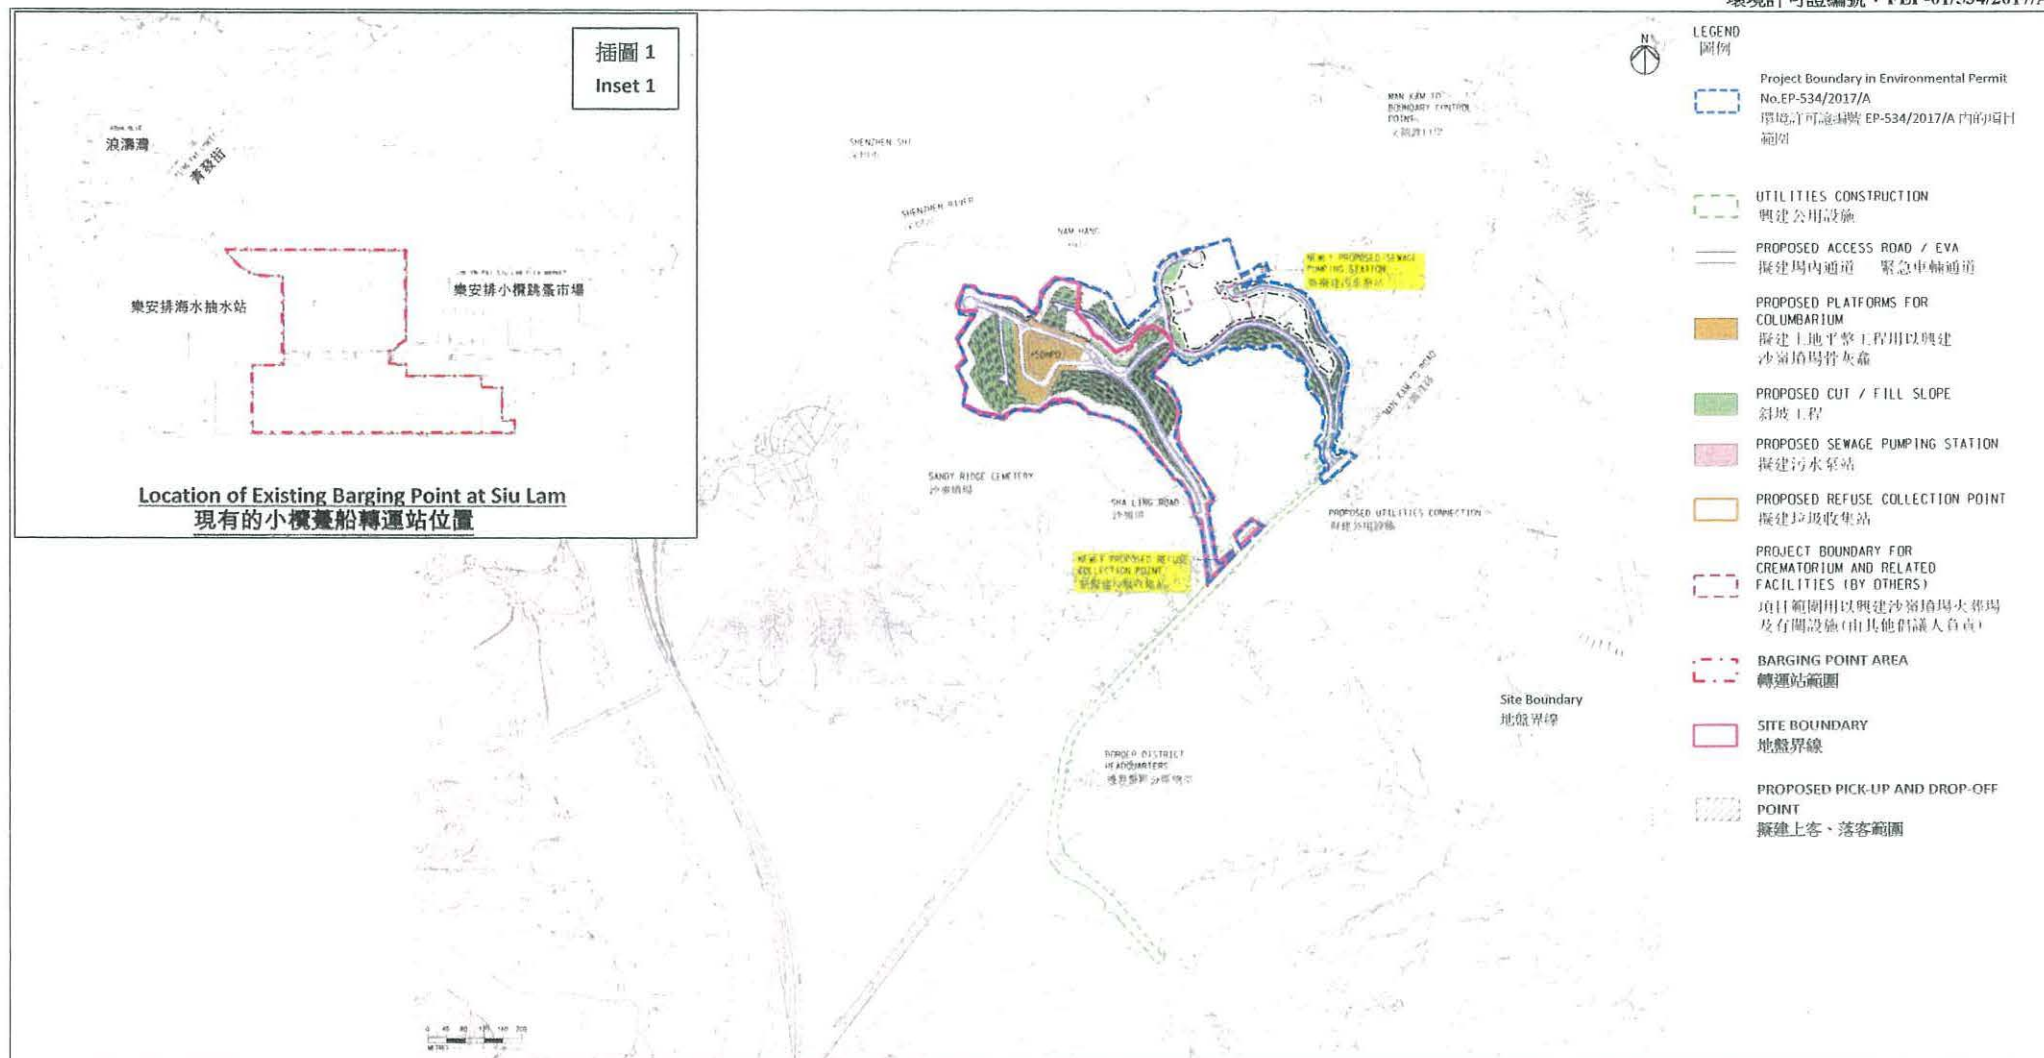

**Project Title: Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery**  
**工程名稱: 沙嶺墳場興建骨灰龕的工地平整及相關基建工程**

**Figure 1: Project Location Plan**

**圖 1: 項目位置圖**

(This figure was prepared based on Figure 1 attached to the VEP Application No. VEP-555/2018 and Figures 1.3 of the Approved EIA Report No. AEIAR-198/2016)


(本圖是根據更改環境許可證申請文件編號: VEP-555/2018 所隨附的圖 1 和環境影響評估報告編號 AEIAR-198/2016 圖 1.3 編制)

**Environmental Permit No.: FEP-01/534/2017/A**  
**環境許可證編號: FEP-01/534/2017/A**





Printed by : 11/27/2017  
Filename : j:\231448\record\contract\contract 1\civil\231448\_C1\_G\_1001.dgn

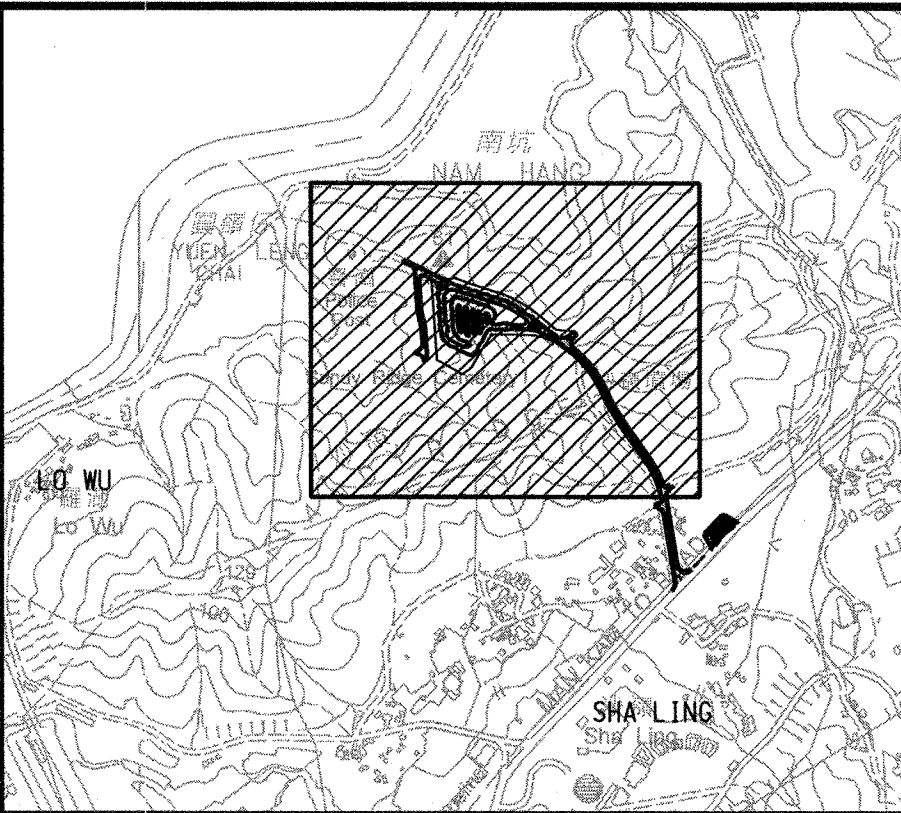

KEY PLAN	
LEGEND:	
-----	PROPOSED WORKS SITE
+50mPD	SITE FORMATION LEVEL

Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title:			
Contract No. CV/2016/10			
Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery			
Drawing title			
GENERAL LAYOUT (SHEET 1 OF 3)			
Drawing no.		Rev.	
231448/C1/G/1001		-	
Drawn	Date	Checked	Approved
WM	12/16	AW	DL
Scale	1:1000 @A1	Status	CONTRACT



土木工程拓展署  
Civil Engineering and Development Department













DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
© OVE ARUP & PARTNERS HONG KONG LIMITED.

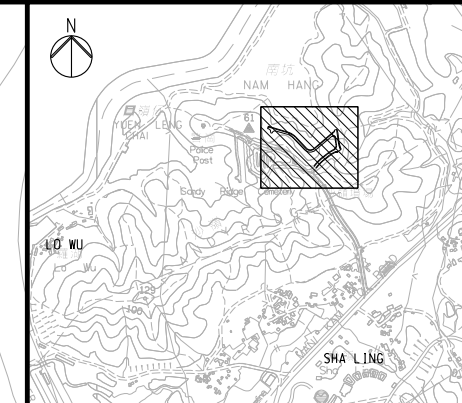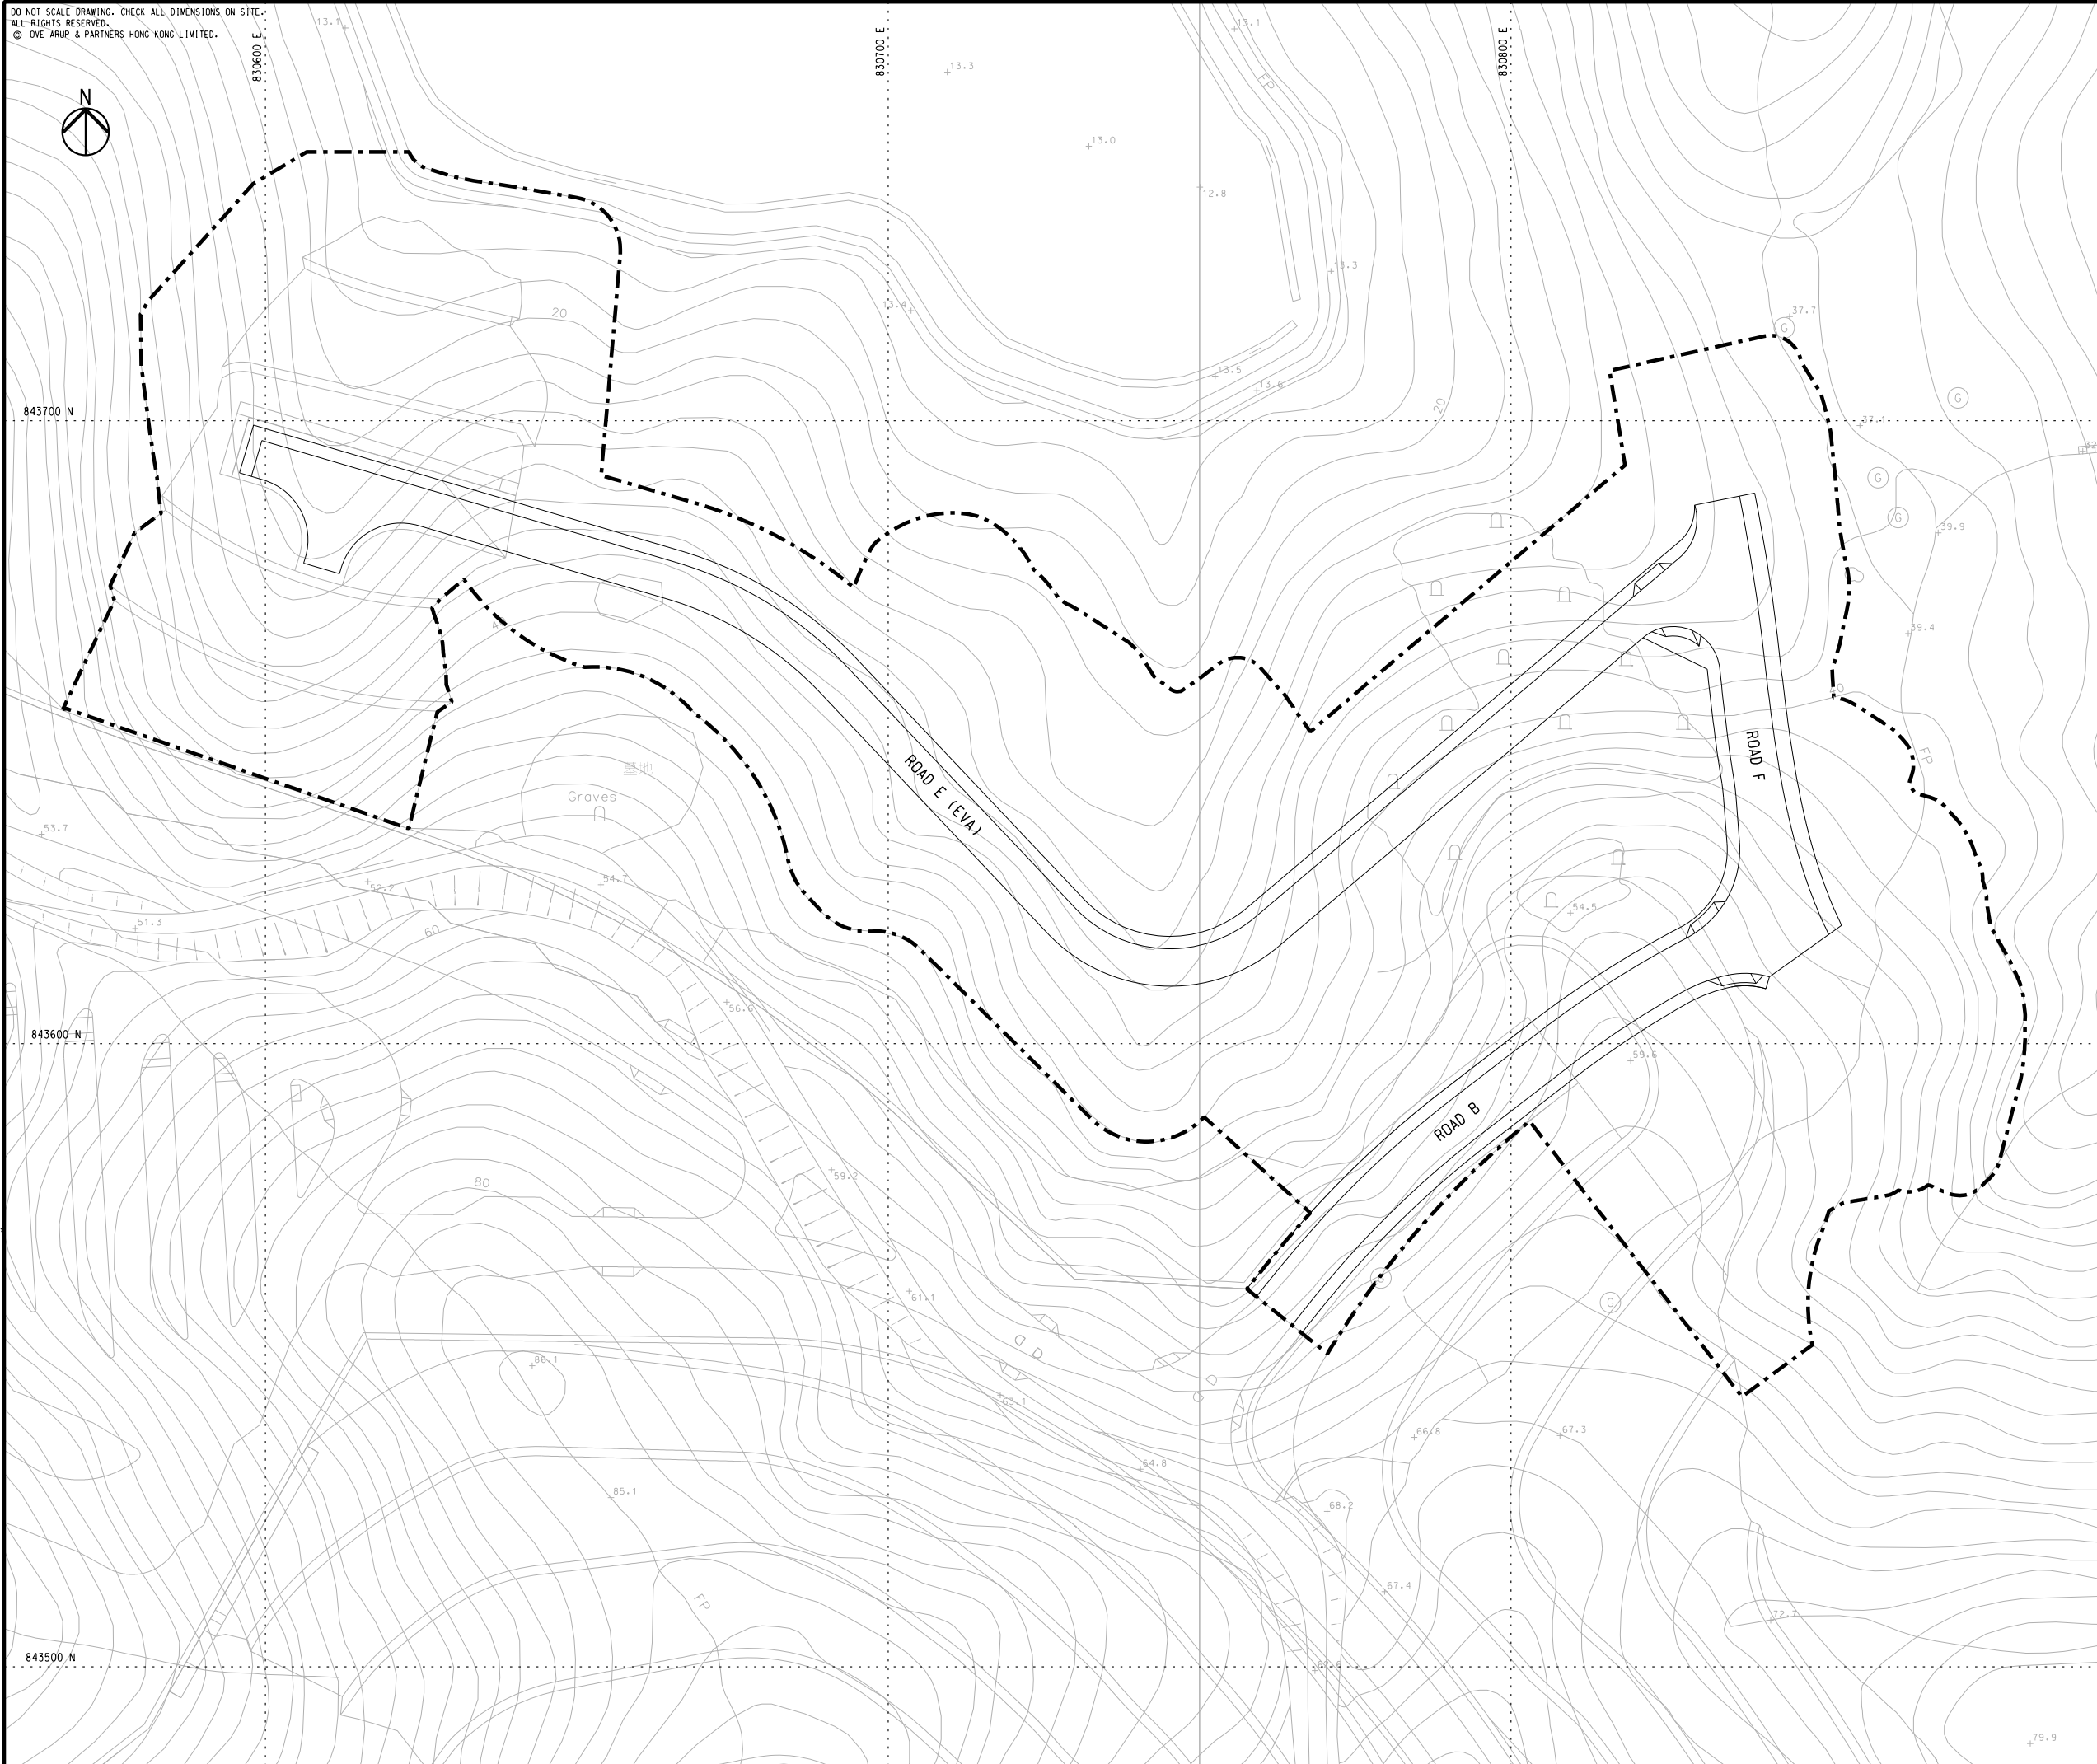

## KEY PLAN

LEGEND:

\_\_\_\_\_

SITE BOUNDARY

-	TENDER DRAWING	AW	11/17
Rev	Description	By	Date
Consultant			
<h1>ARUP</h1>			
Contract No. and Title:			
Contract No. CV/2017/02			
Development of Columbarium at Sandy Ridge Cemetery - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road			
Drawing title			
GENERAL LAYOUT (SHEET 1 OF 5)			
Drawing no.			Rev.
231448/C2/G/1001			-
Drawn WM	Date 07/17	Checked AW	Approved DL
Scale 1:500 @A1		Status TENDER	

COPYRIGHT RESERVED





土木工程拓展署  
Civil Engineering and  
Development Department

Printed by : 12/27/2017  
 Filename : J:\231448\ARUP\Civil\CONTRACT 2\231448\_C2\_G\_1001.dgn




DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
© OVE ARUP & PARTNERS HONG KONG LIMITED.

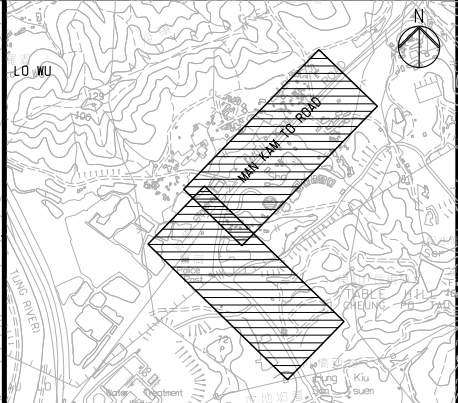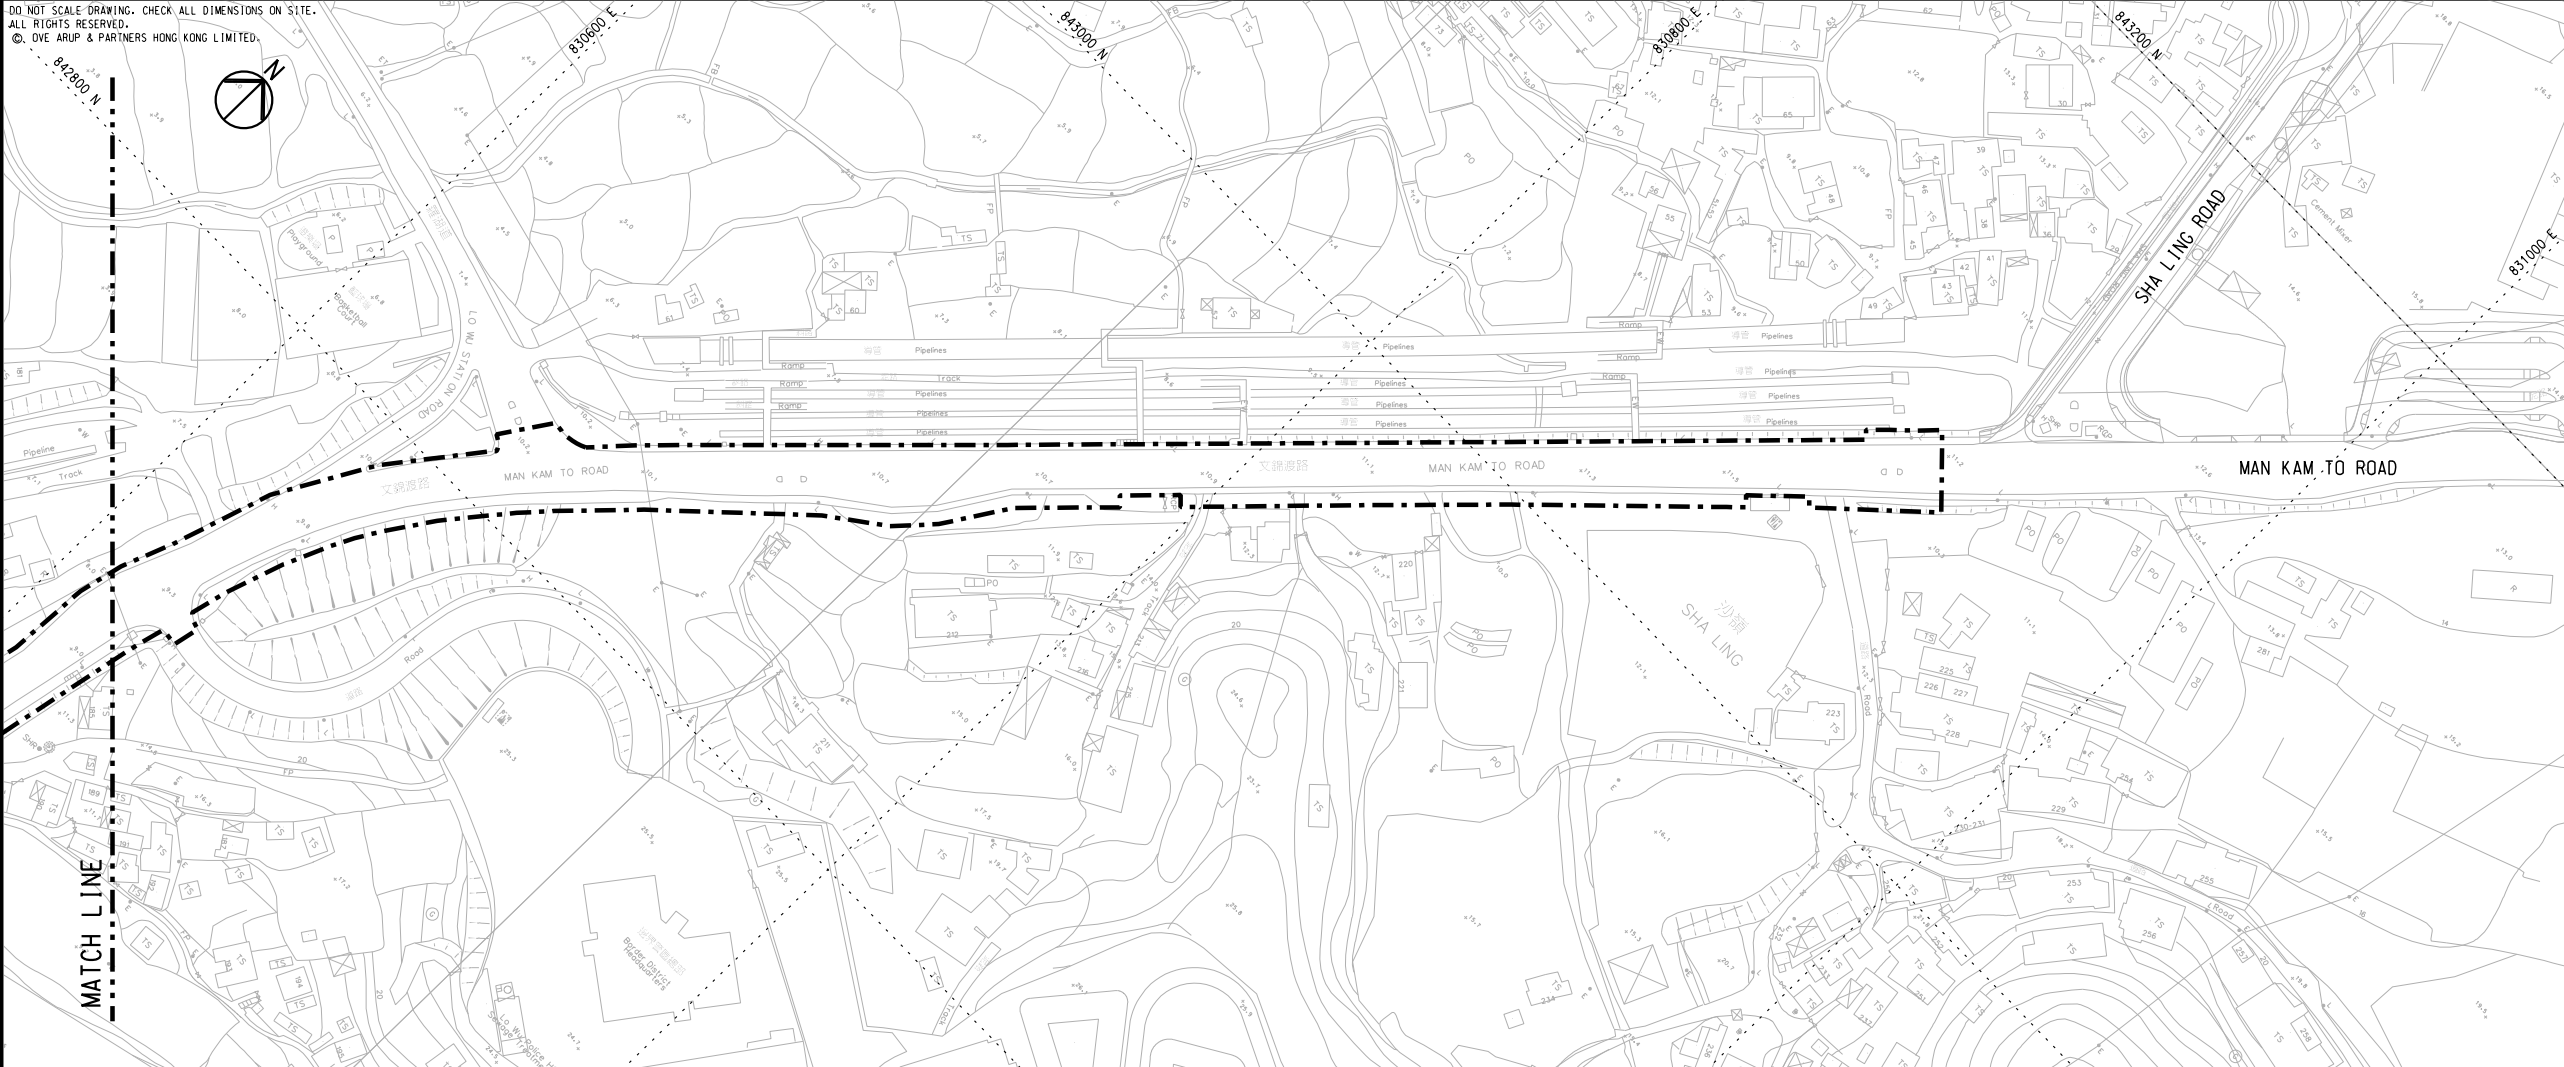

KEY PLAN

LEGEND:

--- SITE BOUNDARY

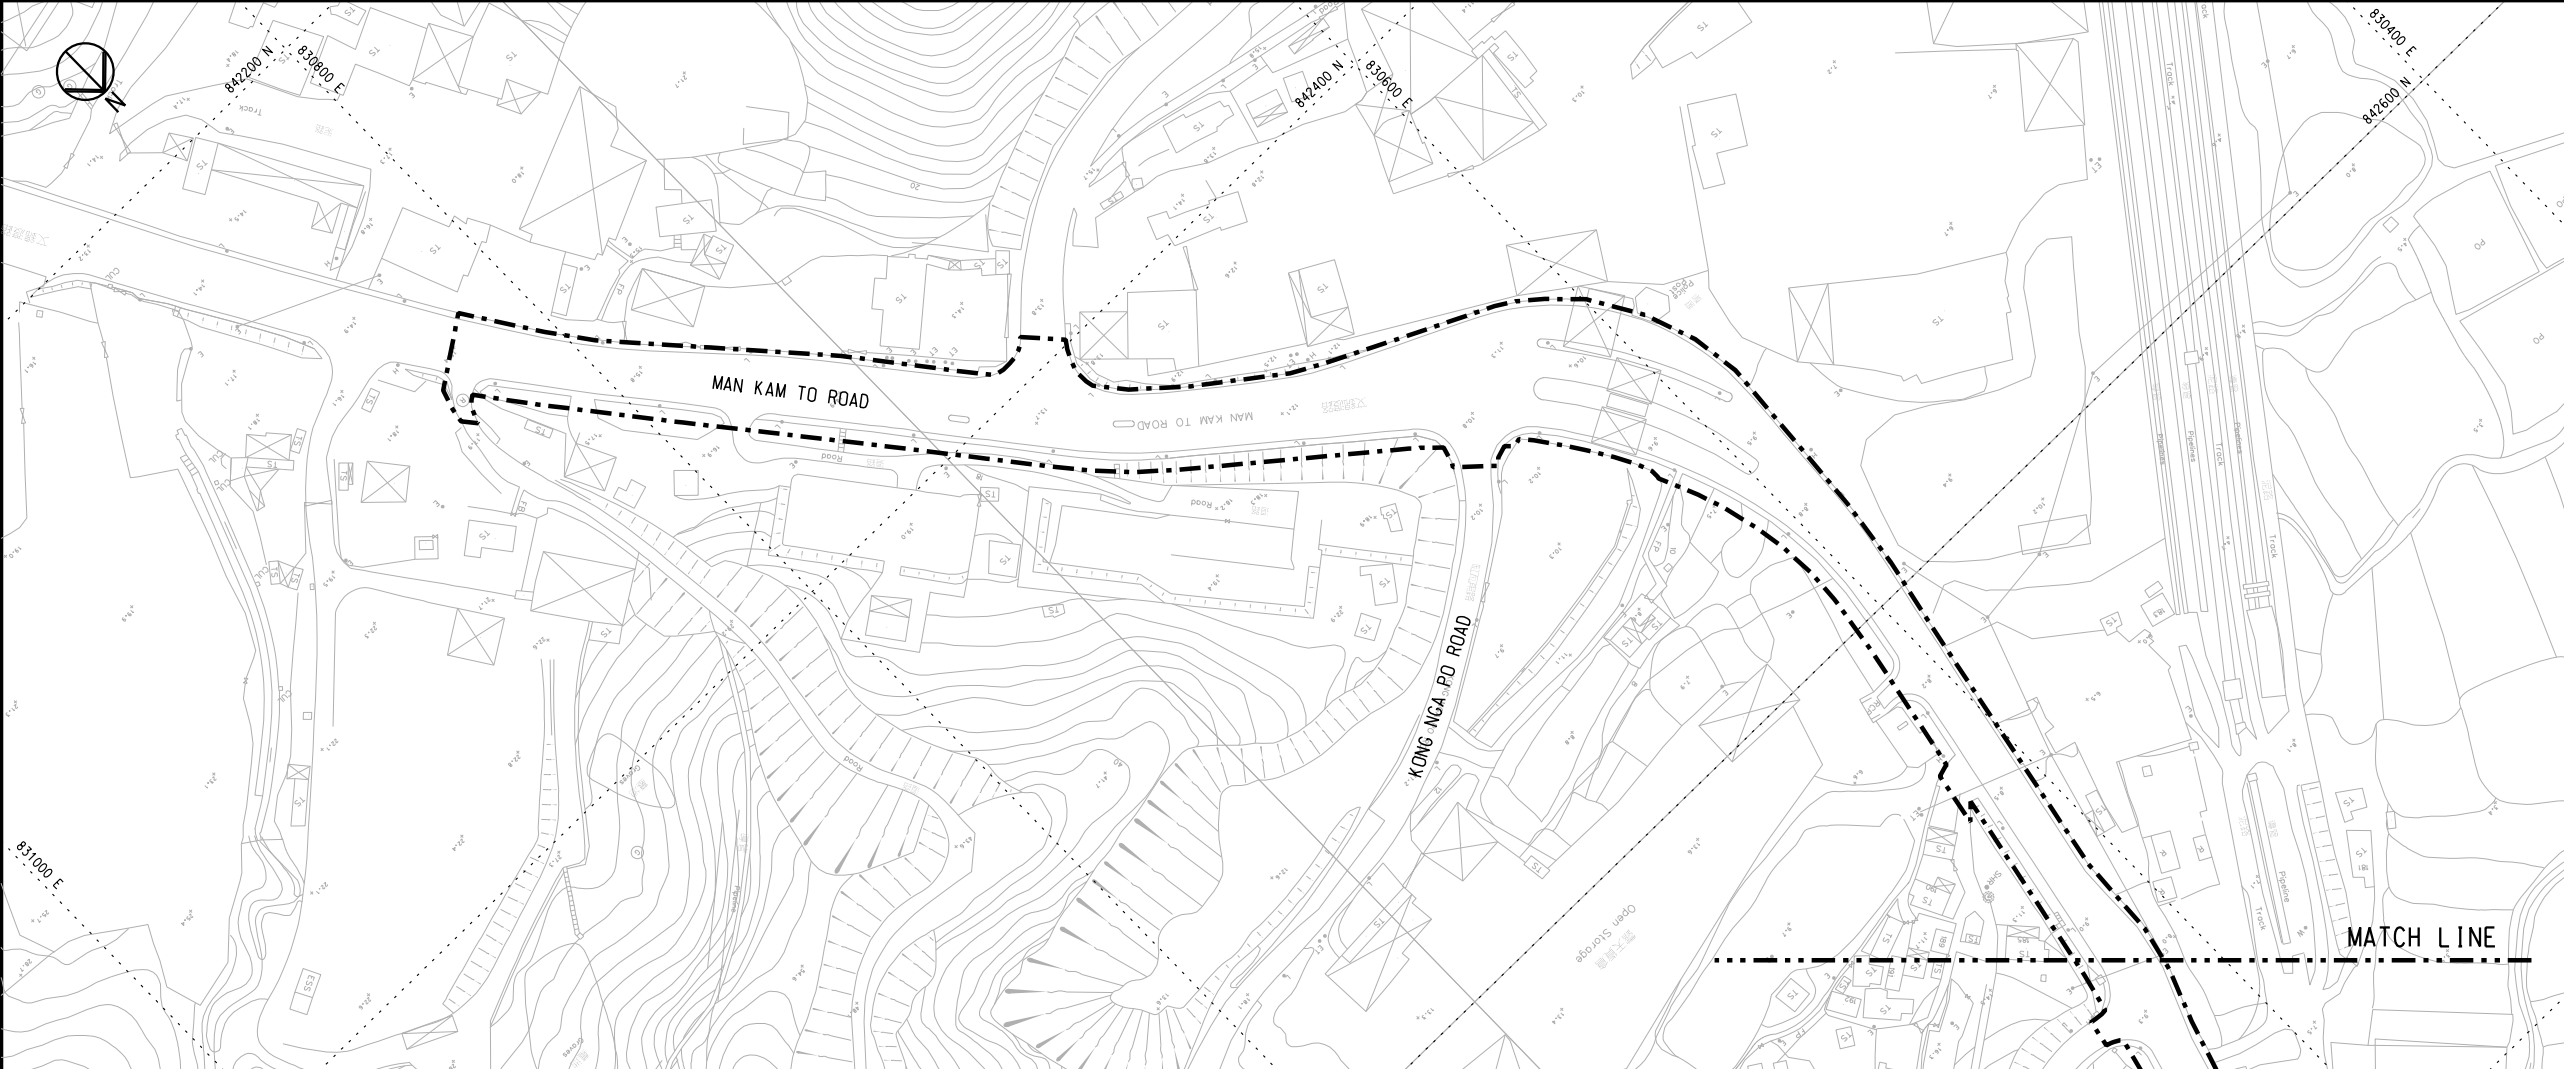

-	TENDER DRAWING	AW	11/17
Rev	Description	By	Date

Consultant

**ARUP**

Contract No. and Title:

Contract No. CV/2017/02

Development of Columbarium  
at Sandy Ridge Cemetery -  
Infrastructural Works at  
Man Kam To Road and  
Lin Ma Hang Road

Drawing title

**GENERAL LAYOUT  
(SHEET 2 OF 5)**

Drawing no. <b>231448/C2/G/1002</b>		Rev. -	
Drawn WM	Date 07/17	Checked AW	Approved DL
Scale 1:1000 @A1		Status <b>TENDER</b>	

COPYRIGHT RESERVED



土木工程拓展署  
Civil Engineering and  
Development Department



DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
© OVE ARUP & PARTNERS HONG KONG LIMITED.

844000 N



844200 N

844000 N


832800 E

832000 E

832200 E

MATCH LINE  
FOR CONTINUATION SEE  
DRG 231448/C2/G/1004

LIN MA HANG ROAD



KEY PLAN

LEGEND:

--- SITE BOUNDARY


-	TENDER DRAWING	AW	11/17
Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title:			
Contract No. CV/2017/02			
Development of Columbarium at Sandy Ridge Cemetery - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road			
Drawing title			
GENERAL LAYOUT (SHEET 3 OF 5)			
Drawing no.			Rev.
231448/C2/G/1003			-
Drawn WM	Date 07/17	Checked AW	Approved DL
Scale 1:1000 @A1	Status TENDER		



土木工程拓展署  
Civil Engineering and  
Development Department



DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
© OVE ARUP & PARTNERS HONG KONG LIMITED.

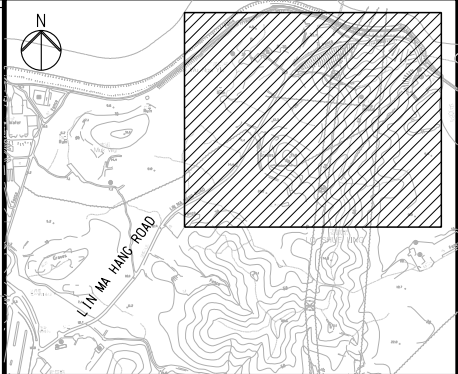

KEY PLAN

LEGEND:  
- - - SITE BOUNDARY

-	TENDER DRAWING	AW	11/17
Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title:			
Contract No. CV/2017/02			
Development of Columbarium at Sandy Ridge Cemetery - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road			
Drawing title			
GENERAL LAYOUT (SHEET 4 OF 5)			
Drawing no.			Rev.
231448/C2/G/1004			-
Drawn	Date	Checked	Approved
WM	07/17	AW	DL
Scale	1:1000 @A1		Status
		TENDER	




COPYRIGHT RESERVED



土木工程拓展署  
Civil Engineering and Development Department



DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
© OVE ARUP & PARTNERS HONG KONG LIMITED.

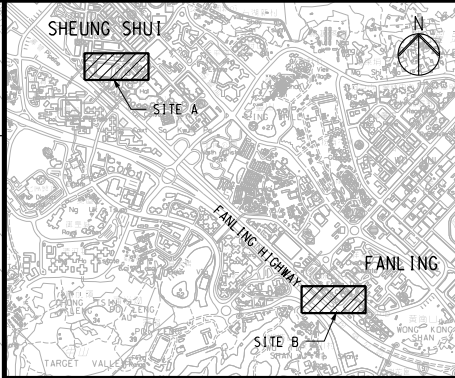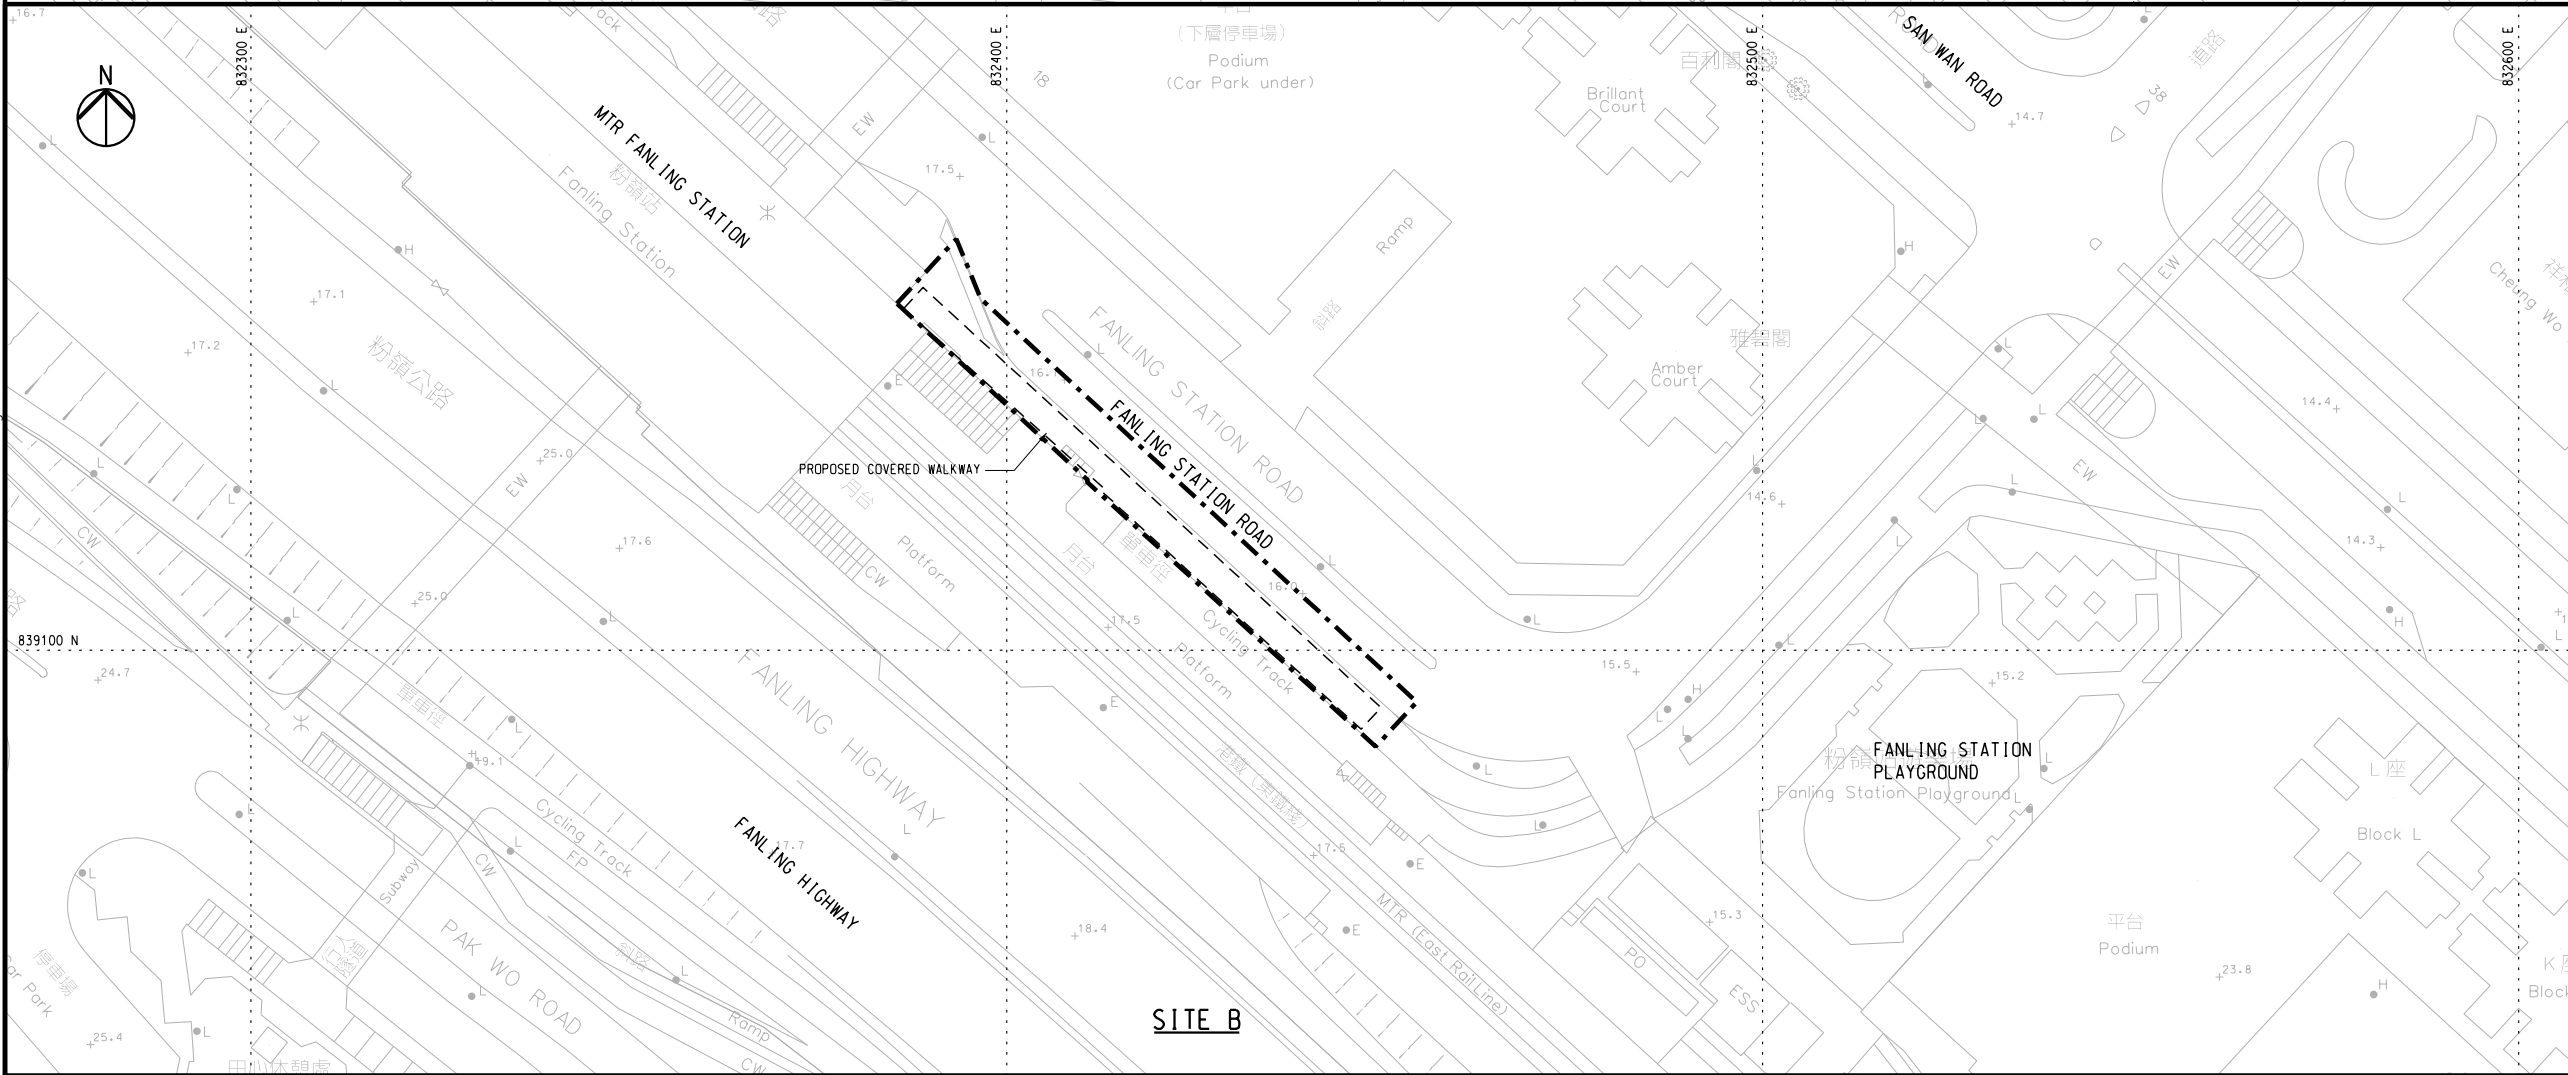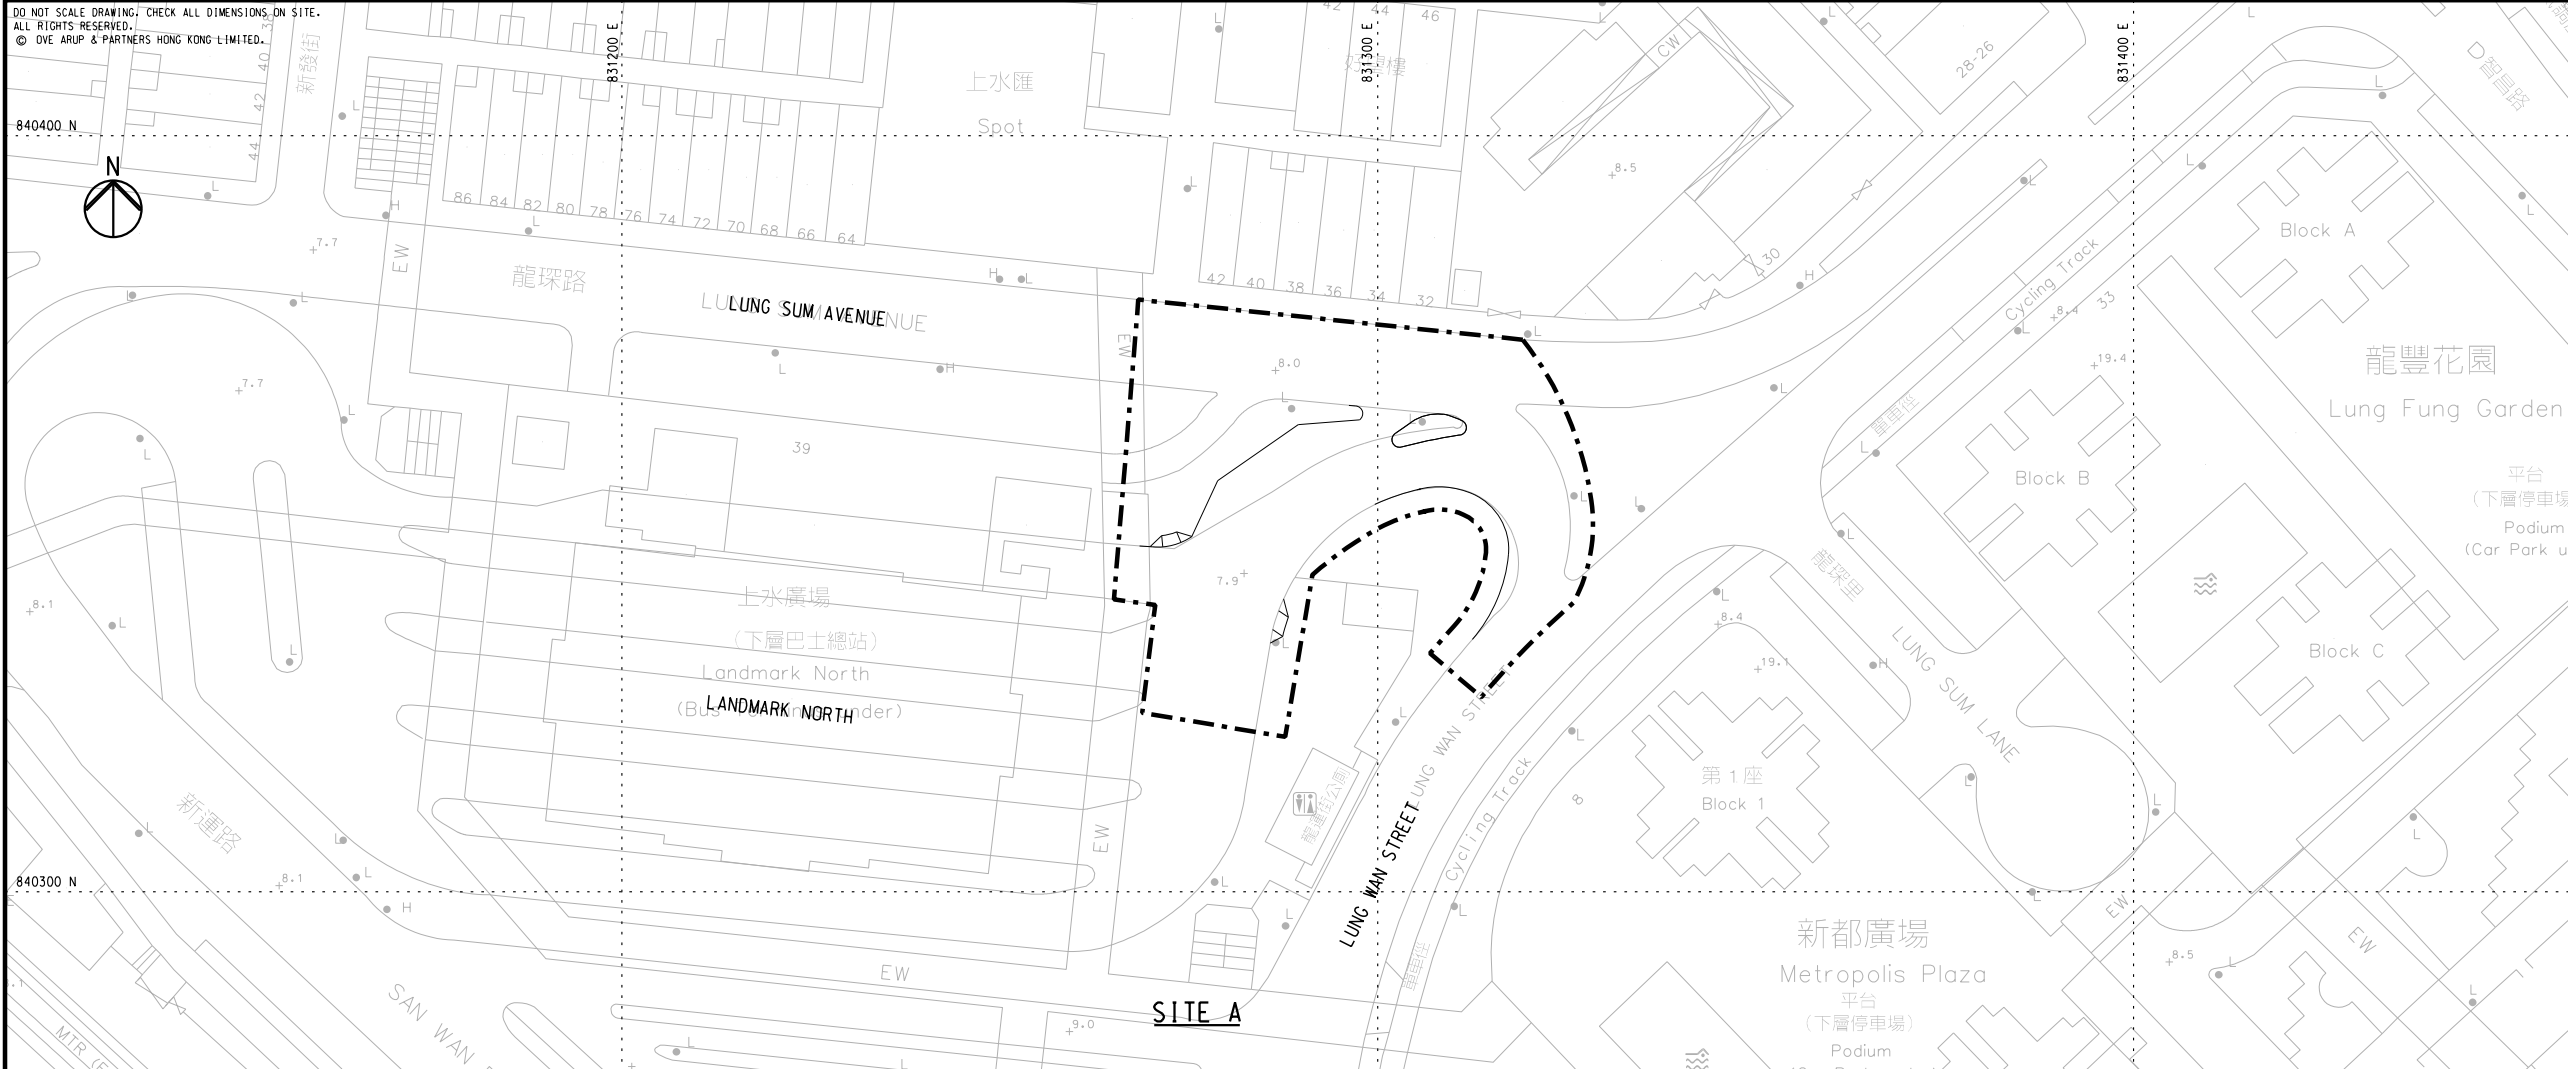

## KEY PLAN

**LEGEND:**

--- SITE BOUNDARY


-	TENDER DRAWING	AW	11/17
Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title:			
Contract No. CV/2017/02			
Development of Columbarium at Sandy Ridge Cemetery - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road			
Drawing title			
GENERAL LAYOUT (SHEET 5 OF 5)			
Drawing no.			Rev.
231448/C2/G/1005			-
Drawn	Date	Checked	Approved
WM	07/17	AW	DL
Scale	1:500 @A1	Status	TENDER
COPYRIGHT RESERVED			
CEDD 土木工程拓展署 Civil Engineering and Development Department			


## **Appendix B**

### **Organization Structure and Contact Details of Relevant Parties**



### **The Contract's Environmental Management Organization**

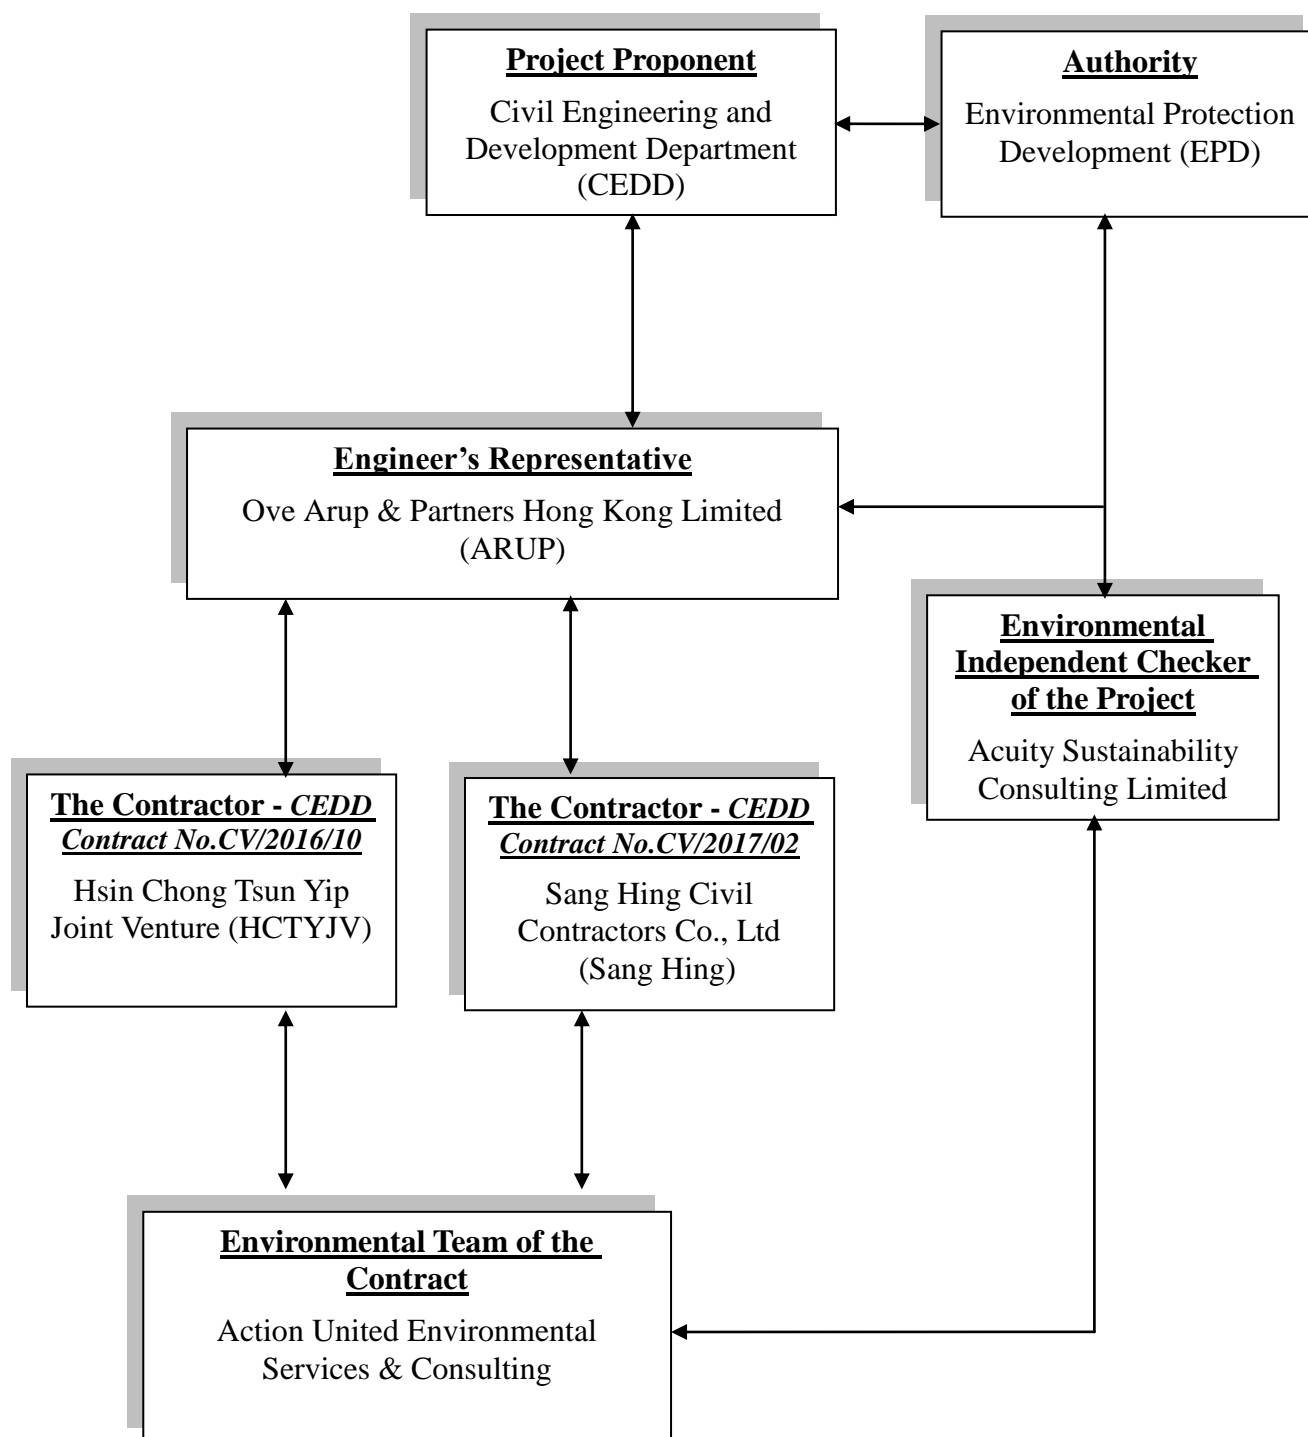

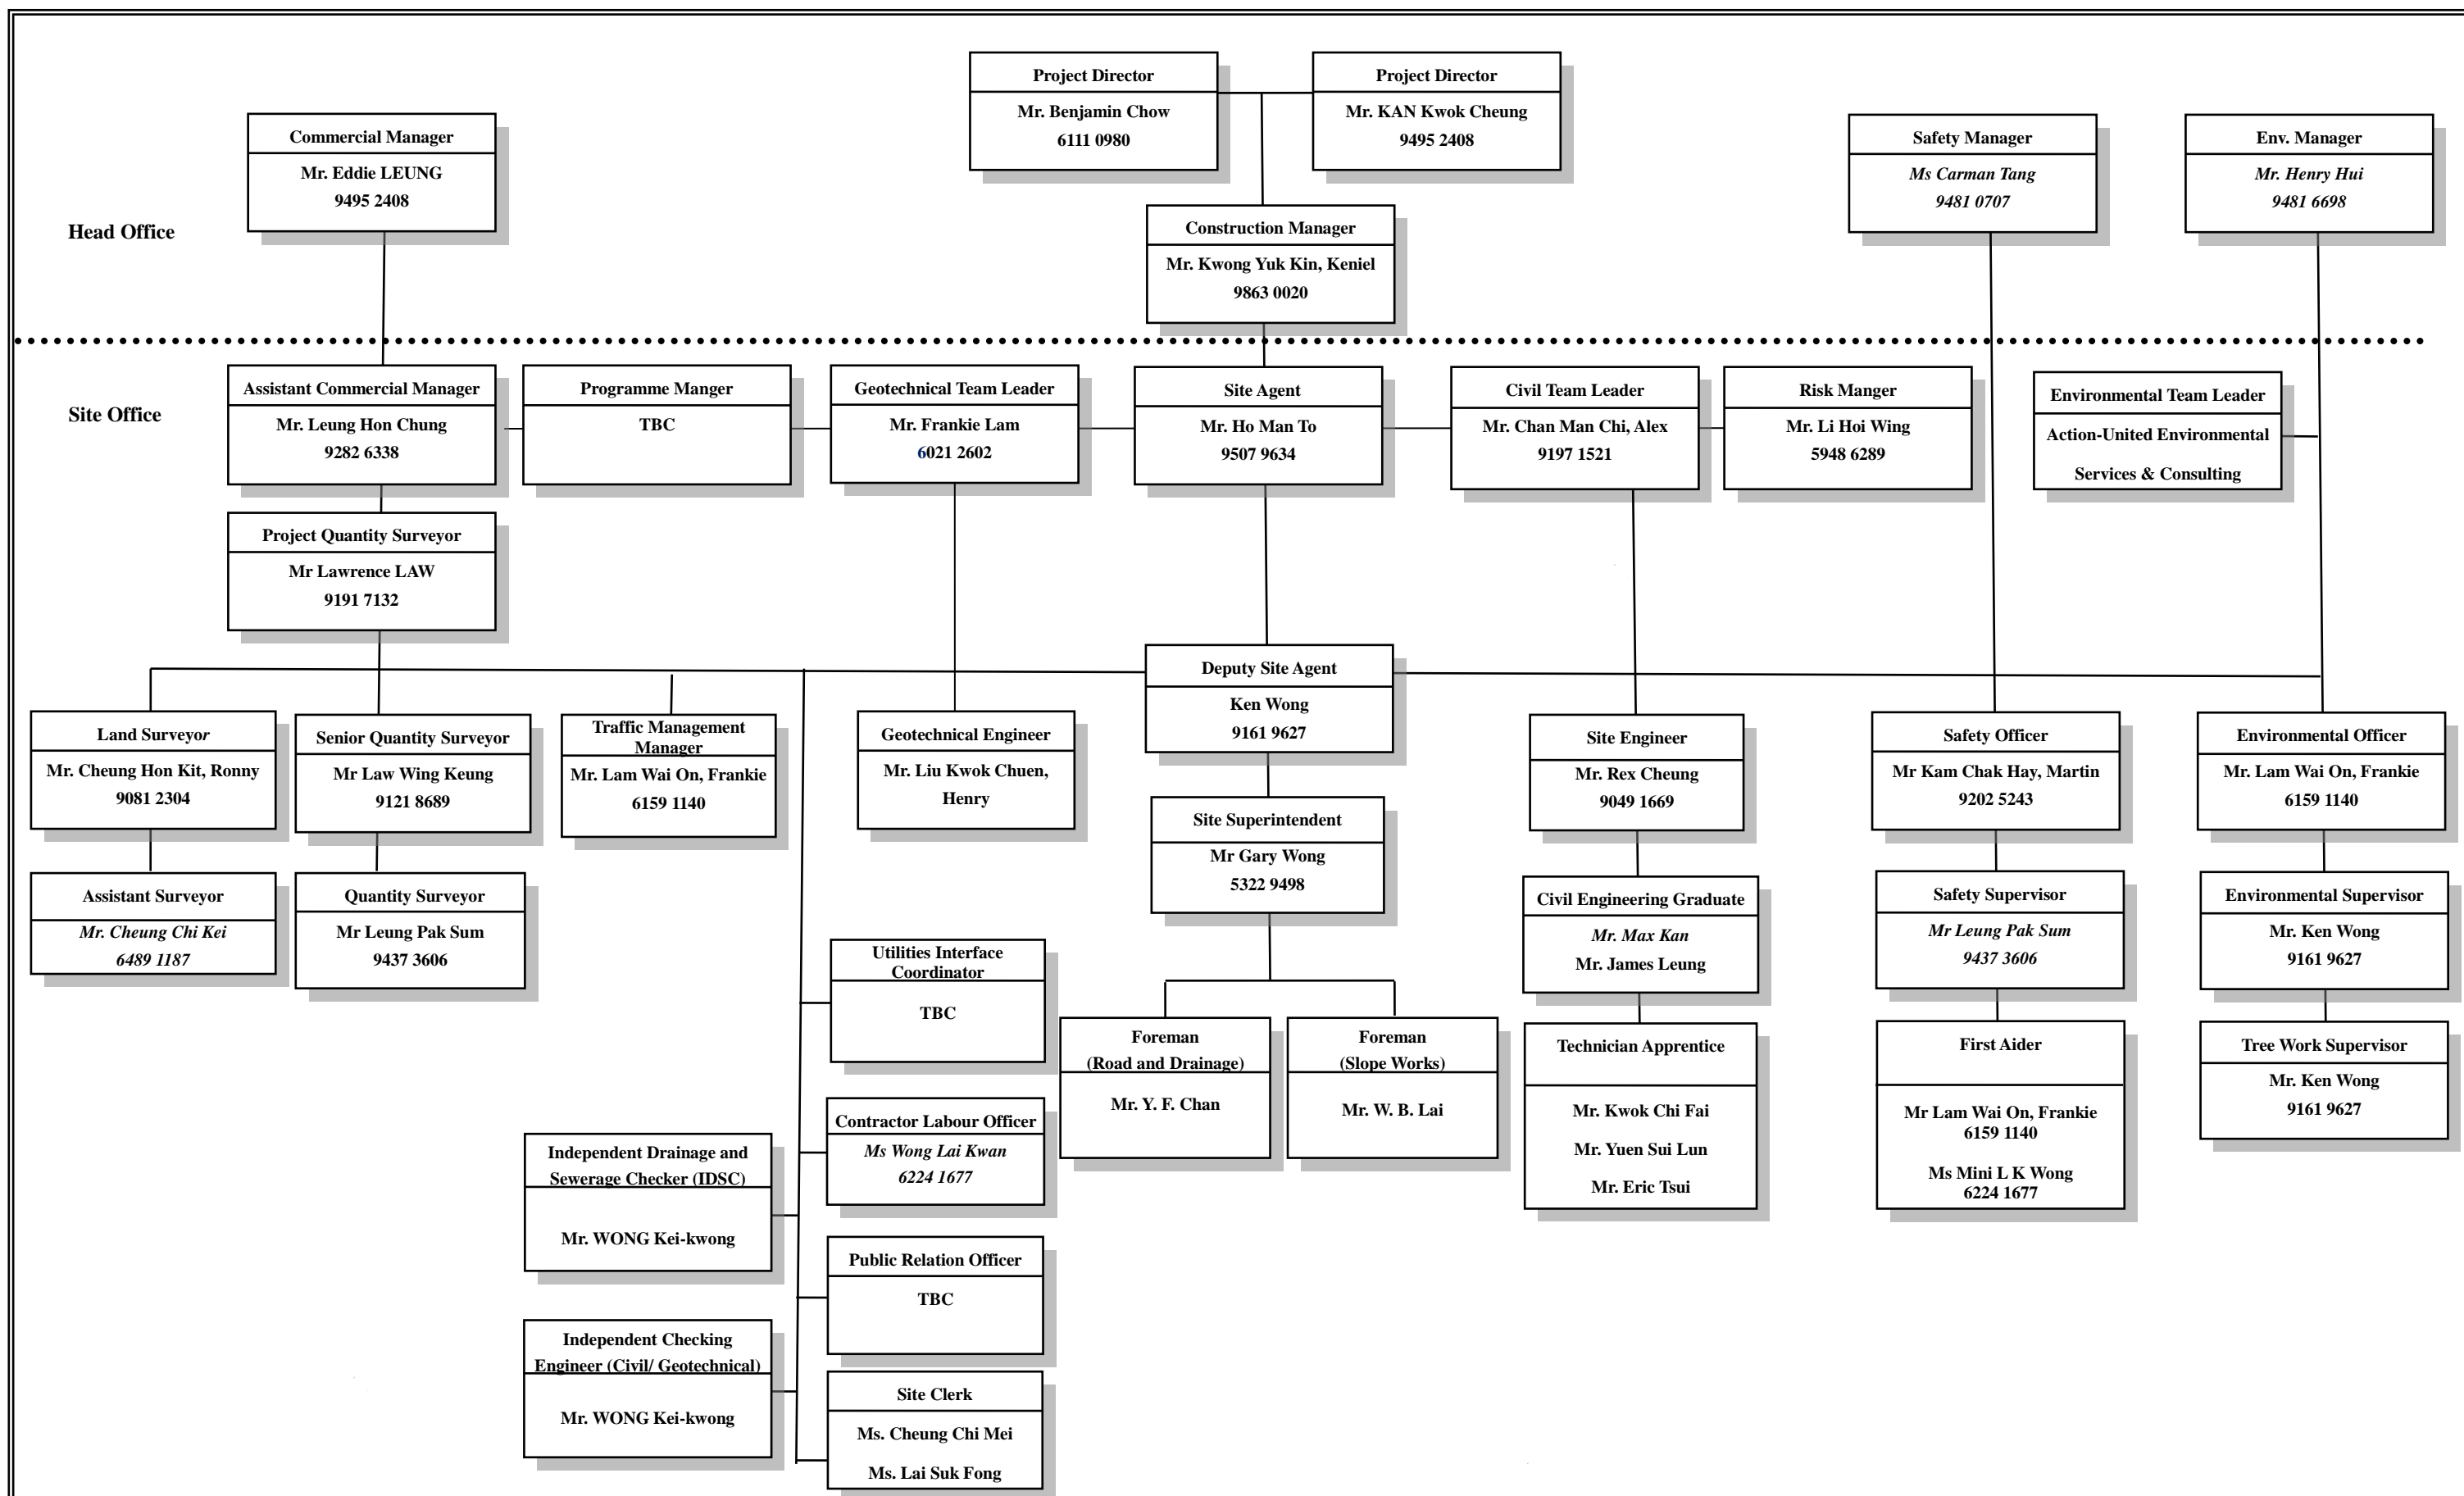


SANG HING CIVIL CONTRACTORS CO., LTD.

CONTRACT NO. CV/2017/02

Development of Columbarium at Sandy Ridge Cemetery -Infrastructural Works  
at Man Kam To Road and Lin Ma Hang Road

PROJECT ORGANIZATION CHART


(Revision Date : 28 Sept 2018)

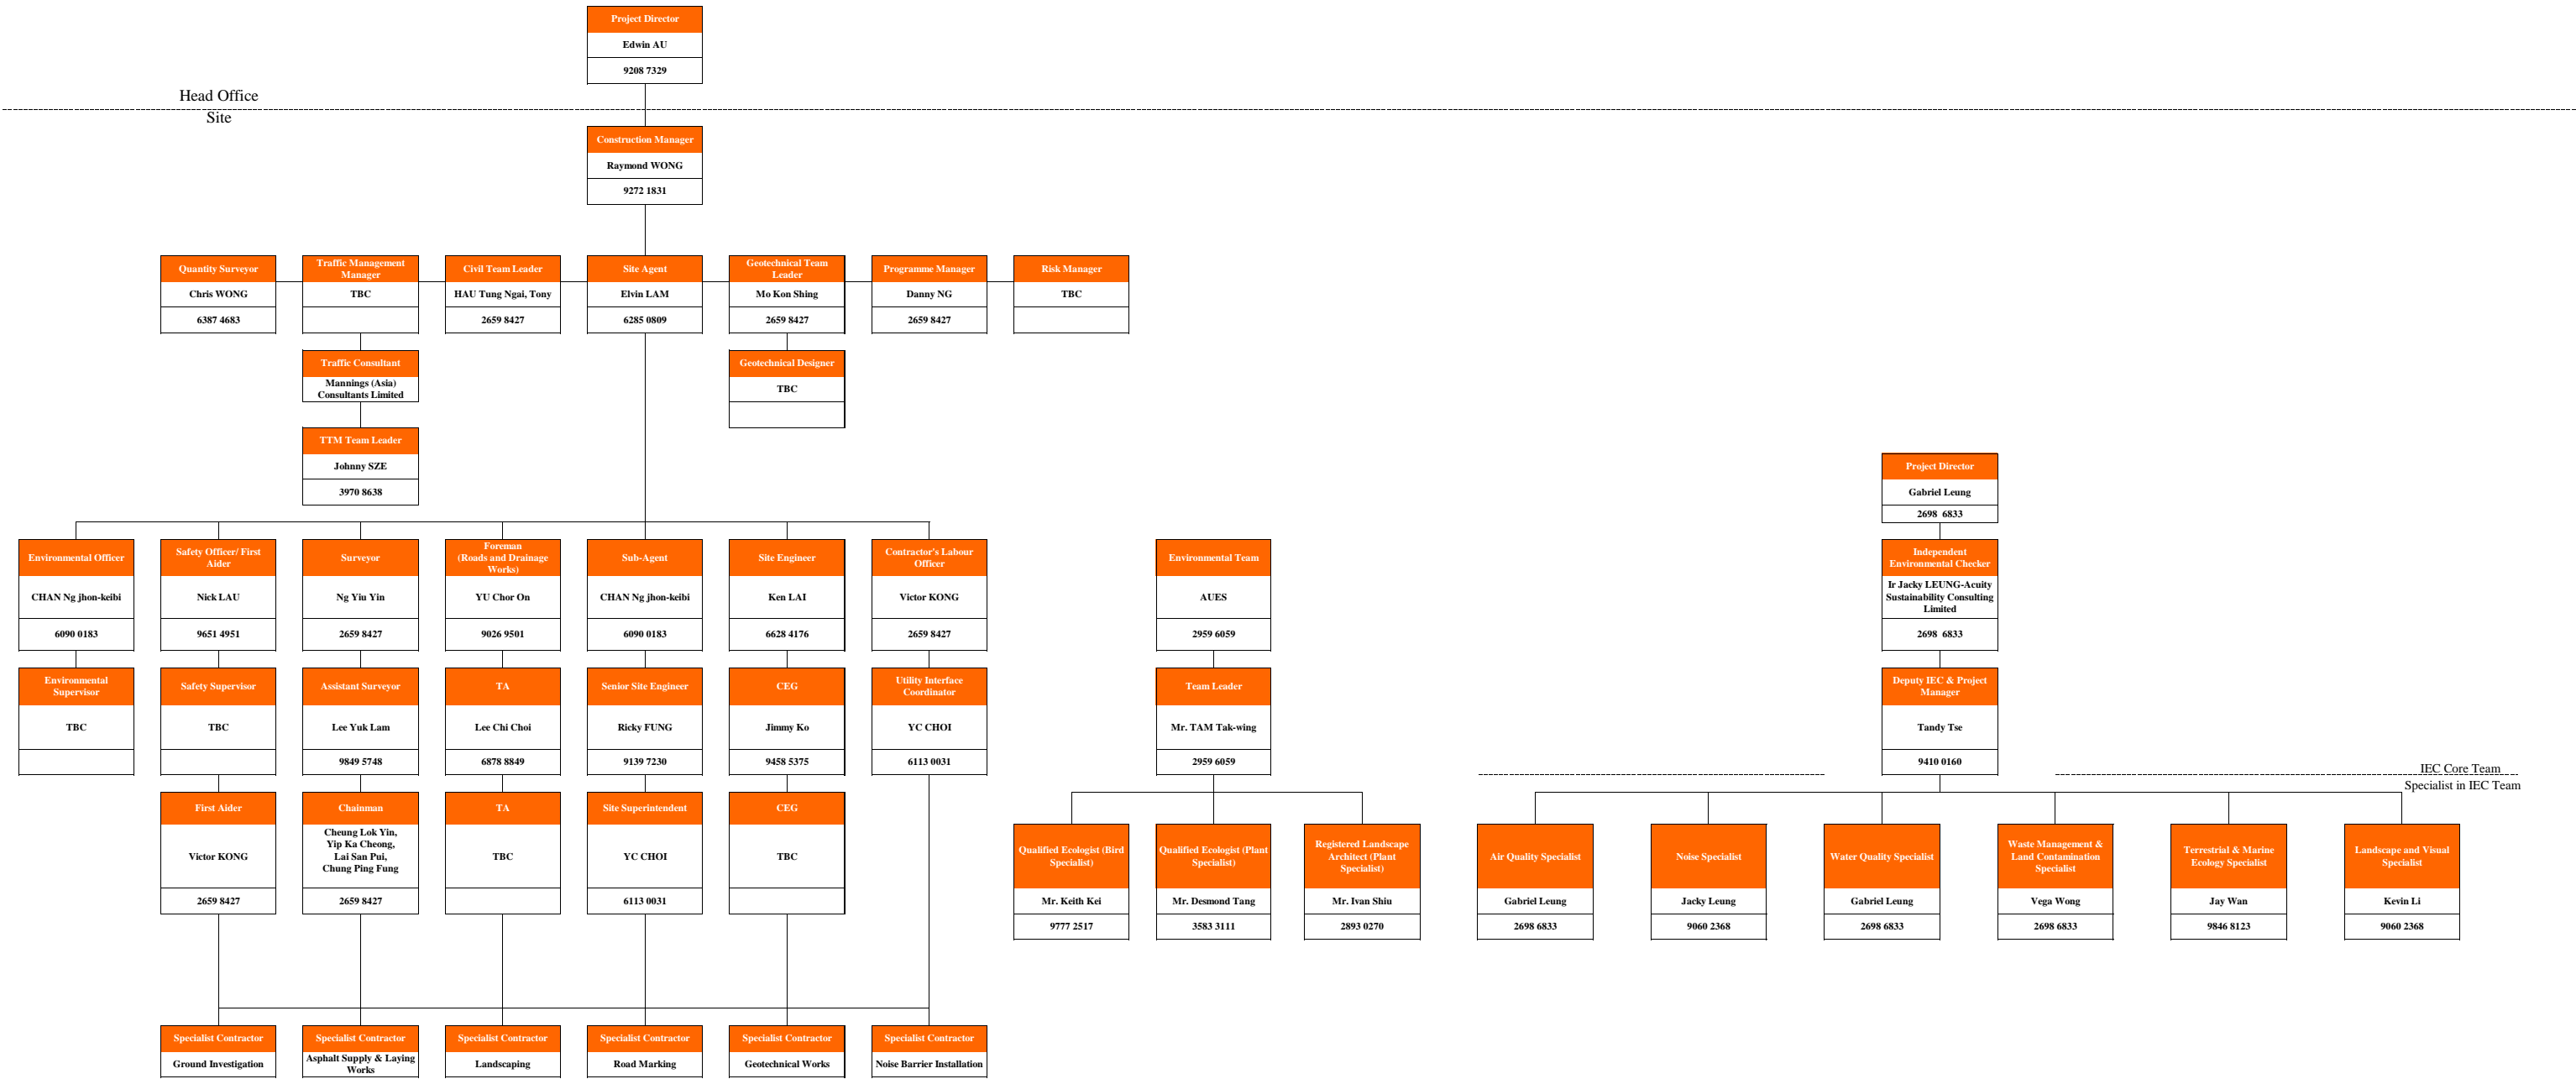

Legend:  
TBC= To be Confirmed



## Organisation Chart of IEC Team




Contract No. CV/2016/10

Site Formation and Associated Infrastructural Works for Development of  
Columbarium at Sandy Ridge Cemetery

Organization Chart of the Environmental Team

**AUES**

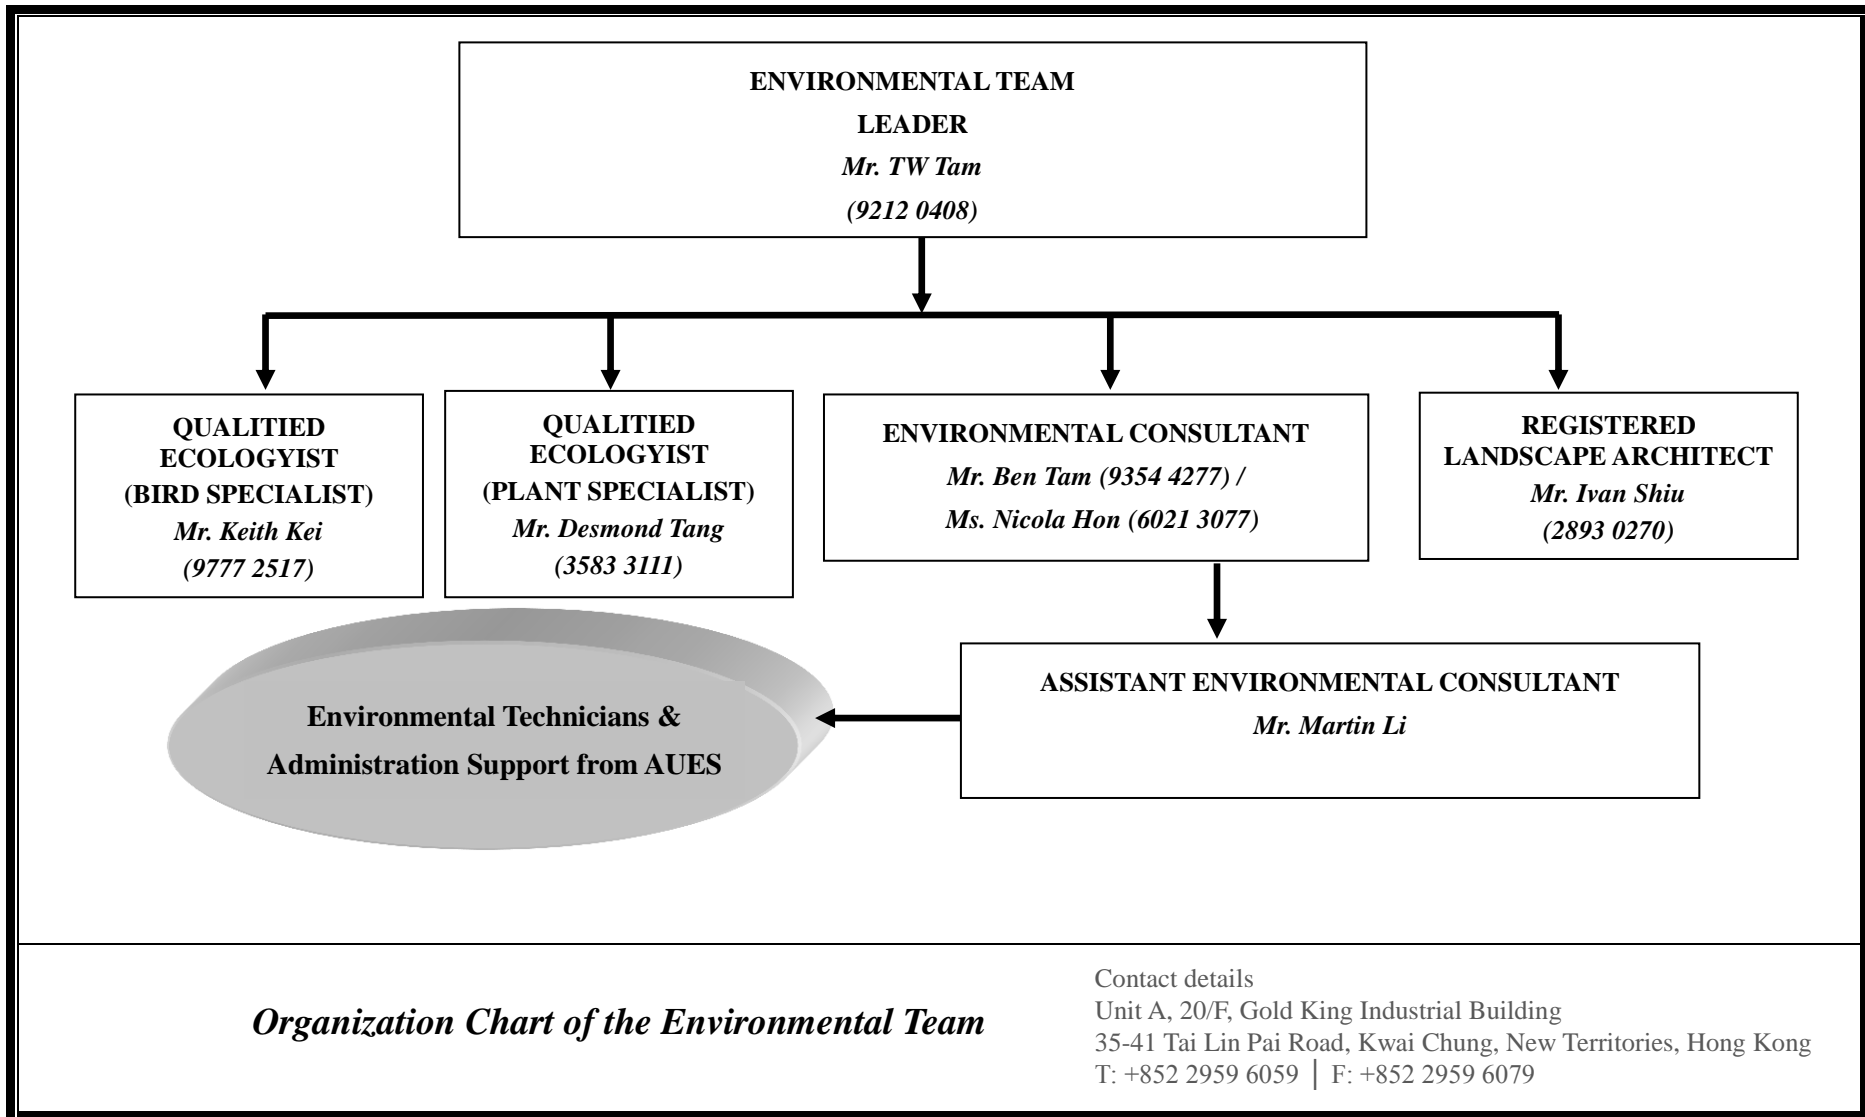

**Contact Details of Key Personnel for CV/2016/10 (Contact 1)**

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
CEDD	Employer	Joseph Wong	2762-5658	2714-0079
ARUP	Engineer's Representative	Steve Tang	6190-1513	2268-3950
ACUITY	Independent Environmental Checker	Ir. Leung CH Jacky	2698-6833	2698-9383
HCTYJV	Project Director	Mr. Kan Kwok Cheung	9495-2408	2633-4691
HCTYJV	Project Manager	Mr. Keniel Kwong	9863-0020	2633-4691
HCTYJV	Site Agent	Mr. Ho Man To	9507-9634	2633-4691
HCTYJV	Environmental Officer	Mr. Frankie Lam	6159-1140	2633-4691
HCTYJV	Safety Officer	Mr. Martin Kam	9202-5243	2633-4691
AUES	Environmental Team Leader	Mr. T.W. Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Mr. Ben Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959-6059	2959-6079
AUES	Environmental Site Inspector	Mr. Martin Li	2959-6059	2959-6079

**Legend:**

*CEDD (Employer) – Civil Engineering and Development Department*

*ARUP (Engineer) – Ove Arup & Partners Hong Kong Limited*

*HCTYJV (Main Contractor) – Hsin Chong Tsun Yip Joint Venture*

*ACUITY (IEC) – Acuity Sustainability Consulting Limited*

*AUES (ET) – Action-United Environmental Services & Consulting*

**Contact Details of Key Personnel for CV/2017/01 (Contact 2)**

<b>Organization</b>	<b>Project Role</b>	<b>Name of Key Staff</b>	<b>Tel No.</b>	<b>Fax No.</b>
CEDD	Employer	Joseph Wong	2762-5658	2714-0079
ARUP	Engineer's Representative	Anthony Lau	6190-1513	2268-3950
ACUITY	Independent Environmental Checker	Ir. Leung CH Jacky	2698-6833	2698-9383
SANG HING	Project Director	Edwin Au	9208-7329	2403-1162
SANG HING	Construction Manager	Raymond Wong	9272-1831	2403-1162
SANG HING	Site Agent	Elvin Lam	6285-0803	2403-1162
SANG HING	Environmental Officer	Chan Ng jhon-keibi	6090-0183	2403-1162
SANG HING	Environmental Supervisor	TBA	TBA	TBA
AUES	Environmental Team Leader	Mr. T.W. Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Mr. Ben Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959-6059	2959-6079
AUES	Environmental Site Inspector	Mr. Martin Li	2959-6059	2959-6079

**Legend:**

*CEDD (Employer) – Civil Engineering and Development Department*

*ARUP (Engineer) – Ove Arup & Partners Hong Kong Limited*

*Sang Hing (Main Contractor) – Sang Hing Civil Contractors Co., Ltd*

*ACUITY (IEC) – Acuity Sustainability Consulting Limited*

*AUES (ET) – Action-United Environmental Services & Consulting*



## **Appendix C**

### **Three Months rolling Programme**

3-month Rolling Programme (Jan 2019 to Mar 2019)

Date: Jan 2019

Task Split

Milestone Summary

Project Summary

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

ID	Task Name	Duration	Start	Finish	tr 1, 2019	Jan	Feb	Mar	Qtr 2, 2019	Apr
302	<b>Landscape Works at Cut Slopes CS16 and CS17</b>	<b>460 days</b>	<b>Tue 3/7/18</b>	<b>Thu 23/1/20</b>						
303	Planter W2 Construction	196 days	Mon 24/12/18	Tue 27/8/19						
307	Hydroseeding	360 days	Tue 3/7/18	Fri 20/9/19						
376	<b>Part B2</b>	<b>887 days</b>	<b>Fri 15/12/17</b>	<b>Wed 23/12/20</b>						
387	<b>Sha Ling Road (M001 CH +40 to +180)</b>	<b>602 days</b>	<b>Sat 1/12/18</b>	<b>Sat 19/12/20</b>						
388	TTA and XP Application for Existing Sha Ling Road	180 days	Sat 1/12/18	Wed 17/7/19						
413	<b>Man Kam To Road Bus Shelter</b>	<b>836 days</b>	<b>Fri 15/12/17</b>	<b>Wed 21/10/20</b>						
414	Temporary Storage and Secondary Site Office	600 days	Fri 15/12/17	Fri 3/1/20						
421	<b>Sha Ling Road (M001 CH+0 to +40), Man Kam To Road Drainage, Sewerage, Watermains and Other Utilities</b>	<b>749 days</b>	<b>Fri 8/6/18</b>	<b>Wed 23/12/20</b>						
422	TTA and XP Application at Man Kam To Road	270 days	Fri 8/6/18	Sat 11/5/19						
454	<b>Part C</b>	<b>570 days</b>	<b>Tue 15/1/19</b>	<b>Wed 23/12/20</b>						
455	Installation of Temporary Works	60 days	Tue 15/1/19	Thu 28/3/19						
456	Excavation to Formation Level and Blinding Layer	45 days	Fri 29/3/19	Wed 29/5/19						
464	<b>E&amp;M and Waterworks</b>	<b>570 days</b>	<b>Tue 15/1/19</b>	<b>Wed 23/12/20</b>						
465	Water Meter Application	150 days	Tue 15/1/19	Tue 23/7/19						
472	<b>Part D</b>	<b>586 days</b>	<b>Sat 15/12/18</b>	<b>Tue 15/12/20</b>						
473	Woodland Planting	586 days	Sat 15/12/18	Tue 15/12/20						
495	<b>Section 3 of the Works (Part E)</b>	<b>721 days</b>	<b>Fri 15/12/17</b>	<b>Thu 5/12/19</b>						
505	<b>Fill Slope FS3</b>	<b>278 days</b>	<b>Thu 16/8/18</b>	<b>Tue 30/7/19</b>						
506	Backfilling Stage 1 (~11m, up to +27 mPD at Section 17) + Filter Blanket from +16mPD to 27mPD	148 days	Thu 16/8/18	Sat 16/2/19						
507	Drainage, Maintenance Access after Backfilling Stage 1	94 days	Sat 17/11/18	Wed 13/3/19						
511	<b>Retaining Wall RW4</b>	<b>192 days</b>	<b>Mon 18/2/19</b>	<b>Wed 16/10/19</b>						
512	Backfilling to Formation Level, Plate Load Test, Blinding Layer	30 days	Mon 18/2/19	Sat 23/3/19						
513	Base Slab of Retaining Wall RW4 Bay 1-8	32 days	Sat 23/2/19	Tue 2/4/19						
514	Wall Stem of Retaining Wall RW4 Bay 1-8	52 days	Tue 5/3/19	Sat 11/5/19						
518	<b>Fill Slope FS2</b>	<b>224 days</b>	<b>Mon 18/2/19</b>	<b>Fri 22/11/19</b>						
519	Backfilling Stage 1 (~16m, up to Maintenance Berm +43 mPD) + filter Blanket from +27mPD to 35mPD on temporary cut+ 2.5m depth filter blanket 3m below berm surface	167 days	Mon 18/2/19	Wed 11/9/19						
535	<b>Cut Slope CS19</b>	<b>204 days</b>	<b>Thu 3/1/19</b>	<b>Thu 12/9/19</b>						
536	Excavate to +54.5 mPD	50 days	Thu 3/1/19	Tue 5/3/19						
537	Excavate to +47mPD, Soil Nails and Raking Drains (17 nos. of Soil Nail, 13 Nos. of Raking Drain)	89 days	Wed 6/3/19	Thu 27/6/19						
539	Drainage and Maintenance Access	196 days	Sat 12/1/19	Thu 12/9/19						


## Development of Columbarium at Sandy Ridge Cemetery

## - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

ID	WBS	Task Name	Duration	Start Date	Completion Date	3rd Quarter					1st Half	
						May 2018	July 2018	September 2018	November 2018		1st Quarter	
											January 2019	March 2019
2	2	<b>Starting Date</b>	0 days	Thu 31/5/18	Thu 31/5/18							
3	3	ET Submissions	9 days	Wed 26/9/18	Fri 5/10/18							
4	3.1	monitoring and survey plan for golden-headed cisticola	0 days	Thu 4/10/18	Thu 4/10/18							
5	3.2	management organization	0 days	Thu 27/9/18	Thu 27/9/18							
6	3.3	layout plan of footpath at Lin Ma Hang Road	0 days	Fri 28/9/18	Fri 28/9/18							
7	3.4	construction works schedule and location plan	0 days	Wed 26/9/18	Wed 26/9/18							
8	3.5	project specific EM&A manual	0 days	Fri 5/10/18	Fri 5/10/18							
9	3.6	vegetation survey report and transplantation proposal	0 days	Fri 28/9/18	Fri 28/9/18							
10	3.7	landscape & visual mitigation and tree preservation plans(s)	0 days	Fri 5/10/18	Fri 5/10/18							
11	3.8	traffic noise mitigation plan	0 days	Thu 4/10/18	Thu 4/10/18							
12	4	Applications to Government Department	27 days	Mon 4/6/18	Sat 30/6/18							
13	4.1	Application of Waste water discharge license	27 days	Mon 4/6/18	Sat 30/6/18							
14	4.2	Application of chemical waste producer permit	27 days	Mon 4/6/18	Sat 30/6/18							
15	4.3	Application of trip ticket system	27 days	Mon 4/6/18	Sat 30/6/18							
16	4.4	Notify the starting date of the Contract to CIC (Construction Industry Council Ordinance (Ch587) - Form)	0 days	Thu 14/6/18	Thu 14/6/18							
17	4.5	Notify the starting date of the Contract to Labour Dept (Construction Site (Safety) Regulation - Regulation 56(1))	0 days	Thu 14/6/18	Thu 14/6/18							
18	4.6	Notify the starting date of the Contract to CWRA (Application Form for Web Submission Administrator)	0 days	Thu 14/6/18	Thu 14/6/18							
19	4.7	Notify the starting date of the Contract to PCFB (Pneumoconiosis (Compensation) Ordinance - Form 1(B))	0 days	Thu 14/6/18	Thu 14/6/18							
20	5	Submissions & acceptances	835 days	Mon 4/6/18	Tue 15/9/20							
21	5.1	Submission of Subcontractor Management Plan	0 days	Tue 12/6/18	Tue 12/6/18							
22	5.2	acceptance of Subcontractor Management Plan	0 days	Fri 27/7/18	Fri 27/7/18							
23	5.3	Submission of Safety Plan	0 days	Tue 12/6/18	Tue 12/6/18							
24	5.4	acceptance of Safety Plan	0 days	Tue 28/8/18	Tue 28/8/18							
25	5.5	Submissions of Draft Environmental Management Plan	0 days	Fri 15/6/18	Fri 15/6/18							
26	5.6	acceptance of Draft Environmental Management Plan	0 days	Tue 11/12/18	Tue 11/12/18							
27	5.7	Submissions for acceptance of Environmental Management Plan	0 days	Tue 18/12/18	Tue 18/12/18							
28	5.8	acceptance of Environmental Management Plan	0 days	Tue 8/1/19	Tue 8/1/19							
29	5.9	Submissions for acceptance of Site Management Plan for Trip Ticket Implementation	0 days	Fri 10/8/18	Fri 10/8/18							
30	5.10	acceptance of Site Management Plan for Trip Ticket Implementation	0 days	Mon 12/11/18	Mon 12/11/18							

## Development of Columbarium at Sandy Ridge Cemetery

## - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

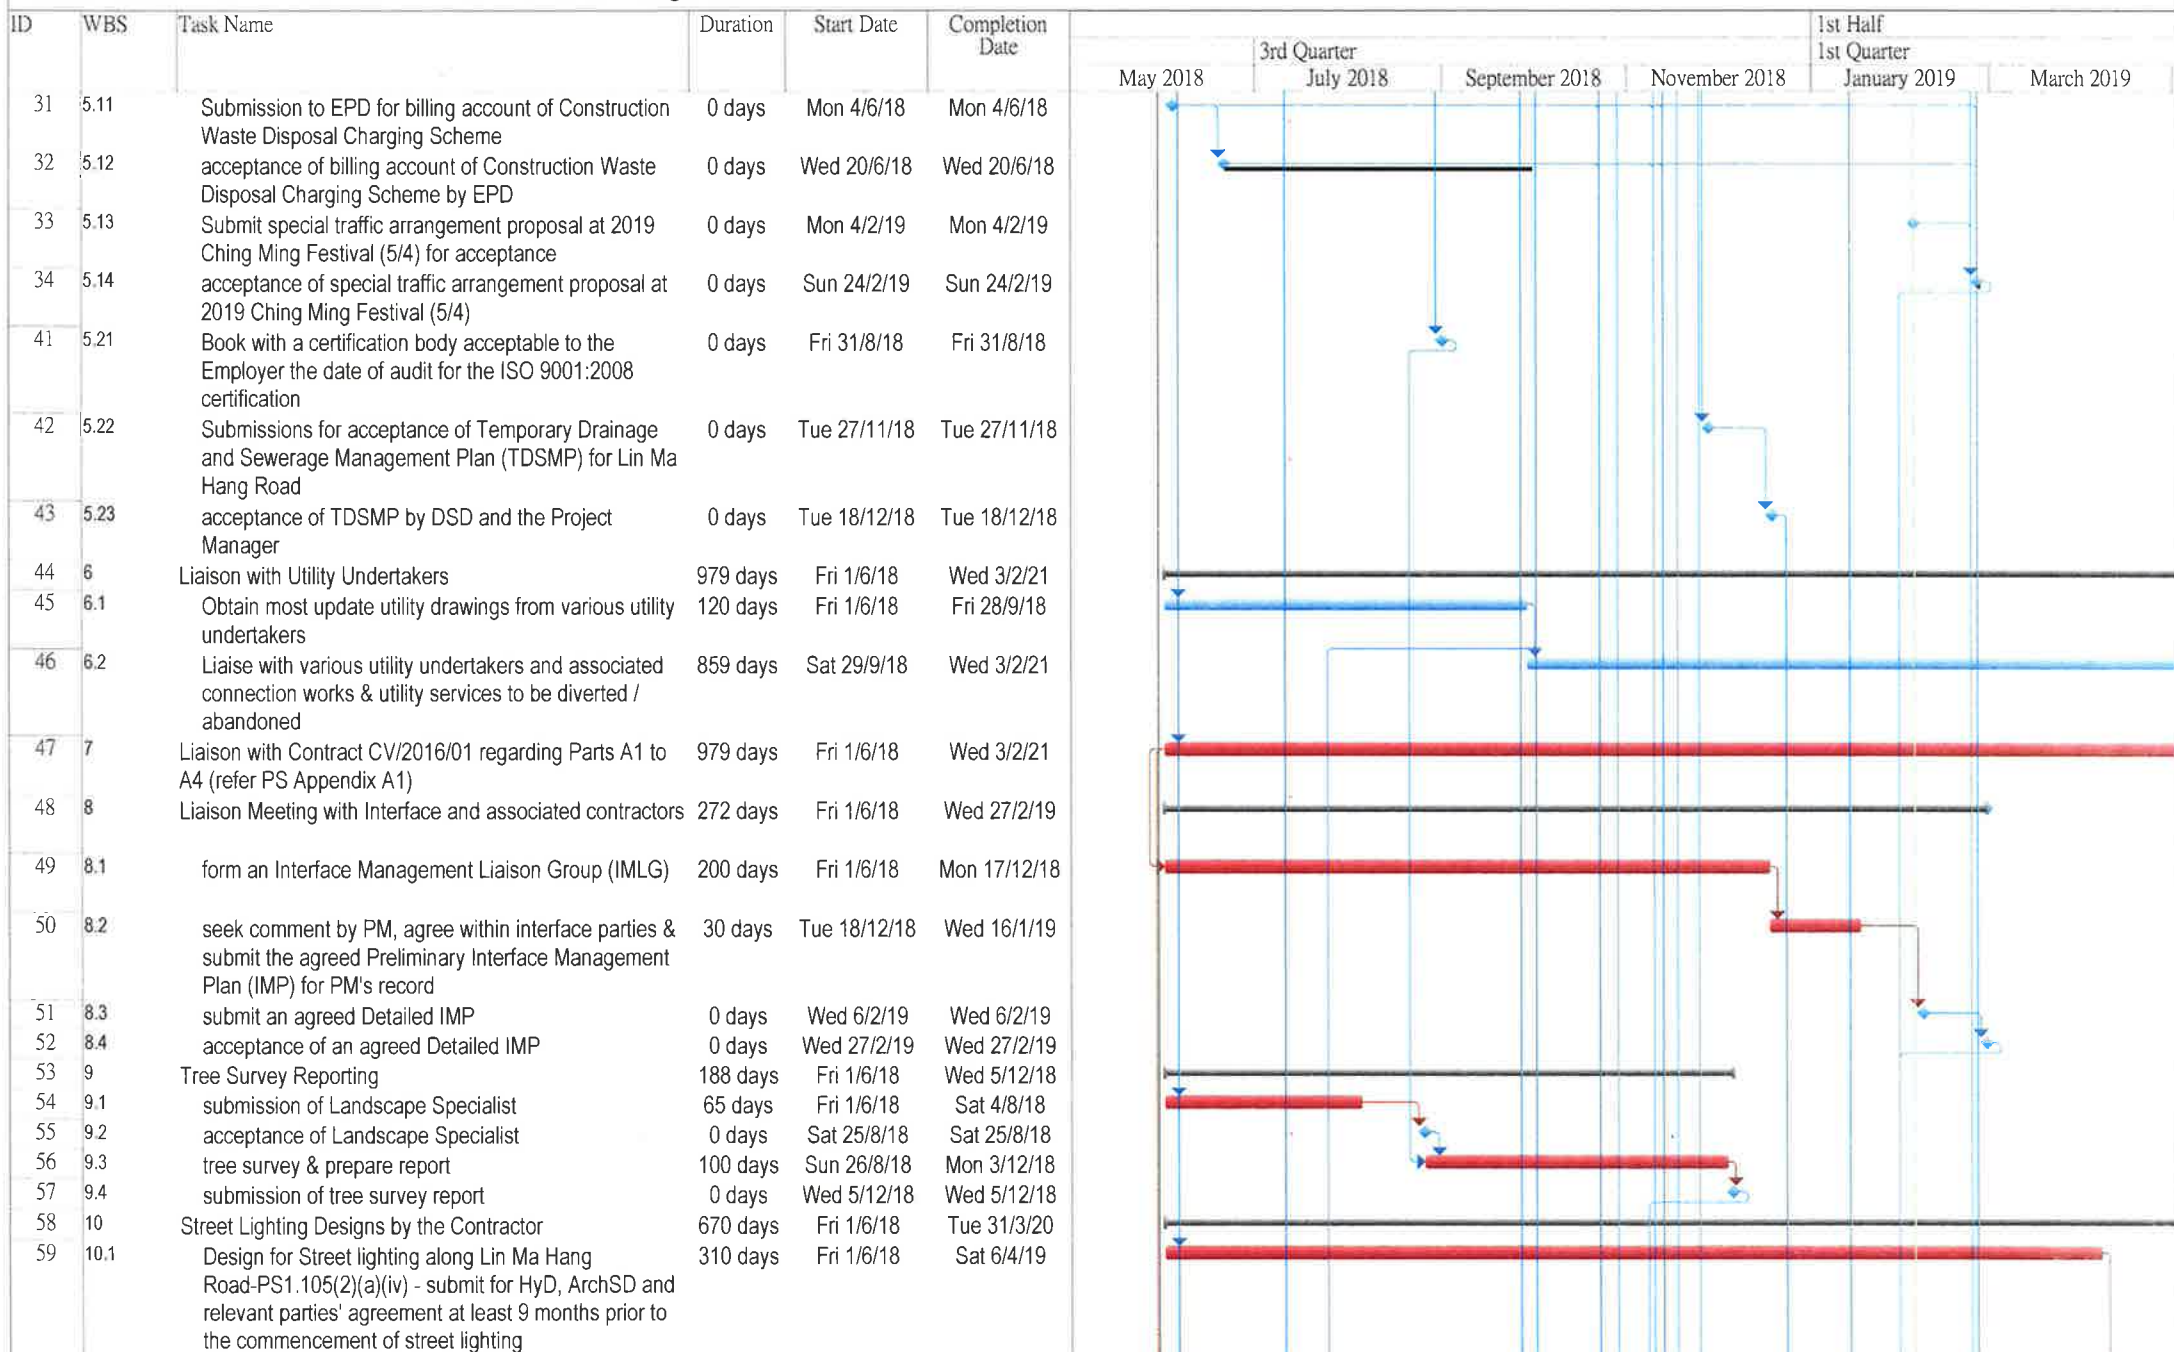



Development of Columbarium at Sandy Ridge Cemetery  
- Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

ID	WBS	Task Name	Duration	Start Date	Completion Date	3rd Quarter						1st Half	
						May 2018	July 2018	September 2018	November 2018	January 2019	March 2019	1st Quarter	
60	10.2	submission of designs for street lighting along Lin Ma Hang Road	0 days	Sat 6/4/19	Sat 6/4/19								
62	10.4	Design for Street lighting along Road B, Road E, Road F(part) and Sheung Shui Landmark PTI -PS1.105(2)(a)(iv) - submit for HyD, ArchSD and relevant parties' agreement at least 9 months prior to the commencement of street lighting	57 days	Sun 7/4/19	Sun 2/6/19								
66	11	Provision of Project Manager's Site Accommodation (PS1.08A(b) & 1.49)	28 days	Fri 1/6/18	Thu 28/6/18								
70	13	Condition Survey	87 days	Thu 23/8/18	Wed 5/12/18								
71	13.1	submit of Qualified Engineer for Condition Survey	0 days	Thu 23/8/18	Thu 23/8/18								
72	13.2	acceptance of Qualified Engineer for Condition Survey	0 days	Wed 12/9/18	Wed 12/9/18								
73	13.3	submit condition survey of graded historic buildings and other built heritage under PS 25.40 for acceptance	0 days	Wed 14/11/18	Wed 14/11/18								
74	13.4	acceptance of condition survey of graded historic buildings and other built heritage	0 days	Wed 5/12/18	Wed 5/12/18								
75	13.5	submit condition survey of existing properties under PS 1.71 for acceptance	0 days	Sat 29/9/18	Sat 29/9/18								
76	13.6	acceptance of condition survey of existing properties	0 days	Sat 20/10/18	Sat 20/10/18								
77	14	<b>section 1 of the works - Completion of all works within Parts A1, A2 and B of the Site except Establishment works</b>	981 days	Wed 30/5/18	Wed 3/2/21								
78	14.1	<b>Parts A1</b>	859 days	Fri 28/9/18	Wed 3/2/21								
79	14.1.1	<b>access date for section 1 (Parts A1) - not more than 120 days after the starting date</b>	0 days	Fri 28/9/18	Fri 28/9/18								
80	14.1.2	form temporary haul road from the south side to Parts A1	14 days	Tue 2/10/18	Mon 22/10/18								
81	14.1.3	general site clearance	28 days	Tue 23/10/18	Mon 26/11/18								
82	14.1.4	initial survey	19 days	Tue 27/11/18	Tue 18/12/18								
83	14.1.5	construction of temporary drainage	15 days	Wed 19/12/18	Tue 8/1/19								
84	14.1.6	Site Formation works for Cut Slope CS22 (in Parts A1)	166 days	Wed 9/1/19	Thu 8/8/19								
85	14.1.6.1	install test nails & pull out test	2 days	Wed 9/1/19	Thu 10/1/19								
86	14.1.6.2	soil nails & raking drain	20 days	Fri 11/1/19	Sat 2/2/19								
90	14.1.7	A1) Construction of Retaining Wall RW13 (bays 1 to 5)	121 days	Mon 4/2/19	Fri 12/7/19								
92	14.1.7.2	concrete blinding layers for 5 bays	3 days	Sat 9/3/19	Tue 12/3/19								
93	14.1.7.3	formwork for bases of alternative first 3 bays	2 days	Tue 12/3/19	Wed 13/3/19								
94	14.1.7.4	steel fixing for 3 bases	3 days	Wed 13/3/19	Fri 15/3/19								
95	14.1.7.5	concrete and curing for 3 bases	5 days	Mon 18/3/19	Fri 22/3/19								
96	14.1.7.6	remove formwork	3 days	Fri 22/3/19	Tue 26/3/19								

Development of Columbarium at Sandy Ridge Cemetery  
- Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

ID	WBS	Task Name	Duration	Start Date	Completion Date	1st Half					
						May 2018	3rd Quarter July 2018	September 2018	November 2018	1st Quarter January 2019	March 2019
97	14.1.7.7	falsework and formwork for alternative 3 walls	4 days	Tue 26/3/19	Fri 29/3/19						
98	14.1.7.8	steel fixing for 3 walls	9 days	Fri 29/3/19	Thu 11/4/19						
99	14.1.7.9	close formwork for 3 walls	3 days	Thu 11/4/19	Mon 15/4/19						
100	14.1.7.10	concrete and curing for 3 walls	6 days	Mon 15/4/19	Wed 24/4/19						
101	14.1.7.11	remove formwork	3 days	Tue 23/4/19	Thu 25/4/19						
102	14.1.7.12	formwork for bases of alternative second two bays	2 days	Thu 25/4/19	Fri 26/4/19						
91	14.1.7.1	excavation with temporary soil nails behind RW13 (bays 1 to 5)	26 days	Mon 4/2/19	Fri 8/3/19						
113	14.1.8	Site Formation works for Fill Slope FS18	257 days	Mon 4/2/19	Tue 31/12/19						
114	14.1.8.1	excavate & re-compact top 3.5m (extent to be directed by PM) & Rd E(Drg.GE/2305), then backfill FS18 (filter blanket) (extent to be agreed by PM (GE/2601)(>3m) at the front of RW13 (bay 1 & 2)	90 days	Mon 4/2/19	Tue 4/6/19						
208	14.3	<b>Parts B - refer Appendix MKTR01A &amp; Appendix MKTR01B</b>	981 days	Wed 30/5/18	Wed 3/2/21						
209	14.3.1	<b>access date for section 1 (Parts B) - the starting date</b>	0 days	Thu 31/5/18	Thu 31/5/18						
210	14.3.2	Initial Survey	106 days	Wed 30/5/18	Thu 4/10/18						
211	14.3.3	utility detection and submit reports	30 days	Fri 5/10/18	Fri 9/11/18						
212	14.3.4	Temporary Traffic Arrangement (TTA) Scheme for Man Kam Road	134 days	Fri 1/6/18	Fri 9/11/18						
213	14.3.4.1	Preparation of TTA for TMLG and acceptance from TD and RMO	54 days	Fri 1/6/18	Sat 4/8/18						
214	14.3.4.2	Comment & acceptance of TTA scheme by TD & RMO	68 days	Mon 6/8/18	Fri 26/10/18						
215	14.3.4.3	Obtain roadwork advice from RMO	12 days	Sat 27/10/18	Fri 9/11/18						
216	14.3.5	Construction of Fresh Water Mains (DN400)-refer to Drawings No. <KTR Programme/W/001 & 002	352 days	Sat 10/11/18	Fri 17/1/20						
217	14.3.5.1	Phase 1: TTA 1s	52 days	Sat 10/11/18	Sat 12/1/19						
218	14.3.5.1.1	trial run for TTA	7 days	Sat 10/11/18	Sat 17/11/18						
219	14.3.5.1.2	saw cut existing pavement and removal	8 days	Mon 19/11/18	Tue 27/11/18						
220	14.3.5.1.3	trial pits	8 days	Wed 28/11/18	Thu 6/12/18						
224	14.3.5.1.7	backfill trench & remove sheetpile, rail & strut	8 days	Mon 31/12/18	Wed 9/1/19						
222	14.3.5.1.5	excavate trench & shoring	5 days	Sat 15/12/18	Thu 20/12/18						
221	14.3.5.1.4	trench sheetpiling	7 days	Fri 7/12/18	Fri 14/12/18						
223	14.3.5.1.6	pipe laying	6 days	Fri 21/12/18	Sat 29/12/18						
225	14.3.5.1.8	reinstate trench & curing	3 days	Thu 10/1/19	Sat 12/1/19						
226	14.3.5.2	Phase 1: TTA 8s	49 days	Wed 14/11/18	Sat 12/1/19						



## Development of Columbarium at Sandy Ridge Cemetery

## - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

ID	WBS	Task Name	Duration	Start Date	Completion Date	1st Half					
						3rd Quarter			1st Quarter		
						May 2018	July 2018	September 2018	November 2018	January 2019	March 2019
227	14.3.5.2.1	trial run for TTA	7 days	Wed 14/11/18	Wed 21/11/18						
228	14.3.5.2.2	saw cut existing pavement and removal	4 days	Thu 22/11/18	Mon 26/11/18						
229	14.3.5.2.3	trial pits	4 days	Tue 27/11/18	Fri 30/11/18						
233	14.3.5.2.7	backfill trench & remove sheetpile, rail & strut	8 days	Mon 31/12/18	Wed 9/1/19						
231	14.3.5.2.5	excavate trench & shoring	5 days	Mon 10/12/18	Fri 14/12/18						
230	14.3.5.2.4	trench sheetpiling	7 days	Sat 1/12/18	Sat 8/12/18						
232	14.3.5.2.6	pipe laying & 2 sluice valve in chamber	11 days	Sat 15/12/18	Sat 29/12/18						
234	14.3.5.2.8	reinstate trench & curing	3 days	Thu 10/1/19	Sat 12/1/19						
235	14.3.5.3	Phase 1: TTA 15s	44 days	Tue 20/11/18	Sat 12/1/19						
236	14.3.5.3.1	trial run for TTA	7 days	Tue 20/11/18	Tue 27/11/18						
237	14.3.5.3.2	saw cut existing pavement and removal	4 days	Wed 28/11/18	Sat 1/12/18						
238	14.3.5.3.3	trial pits	4 days	Mon 3/12/18	Thu 6/12/18						
242	14.3.5.3.7	backfill trench & remove sheetpile, rail & strut	8 days	Mon 31/12/18	Wed 9/1/19						
240	14.3.5.3.5	excavate trench & shoring	5 days	Sat 15/12/18	Thu 20/12/18						
239	14.3.5.3.4	trench sheetpiling	7 days	Fri 7/12/18	Fri 14/12/18						
241	14.3.5.3.6	pipe laying	6 days	Fri 21/12/18	Sat 29/12/18						
243	14.3.5.3.8	reinstate trench & curing	3 days	Thu 10/1/19	Sat 12/1/19						
244	14.3.5.4	Phase 2: TTA 2s	39 days	Tue 15/1/19	Mon 4/3/19						
245	14.3.5.4.1	mobilisation & set up TTA	2 days	Tue 15/1/19	Wed 16/1/19						
246	14.3.5.4.2	saw cut existing pavement and removal	4 days	Thu 17/1/19	Mon 21/1/19						
247	14.3.5.4.3	trial pits	4 days	Tue 22/1/19	Fri 25/1/19						
251	14.3.5.4.7	backfill trench & remove sheetpile, rail & strut	8 days	Wed 20/2/19	Thu 28/2/19						
249	14.3.5.4.5	excavate trench & shoring	5 days	Mon 4/2/19	Tue 12/2/19						
248	14.3.5.4.4	trench sheetpiling	7 days	Sat 26/1/19	Sat 2/2/19						
250	14.3.5.4.6	pipe laying	6 days	Wed 13/2/19	Tue 19/2/19						
252	14.3.5.4.8	reinstate trench & curing	3 days	Fri 1/3/19	Mon 4/3/19						
253	14.3.5.5	Phase 2: TTA 9s	39 days	Tue 15/1/19	Mon 4/3/19						
254	14.3.5.5.1	mobilisation & set up TTA	2 days	Tue 15/1/19	Wed 16/1/19						
255	14.3.5.5.2	saw cut existing pavement and removal	4 days	Thu 17/1/19	Mon 21/1/19						
256	14.3.5.5.3	trial pits	4 days	Tue 22/1/19	Fri 25/1/19						
260	14.3.5.5.7	backfill trench & remove sheetpile, rail & strut	8 days	Wed 20/2/19	Thu 28/2/19						
258	14.3.5.5.5	excavate trench & shoring	5 days	Mon 4/2/19	Tue 12/2/19						

Development of Columbarium at Sandy Ridge Cemetery  
- Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

ID	WBS	Task Name	Duration	Start Date	Completion Date					1st Half	
						May 2018	3rd Quarter July 2018	September 2018	November 2018	1st Quarter January 2019	March 2019
257	14.3.5.5.4	trench sheetpiling	7 days	Sat 26/1/19	Sat 2/2/19						
259	14.3.5.5.6	pipe laying	6 days	Wed 13/2/19	Tue 19/2/19						
261	14.3.5.5.8	reinstate trench & curing	3 days	Fri 1/3/19	Mon 4/3/19						
262	14.3.5.6	Phase 2: TTA 16s	40 days	Mon 14/1/19	Mon 4/3/19						
263	14.3.5.6.1	mobilisation & set up TTA	2 days	Mon 14/1/19	Tue 15/1/19						
264	14.3.5.6.2	saw cut existing pavement and removal	4 days	Wed 16/1/19	Sat 19/1/19						
265	14.3.5.6.3	trial pits	4 days	Mon 21/1/19	Thu 24/1/19						
269	14.3.5.6.7	backfill trench & remove sheetpile, rail & strut	9 days	Tue 19/2/19	Thu 28/2/19						
267	14.3.5.6.5	excavate trench & shoring	5 days	Sat 2/2/19	Mon 11/2/19						
266	14.3.5.6.4	trench sheetpiling	7 days	Fri 25/1/19	Fri 1/2/19						
268	14.3.5.6.6	pipe laying	6 days	Tue 12/2/19	Mon 18/2/19						
270	14.3.5.6.8	reinstate trench & curing	3 days	Fri 1/3/19	Mon 4/3/19						
271	14.3.5.7	Phase 3: TTA3s	39 days	Tue 5/3/19	Tue 23/4/19						
272	14.3.5.7.1	mobilisation & set up TTA	2 days	Tue 5/3/19	Wed 6/3/19						
273	14.3.5.7.2	saw cut existing pavement and removal	4 days	Thu 7/3/19	Mon 11/3/19						
274	14.3.5.7.3	trial pits	4 days	Tue 12/3/19	Fri 15/3/19						
278	14.3.5.7.7	backfill trench & remove sheetpile, rail & strut	8 days	Mon 8/4/19	Tue 16/4/19						
276	14.3.5.7.5	excavate trench & shoring	5 days	Mon 25/3/19	Fri 29/3/19						
275	14.3.5.7.4	trench sheetpiling	7 days	Sat 16/3/19	Sat 23/3/19						
277	14.3.5.7.6	pipe laying	6 days	Sat 30/3/19	Sat 6/4/19						
279	14.3.5.7.8	reinstate trench & curing	3 days	Wed 17/4/19	Tue 23/4/19						
280	14.3.5.8	Phase 3: TTA10s	39 days	Tue 5/3/19	Tue 23/4/19						
281	14.3.5.8.1	mobilisation & set up TTA	2 days	Tue 5/3/19	Wed 6/3/19						
282	14.3.5.8.2	saw cut existing pavement and removal	4 days	Thu 7/3/19	Mon 11/3/19						
283	14.3.5.8.3	trial pits	4 days	Tue 12/3/19	Fri 15/3/19						
287	14.3.5.8.7	backfill trench & remove sheetpile, rail & strut	8 days	Mon 8/4/19	Tue 16/4/19						
285	14.3.5.8.5	excavate trench & shoring	5 days	Mon 25/3/19	Fri 29/3/19						
284	14.3.5.8.4	trench sheetpiling	7 days	Sat 16/3/19	Sat 23/3/19						
286	14.3.5.8.6	pipe laying	6 days	Sat 30/3/19	Sat 6/4/19						
288	14.3.5.8.8	reinstate trench & curing	3 days	Wed 17/4/19	Tue 23/4/19						
289	14.3.5.9	Phase 3: TTA17s	39 days	Tue 5/3/19	Tue 23/4/19						
290	14.3.5.9.1	mobilisation & set up TTA	2 days	Tue 5/3/19	Wed 6/3/19						
291	14.3.5.9.2	saw cut existing pavement and removal	4 days	Thu 7/3/19	Mon 11/3/19						

Development of Columbarium at Sandy Ridge Cemetery  
- Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

ID	WBS	Task Name	Duration	Start Date	Completion Date	3rd Quarter					1st Half	
						May 2018	July 2018	September 2018	November 2018		1st Quarter	March 2019
292	14.3.5.9.3	trial pits	4 days	Tue 12/3/19	Fri 15/3/19							
296	14.3.5.9.7	backfill trench & remove sheetpile, rail & strut	8 days	Mon 8/4/19	Tue 16/4/19							
294	14.3.5.9.5	excavate trench & shoring	5 days	Mon 25/3/19	Fri 29/3/19							
293	14.3.5.9.4	trench sheetpiling	7 days	Sat 16/3/19	Sat 23/3/19							
295	14.3.5.9.6	pipe laying	6 days	Sat 30/3/19	Sat 6/4/19							
297	14.3.5.9.8	reinstate trench & curing	3 days	Wed 17/4/19	Tue 23/4/19							
316	14.3.5.12	Phase 4: TTA18s	42 days	Wed 24/4/19	Fri 14/6/19							
317	14.3.5.12.1	mobilisation & set up TTA	2 days	Wed 24/4/19	Thu 25/4/19							
537	17	<b>section 2 of the works - Completion of all works within Parts C1 and C2 of the Site except Establishment works</b>	979 days	Thu 31/5/18	Wed 3/2/21							
538	17.1	<b>access date for section 2 (Part C1)</b>	0 days	Thu 31/5/18	Thu 31/5/18							
539	17.2	Temporary Traffic Arrangement (TTA) Scheme for Lin Ma Hang Road	162 days	Fri 1/6/18	Fri 9/11/18							
540	17.2.1	Submission / acceptance of traffic consultant	14 days	Fri 1/6/18	Thu 14/6/18							
541	17.2.2	Preparation of TTA for TMLG and acceptance from TD and RMO	44 days	Fri 15/6/18	Sat 28/7/18							
542	17.2.3	Application for XP	115 days	Wed 11/7/18	Fri 2/11/18							
543	17.2.4	Comment & acceptance of TTA scheme by TD & RMO	90 days	Mon 30/7/18	Sat 27/10/18							
544	17.2.5	Obtain roadwork advice from RMO	7 days	Sat 3/11/18	Fri 9/11/18							
545	17.3	works at Lin Ma Hang Road (section 2 Part C1) refer Appendix LMHR01a to d	817 days	Sat 10/11/18	Wed 3/2/21							
546	17.3.1	Phase I (stage 1)-south lane (chainage 240-283)	21 days	Sat 10/11/18	Tue 4/12/18							
547	17.3.1.1	TTA & UU detection	2 days	Sat 10/11/18	Mon 12/11/18							
549	17.3.1.3	saw cut & remove existing pavement	2 days	Tue 13/11/18	Wed 14/11/18							
552	17.3.1.6	backfill formation	2 days	Sat 24/11/18	Mon 26/11/18							
553	17.3.1.7	lay kerb, sub-base	3 days	Tue 27/11/18	Thu 29/11/18							
554	17.3.1.8	DBM (Roadbase)	2 days	Fri 30/11/18	Sat 1/12/18							
555	17.3.1.9	base course and wearing course	2 days	Mon 3/12/18	Tue 4/12/18							
548	17.3.1.2	tree felling	2 days	Tue 13/11/18	Wed 14/11/18							
550	17.3.1.4	excavate pipe trench and manhole(s)	3 days	Thu 15/11/18	Sat 17/11/18							
551	17.3.1.5	lay pipes & construct manhole(s)	5 days	Mon 19/11/18	Fri 23/11/18							
556	17.3.2	Phase I (stage 2)-north lane (chainage 240-283)	17 days	Wed 5/12/18	Mon 24/12/18							
557	17.3.2.1	TTA & UU detection	2 days	Wed 5/12/18	Thu 6/12/18							
559	17.3.2.3	saw cut & remove existing pavement	2 days	Fri 7/12/18	Sat 8/12/18							
562	17.3.2.6	backfill formation	2 days	Fri 14/12/18	Sat 15/12/18							

## Development of Columbarium at Sandy Ridge Cemetery

## - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

ID	WBS	Task Name	Duration	Start Date	Completion Date	1st Half					
						3rd Quarter			1st Quarter		
						May 2018	July 2018	September 2018	November 2018	January 2019	March 2019
563	17.3.2.7	lay kerb, sub-base	3 days	Mon 17/12/18	Wed 19/12/18						
564	17.3.2.8	DBM (Roadbase)	2 days	Thu 20/12/18	Fri 21/12/18						
565	17.3.2.9	base course and wearing course	2 days	Sat 22/12/18	Mon 24/12/18						
560	17.3.2.4	excavate gully trench and gully pot(s)	1 day	Mon 10/12/18	Mon 10/12/18						
558	17.3.2.2	tree felling	2 days	Fri 7/12/18	Sat 8/12/18						
561	17.3.2.5	lay& connect gully pipes& construct gully pot(s)	3 days	Tue 11/12/18	Thu 13/12/18						
566	17.3.3	Phase I (stage 3)-south lane (chainage 283-335)	24 days	Thu 27/12/18	Thu 24/1/19						
567	17.3.3.1	TTA & UU detection	2 days	Thu 27/12/18	Fri 28/12/18						
569	17.3.3.3	saw cut & remove existing pavement	3 days	Sat 29/12/18	Wed 2/1/19						
572	17.3.3.6	backfill formation	2 days	Tue 15/1/19	Wed 16/1/19						
573	17.3.3.7	lay kerb, sub-base	3 days	Thu 17/1/19	Sat 19/1/19						
574	17.3.3.8	DBM (Roadbase)	2 days	Mon 21/1/19	Tue 22/1/19						
575	17.3.3.9	base course and wearing course	2 days	Wed 23/1/19	Thu 24/1/19						
568	17.3.3.2	tree felling	3 days	Sat 29/12/18	Wed 2/1/19						
570	17.3.3.4	excavate pipe trench and manhole(s)	2 days	Thu 3/1/19	Fri 4/1/19						
571	17.3.3.5	lay pipes & construct manhole(s)	8 days	Sat 5/1/19	Mon 14/1/19						
576	17.3.4	Phase I (stage 4)-north lane (chainage 283-335)	18 days	Fri 25/1/19	Mon 18/2/19						
577	17.3.4.1	TTA & UU detection	2 days	Fri 25/1/19	Sat 26/1/19						
579	17.3.4.3	saw cut & remove existing pavement	3 days	Mon 28/1/19	Wed 30/1/19						
582	17.3.4.6	backfill formation	2 days	Fri 8/2/19	Sat 9/2/19						
583	17.3.4.7	lay kerb, sub-base	3 days	Mon 11/2/19	Wed 13/2/19						
584	17.3.4.8	DBM (Roadbase)	2 days	Thu 14/2/19	Fri 15/2/19						
585	17.3.4.9	base course and wearing course	2 days	Sat 16/2/19	Mon 18/2/19						
580	17.3.4.4	excavate gully trench and gully pot(s)	1 day	Thu 31/1/19	Thu 31/1/19						
578	17.3.4.2	tree felling	3 days	Mon 28/1/19	Wed 30/1/19						
581	17.3.4.5	lay& connect gully pipes& construct gully pot(s)	3 days	Fri 1/2/19	Mon 4/2/19						
586	17.3.5	Phase I (stage 5)-south lane (chainage 335-380)	19 days	Tue 19/2/19	Tue 12/3/19						
587	17.3.5.1	TTA & UU detection	2 days	Tue 19/2/19	Wed 20/2/19						
588	17.3.5.2	saw cut & remove existing pavement	2 days	Thu 21/2/19	Fri 22/2/19						
591	17.3.5.5	backfill formation	2 days	Sat 2/3/19	Mon 4/3/19						
592	17.3.5.6	lay kerb, sub-base	3 days	Tue 5/3/19	Thu 7/3/19						
593	17.3.5.7	DBM (Roadbase)	2 days	Fri 8/3/19	Sat 9/3/19						
594	17.3.5.8	base course and wearing course	2 days	Mon 11/3/19	Tue 12/3/19						
589	17.3.5.3	excavate pipe trench and manhole(s)	2 days	Sat 23/2/19	Mon 25/2/19						
590	17.3.5.4	lay pipes & construct manhole(s)	4 days	Tue 26/2/19	Fri 1/3/19						
595	17.3.6	Phase I (stage 6)-north lane (chainage 335-380)	17 days	Wed 13/3/19	Mon 1/4/19						



## Development of Columbarium at Sandy Ridge Cemetery

## - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

ID	WBS	Task Name	Duration	Start Date	Completion Date							1st Half	
						3rd Quarter						1st Quarter	
						May 2018	July 2018	September 2018	November 2018	January 2019	March 2019		
596	17.3.6.1	TTA & UU detection	2 days	Wed 13/3/19	Thu 14/3/19								
597	17.3.6.2	saw cut & remove existing pavement	2 days	Fri 15/3/19	Sat 16/3/19								
600	17.3.6.5	backfill formation	2 days	Fri 22/3/19	Sat 23/3/19								
601	17.3.6.6	lay kerb, sub-base	3 days	Mon 25/3/19	Wed 27/3/19								
602	17.3.6.7	DBM (Roadbase)	2 days	Thu 28/3/19	Fri 29/3/19								
603	17.3.6.8	base course and wearing course	2 days	Sat 30/3/19	Mon 1/4/19								
598	17.3.6.3	excavate gully trench and gully pot(s)	1 day	Mon 18/3/19	Mon 18/3/19								
599	17.3.6.4	lay& connect gully pipes& construct gully pot(s)	3 days	Tue 19/3/19	Thu 21/3/19								
604	17.3.7	Phase I (stage 7)-south lane (chainage 380-435)	24 days	Tue 2/4/19	Sat 4/5/19								
605	17.3.7.1	TTA & UU detection	2 days	Tue 2/4/19	Wed 3/4/19								
607	17.3.7.3	saw cut & remove existing pavement	3 days	Thu 4/4/19	Mon 8/4/19								
610	17.3.7.6	backfill formation	2 days	Wed 24/4/19	Thu 25/4/19								
606	17.3.7.2	tree felling	3 days	Thu 4/4/19	Mon 8/4/19								
608	17.3.7.4	excavate pipe trench and manhole(s)	3 days	Tue 9/4/19	Thu 11/4/19								
609	17.3.7.5	lay pipes & construct manhole(s)	7 days	Fri 12/4/19	Tue 23/4/19								
862	17.3.23	Phase Ia (stage 101)-south lane (chainage 633-685)	20 days	Sat 10/11/18	Mon 3/12/18								
863	17.3.23.1	TTA & UU detection	2 days	Sat 10/11/18	Mon 12/11/18								
864	17.3.23.2	saw cut & remove existing pavement	2 days	Tue 13/11/18	Wed 14/11/18								
867	17.3.23.5	backfill trench to formation	2 days	Fri 23/11/18	Sat 24/11/18								
868	17.3.23.6	lay kerb, sub-base	3 days	Mon 26/11/18	Wed 28/11/18								
869	17.3.23.7	DBM (Roadbase)	2 days	Thu 29/11/18	Fri 30/11/18								
870	17.3.23.8	base course and wearing course	2 days	Sat 1/12/18	Mon 3/12/18								
865	17.3.23.3	excavate pipe trench and manhole(s)	2 days	Thu 15/11/18	Fri 16/11/18								
866	17.3.23.4	lay pipes & construct manhole(s)	5 days	Sat 17/11/18	Thu 22/11/18								
871	17.3.24	Phase Ia (stage 102)-north lane (chainage 633-685)	16 days	Tue 4/12/18	Fri 21/12/18								
872	17.3.24.1	TTA & UU detection	2 days	Tue 4/12/18	Wed 5/12/18								
874	17.3.24.3	saw cut & remove existing pavement	2 days	Thu 6/12/18	Fri 7/12/18								
877	17.3.24.6	backfill formation	2 days	Wed 12/12/18	Thu 13/12/18								
878	17.3.24.7	lay kerb, sub-base	3 days	Fri 14/12/18	Mon 17/12/18								
879	17.3.24.8	DBM (Roadbase)	2 days	Tue 18/12/18	Wed 19/12/18								
880	17.3.24.9	base course and wearing course	2 days	Thu 20/12/18	Fri 21/12/18								
875	17.3.24.4	excavate gully trench and gully pot(s)	1 day	Sat 8/12/18	Sat 8/12/18								
873	17.3.24.2	tree felling	2 days	Thu 6/12/18	Fri 7/12/18								
876	17.3.24.5	lay& connect gully pipes& construct gully pot(s)	2 days	Mon 10/12/18	Tue 11/12/18								

## Development of Columbarium at Sandy Ridge Cemetery

## - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

ID	WBS	Task Name	Duration	Start Date	Completion Date	1st Half					
						May 2018	3rd Quarter July 2018	September 2018	November 2018	1st Quarter January 2019	March 2019
881	17.3.25	Phase Ia (stage 103)-south lane (chainage 685-740)	22 days	Sat 22/12/18	Sat 19/1/19						
882	17.3.25.1	TTA & UU detection	2 days	Sat 22/12/18	Mon 24/12/18						
884	17.3.25.3	saw cut & remove existing pavement	2 days	Fri 28/12/18	Sat 29/12/18						
887	17.3.25.6	backfill trench to formation	2 days	Thu 10/1/19	Fri 11/1/19						
888	17.3.25.7	lay kerb, sub-base	3 days	Sat 12/1/19	Tue 15/1/19						
889	17.3.25.8	DBM (Roadbase)	2 days	Wed 16/1/19	Thu 17/1/19						
890	17.3.25.9	base course and wearing course	2 days	Fri 18/1/19	Sat 19/1/19						
883	17.3.25.2	tree transplant	1 day	Thu 27/12/18	Thu 27/12/18						
885	17.3.25.4	excavate pipe trench and manhole(s)	2 days	Mon 31/12/18	Wed 2/1/19						
886	17.3.25.5	lay pipes & construct manhole(s)	6 days	Thu 3/1/19	Wed 9/1/19						
891	17.3.26	Phase Ia (stage 104)-north lane (chainage 685-740)	17 days	Mon 21/1/19	Tue 12/2/19						
892	17.3.26.1	TTA & UU detection	2 days	Mon 21/1/19	Tue 22/1/19						
893	17.3.26.2	saw cut & remove existing pavement	2 days	Wed 23/1/19	Thu 24/1/19						
896	17.3.26.5	backfill formation	2 days	Wed 30/1/19	Thu 31/1/19						
897	17.3.26.6	lay kerb, sub-base	3 days	Fri 1/2/19	Mon 4/2/19						
898	17.3.26.7	DBM (Roadbase)	2 days	Fri 8/2/19	Sat 9/2/19						
899	17.3.26.8	base course and wearing course	2 days	Mon 11/2/19	Tue 12/2/19						
894	17.3.26.3	excavate gully trench and gully pot(s)	1 day	Fri 25/1/19	Fri 25/1/19						
895	17.3.26.4	lay & connect gully pipes & construct gully pot(s)	3 days	Sat 26/1/19	Tue 29/1/19						
900	17.3.27	Phase Ia (stage 105)-south lane (chainage 740-790)	21 days	Wed 13/2/19	Fri 8/3/19						
901	17.3.27.1	TTA & UU detection	2 days	Wed 13/2/19	Thu 14/2/19						
903	17.3.27.3	saw cut & remove existing pavement	2 days	Fri 15/2/19	Sat 16/2/19						
906	17.3.27.6	backfill trench to formation	2 days	Wed 27/2/19	Thu 28/2/19						
907	17.3.27.7	lay kerb, sub-base	3 days	Fri 1/3/19	Mon 4/3/19						
908	17.3.27.8	DBM (Roadbase)	2 days	Tue 5/3/19	Wed 6/3/19						
909	17.3.27.9	base course and wearing course	2 days	Thu 7/3/19	Fri 8/3/19						
902	17.3.27.2	tree felling	2 days	Fri 15/2/19	Sat 16/2/19						
904	17.3.27.4	excavate pipe trench and manhole(s)	2 days	Mon 18/2/19	Tue 19/2/19						
905	17.3.27.5	lay pipes & construct manhole(s)	6 days	Wed 20/2/19	Tue 26/2/19						
910	17.3.28	Phase Ia (stage 106) north lane (chainage 740-790)	17 days	Sat 9/3/19	Thu 28/3/19						
911	17.3.28.1	TTA & UU detection	2 days	Sat 9/3/19	Mon 11/3/19						
913	17.3.28.3	saw cut & remove existing pavement	2 days	Tue 12/3/19	Wed 13/3/19						
916	17.3.28.6	backfill formation	2 days	Tue 19/3/19	Wed 20/3/19						

## Development of Columbarium at Sandy Ridge Cemetery

## - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

ID	WBS	Task Name	Duration	Start Date	Completion Date					1st Half	
						May 2018	3rd Quarter July 2018	September 2018	November 2018	1st Quarter January 2019	March 2019
917	17.3.28.7	lay kerb, sub-base	3 days	Thu 21/3/19	Sat 23/3/19						
918	17.3.28.8	DBM (Roadbase)	2 days	Mon 25/3/19	Tue 26/3/19						
919	17.3.28.9	base course and wearing course	2 days	Wed 27/3/19	Thu 28/3/19						
914	17.3.28.4	excavate gully trench and gully pot(s)	1 day	Thu 14/3/19	Thu 14/3/19						
912	17.3.28.2	tree felling	2 days	Tue 12/3/19	Wed 13/3/19						
915	17.3.28.5	lay& connect gully pipes& construct gully pot(s)	3 days	Fri 15/3/19	Mon 18/3/19						
920	17.3.29	Phase Ia stage 107)-south lane (chainage 790-840)	21 days	Fri 29/3/19	Fri 26/4/19						
921	17.3.29.1	TTA & UU detection	2 days	Fri 29/3/19	Sat 30/3/19						
923	17.3.29.3	saw cut & remove existing pavement	2 days	Mon 1/4/19	Tue 2/4/19						
926	17.3.29.6	backfill trench to formation	2 days	Sat 13/4/19	Mon 15/4/19						
927	17.3.29.7	lay kerb, sub-base	3 days	Tue 16/4/19	Thu 18/4/19						
928	17.3.29.8	DBM (Roadbase)	2 days	Tue 23/4/19	Wed 24/4/19						
929	17.3.29.9	base course and wearing course	2 days	Thu 25/4/19	Fri 26/4/19						
922	17.3.29.2	tree felling	2 days	Mon 1/4/19	Tue 2/4/19						
924	17.3.29.4	excavate pipe trench and manhole(s)	2 days	Wed 3/4/19	Thu 4/4/19						
925	17.3.29.5	lay pipes & construct manhole(s)	6 days	Sat 6/4/19	Fri 12/4/19						
1227	17.4	Noise Barrier works above the concrete substructure of the noise barrier (section 2 Part C1)	674 days	Mon 29/10/18	Wed 3/2/21						
1228	17.4.1	seek specialist subcontractor to design and build	210 days	Mon 29/10/18	Sun 26/5/19						
1272	17.5	<b>access date for section 2 (Part C2)</b>	0 days	Sun 24/2/19	Sun 24/2/19						
1273	17.6	<b>additional site possession for areas outside site boundary {for 3NW-C/C470 (existing D-DH7), C224 (existing D-DH11) &amp; C225 new drillholes DHA1,A2 &amp; A3 }</b>	0 days	Sun 24/2/19	Sun 24/2/19						
1274	17.7	<b>Slope Upgrading works (section 2 Part C2)</b>	578 days	Mon 25/2/19	Wed 3/2/21						
1275	17.7.1	general site clearance	45 days	Mon 25/2/19	Thu 18/4/19						
1276	17.7.2	Initial topographic survey	30 days	Thu 11/4/19	Tue 21/5/19						
1337	20	<b>section 3 of the works - Completion of all works within Parts D and E of the Site</b>	797 days	Thu 31/5/18	Wed 3/2/21						
1338	20.1	<b>Parts D</b>	979 days	Fri 1/6/18	Wed 3/2/21						
1339	20.1.1	<b>access date for section 3 (Parts D) - not more than 180 days after the starting date</b>	0 days	Mon 26/11/18	Mon 26/11/18						
1340	20.1.2	seek specialist for design, supply and installation of the covered walkway	238 days	Fri 1/6/18	Thu 24/1/19						
1341	20.1.3	acceptance of specialist	0 days	Thu 14/2/19	Thu 14/2/19						
1342	20.1.4	design for approval for lighting system for the covered walkway	150 days	Fri 15/2/19	Sun 14/7/19						
1346	20.1.8	design for glazing system of the proposed covered walkway at Fanling Station Road	150 days	Fri 15/2/19	Sun 14/7/19						

## Development of Columbarium at Sandy Ridge Cemetery

## - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

ID	WBS	Task Name	Duration	Start Date	Completion Date	May 2018	3rd Quarter July 2018	September 2018	November 2018	1st Half 1st Quarter January 2019	March 2019
1349	20.1.11	design for fall arrest system of the proposed covered walkway at Fanling Station Road	150 days	Fri 15/2/19	Sun 14/7/19						
1358	20.1.20	application of XP (for Parts D)	0 days	Thu 29/11/18	Thu 29/11/18						
1368	20.2	<b>Parts E</b>	530 days	Thu 31/5/18	Thu 12/3/20						
1369	20.2.1	<b>access date for section 3 (Parts E)</b>	0 days	Thu 31/5/18	Thu 31/5/18						
1370	20.2.2	application of XP (for Parts E)	0 days	Thu 29/11/18	Thu 29/11/18						
1372	20.2.4	Temporary Traffic Arrangement (TTA) Scheme for Sheung Shui Landmark North PTI and Fanling Station Road	185 days	Fri 30/11/18	Sun 2/6/19						
1373	20.2.4.1	Preparation of TTA for TMLG and acceptance from TD and RMO	88 days	Fri 30/11/18	Mon 25/2/19						
1374	20.2.4.2	Comment & acceptance of TTA scheme by TD & RMO	49 days	Tue 26/2/19	Mon 15/4/19						
1375	20.2.4.3	Obtain roadwork advice from RMO	48 days	Tue 16/4/19	Sun 2/6/19						
1399	29	<b>section 6 of the works (section Subject to Excision) - Completion of all works within Parts A3 and A4 of the Site except Establishment works. Extent of works under section 6 of the works is defined in Drawing No.: 231448/C2/G/1031</b>	859 days	Fri 28/9/18	Wed 3/2/21						
1400	29.1	<b>Parts A3</b>	859 days	Fri 28/9/18	Wed 3/2/21						
1401	29.1.1	<b>access date for section 6 (Part A3) - not more than 120 days after the starting date</b>	0 days	Fri 28/9/18	Fri 28/9/18						



## **Appendix D**

### **Monitoring Locations**

## **Air Quality Monitoring Location**

Printed by : 2/26/2016  
Filename : G:\env\project\231448\13\_Drawing Deliverables\Reports\018\_EIM&A Manual\20160226 Revised Final\Figure 5.12 - Locations of Construction Dust Monitoring (Sheet 2 of 4).dgn



Legend

- Project Boundary
- Utilities Construction
- Proposed Air Monitoring Stations

E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15
Rev	Description	By	Date
Consultant			

Contract No. and Title:

Agreement No. CE 1/2013(CE)

Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery - Design and Construction

Drawing title


COPYRIGHT RESERVED

Location ID	Description
ASR-1	Village House along Man Kam To Road



DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
© THE ARUP & PARTNERS HONG KONG LIMITED.

Printed by : 2/26/2016  
Filename : G:\env\project\231448\13\_Drawing Deliverables\Reports\018\_EW&A Manual\20160226 Revised Final\Figure 5.1.3 - Locations of Construction Dust Monitoring (Sheet 3 of 4).dgn

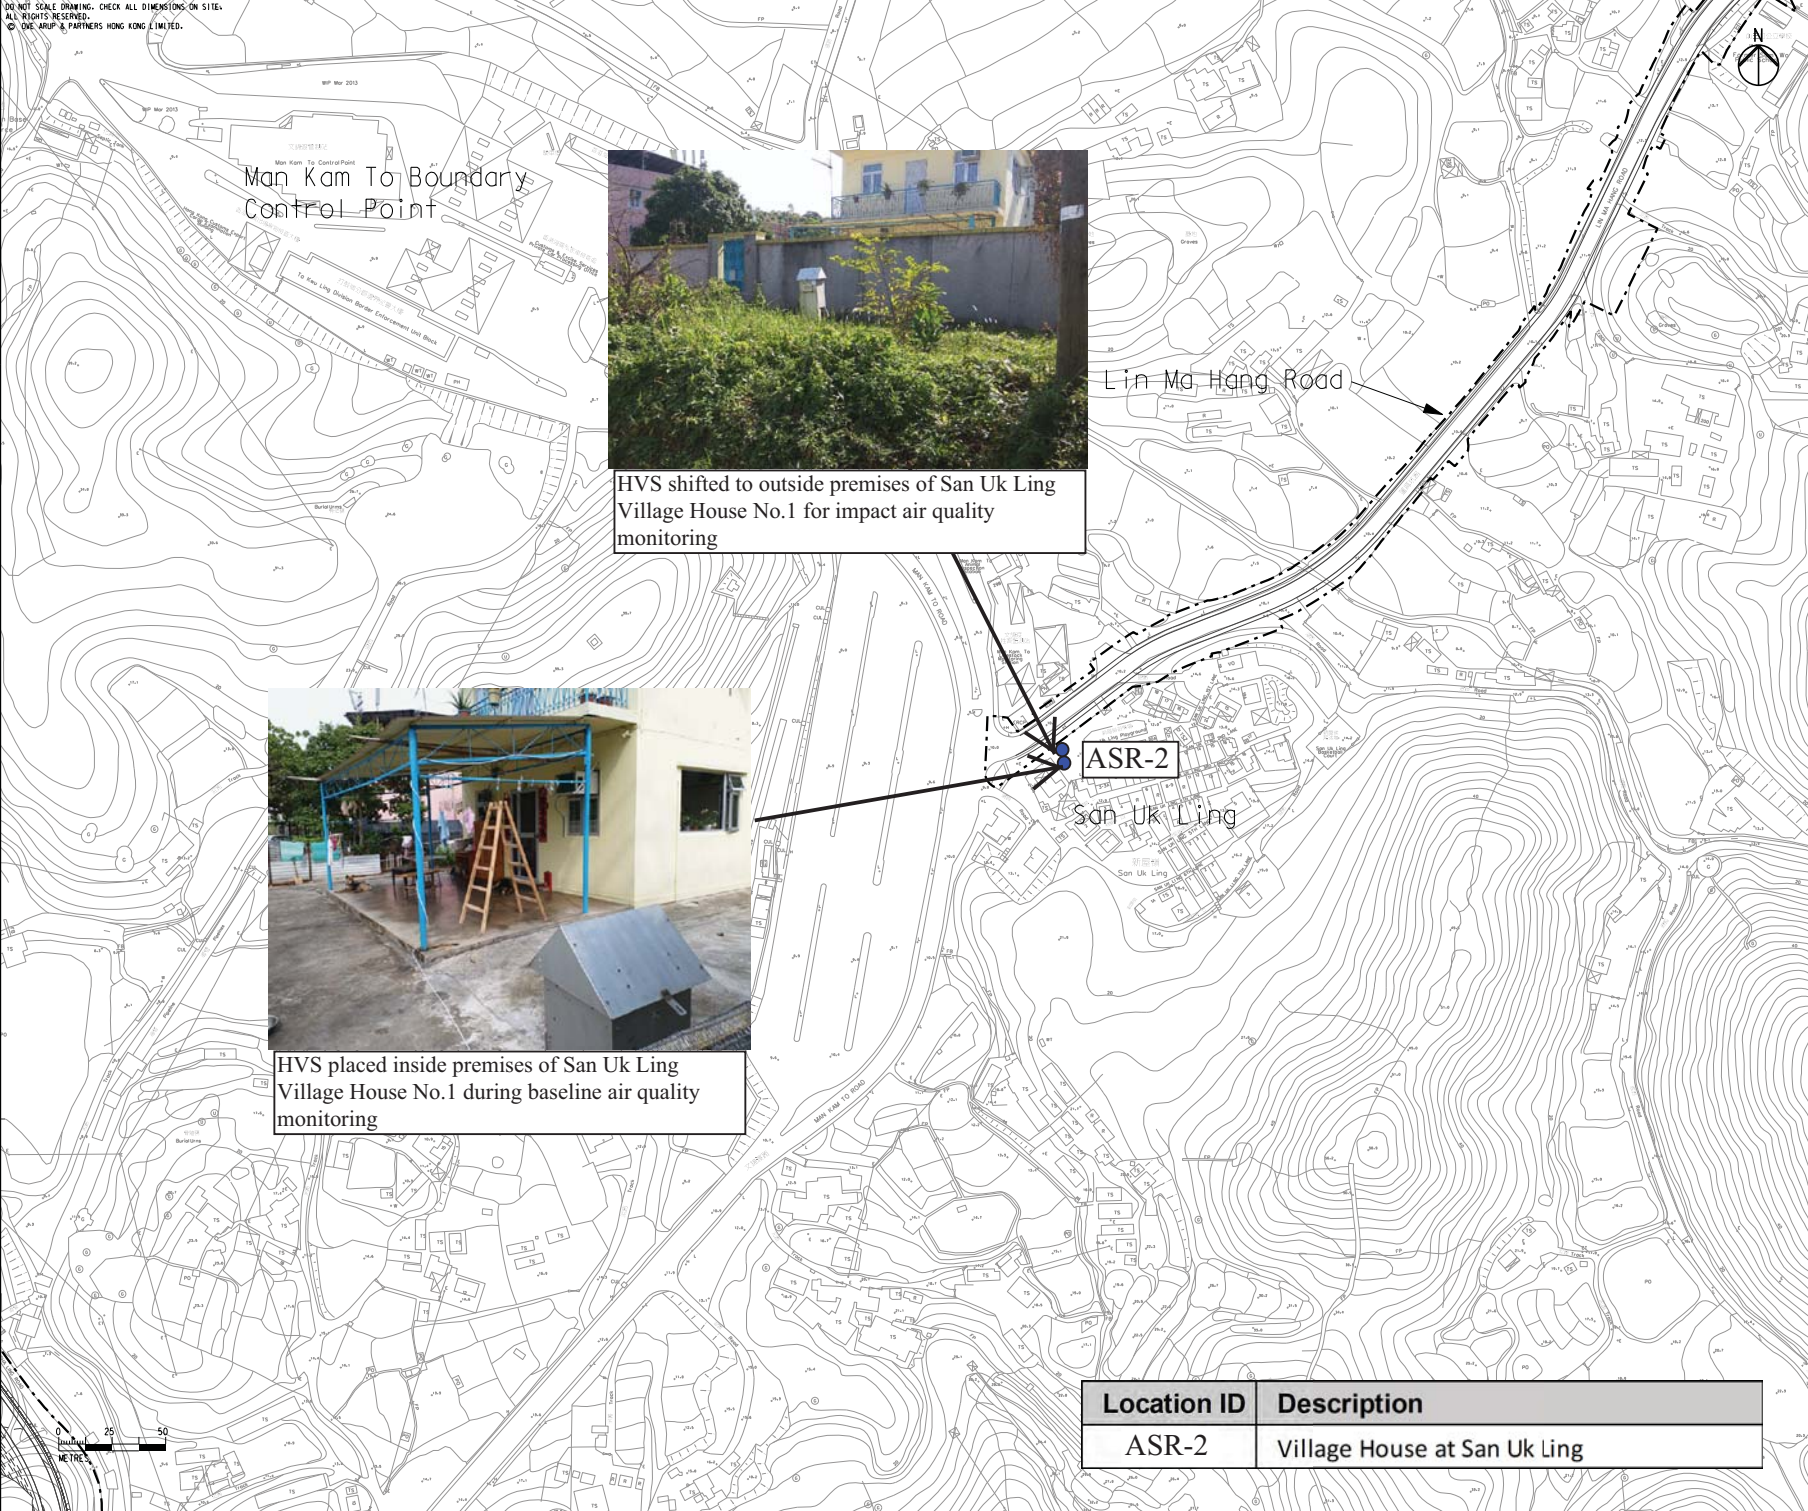

Man Kam To Boundary  
Control Point



HVS shifted to outside premises of San Uk Ling Village House No.1 for impact air quality monitoring



HVS placed inside premises of San Uk Ling Village House No.1 during baseline air quality monitoring

Lin Ma Hang Road

ASR-2

San Uk Ling

Location ID	Description
ASR-2	Village House at San Uk Ling

Legend




- Project Boundary
- Existing Air Monitoring Stations

E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15
Rev	Description	By	Date
Consultant			
Contract No. and Title:			
Agreement No. CE 1/2013(CE)			
Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery - Design and Construction			
Drawing title			
Figure 1			
Air Quality Monitoring Location (ASR-2)			
COPYRIGHT RESERVED			





### Legend

-  Project Boundary
-  Existing Air Monitoring Station
-  Proposed Air Monitoring Station



Location ASR-3 at Muk Wu Nga Yiu House No. 28 during baseline monitoring

Muk Wu Nga Yiu

ASR-3

ASR-3a

100m

Lin Ma Hang Road



Proposed Location ASR-3a at Muk Wu Nga Yiu House No. 2A for impact monitoring

Location ID	Description
ASR-3	Village House at Muk Wu Nga Yiu

E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15
Rev	Description	By	Date

Consultant

Contract No. and Title:

Agreement No. CE 1/2013(CE)

Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery - Design and Construction

Drawing title

Figure 2  
Air Quality Monitoring  
Location (ASR-3)

COPYRIGHT RESERVED

## **Noise Monitoring Location**



Printed by : 2/29/2016  
Filename : G:\env\project\231448\13 Drawing Deliverables\Reports\018 EMB4 Manual\20160226 Revised Final.v1\Figure 6.2.2 - Locations of Proposed Construction Noise Monitoring (Sheet 2 of 4).dgn

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
© THE AMP & PARTNERS HONG KONG LIMITED.



- Legend
- Project Boundary
  - Utilities Construction
  - 300m Assessment Area
  - Proposed Construction Noise Monitoring Locations

E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15
Rev	Description	By	Date

Consultant

Contract No. and Title:  
Agreement No. CE 1/2013(CE)  
Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery - Design and Construction

Drawing title

COPYRIGHT RESERVED

Location ID	Description
CN-1	Village house to the west of Sha Ling Road



Printed by : 2/29/2016  
Filename : G:\env\proj\ec\231448\13\_Drawing\_Deliverables\Reports\018\_EWA Manual\20160226 Revised Final.vla\Figure 6.2.3 - Locations of Proposed Construction Noise Monitoring (Sheet 3 of 4).dgn

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
THIS MAP IS THE PROPERTY OF HONG KONG LIMITED.



- Legend
- Project Boundary
  - Utilities Construction
  - 300m Assessment Area
  - Proposed Construction Noise Monitoring Locations

E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15
Rev	Description	By	Date

Consultant

Contract No. and Title:  
Agreement No. CE 1/2013(CE)  
Site Formation and Associated  
Infrastructural Works for Development  
of Columbarium, Crematorium and  
Related Facilities at Sandy Ridge  
Cemetery - Design and Construction

Drawing title

COPYRIGHT RESERVED

Location ID	Description
CN-2	Village house to the north of Man Kam To Road



Printed by : 2/29/2016  
Filename : G:\env\proj\ec\231448\13\_Drawing\Deliverables\Reports\018\_EW&A Manual\20160226 Revised Final.v1\Figure 6.2.4 - Locations of Proposed Construction Noise Monitoring (Sheet 4 of 4).dgn

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
© DYE NIP & PARTNERS HONG KONG LIMITED.



**Legend**

- Project Boundary
- 300m Assessment Area
- Proposed Construction Noise Monitoring Locations

E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15
Rev	Description	By	Date

Consultant

Contract No. and Title:  
Agreement No. CE 1/2013(CE)  
Site Formation and Associated  
Infrastructural Works for Development  
of Columbarium, Crematorium and  
Related Facilities at Sandy Ridge  
Cemetery - Design and Construction

Drawing title

COPYRIGHT RESERVED

Location ID	Description
CN-3	Village house near San Uk Ling
CN-4	Village house of Muk Wu

## **Water Quality Monitoring Station**



Printed by : 2/29/2016  
Filename : G:\env\project\231448\13 Drawing Deliverables\Reports\018 EM&A Manual\20160226 Revised Final\_v1\Figure 7.11 - Water Quality Monitoring Locations.dgn

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
© DVE ARUP & PARTNERS HONG KONG LIMITED.



- Legend
- Project Boundary
  - Utilities Construction
  - 500m Assessment Area
  - Channelized River
  - Pond
  - Watercourse
  - Conservation Area (CA)
  - Wet Woodland
  - Seasonal Watercourse
  - Water Quality Monitoring Stations in EM&A Manual

E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15
Rev	Description	By	Date

Consultant

Contract No. and Title:

Agreement No. CE 1/2013(CE)

Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery - Design and Construction

Drawing title

COPYRIGHT RESERVED



## **Appendix E**

### **Calibration Certificate of Monitoring Equipment and Laboratory Certificate**



**CALIBRATION CERTIFICATES FOR MONITORING EQUIPMENT USED IN THE REPORTING PERIOD**

Items	Aspect	Description of Equipment	Date of Calibration	Date of Next Calibration
1	Air	TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-1	6 Nov 18	5 Jan 19
1a		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-1	4 Jan 19	3 Mar 19
2		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-2	6 Nov 18	5 Jan 19
2a		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-2	4 Jan 19	3 Mar 19
3		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-3	6 Nov 18	5 Jan 19
3a		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-3	4 Jan 19	3 Mar 19
4		Calibration Kit TISCH Model TE-5025A Orifice ID 1612 and Rootsmeter S/N 438320	13 Feb 18	1 Feb 19
5		Laser Dust Monitor, Model LD-3B (Serial No. 456660) – EQ117	15 Mar 18	14 Mar 19
6		Laser Dust Monitor, Model LD-3B (Serial No. 456659) – EQ116	15 Mar 18	14 Mar 19
7		Laser Dust Monitor, Model LD-3B (Serial No. 45662) – EQ118	15 Mar 18	14 Mar 19
8	Noise	Brüel & Kjær 2238 Sound Level Meter (Serial No. 2285762) – EQ006	11 Jun 18	10 Jun 19
9		Brüel & Kjær 2238 Sound Level Meter (Serial No. 2285690) – EQ008	29 Jun 18	28 Jun 19
10		Brüel & Kjær 4231 Acoustical Calibrator (Serial No. 2326408) – EQ081	11 Jun 18	10 Jun 19
13	Water	YS1 550A (Serial No. 16A104433)	11 Oct 18	11 Jan 19
14		YSI Pro 20 (Serial No. 12C100570)	10 Jan 2019	10 Apr 2019
15		HACH 2100Q Turbidimeter (Serial No. 11030C008499)	30 Nov 18	28 Feb 19
16		AX 8685 pH Meter (Serial No. 1118396)	30 Nov 18	28 Feb 19
17		AZ8371 Salinity Meter (Serial No. 1118396)	11 Dec 18	11 Mar 19
18		Global Water FP211 Flow Meter (Serial No. 1449006330)	6 Apr 18	5 Apr 19

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Sha Ling Village House No.6

Date of Calibration: 6-Nov-18

Location ID : ASR-1

Next Calibration Date: 5-Jan-19

Name and Model: TISCH HVS Model TE-5170

Technician: Ip Ka Hing

### CONDITIONS

Sea Level Pressure (hPa)

1017.5

Corrected Pressure (mm Hg)

763.125

Temperature (°C)

24.7

Temperature (K)

298

### CALIBRATION ORIFICE

Make-> TISCH

Qstd Slope ->

2.02017

Model-> 5025A

Qstd Intercept ->

-0.03691

Serial # -> 1612

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.10	6.10	12.2	1.752	56	56.17	Slope = 35.0169
13	5.05	5.05	10.1	1.595	48	48.15	Intercept = -6.0477
10	3.70	3.70	7.4	1.368	42	42.13	Corr. coeff. = 0.9940
7	2.25	2.25	4.5	1.071	33	33.10	
5	1.55	1.55	3.1	0.892	24	24.07	

#### Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta)) - b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K

Pstd = actual pressure during calibration ( mm Hg

#### For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)] - b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

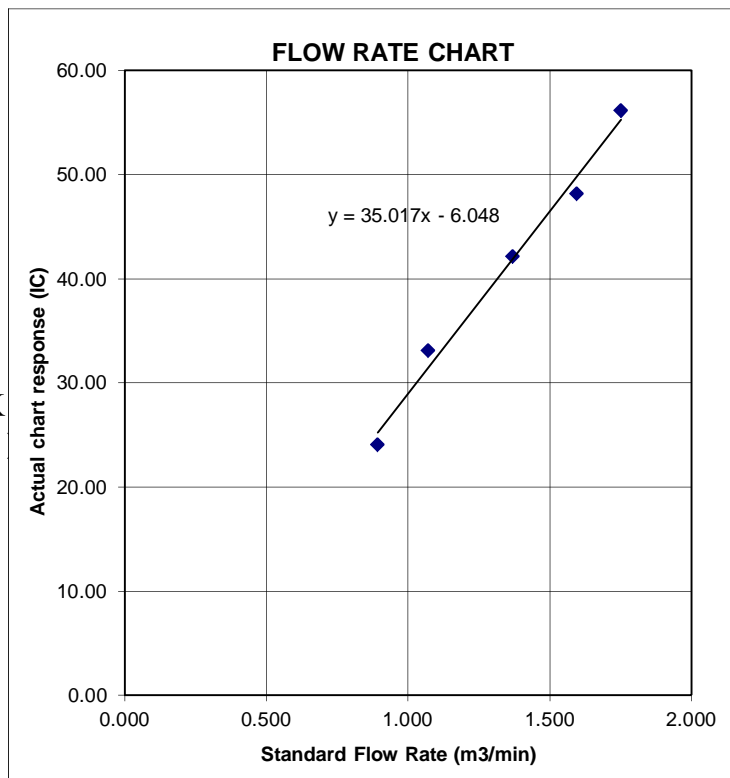

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : San Uk Ling Village House No.1  
 Location ID : ASR-2  
 Name and Model: TISCH HVS Model TE-5170

Date of Calibration: 6-Nov-18  
 Next Calibration Date: 5-Jan-19  
 Technician: Ip Ka Hing

### CONDITIONS

Sea Level Pressure (hPa)	1017.5	Corrected Pressure (mm Hg)	763.125
Temperature (°C)	24.7	Temperature (K)	298

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.02017
Model->	5025A	Qstd Intercept ->	-0.03691
Serial # ->	1612		

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.25	6.25	12.5	1.773	54	54.17	Slope = 33.2573 Intercept = -3.8723 Corr. coeff. = 0.9979
13	4.75	4.75	9.5	1.548	48	48.15	
10	3.65	3.65	7.3	1.359	42	42.13	
7	2.25	2.25	4.5	1.071	32	32.10	
5	1.45	1.45	2.9	0.863	24	24.07	

#### Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K

Pstd = actual pressure during calibration ( mm Hg

#### For subsequent calculation of sampler flow:

$$1/m((I) [\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope


b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

**FLOW RATE CHART**

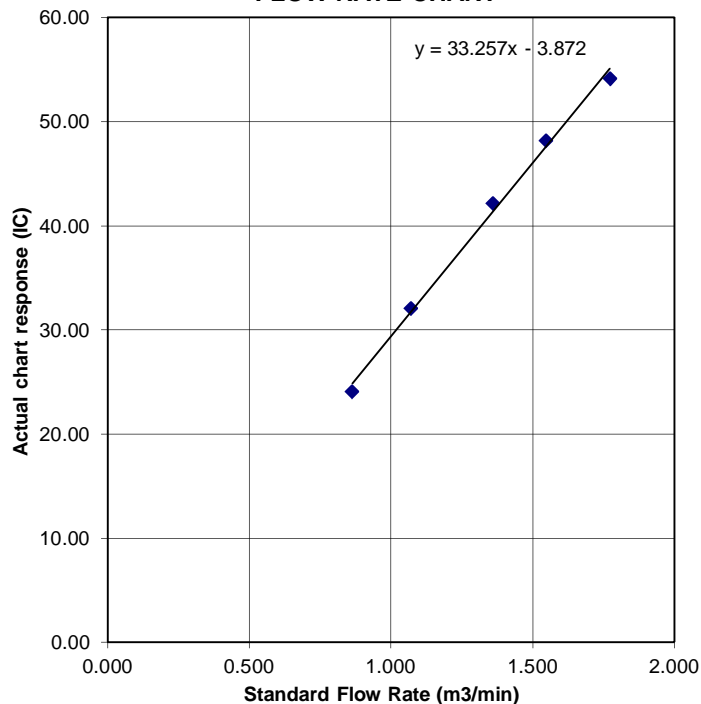

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Muk Wu Nga Yiu House No.2A  
 Location ID : ASR-3a  
 Name and Model: TISCH HVS Model TE-5170

Date of Calibration: 6-Nov-18  
 Next Calibration Date: 5-Jan-19  
 Technician: Ip Ka Hing

### CONDITIONS

Sea Level Pressure (hPa)  
 Temperature (°C)

1017.5  
 24.7

Corrected Pressure (mm Hg)  
 Temperature (K)

763.125  
 298

### CALIBRATION ORIFICE

Make-> TISCH  
 Model-> 5025A  
 Serial # -> 1612

Qstd Slope ->  
 Qstd Intercept ->

2.02017  
 -0.03691

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.15	6.15	12.3	1.759	58	58.18	Slope = 37.3362 Intercept = -8.9635 Corr. coeff. = 0.9942
13	5.00	5.00	10.0	1.588	48	48.15	
10	3.70	3.70	7.4	1.368	42	42.13	
7	2.50	2.50	5.0	1.128	34	34.10	
5	1.55	1.55	3.1	0.892	24	24.07	

#### Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

#### For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope


b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

### FLOW RATE CHART

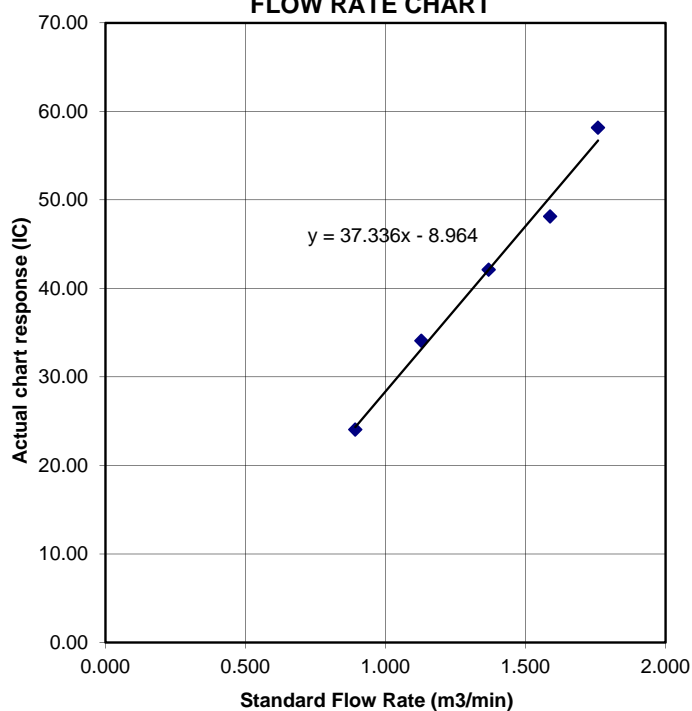

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Sha Ling Village House No.6

Date of Calibration: 4-Jan-19

Location ID : ASR-1

Next Calibration Date: 3-Mar-19

Name and Model: TISCH HVS Model TE-5170

Technician: Leung Ka Wai

### CONDITIONS

Sea Level Pressure (hPa)

1022.8

Corrected Pressure (mm Hg)

767.1

Temperature (°C)

18.8

Temperature (K)

292

### CALIBRATION ORIFICE

Make-> TISCH

Qstd Slope ->

2.02017

Model-> 5025A

Qstd Intercept ->

-0.03691

Serial # -> 1612

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.95	5.95	11.9	1.752	55	56.43	Slope = 33.7481
13	4.80	4.80	9.6	1.575	49	50.27	Intercept = -2.7982
10	3.65	3.65	7.3	1.376	42	43.09	Corr. coeff. = 0.9986
7	2.25	2.25	4.5	1.084	34	34.88	
5	1.30	1.30	2.6	0.829	24	24.62	

#### Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta)) - b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

#### For subsequent calculation of sampler flow:

$$1/m((I) [\text{Sqrt}(298/Tav)(Pav/760)] - b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

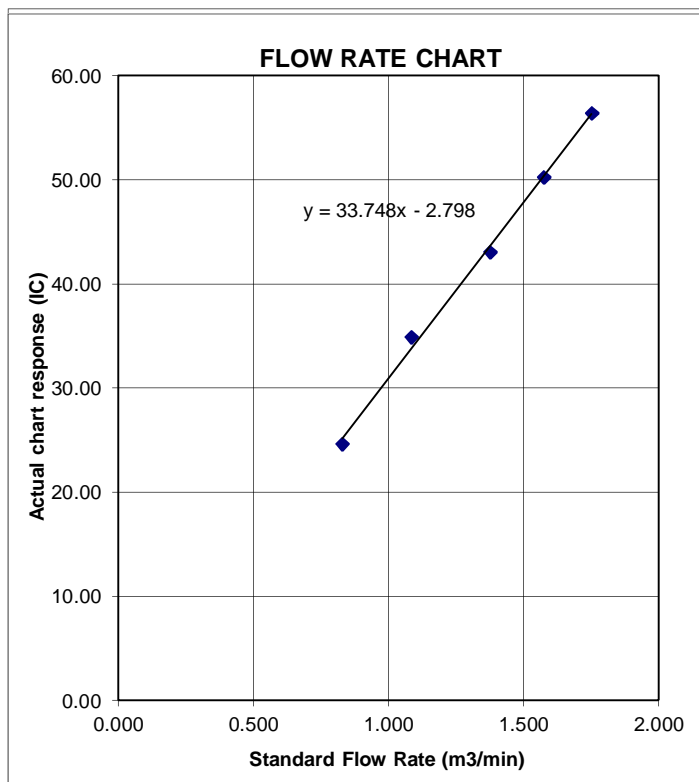



## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : San Uk Ling Village House No.1  
 Location ID : ASR-2  
 Name and Model: TISCH HVS Model TE-5170

Date of Calibration: 4-Jan-19  
 Next Calibration Date: 3-Mar-19  
 Technician: Leung Ka Wai

### CONDITIONS

Sea Level Pressure (hPa)	1022.8	Corrected Pressure (mm Hg)	767.1
Temperature (°C)	18.8	Temperature (K)	292

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.02017
Model->	5025A	Qstd Intercept ->	-0.03691
Serial # ->	1612		

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.90	5.90	11.8	1.745	54	55.40	Slope = 38.3302 Intercept = -11.2245 Corr. coeff. = 0.9999
13	4.75	4.75	9.5	1.567	48	49.25	
10	3.60	3.60	7.2	1.367	40	41.04	
7	2.30	2.30	4.6	1.096	30	30.78	
5	1.30	1.30	2.6	0.829	20	20.52	

#### Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta)) - b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

#### For subsequent calculation of sampler flow:

$$1/m((I) [\text{Sqrt}(298/Tav)(Pav/760)] - b)$$

m = sampler slope


b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

**FLOW RATE CHART**

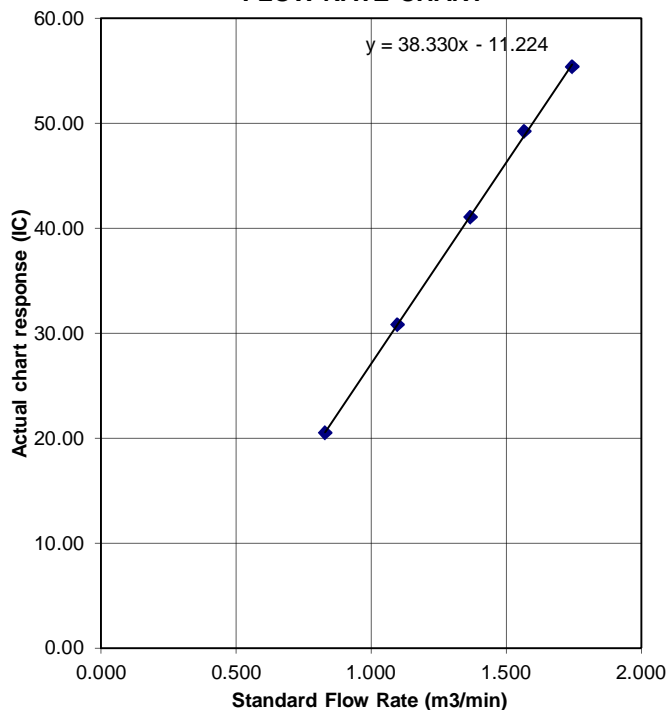

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Muk Wu Nga Yiu House No.2A	Date of Calibration: 4-Jan-19
Location ID : ASR-3a	Next Calibration Date: 3-Mar-19
Name and Model: TISCH HVS Model TE-5170	Technician: Leung Ka Wai

### CONDITIONS

Sea Level Pressure (hPa)	1022.8	Corrected Pressure (mm Hg)	767.1
Temperature (°C)	18.8	Temperature (K)	292

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.02017
Model->	5025A	Qstd Intercept ->	-0.03691
Serial # ->	1612		

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.10	6.10	12.2	1.774	56	57.46	Slope = 28.2448 Intercept = 6.9387 Corr. coeff. = 0.9974
13	4.70	4.70	9.4	1.559	50	51.30	
10	3.65	3.65	7.3	1.376	44	45.14	
7	2.30	2.30	4.6	1.096	36	36.94	
5	1.25	1.25	2.5	0.813	30	30.78	

#### Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

#### For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760))]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

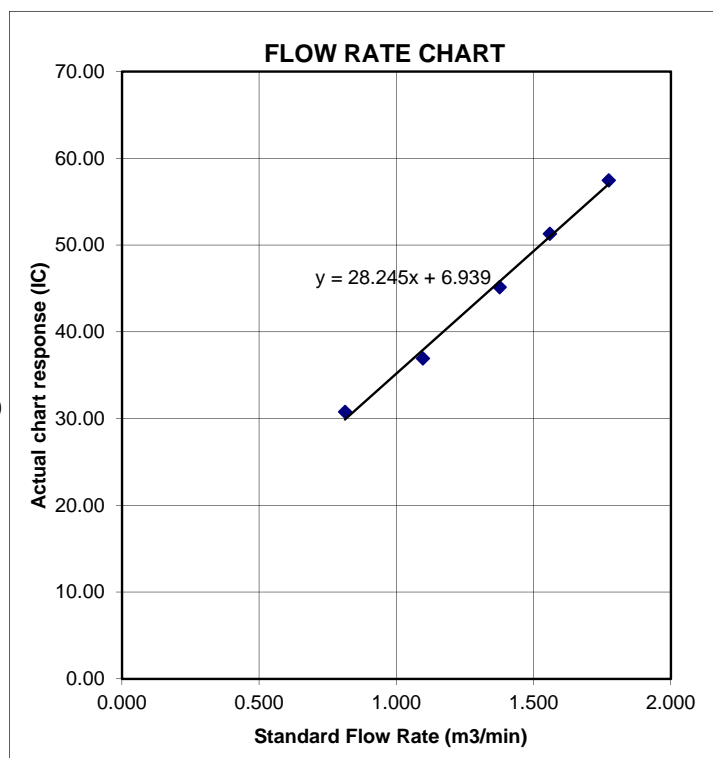

# Certificate of Calibration

## Calibration Certification Information

Cal. Date: February 13, 2018

Rootsmeter S/N: 438320

Ta: 293

°K

Operator: Jim Tisch

Pa: 763.3

mm Hg

Calibration Model #: TE-5025A

Calibrator S/N: 1612

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.3970	3.2	2.00
2	3	4	1	1.0000	6.3	4.00
3	5	6	1	0.8900	7.9	5.00
4	7	8	1	0.8440	8.7	5.50
5	9	10	1	0.7010	12.6	8.00

## Data Tabulation

Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left( \frac{Ta}{Pa} \right)}$ (y-axis)
1.0172	0.7281	1.4293	0.9958	0.7128	0.8762
1.0130	1.0130	2.0213	0.9917	0.9917	1.2392
1.0109	1.1358	2.2599	0.9896	1.1120	1.3854
1.0098	1.1964	2.3702	0.9886	1.1713	1.4530
1.0046	1.4331	2.8586	0.9835	1.4030	1.7524
<b>QSTD</b>	m=	<b>2.02017</b>	<b>QA</b>	m=	<b>1.26500</b>
	b=	<b>-0.03691</b>		b=	<b>-0.02263</b>
	r=	<b>0.99988</b>		r=	<b>0.99988</b>

## Calculations

$$Vstd = \Delta Vol / ((Pa - \Delta P) / Pstd) (Tstd / Ta)$$

$$Va = \Delta Vol / ((Pa - \Delta P) / Pa)$$

$$Qstd = Vstd / \Delta Time$$

$$Qa = Va / \Delta Time$$

For subsequent flow rate calculations:

$$Qstd = 1/m \left( \left( \sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)} \right) - b \right)$$

$$Qa = 1/m \left( \left( \sqrt{\Delta H \left( \frac{Ta}{Pa} \right)} \right) - b \right)$$

## Standard Conditions

Tstd: 298.15 °K

Pstd: 760 mm Hg

## Key

ΔH: calibrator manometer reading (in H2O)

ΔP: rootsmeter manometer reading (mm Hg)

Ta: actual absolute temperature (°K)

Pa: actual barometric pressure (mm Hg)

b: intercept

m: slope

## RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

# ALS Technichem (HK) Pty Ltd

## ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES



### SUB-CONTRACTING REPORT

CONTACT	: MR BEN TAM	WORK ORDER	: HK1825892
CLIENT	: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS	: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG	SUB-BATCH	: 1
		DATE RECEIVED	: 12-APR-2018
		DATE OF ISSUE	: 19-APR-2018
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

#### General Comments

- Sample(s) were received in ambient condition.
- Sample(s) analysed and reported on an as received basis.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

#### Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

##### Signatories

##### Position

Richard Fung  General Manager

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd  
Part of the ALS Laboratory Group

11/F, Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong  
Tel. +852 2610 1044 Fax. +852 2610 2021 [www.alsglobal.com](http://www.alsglobal.com)



WORK ORDER : HK1825892  
SUB-BATCH : 1  
CLIENT : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING  
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1825892-001	S/N: 456660	Equipments	12-Apr-2018	S/N: 456660

## Equipment Verification Report (TSP)

### Equipment Calibrated:

Type: Laser Dust monitor  
Manufacturer: Sibata LD-3B  
Serial No. 456660  
Equipment Ref: EQ117  
Job Order HK1825892

### Standard Equipment:

Standard Equipment: Higher Volume Sampler  
Location & Location ID: AUES office (calibration room)  
Equipment Ref: HVS 018  
Last Calibration Date: 27 February 2018

### Equipment Verification Results:

Calibration Date: 12 & 13 March 2018

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m <sup>3</sup> (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	9:50 ~ 11:57	19.6	1019.0	0.073	4016	31.7
2hr14min	12:05 ~ 14:19	19.6	1019.0	0.075	4544	33.8
2hr17min	9:50 ~ 12:07	20.9	1016.7	0.075	4912	35.7

Sensitivity Adjustment Scale Setting (Before Calibration) 615 (CPM)


Sensitivity Adjustment Scale Setting (After Calibration) 615 (CPM)

### Linear Regression of Y or X

Slope (K-factor): 0.0022

Correlation Coefficient (R) 0.9970

Date of Issue 15 March 2018

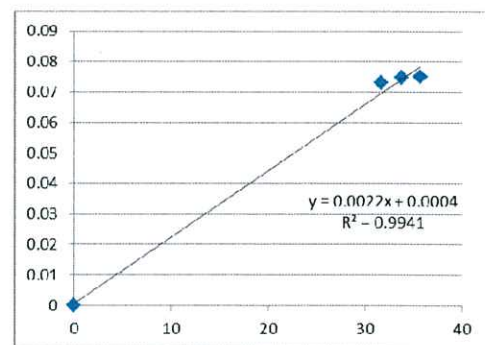

### Remarks:

1. **Strong** Correlation ( $R > 0.8$ )
  2. Factor 0.0022 should be apply for TSP monitoring
- \*If  $R < 0.5$ , repair or re-verification is required for the equipment

Operator : Martin Li Signature :  Date : 15 March 2018

QC Reviewer : Ben Tam Signature :  Date : 15 March 2018

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration: 27-Feb-18
Location ID :	Calibration Room	Next Calibration Date: 27-May-18

### CONDITIONS

Sea Level Pressure (hPa)	1017.3	Corrected Pressure (mm Hg)	762.975
Temperature (°C)	19.1	Temperature (K)	292

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11965
Model->	5025A	Qstd Intercept ->	-0.02696
Calibration Date->	28-Feb-17	Expiry Date->	28-Feb-18

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.2	6.2	12.4	1.694	52	52.63	Slope = 39.8525 Intercept = -14.3322 Corr. coeff. = 0.9974
13	5.1	5.1	10.2	1.538	46	46.55	
10	3.9	3.9	7.8	1.346	40	40.48	
8	2.6	2.6	5.2	1.101	30	30.36	
5	1.7	1.7	3.4	0.893	20	20.24	

#### Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

#### For subsequent calculation of sampler flow:

$$1/m((I) [\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

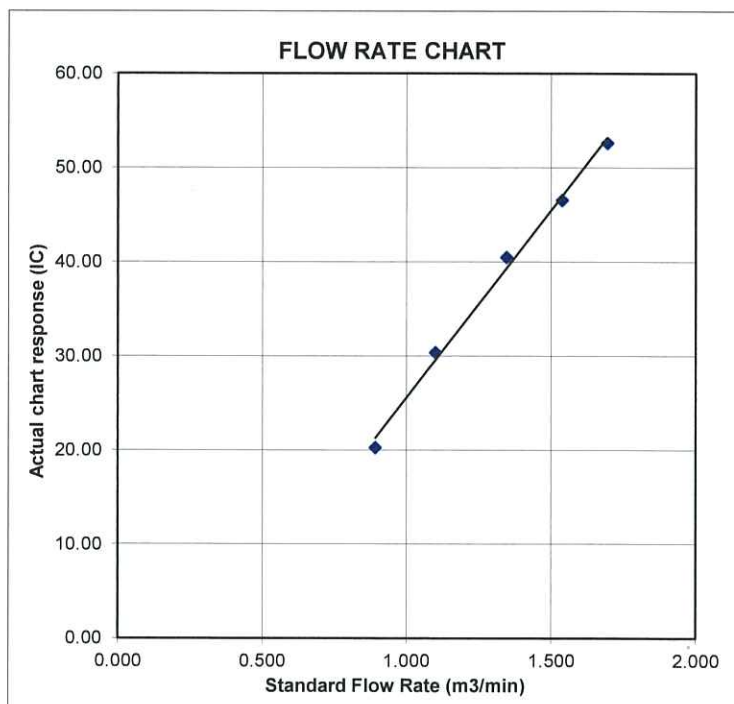



### SUB-CONTRACTING REPORT

CONTACT	: MR BEN TAM	WORK ORDER	: HK1825891
CLIENT	: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS	: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG	SUB-BATCH	: 1
		DATE RECEIVED	: 12-APR-2018
		DATE OF ISSUE	: 19-APR-2018
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

#### General Comments

- Sample(s) were received in ambient condition.
- Sample(s) analysed and reported on an as received basis.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

#### Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

##### Signatories

##### Position

Richard Fung  General Manager

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd  
Part of the ALS Laboratory Group

11/F, Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong  
Tel. +852 2610 1044 Fax. +852 2610 2021 [www.alsglobal.com](http://www.alsglobal.com)



WORK ORDER : HK1825891  
SUB-BATCH : 1  
CLIENT : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING  
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1825891-001	S/N: 456659	Equipments	12-Apr-2018	S/N: 456659

## Equipment Verification Report (TSP)

### Equipment Calibrated:

Type: Laser Dust monitor  
Manufacturer: Sibata LD-3B  
Serial No. 456659  
Equipment Ref: EQ116  
Job Order HK1825891

### Standard Equipment:

Standard Equipment: Higher Volume Sampler  
Location & Location ID: AUES office (calibration room)  
Equipment Ref: HVS 018  
Last Calibration Date: 27 February 2018

### Equipment Verification Results:

Calibration Date: 12 & 13 March 2018

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m <sup>3</sup> (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	9:50 ~ 11:57	19.6	1019.0	0.073	4313	34.1
2hr14min	12:05 ~ 14:19	19.6	1019.0	0.075	4413	32.8
2hr17min	9:50 ~ 12:07	20.9	1016.7	0.075	4906	35.7

Sensitivity Adjustment Scale Setting (Before Calibration) 726 (CPM)

Sensitivity Adjustment Scale Setting (After Calibration) 724 (CPM)

### Linear Regression of Y or X


Slope (K-factor): 0.0022

Correlation Coefficient (R) 0.9977

Date of Issue 15 March 2018

### Remarks:

1. **Strong** Correlation ( $R > 0.8$ )
  2. Factor 0.0022 should be apply for TSP monitoring
- \*If  $R < 0.5$ , repair or re-verification is required for the equipment

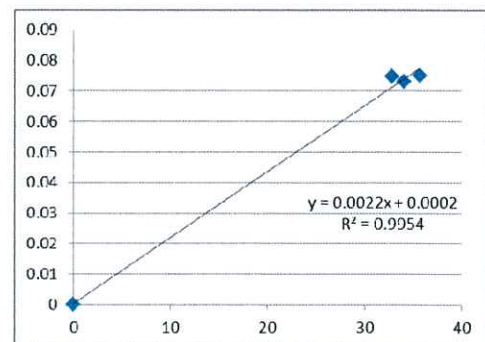

Operator : Martin Li Signature :  Date : 15 March 2018

QC Reviewer : Ben Tam Signature :  Date : 15 March 2018

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration: 27-Feb-18
Location ID :	Calibration Room	Next Calibration Date: 27-May-18

### CONDITIONS

Sea Level Pressure (hPa)	1017.3	Corrected Pressure (mm Hg)	762.975
Temperature (°C)	19.1	Temperature (K)	292

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11965
Model->	5025A	Qstd Intercept ->	-0.02696
Calibration Date->	28-Feb-17	Expiry Date->	28-Feb-18

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.2	6.2	12.4	1.694	52	52.63	Slope = 39.8525 Intercept = -14.3322 Corr. coeff. = 0.9974
13	5.1	5.1	10.2	1.538	46	46.55	
10	3.9	3.9	7.8	1.346	40	40.48	
8	2.6	2.6	5.2	1.101	30	30.36	
5	1.7	1.7	3.4	0.893	20	20.24	

#### Calculations :

$$Q_{std} = 1/m[\text{Sqrt}(H2O(Pa/P_{std})(T_{std}/T_a))-b]$$

$$IC = I[\text{Sqrt}(Pa/P_{std})(T_{std}/T_a)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

#### For subsequent calculation of sampler flow:

$$1/m((I) [\text{Sqrt}(298/T_{av})(P_{av}/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

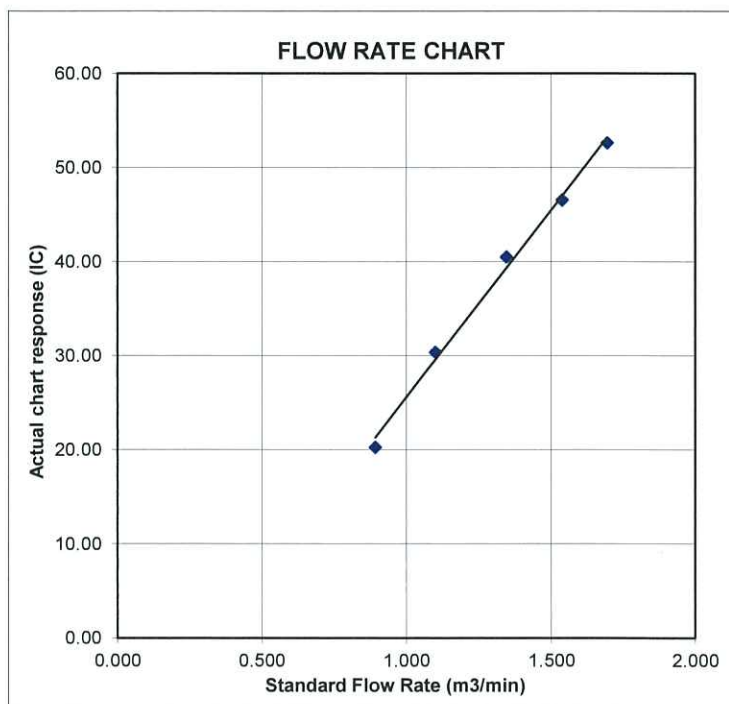

# ALS Technichem (HK) Pty Ltd

## ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES



### SUB-CONTRACTING REPORT

CONTACT	: MR BEN TAM	WORK ORDER	: HK1825893
CLIENT	: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS	: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG	SUB-BATCH	: 1
		DATE RECEIVED	: 12-APR-2018
		DATE OF ISSUE	: 19-APR-2018
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

#### General Comments

- Sample(s) were received in ambient condition.
- Sample(s) analysed and reported on an as received basis.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

#### Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung

General Manager

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd  
Part of the ALS Laboratory Group

11/F, Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong  
Tel. +852 2610 1044 Fax. +852 2610 2021 [www.alsglobal.com](http://www.alsglobal.com)



WORK ORDER : HK1825893  
SUB-BATCH : 1  
CLIENT : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING  
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1825893-001	S/N: 456662	Equipments	17-Apr-2018	S/N: 456662

## Equipment Verification Report (TSP)

### Equipment Calibrated:

Type: Laser Dust monitor  
Manufacturer: Sibata LD-3B  
Serial No. 456662  
Equipment Ref: EQ118  
Job Order HK1825893

### Standard Equipment:

Standard Equipment: Higher Volume Sampler  
Location & Location ID: AUES office (calibration room)  
Equipment Ref: HVS 018  
Last Calibration Date: 27 February 2018

### Equipment Verification Results:

Calibration Date: 12 & 13 March 2018

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m <sup>3</sup> (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	9:50 ~ 11:57	19.6	1019.0	0.073	4108	32.4
2hr14min	12:05 ~ 14:19	19.6	1019.0	0.075	4532	33.7
2hr17min	9:50 ~ 12:07	20.9	1016.7	0.075	5016	36.5

Sensitivity Adjustment Scale Setting (Before Calibration) 591 (CPM)


Sensitivity Adjustment Scale Setting (After Calibration) 591 (CPM)

### Linear Regression of Y or X

Slope (K-factor): 0.0022

Correlation Coefficient (R) 0.9967

Date of Issue 15 March 2018

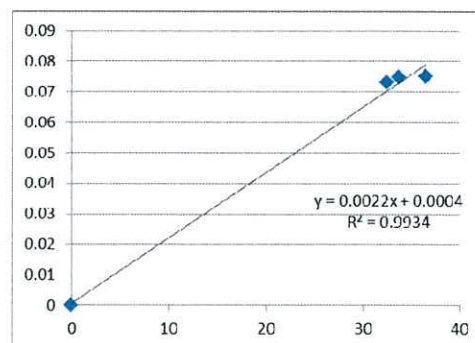

### Remarks:

1. **Strong** Correlation ( $R > 0.8$ )
  2. Factor 0.0022 should be apply for TSP monitoring
- \*If  $R < 0.5$ , repair or re-verification is required for the equipment

Operator : Martin Li Signature :  Date : 15 March 2018

QC Reviewer : Ben Tam Signature :  Date : 15 March 2018

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration: 27-Feb-18
Location ID :	Calibration Room	Next Calibration Date: 27-May-18

### CONDITIONS

Sea Level Pressure (hPa)	1017.3	Corrected Pressure (mm Hg)	762.975
Temperature (°C)	19.1	Temperature (K)	292

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11965
Model->	5025A	Qstd Intercept ->	-0.02696
Calibration Date->	28-Feb-17	Expiry Date->	28-Feb-18

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.2	6.2	12.4	1.694	52	52.63	Slope = 39.8525 Intercept = -14.3322 Corr. coeff. = 0.9974
13	5.1	5.1	10.2	1.538	46	46.55	
10	3.9	3.9	7.8	1.346	40	40.48	
8	2.6	2.6	5.2	1.101	30	30.36	
5	1.7	1.7	3.4	0.893	20	20.24	

#### Calculations :

$$Q_{std} = 1/m[\sqrt{H_2O(P_a/P_{std})(T_{std}/T_a)}] - b]$$

$$IC = I[\sqrt{P_a/P_{std}}(T_{std}/T_a)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

#### For subsequent calculation of sampler flow:

$$1/m((I) [\sqrt{298/T_{av}}(P_{av}/760)] - b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

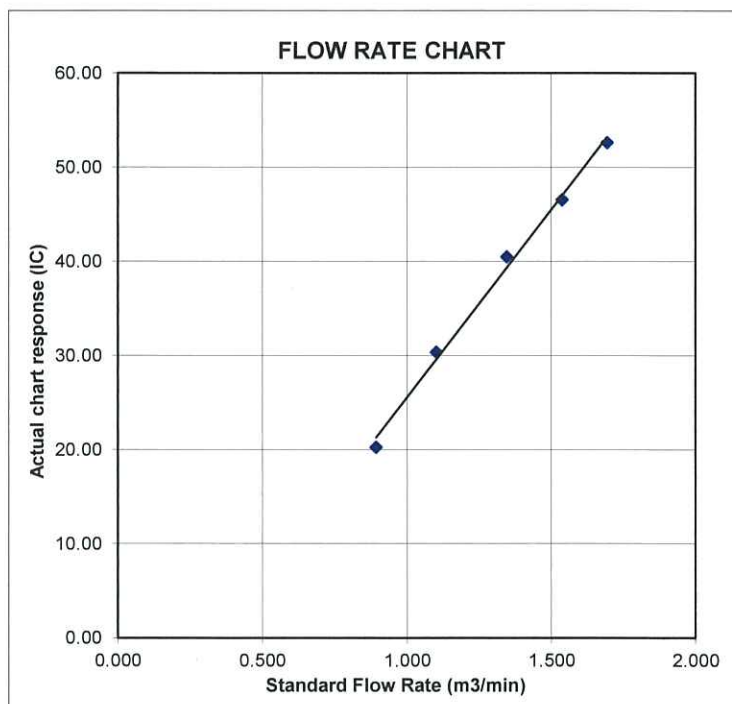

# Certificate of Calibration

## 校正證書

Certificate No. : C183085  
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC18-0867)

Date of Receipt / 收件日期 : 28 May 2018

Description / 儀器名稱 : Integrating Sound Level Meter (EQ006)  
Manufacturer / 製造商 : Brüel & Kjær  
Model No. / 型號 : 2238  
Serial No. / 編號 : 2285762  
Supplied By / 委託者 : Action-United Environmental Services and Consulting  
Unit A, 20/F., Gold King Industrial Building,  
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

### TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$   
Line Voltage / 電壓 : ---

Relative Humidity / 相對濕度 :  $(50 \pm 25)\%$

### TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 10 June 2018

### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
The results do not exceed manufacturer's specification.  
The results are detailed in the subsequent page(s).


The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By  
測試

  
K C Lee  
Engineer

Certified By  
核證

  
H C Chan  
Engineer

Date of Issue  
簽發日期

11 June 2018

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



# Certificate of Calibration

## 校正證書

Certificate No. : C183085  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration using laboratory acoustic calibrator was performed before the test from 6.1.1.2 to 6.4.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C180024
CL281	Multifunction Acoustic Calibrator	PA160023

- Test procedure : MA101N.

- Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

- 6.1.1.1 Before Self-calibration

UUT Setting				Applied Value		UUT Reading
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)
52 - 132	L <sub>AFP</sub>	A	F	94.00	1	94.1

- 6.1.1.2 After Self-calibration

UUT Setting				Applied Value		UUT Reading	IEC 60651 Type 1 Spec.
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)	(dB)
52 - 132	L <sub>AFP</sub>	A	F	94.00	1	94.0	± 0.7

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)
52 - 132	L <sub>AFP</sub>	A	F	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		114.0

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

# Certificate of Calibration

## 校正證書

Certificate No. : C183085  
證書編號

### 6.2 Time Weighting

#### 6.2.1 Continuous Signal

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
52 - 132	L <sub>AFP</sub>	A	F	94.00	1	94.0	Ref.
	L <sub>ASP</sub>		S			94.0	± 0.1
	L <sub>AIP</sub>		I			94.1	± 0.1

#### 6.2.2 Tone Burst Signal (2 kHz)

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Burst Duration		
32 - 112	L <sub>AFP</sub>	A	F	106.0	Continuous	106.0	Ref.
	L <sub>AFMax</sub>				200 ms	104.9	-1.0 ± 1.0
	L <sub>ASP</sub>	S	Continuous		106.0	Ref.	
	L <sub>ASMax</sub>		500 ms		102.0	-4.1 ± 1.0	

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
52 - 132	L <sub>AFP</sub>	A	F	94.00	31.5 Hz	55.0	-39.4 ± 1.5
					63 Hz	67.9	-26.2 ± 1.5
					125 Hz	77.8	-16.1 ± 1.0
					250 Hz	85.3	-8.6 ± 1.0
					500 Hz	90.7	-3.2 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	95.2	+1.2 ± 1.0
					4 kHz	95.0	+1.0 ± 1.0
					8 kHz	92.9	-1.1 (+1.5 ; -3.0)
					12.5 kHz	89.8	-4.3 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

# Certificate of Calibration

## 校正證書

Certificate No. : C183085

證書編號

### 6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
52 - 132	L <sub>CFP</sub>	C	F	94.00	31.5 Hz	91.4	-3.0 ± 1.5
					63 Hz	93.3	-0.8 ± 1.5
					125 Hz	93.8	-0.2 ± 1.0
					250 Hz	94.0	0.0 ± 1.0
					500 Hz	94.0	0.0 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	93.8	-0.2 ± 1.0
					4 kHz	93.2	-0.8 ± 1.0
					8 kHz	90.9	-3.0 (+1.5 ; -3.0)
					12.5 kHz	87.8	-6.2 (+3.0 ; -6.0)

### 6.4 Time Averaging

UUT Setting				Applied Value					UUT Reading (dB)	IEC 60804 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Integrating Time	Frequency (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)		
32 - 112	L <sub>Aeq</sub>	A	10 sec.	4	1	1/10	110.0	100	100.0	± 0.5
								90	89.5	± 0.5
			60 sec.					80	79.2	± 1.0
			5 min.					70	69.3	± 1.0

Remarks : - UUT Microphone Model No. : 4188 & S/N : 2812706

- Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value :

94 dB	31.5 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	12.5 kHz	: ± 0.70 dB
104 dB	1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	1 kHz	: ± 0.10 dB (Ref. 94 dB)
Burst equivalent level		: ± 0.2 dB (Ref. 110 dB continuous sound level)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



# Certificate of Calibration

## 校正證書

Certificate No. : C183441

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC18-0867)

Date of Receipt / 收件日期 : 13 June 2018

Description / 儀器名稱 : Integrating Sound Level Meter (EQ008)  
Manufacturer / 製造商 : Brüel & Kjær  
Model No. / 型號 : 2238  
Serial No. / 編號 : 2285690  
Supplied By / 委託者 : Action-United Environmental Services and Consulting  
Unit A, 20/F., Gold King Industrial Building,  
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

### TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$

Relative Humidity / 相對濕度 :  $(50 \pm 25)\%$

Line Voltage / 電壓 : ---

### TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 23 June 2018

### TEST RESULTS / 測試結果


The results apply to the particular unit-under-test only.  
The results do not exceed manufacturer's specification.  
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA


Tested By

測試

  
K C Lee  
Engineer

Certified By

核證

  
H C Chan  
Engineer

Date of Issue

簽發日期

29 June 2018

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。



# Certificate of Calibration

## 校正證書

Certificate No. : C183441

證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration using laboratory acoustic calibrator was performed before the test from 6.1.1.2 to 6.4.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C180024
CL281	Multifunction Acoustic Calibrator	PA160023

- Test procedure : MA101N.

- Results :

### 6.1 Sound Pressure Level

#### 6.1.1 Reference Sound Pressure Level

##### 6.1.1.1 Before Self-calibration

UUT Setting				Applied Value		UUT Reading
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)
50 - 130	$L_{AFP}$	A	F	94.00	1	94.2

##### 6.1.1.2 After Self-calibration

UUT Setting				Applied Value		UUT Reading	IEC 60651 Type 1 Spec.
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)	(dB)
50 - 130	$L_{AFP}$	A	F	94.00	1	94.1	$\pm 0.7$

##### 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)
50 - 130	$L_{AFP}$	A	F	94.00	1	94.1 (Ref.)
				104.00		104.1
				114.00		114.0

IEC 60651 Type 1 Spec. :  $\pm 0.4$  dB per 10 dB step and  $\pm 0.7$  dB for overall different.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Page 2 of 4

# Certificate of Calibration

## 校正證書

Certificate No. : C183441

證書編號

### 6.2 Time Weighting

#### 6.2.1 Continuous Signal

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 130	L <sub>AFP</sub>	A	F	94.00	1	94.1	Ref.
	L <sub>ASP</sub>		S			94.2	± 0.1
	L <sub>AIP</sub>		I			94.1	± 0.1

#### 6.2.2 Tone Burst Signal (2 kHz)

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Burst Duration		
30 - 110	L <sub>AFP</sub>	A	F	106.0	Continuous	106.0	Ref.
	L <sub>AFMax</sub>				200 ms	105.0	-1.0 ± 1.0
	L <sub>ASP</sub>	S	Continuous		106.0	Ref.	
	L <sub>ASMax</sub>		500 ms		102.0	-4.1 ± 1.0	

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L <sub>AFP</sub>	A	F	94.00	31.5 Hz	54.8	-39.4 ± 1.5
					63 Hz	68.0	-26.2 ± 1.5
					125 Hz	77.9	-16.1 ± 1.0
					250 Hz	85.4	-8.6 ± 1.0
					500 Hz	90.8	-3.2 ± 1.0
					1 kHz	94.1	Ref.
					2 kHz	95.3	+1.2 ± 1.0
					4 kHz	95.1	+1.0 ± 1.0
					8 kHz	93.0	-1.1 (+1.5 ; -3.0)
					12.5 kHz	89.9	-4.3 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Page 3 of 4



# Certificate of Calibration

## 校正證書

Certificate No. : C183441

證書編號

### 6.3.2 C-Weighting

UUT Setting				Applied Value		UUT	IEC 60651
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Type 1 Spec. (dB)
50 - 130	L <sub>CFF</sub>	C	F	94.00	31.5 Hz	91.2	-3.0 ± 1.5
					63 Hz	93.3	-0.8 ± 1.5
					125 Hz	93.9	-0.2 ± 1.0
					250 Hz	94.1	0.0 ± 1.0
					500 Hz	94.1	0.0 ± 1.0
					1 kHz	94.1	Ref.
					2 kHz	93.9	-0.2 ± 1.0
					4 kHz	93.3	-0.8 ± 1.0
					8 kHz	91.1	-3.0 (+1.5 ; -3.0)
					12.5 kHz	88.0	-6.2 (+3.0 ; -6.0)

### 6.4 Time Averaging

UUT Setting				Applied Value					UUT	IEC 60804
Range (dB)	Parameter	Frequency Weighting	Integrating Time	Frequency (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)	Reading (dB)	Type 1 Spec. (dB)
30 - 110	L <sub>Aeq</sub>	A	10 sec.	4	1	1/10	110.0	100	99.9	± 0.5
			60 sec.			1/10 <sup>2</sup>		90	89.7	± 0.5
						1/10 <sup>3</sup>		80	79.7	± 1.0
						5 min.		1/10 <sup>4</sup>	70	69.7

Remarks : - UUT Microphone Model No. : 4188 & S/N : 2812705

- Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value :

94 dB : 31.5 Hz - 125 Hz	: ± 0.35 dB
250 Hz - 500 Hz	: ± 0.30 dB
1 kHz	: ± 0.20 dB
2 kHz - 4 kHz	: ± 0.35 dB
8 kHz	: ± 0.45 dB
12.5 kHz	: ± 0.70 dB
104 dB : 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB : 1 kHz	: ± 0.10 dB (Ref. 94 dB)
Burst equivalent level	: ± 0.2 dB (Ref. 110 dB continuous sound level)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Page 4 of 4

# Certificate of Calibration

## 校正證書

Certificate No. : C183082  
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC18-0867)

Date of Receipt / 收件日期 : 28 May 2018

Description / 儀器名稱 : Acoustical Calibrator (EQ081)  
Manufacturer / 製造商 : Brüel & Kjær  
Model No. / 型號 : 4231  
Serial No. / 編號 : 2326408  
Supplied By / 委託者 : Action-United Environmental Services and Consulting  
Unit A, 20/F., Gold King Industrial Building,  
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

### TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$   
Line Voltage / 電壓 : ---

Relative Humidity / 相對濕度 :  $(50 \pm 25)\%$

### TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 9 June 2018

### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
The results do not exceed manufacturer's specification.  
The results are detailed in the subsequent page(s).


The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By  
測試

  
K C Lee  
Engineer

Certified By  
核證

  
H C Chan  
Engineer

Date of Issue  
簽發日期

11 June 2018

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



# Certificate of Calibration

## 校正證書

Certificate No. : C183082  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C173864
CL281	Multifunction Acoustic Calibrator	PA160023
TST150A	Measuring Amplifier	C181288

- Test procedure : MA100N.

- Results :

### 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.0		

### 5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



## REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:	MR BEN TAM	WORK ORDER:	HK1853068
CLIENT:	ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS:	RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, Kwai Chung, N.T., HONG KONG.	SUB-BATCH:	0
		LABORATORY:	HONG KONG
		DATE RECEIVED:	05-Oct-2018
		DATE OF ISSUE:	11-Oct-2018

### COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

**The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.**

**The "Next Calibration Date" is recommended according to best practice principle as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.**

Scope of Test:	Dissolved Oxygen and Temperature
Equipment Type:	Dissolved Oxygen Meter
Brand Name:	YSI
Model No.:	550A
Serial No.:	16A104433
Equipment No.:	--
Date of Calibration:	11 October, 2018

### NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr Chan Siu Ming, Vico  
Manager - Inorganic

*This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.*

# REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



WORK ORDER: HK1853068  
SUB-BATCH: 0  
DATE OF ISSUE: 11-Oct-2018  
CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: Dissolved Oxygen Meter  
Brand Name: YSI  
Model No.: 550A  
Serial No.: 16A104433  
Equipment No.: --  
Date of Calibration: 11 October, 2018

Date of Next Calibration: 11 January, 2019

## PARAMETERS:

Dissolved Oxygen Method Ref: APHA (21st edition), 4500-O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
2.87	3.01	+0.14
5.23	5.16	-0.07
7.85	7.96	+0.11
Tolerance Limit (mg/L)		±0.20

## Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
9.0	10.8	+1.8
20.0	19.9	-0.1
38.5	37.4	-1.1
Tolerance Limit (°C)		±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr Chan Siu Ming, Vico  
Manager - Inorganic



## REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:	MR BEN TAM	WORK ORDER:	HK1901083
CLIENT:	ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS:	RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, Kwai Chung, N.T., HONG KONG.	SUB-BATCH:	0
		LABORATORY:	HONG KONG
		DATE RECEIVED:	07-Jan-2019
		DATE OF ISSUE:	10-Jan-2019

### COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

**The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.**

**The "Next Calibration Date" is recommended according to best practice principle as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.**

Scope of Test:	Dissolved Oxygen and Temperature
Equipment Type:	Dissolved Oxygen Meter
Brand Name:	YSI
Model No.:	Pro 20
Serial No.:	12C100570
Equipment No.:	--
Date of Calibration:	10 January, 2019

### NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr Chan Siu Ming, Vico  
Manager - Inorganic

*This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.*



# REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



WORK ORDER: HK1901083  
SUB-BATCH: 0  
DATE OF ISSUE: 10-Jan-2019  
CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: Dissolved Oxygen Meter  
Brand Name: YSI  
Model No.: Pro 20  
Serial No.: 12C100570  
Equipment No.: --  
Date of Calibration: 10 January, 2019

Date of Next Calibration: 10 April, 2019

## PARAMETERS:

Dissolved Oxygen Method Ref: APHA (21st edition), 4500-O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
2.67	2.59	-0.08
6.20	6.30	+0.10
8.88	8.97	+0.09
	Tolerance Limit (mg/L)	±0.20

## Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
11.0	10.4	-0.6
21.0	19.8	-1.2
40.5	38.9	-1.6
	Tolerance Limit (°C)	±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr Chan Siu Ming, Vico  
Manager - Inorganic



**ALS Technichem (HK) Pty Ltd**

11/F, Chung Shun Knitting Centre

1-3 Wing Yip Street, Kwai Chung

N.T., Hong Kong

T: +852 2610 1044 | F: +852 2610 2021

## REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR BEN TAM  
CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING  
ADDRESS: RM A 20/F., GOLD KING IND BLDG,  
NO. 35-41 TAI LIN PAI ROAD,  
Kwai Chung,  
N.T., HONG KONG.

WORK ORDER: HK1861699  
SUB-BATCH: 0  
LABORATORY: HONG KONG  
DATE RECEIVED: 26-Nov-2018  
DATE OF ISSUE: 04-Dec-2018

### COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.

Scope of Test: Turbidity  
Equipment Type: Turbidimeter  
Brand Name: Hach  
Model No.: 2100Q  
Serial No.: 11030C008499  
Equipment No.: --  
Date of Calibration: 30 November, 2018

### NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr Chan Siu Ming, Vico  
Manager - Inorganic

*This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.*

## REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



WORK ORDER: HK1861699  
SUB-BATCH: 0  
DATE OF ISSUE: 04-Dec-2018  
CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: Turbidimeter  
Brand Name: Hach  
Model No.: 2100Q  
Serial No.: 11030C008499  
Equipment No.: --  
Date of Calibration: 30 November, 2018

Date of Next Calibration: 28 February, 2019

### PARAMETERS:

Turbidity Method Ref: APHA (21<sup>st</sup> edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.18	--
4	4.28	+7.0
40	40.70	+1.8
80	81.4	+1.8
	Tolerance Limit (%)	±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr Chan Siu Ming, Vico  
Manager - Inorganic



## REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:	MR BEN TAM	WORK ORDER:	HK1861703
CLIENT:	ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS:	RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, Kwai Chung, N.T., HONG KONG.	SUB-BATCH:	0
		LABORATORY:	HONG KONG
		DATE RECEIVED:	26-Nov-2018
		DATE OF ISSUE:	03-Dec-2018

### COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.

Scope of Test:	pH Value and Temperature
Equipment Type:	pH meter
Brand Name:	AZ
Model No.:	8685
Serial No.:	1118396
Equipment No.:	--
Date of Calibration:	30 November, 2018

### NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Ms. Lin Wai Yu  
Assistant Manager - Inorganic

*This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.*



# REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



WORK ORDER: HK1861703  
SUB-BATCH: 0  
DATE OF ISSUE: 03-Dec-2018  
CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: pH meter  
Brand Name: AZ  
Model No.: 8685  
Serial No.: 1118396  
Equipment No.: --  
Date of Calibration: 30 November, 2018      Date of Next Calibration: 28 February, 2019

## PARAMETERS:

pH Value

Method Ref: APHA (21st edition), 4500H:B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)
4.0	4.1	+0.10
7.0	6.8	-0.20
10.0	10.0	+0.00
	Tolerance Limit (pH unit)	±0.20

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
11.0	10.5	-0.5
20.0	20.0	+0.0
39.0	39.0	+0.0
	Tolerance Limit (°C)	±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu  
Assistant Manager - Inorganic



## REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:	MR BEN TAM	WORK ORDER:	HK1862946
CLIENT:	ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS:	RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, Kwai Chung, N.T., HONG KONG.	SUB-BATCH:	0
		LABORATORY:	HONG KONG
		DATE RECEIVED:	04-Dec-2018
		DATE OF ISSUE:	11-Dec-2018

### COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

**The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.**

**The "Next Calibration Date" is recommended according to best practice principle as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.**

Scope of Test:	Salinity
Equipment Type:	Salinity Meter
Brand Name:	AZ
Model No.:	AZ8371
Serial No.:	1118267
Equipment No.:	--
Date of Calibration:	11 December, 2018

### NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr Chan Siu Ming, Vico  
Manager - Inorganic

*This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.*

# REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



WORK ORDER: HK1862946  
SUB-BATCH: 0  
DATE OF ISSUE: 11-Dec-2018  
CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: Salinity Meter  
Brand Name: AZ  
Model No.: AZ8371  
Serial No.: 1118267  
Equipment No.: --  
Date of Calibration: 11 December, 2018

Date of Next Calibration: 11 March, 2019

## PARAMETERS:

Salinity Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.00	--
10	9.56	-4.4
20	19.9	-0.5
30	28.7	-4.3
	Tolerance Limit (%)	±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr Chan Siu Ming, Vico  
Manager - Inorganic



## **REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION**

**CONTACT:** MR IVAN LEUNG  
**CLIENT:** ALS TECHNICHEM (HK) PTY LTD  
**ADDRESS:** 11/F, CHUNG SHUN KNITTING CENTRE,  
1-3 WING YIP STREET,  
KWAI CHUNG,  
N.T., HONG KONG

**WORK ORDER:** HK1827786  
**SUB-BATCH:** 0  
**LABORATORY:** HONG KONG  
**DATE RECEIVED:** 06-Apr-2018  
**DATE OF ISSUE:** 02-May-2018

### COMMENTS

The calibration of flow rate performed by AUES staff on 6 April 2018.

Scope of Test: Flow rate  
Equipment Type: Flow Meter  
Brand Name: Global Water  
Model No.: FP211  
Serial No.: 1449006330  
Equipment No.: --  
Calibration Factor: 314  
Date of Calibration: 06 April, 2018

### NOTES

This is the Final Report and supersedes any preliminary report with this batch number.  
Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

  
Mr. Fung Lim Chee, Richard  
General Manager  
Greater China & Hong Kong



# REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION



Work Order: HK1827786  
Sub-batch: 0  
Date of Issue: 02-May-2018  
Client: ALS TECHNICHEM (HK) PTY LTD

Equipment Type: Flow Meter  
Brand Name: Global Water  
Model No.: FP211  
Serial No.: 1449006330  
Equipment No.: --  
Calibration Factor: 314

Date of Calibration: 06 April, 2018

**Parameters:** The calibration of flow meter is verified with another standard flow meter (SonTek IQ Standard Serial Number : IQ1217004) on site by AUES Staff.

## Flow rate

Test	Standard Equipment Reading (m/s)	Verification Equipment Reading (m/s)
1 <sup>st</sup>	0.12	0.1
2 <sup>nd</sup>	0.21	0.2
3 <sup>rd</sup>	0.18	0.2
4 <sup>th</sup>	0.49	0.5
5 <sup>th</sup>	1.03	1.0
6 <sup>th</sup>	0.97	1.0

  
Mr. Fung Lim Chee, Richard  
General Manager -  
Greater China & Hong Kong



Hong Kong Accreditation Service  
香港認可處

**Certificate of Accreditation**  
**認可證書**

*This is to certify that*  
特此證明

**ALS TECHNICHEM (HK) PTY LIMITED**

**11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong**  
香港新界葵涌永業街1-3號忠信針織中心11樓

*has been accepted by the HKAS Executive, on the recommendation of the Accreditation Advisory Board, as a*  
為香港認可處執行機關根據認可諮詢委員會建議而接受的

**HOKLAS Accredited Laboratory**  
「香港實驗所認可計劃」認可實驗所

*This laboratory meets the requirements of ISO / IEC 17025 : 2005 – General requirements for the competence*  
此實驗所符合ISO / IEC 17025 : 2005 –《測試及校正實驗所能力的通用規定》所訂的要求，  
*of testing and calibration laboratories and it has been accredited for performing specific tests or calibrations as*  
獲認可進行載於香港實驗所認可計劃《認可實驗所名冊》內下述測試類別中的指定  
*listed in the HOKLAS Directory of Accredited Laboratories within the test category of*  
測試或校正工作

**Environmental Testing**  
環境測試

*This laboratory is accredited in accordance with the recognised International Standard ISO / IEC 17025 : 2005.*  
本實驗所乃根據公認的國際標準 ISO / IEC 17025 : 2005 獲得認可。

*This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory*  
這項認可資格演示在指定範疇所需的技術能力及實驗所質量管理體系的運作  
*quality management system (see joint IAF-ILAC-ISO Communiqué).*  
(見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

*The common seal of the Hong Kong Accreditation Service is affixed hereto by the authority of the HKAS Executive*  
香港認可處根據認可處執行機關的權限在此蓋上通用印章

CHAN Sing Sing, Terence, Executive Administrator  
執行幹事 陳成城  
Issue Date : 5 May 2009  
簽發日期：二零零九年五月五日

Registration Number : **HOKLAS** 066  
註冊號碼：

Date of First Registration : 15 September 1995  
首次註冊日期：一九九五年九月十五日



## **Appendix F**

### **Event and Action Plan of Air Quality, Noise and Water Quality**

### Event and Action Plan for air quality

Event	Action			
	ET	IEC	ER	Contractor
Action level exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method.	1. Notify Contractor	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Action level exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented.	1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.
Limit level exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
Limit level exceedance for two or more consecutive samples	1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Note: ET – Environmental Team IEC – Independent Environmental Checker ER – Engineer's Representative



### Event and Action Plan for Construction Noise

Event	Action			
	ET	IEC	ER	Contractor
Action Level Exceedance	<ol style="list-style-type: none"> <li>1. Notify IEC, ER and Contractor;</li> <li>2. Carry out investigation;</li> <li>3. Report the results of investigation to the IEC, ER and Contractor;</li> <li>4. Discuss with the Contractor and formulate remedial measures;</li> <li>5. Increase monitoring frequency to check mitigation effectiveness</li> </ol>	<ol style="list-style-type: none"> <li>1. Review the analyzed results submitted by the ET;</li> <li>2. Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analyzed noise problem;</li> <li>4. Ensure remedial measures are properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposals to IEC and ER;</li> <li>2. Implement noise mitigation proposals</li> </ol>
Limit Level Exceedance	<ol style="list-style-type: none"> <li>1. Identify source;</li> <li>2. Inform IEC, ER, EPD and Contractor;</li> <li>3. Repeat measurements to confirm findings;</li> <li>4. Increase monitoring frequency;</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>6. Inform IEC, ER and EPD the causes and actions taken for the exceedances;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analyzed noise problem;</li> <li>4. Ensure remedial measures properly implemented;</li> <li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Resubmit proposals if problem still not under control;</li> <li>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol>

*Note:*

*ET – Environmental Team*

*IEC – Independent Environmental Checker*

*ER – Engineer's Representative*

### Event and Action Plan for Water Quality

Event	Action			
	ET	IEC	ER	Contractor
Action level exceedance for one sampling day	1. Inform IEC, Contractor and ER; 2. Check monitoring data, all plant, equipment and Contractor's working methods; and 3. Discuss remedial measures with IEC and Contractor and ER.	1. Discuss with ET, ER and Contractor on the implemented mitigation measures; 2. Review proposals on remedial measures submitted by Contractor and advise the ER accordingly; and 3. Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.	1. Discuss with IEC, ET and Contractor on the implemented mitigation measures; 2. Make agreement on the remedial measures to be implemented; 3. Supervise the implementation of agreed remedial measures.	1. Identify source(s) of impact; 2. Inform the ER and confirm notification of the non-compliance in writing; 3. Rectify unacceptable practice; 4. Check all plant and equipment; 5. Consider changes of working methods; 6. Discuss with ER, ET and IEC and purpose remedial measures to IEC and ER; and 7. Implement the agreed mitigation measures.
Action level exceedance for more than one consecutive sampling days	1. Repeat in-situ measurement on next day of exceedance to confirm findings; 2. Inform IEC, contractor and ER; 3. Check monitoring data, all plant, equipment and Contractor's working methods; 4. Discuss remedial measures with IEC, contractor and ER 5. Ensure remedial measures are implemented	1. Discuss with ET, Contractor and ER on the implemented mitigation measures; 2. Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and 3. Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.	1. Discuss with ET, IEC and Contractor on the proposed mitigation measures; 2. Make agreement on the remedial measures to be implemented ; and 3. Discuss with ET, IEC and Contractor on the effectiveness of the implemented remedial measures.	1. Identify source(s) of impact; 2. Inform the ER and confirm notification of the non-compliance in writing; 3. Rectify unacceptable practice; 4. Check all plant and equipment and consider changes of working methods; 5. Discuss with ET, IEC and ER and submit proposal of remedial measures to ER and IEC within 3 working days of notification; and 6. Implement the agreed mitigation measures.
Limit level exceedance for one sampling day	1. Repeat measurement on next day of exceedance to confirm findings; 2. Inform IEC, contractor and ER; 3. Rectify unacceptable practice; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 6. Consider changes of working methods; 7. Discuss mitigation measures with IEC, ER and Contractor; and 8. Ensure the agreed remedial measures are implemented	1. Discuss with ET, Contractor and ER on the implemented mitigation measures; 2. Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and 3. Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.	1. Discuss with ET, IEC and Contractor on the implemented remedial measures; 2. Request Contractor to critically review the working methods; 3. Make agreement on the remedial measures to be implemented; and 4. Discuss with ET, IEC and Contractor on the effectiveness of the implemented remedial measures.	1. Identify source(s) of impact; 2. Inform the ER and confirm notification of the non-compliance in writing; 3. Rectify unacceptable practice; 4. Check all plant and equipment and consider changes of working methods; 5. Discuss with ET, IEC and ER and submit proposal of additional mitigation measures to ER and IEC within 3 working days of notification; and 6. Implement the agreed remedial measures.
Limit level exceedance for more than one consecutive sampling days	1. Inform IEC, contractor and ER; 2. Check monitoring data, all plant, equipment and Contractor's working methods; 3. Discuss mitigation measures with IEC, ER and Contractor; 4. Ensure mitigation measures are implemented; and 5. Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days	1. Discuss with ET, Contractor and ER on the implemented mitigation measures; 2. Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and 3. Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.	1. Discuss with ET, IEC and Contractor on the implemented remedial measures; 2. Request Contractor to critically review the working methods; 3. Make agreement on the remedial measures to be implemented; 4. Discuss with ET and IEC on the effectiveness of the implemented mitigation measures; and 5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level.	1. Identify source(s) of impact; 2. Inform the ER and confirm notification of the non-compliance in writing; 3. Rectify unacceptable practice; 4. Check all plant and equipment and consider changes of working methods; 5. Discuss with ET, IEC and ER and submit proposal of additional mitigation measures to ER and IEC within 3 working days of notification; and 6. Implement the agreed remedial measures; and 7. As directed by the ER, to slow down or stop all or part of the construction activities until no exceedance of Limit level.

Note: ET – Environmental Team IEC – Independent Environmental Checker ER – Engineer's Representative  
Each step of actions required shall be implemented within 1 working day unless otherwise specified or agreed with EPD.

## **Appendix G**

### **Monitoring Schedules of the Reporting Month and Coming Month**

**Impact Monitoring Schedule of Air Quality, Noise and Water Quality - January 2019**

Date		Noise Monitoring	Air Quality Monitoring		Water Quality
			1-Hour TSP	24-Hour TSP	
Tue	1-Jan-19				
Wed	2-Jan-19				
Thu	3-Jan-19			✓	✓
Fri	4-Jan-19	✓	✓		
Sat	5-Jan-19				✓
Sun	6-Jan-19				
Mon	7-Jan-19				
Tue	8-Jan-19				✓
Wed	9-Jan-19			✓	
Thu	10-Jan-19	✓	✓		✓
Fri	11-Jan-19				
Sat	12-Jan-19				✓
Sun	13-Jan-19				
Mon	14-Jan-19				
Tue	15-Jan-19			✓	✓
Wed	16-Jan-19	✓	✓		
Thu	17-Jan-19				✓
Fri	18-Jan-19				
Sat	19-Jan-19				✓
Sun	20-Jan-19				
Mon	21-Jan-19			✓	
Tue	22-Jan-19	✓	✓		✓
Wed	23-Jan-19				
Thu	24-Jan-19				✓
Fri	25-Jan-19				
Sat	26-Jan-19			✓	✓
Sun	27-Jan-19				
Mon	28-Jan-19	✓	✓		
Tue	29-Jan-19				✓
Wed	30-Jan-19				
Thu	31-Jan-19				✓

✓	Monitoring Day
	Sunday or Public Holiday

Environmental Aspect	Location ID	Description of Location	Related Contract
Construction Noise	CN-1	Village house to the west of Sha Ling Road	CV/2016/10
	CN-2	San Uk Ling Village House No.1	
	CN-3	San Uk Ling Village House No. 18	CV/2017/02
	CN-4	Muk Wu Village House No. 267	
Air Quality	ASR-1	Sha Ling Village House No. 6	CV/2016/10
	ASR-2	San Uk Ling Village House No.1	CV/2017/02
	ASR-3a	Muk Wu Nga Yiu House No.28	
Water Quality	M3	Wetland in the Conservation Area near Yuen Leng Chai	CV/2016/10
	M1	Midstream of Nam Hang Stream	CV/2017/02
	M2	Downstream of Nam Hang Stream	
	M4	Watercourse across Lin Ma Hang Road	



**Impact Monitoring Schedule of Air Quality, Noise and Water Quality – February 2019**

Date		Noise Monitoring	Air Quality Monitoring		Water Quality
			1-Hour TSP	24-Hour TSP	
Fri	1-Feb-19			✓	
Sat	2-Feb-19		✓		✓
Sun	3-Feb-19				
Mon	4-Feb-19			✓	✓
Tue	5-Feb-19				
Wed	6-Feb-19				
Thu	7-Feb-19				
Fri	8-Feb-19	✓	✓		
Sat	9-Feb-19			✓	✓
Sun	10-Feb-19				
Mon	11-Feb-19				
Tue	12-Feb-19				✓
Wed	13-Feb-19				
Thu	14-Feb-19	✓	✓		✓
Fri	15-Feb-19			✓	
Sat	16-Feb-19				✓
Sun	17-Feb-19				
Mon	18-Feb-19				✓
Tue	19-Feb-19				
Wed	20-Feb-19	✓	✓		✓
Thu	21-Feb-19			✓	
Fri	22-Feb-19				
Sat	23-Feb-19				✓
Sun	24-Feb-19				
Mon	25-Feb-19				
Tue	26-Feb-19	✓	✓		✓
Wed	27-Feb-19			✓	
Thu	28-Feb-19				✓

*Remark: There will be no construction activity during Lunar New Year holiday on 5 to 7 Feb 2019.*

✓	Monitoring Day
	Sunday or Public Holiday

Environmental Aspect	Location ID	Description of Location	Related Contract
Construction Noise	CN-1	Village house to the west of Sha Ling Road	CV/2016/10
	CN-2	San Uk Ling Village House No.1	
	CN-3	San Uk Ling Village House No. 18	CV/2017/02
	CN-4	Muk Wu Village House No. 267	
Air Quality	ASR-1	Sha Ling Village House No. 6	CV/2016/10
	ASR-2	San Uk Ling Village House No.1	CV/2017/02
	ASR-3a	Muk Wu Nga Yiu House No.28	
Water Quality	M3	Wetland in the Conservation Area near Yuen Leng Chai	CV/2016/10
	M1	Midstream of Nam Hang Stream	CV/2017/02
	M2	Downstream of Nam Hang Stream	
	M4	Watercourse across Lin Ma Hang Road	

## **Appendix H**

### **Monitoring Data**

- **24-hour TSP Air Quality**
- **Noise**
- **Water Quality**

## **Air Quality (24-hour TSP)**

### 24-Hour TSP Monitoring Data for ASR-1

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP	AVG AIR PRESS	STANDARD FLOW RATE	AIR VOLUME	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED	24-Hr TSP ( $\mu\text{g}/\text{m}^3$ )
		INITIAL	FINAL	(min)	MIN	MAX	AVG	(°C)	(hPa)	( $\text{m}^3/\text{min}$ )	(std $\text{m}^3$ )	INITIAL	FINAL	(g)	
3-Jan-19	23556	9270.25	9294.67	1465.20	30	30	30.0	16.2	1024.3	1.05	1534	2.6440	2.8215	0.1775	116
9-Jan-19	23570	9294.67	9319.17	1470.00	36	36	36.0	16.8	1020.4	1.17	1718	2.6429	2.8804	0.2375	138
15-Jan-19	23585	9319.17	9343.67	1470.00	37	38	37.5	19	1018.8	1.21	1776	2.6660	2.8022	0.1362	77
21-Jan-19	23534	9343.67	9368.14	1468.20	46	46	46.0	17.8	1021.8	1.47	2156	2.6635	2.9871	0.3236	150
26-Jan-19	23595	9368.14	9392.63	1469.40	46	46	46.0	15.3	1020.8	1.47	2166	2.6461	3.0236	0.3775	174

### 24-Hour TSP Monitoring Data for ASR-2

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP	AVG AIR PRESS	STANDARD FLOW RATE	AIR VOLUME	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED	24-Hr TSP ( $\mu\text{g}/\text{m}^3$ )
		INITIAL	FINAL	(min)	MIN	MAX	AVG	(°C)	(hPa)	( $\text{m}^3/\text{min}$ )	(std $\text{m}^3$ )	INITIAL	FINAL	(g)	
3-Jan-19	23559	17788.87	17812.87	1440.00	32	32	32.0	16.2	1024.3	1.10	1582	2.6444	2.7110	0.0666	42
9-Jan-19	23568	17812.87	17836.88	1440.60	31	32	31.5	16.8	1020.4	1.13	1627	2.6550	2.7836	0.1286	79
15-Jan-19	23586	17836.88	17860.88	1440.00	32	32	32.0	19	1018.8	1.14	1639	2.6620	2.7617	0.0997	61
21-Jan-19	23535	17860.88	17884.88	1440.00	34	34	34.0	17.8	1021.8	1.19	1720	2.6587	2.7818	0.1231	72
26-Jan-19	23655	17884.88	17908.88	1440.00	34	34	34.0	15.3	1020.8	1.20	1725	2.6558	2.8284	0.1726	100

### 24-Hour TSP Monitoring Data for ASR-3a

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP	AVG AIR PRESS	STANDARD FLOW RATE	AIR VOLUME	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED	24-Hr TSP ( $\mu\text{g}/\text{m}^3$ )
		INITIAL	FINAL	(min)	MIN	MAX	AVG	(°C)	(hPa)	( $\text{m}^3/\text{min}$ )	(std $\text{m}^3$ )	INITIAL	FINAL	(g)	
3-Jan-19	23558	11590.25	11614.39	1448.40	36	36	36.0	16.2	1024.3	1.22	1773	2.6464	2.7090	0.0626	35
9-Jan-19	23569	11614.39	11638.71	1459.20	34	35	34.5	16.8	1020.4	1.00	1455	2.6502	2.7424	0.0922	63
15-Jan-19	23587	11638.71	11663.09	1462.80	34	34	34.0	19	1018.8	0.97	1424	2.6643	2.7432	0.0789	55
21-Jan-19	23536	11663.09	11687.38	1457.40	30	30	30.0	17.8	1021.8	0.83	1216	2.6642	2.7755	0.1113	92
26-Jan-19	23658	11687.38	11711.68	1458.00	34	34	34.0	15.3	1020.8	0.98	1433	2.6560	2.8260	0.1700	119



## **Noise**

Noise Measurement Results (dB(A)) of CN-1																					
Date	Start Time	1 <sup>st</sup> Leq <sub>5mi</sub> n	L10	L90	2 <sup>nd</sup> Leq <sub>5mi</sub> n	L10	L90	3 <sup>rd</sup> Leq <sub>5mi</sub> n	L10	L90	4 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	5 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	6 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	Leq <sub>30min</sub>	Façade Collection (*)
4-Jan-19	9:54	70.3	64.4	56.4	60.6	62.4	56.9	59.5	61.7	56.5	63.7	64.7	55.4	60.1	62.7	55.7	61.5	63.6	55.7	65	68
10-Jan-19	9:34	61.6	64.0	54.0	65.0	67.7	61.6	63.9	65.5	62.7	60.7	62.3	57.9	59.6	60.8	57.9	58.2	59.8	57.8	62	65
16-Jan-19	9:14	54.2	55.5	51.5	63.1	65.5	55.5	69.3	71.0	63.0	63.4	66.0	59.0	69.1	72.0	62.0	70.3	72.5	60.5	67	70
22-Jan-19	9:45	67.1	69.5	58.0	66.2	69.0	60.0	65.4	68.0	60.0	68.8	71.0	57.5	69.2	72.5	60.5	69.2	72.5	60.0	68	71
28-Jan-19	13:49	62.3	62.3	58.2	63.4	64.0	57.5	62.5	64.2	58.1	61.9	63.4	57.7	62.5	63.7	57.3	61.7	62.1	57.3	62	65

(\*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

Noise Measurement Results (dB(A)) of CN-2																					
Date	Start Time	1 <sup>st</sup> Leq <sub>5mi</sub> n	L10	L90	2 <sup>nd</sup> Leq <sub>5mi</sub> n	L10	L90	3 <sup>rd</sup> Leq <sub>5mi</sub> n	L10	L90	4 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	5 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	6 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	Leq <sub>30min</sub>	Façade Collection (*)
4-Jan-19	11:30	61.4	62.0	55.5	61.0	61.5	55.5	63.2	64.5	52.5	63.5	64.0	53.5	60.5	61.5	55.0	60.2	61.0	57.5	62	65
10-Jan-19	11:25	62.2	63.0	56.5	60.3	61.0	56.5	61.5	62.5	55.5	61.2	63.0	58.0	58.9	60.0	52.5	57.8	58.5	52.0	61	64
16-Jan-19	11:24	60.3	61.0	55.5	60.3	61.5	55.5	69.2	71.0	55.5	62.3	69.5	56.0	59.2	57.5	55.0	57.9	59.5	54.5	64	67
22-Jan-19	10:27	59.0	61.5	53.0	59.1	61.5	53.5	62.5	66.0	53.5	62.8	67.0	56.0	60.0	61.0	52.5	57.1	59.5	52.0	61	64
28-Jan-19	14:25	64.6	68.4	53.4	64.4	68.6	54.4	64.5	68.9	53.7	63.0	57.5	51.2	64.3	68.2	52.4	63.0	67.2	50.8	64	67

(\*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

Noise Measurement Results (dB(A)) of CN-3																					
Date	Start Time	1 <sup>st</sup> Leq <sub>5mi</sub> n	L10	L90	2 <sup>nd</sup> Leq <sub>5mi</sub> n	L10	L90	3 <sup>rd</sup> Leq <sub>5mi</sub> n	L10	L90	4 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	5 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	6 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	Leq <sub>30min</sub>	Façade Collection (*)
4-Jan-19	10:07	58.7	61.0	50.3	60.5	61.2	50.0	59.3	61.7	51.3	56.5	59.0	52.0	57.9	60.5	51.5	55.2	58.6	51.7	58	61
10-Jan-19	11:10	54.9	58.9	47.9	55.4	59.3	47.4	55.1	58.5	47.7	54.5	58.6	47.3	55.7	59.7	48.2	55.0	59.7	48.4	55	58
16-Jan-19	9:52	56.2	58.0	52.0	56.3	56.0	52.0	52.8	54.0	49.5	56.0	56.5	52.0	54.3	55.5	51.5	55.8	56.5	50.0	55	58
22-Jan-19	11:04	57.3	60.5	52.5	56.7	59.5	52.0	56.0	59.0	51.5	59.3	62.5	51.0	55.0	57.5	50.0	55.6	60.0	56.5	57	60
28-Jan-19	15:04	54.7	58.5	47.7	54.2	57.6	48.2	53.6	57.5	47.7	54.4	58.1	47.9	55.5	59.5	48.2	53.7	58.0	47.2	54	57

(\*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

Noise Measurement Results (dB(A)) of CN-4																				
Date	Start Time	1 <sup>st</sup> Leq <sub>5mi</sub> n	L10	L90	2 <sup>nd</sup> Leq <sub>5mi</sub> n	L10	L90	3 <sup>rd</sup> Leq <sub>5mi</sub> n	L10	L90	4 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	5 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	6 <sup>th</sup> Leq <sub>5mi</sub> n	L10	L90	Leq <sub>30min</sub>
4-Jan-19	9:28	57.2	62.3	44.4	59.0	64.0	44.9	55.3	61.3	43.8	56.5	62.8	44.9	60.2	65.4	43.2	59.0	64.3	44.3	58
10-Jan-19	10:34	57.6	61.9	42.2	56.3	60.3	38.1	70.1	71.4	40.6	58.6	62.4	39.9	59.5	61.5	38.9	58.4	61.9	38.8	64
16-Jan-19	10:31	57.8	59.5	52.5	65.1	69.5	54.0	58.7	59.0	52.5	67.6	59.5	53.0	55.8	56.0	51.5	55.6	56.0	51.5	63
22-Jan-19	13:00	59.7	63.0	52.0	56.9	60.0	51.0	57.2	60.0	51.5	57.3	59.5	53.0	57.4	59.0	53.0	58.7	61.5	53.0	58
28-Jan-19	15:41	62.8	66.4	43.1	60.5	65.8	43.7	59.3	63.9	45.6	58.6	62.5	45.3	58.4	62.9	43.5	59.2	63.3	44.9	60

## **Water Quality**



**Water Quality Impact Monitoring Result for M1**

Date	3-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	14:30	0.13	17.2	17.2	<0.1	<0.1	9.3	9.3	96.3	96.1	3	2.7	7.00	7.0	0.03	0.03	5
			17.2		<0.1		9.25		95.9		2.43		7.00		0.03		4

Date	5-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	9:20	0.15	17.9	17.9	<0.1	<0.1	8.75	8.7	99.3	99.3	1.6	1.6	6.50	6.5	0.02	0.02	3
			17.9		<0.1		8.72		99.2		1.61		6.50		0.02		3

Date	8-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	9:30	0.13	19.5	19.5	<0.1	<0.1	8.77	8.7	95.6	95.2	1.89	1.7	7.50	7.5	0.03	0.03	<2
			19.5		<0.1		8.72		94.7		1.58		7.50		0.03		<2

Date	10-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	20:40	0.15	20.3	20.3	<0.1	<0.1	8.31	8.3	94.7	95.2	1.73	1.7	6.70	6.7	0.03	0.03	7
			20.3		<0.1		8.38		95.6		1.63		6.70		0.03		6

Date	12-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	9:20	0.13	20	20.0	<0.1	<0.1	7.81	7.8	90.7	90.8	1.33	1.4	8.98	9.0	0.06	0.06	<2
			20		<0.1		7.81		90.8		1.47		8.98		0.06		2

Date	15-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	9:40	0.15	19.4	19.4	<0.1	<0.1	6.81	6.6	77.3	75.5	3.91	3.7	6.81	6.8	0.05	0.05	3
			19.4		<0.1		6.43		73.6		3.54		6.81		0.05		3

Date	17-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	11:45	0.13	17.9	17.9	<0.1	<0.1	4.4	4.5	47.9	48.4	2.16	2.3	7.43	7.4	0.05	0.05	<2
			17.9		<0.1		4.5		48.9		2.35		7.43		0.05		<2

Date	19-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	9:40	0.13	18.3	18.3	<0.1	<0.1	8.16	8.2	88.4	88.4	1.82	1.8	8.17	8.2	0.04	0.04	4
			18.3		<0.1		8.17		88.4		1.76		8.17		0.04		4

Date	22-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	10:00	0.13	16.6	16.6	<0.1	<0.1	9.89	10.0	106.4	107.6	2.87	2.7	8.60	8.6	0.03	0.03	4
			16.6		<0.1		10.13		108.7		2.51		8.60		0.03		4

Date	24-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	15:00	0.13	18	18.0	<0.1	<0.1	9.58	9.6	105.1	105.2	2.14	2.0	7.90	7.9	0.03	0.03	8
			18		<0.1		9.59		105.2		1.79		7.90		0.03		7

Date	26-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	9:50	0.13	18.2	18.2	<0.1	<0.1	9.49	9.5	108.0	107.7	1.75	1.7	8.00	8.0	0.03	0.03	4
			18.2		<0.1		9.44		107.4		1.55		8.00		0.03		4

Date	29-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	9:30	0.13	17.5	17.5	<0.1	<0.1	9.04	9.0	102.7	102.7	2.05	2.0	7.40	7.4	0.03	0.03	2
			17.5		<0.1		9.03		102.6		1.86		7.40		0.03		2

Date	31-Jan-19																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)
M1	9:45	0.13	20	20.0	<0.1	<0.1	9.12	9.1	106.4	106.5	1.82	1.7	8.10	8.1	0.03	0.03	
			20		<0.1		9.13		106.6		1.51		8.10		0.03		#DIV/0!

**Water Quality Impact Monitoring Result for M2**

Date	15-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:35	0.15	19.3	19.3	<0.1	<0.1	6.24	6.3	55.3	55.6	5.28	5.5	6.86	6.9	0.07	0.07	5	5.5
			19.3		<0.1		6.3		55.8		5.64		6.86		0.07		6	

Date	22-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:25	0.13	14.6	14.6	<0.1	<0.1	8.92	8.9	87.3	87.4	7.31	7.8	7.90	7.9	0.09	0.09	12	13.0
			14.6		<0.1		8.93		87.4		8.21		7.90		0.09		14	

Date	24-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	9:45	0.12	16.5	16.5	<0.1	<0.1	9.3	9.3	101.6	101.5	2.6	2.6	7.00	7.0	0.10	0.10	9	10.5
			16.5		<0.1		9.28		101.4		2.55		7.00		0.10		12	

**Water Quality Impact Monitoring Result for M3**

Date	3-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	15:00	2.45	17.4	17.4	<0.1	<0.1	8.91	8.9	93.5	94.0	3.2	2.6	7.00	7.0	0.00	0.00	<2	<2
			17.4		<0.1		8.98		94.4		2.06		7.00		0.00		<2	
Date	5-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:00	2.45	18.1	18.1	<0.1	<0.1	8.77	8.8	92.3	92.5	3.06	3.1	6.90	6.9	0.00	0.00	2	2.0
			18.1		<0.1		8.79		92.6		3.2		6.90		0.00		2	
Date	8-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:00	2.45	19.5	19.5	<0.1	<0.1	8.71	8.7	99.0	99.1	2.29	2.3	7.80	7.8	0.00	0.00	2	2.5
			19.5		<0.1		8.72		99.2		2.21		7.80		0.00		3	
Date	10-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:30	2.45	20.3	20.3	<0.1	<0.1	7.62	7.6	84.2	84.2	2.6	2.8	6.90	6.9	0.00	0.00	4	3.0
			20.3		<0.1		7.63		84.2		3.05		6.90		0.00		2	
Date	12-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:15	2.45	20.4	20.4	<0.1	<0.1	6.8	6.7	75.1	74.7	2.38	2.4	8.72	8.7	0.02	0.02	3	3.0
			20.4		<0.1		6.69		74.2		2.39		8.72		0.02		3	
Date	15-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:45	2.48	19.3	19.3	<0.1	<0.1	4.36	4.4	49.5	49.7	2.65	2.6	6.76	6.8	0.01	0.01	<2	<2
			19.3		<0.1		4.42		49.9		2.57		6.76		0.01		<2	
Date	17-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	11:20	2.45	19	19.0	<0.1	<0.1	5.88	5.8	64.7	63.9	3.2	3.2	7.16	7.2	0.01	0.01	3	2.5
			19		<0.1		5.72		63.0		3.13		7.16		0.01		2	
Date	19-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:30	2.45	18.5	18.5	<0.1	<0.1	7.18	7.2	78.0	77.9	1.88	1.9	8.41	8.4	0.01	0.01	2	2.0
			18.5		<0.1		7.16		77.8		1.89		8.41		0.00		2	



Date	22-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:30	2.45	16.6	16.6	<0.1	<0.1	8.82	8.9	89.1	89.9	5.5	5.6	8.40	8.4	0.01	0.01	7	6.5
			16.6		<0.1		9.02		90.6		5.6		8.40		0.01		6	
Date	24-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	9:40	2.45	17.5	17.5	<0.1	<0.1	9.26	9.3	101.7	101.8	5.04	4.6	7.20	7.2	0.00	0.00	9	9.0
			17.5		<0.1		9.27		101.9		4.13		7.20		0.00		9	
Date	26-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:20	2.45	18.5	18.5	<0.1	<0.1	7.74	7.7	82.4	82.5	3.85	4.0	8.20	8.2	0.00	0.00	5	4.5
			18.5		<0.1		7.75		82.5		4.16		8.20		0.00		4	
Date	29-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		7.86		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:40	2.45	19.2	19.2	<0.1	<0.1	7.86	7.9	85.1	85.2	4.4	4.6	7.60	7.6	0.00	0.00	4	4.5
			19.2		<0.1		7.87		85.2		4.76		7.60		0.00		5	
Date	31-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:30	2.45	19.8	19.8	<0.1	<0.1	8.74	8.7	101.6	101.7	3.29	3.1	7.20	7.2	0.00	0.00		#DIV/0!
			19.8		<0.1		8.75		101.8		2.89		7.20		0.00			

**Water Quality Impact Monitoring Result for M4**

Date	3-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	15:15	0.40	19.4	19.4	<0.1	<0.1	9.14	9.1	99.7	99.8	1.3	1.3	6.90	6.9	0.06	0.06	<2	<2
			19.4		<0.1		9.15		99.9		1.3		6.90		0.06		<2	

Date	5-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:20	0.40	19.1	19.1	<0.1	<0.1	9.57	9.5	108.6	108.0	1.0	1.1	6.70	6.7	0.06	0.06	<2	<2
			19.1		<0.1		9.47		107.4		1.1		6.70		0.06		<2	

Date	8-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:15	0.40	20.5	20.5	<0.1	<0.1	8.92	8.9	101.4	101.6	0.7	0.7	6.90	6.9	0.06	0.06	<2	<2
			20.5		<0.1		8.94		101.7		0.8		6.90		0.06		<2	

Date	10-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:50	0.40	19.7	19.7	<0.1	<0.1	7.99	8.0	90.7	90.7	1.7	1.5	6.80	6.8	0.04	0.04	3	3.5
			19.7		<0.1		7.98		90.6		1.4		6.80		0.04		4	

Date	12-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:30	0.40	21.5	21.5	<0.1	<0.1	7.34	7.3	85.1	85.0	1.0	1.0	8.42	8.4	0.03	0.03	<2	2.0
			21.5		<0.1		7.32		84.9		1.0		8.42		0.03		2	

Date	15-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	11:10	0.42	19.5	19.5	<0.1	<0.1	3.81	3.8	43.2	43.1	2.1	2.0	6.59	6.6	0.05	0.05	<2	<2
			19.5		<0.1		3.79		43.0		1.9		6.59		0.05		<2	

Date	17-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M5	11:30	0.40	18.6	18.6	<0.1	<0.1	6.29	6.3	68.6	68.5	1.9	1.8	6.67	6.7	0.07	0.07	<2	<2
			18.6		<0.1		6.26		68.4		1.7		6.68		0.07		<2	

Date	19-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M6	10:50	0.40	18.4	18.4	<0.1	<0.1	7.56	7.4	81.5	80.6	1.1	1.1	7.43	7.4	0.05	0.05	<2	<2
			18.4		<0.1		7.32		79.6		1.1		7.43		0.05		<2	

Date	22-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:45	0.40	16.6	16.6	<0.1	<0.1	11.86	11.9	118.6	119.1	1.4	1.4	8.50	8.5	0.06	0.06	<2	<2
			16.6		<0.1		11.98		119.5		1.4		8.50		0.06		<2	

Date	24-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	15:10	0.40	18.2	18.2	<0.1	<0.1	10.21	10.2	111.4	111.6	1.9	1.6	6.80	6.8	0.04	0.04	<2	<2
			18.2		<0.1		10.23		111.8		1.2		6.80		0.04		<2	

Date	26-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:35	0.40	18	18.0	<0.1	<0.1	10.05	10.1	106.2	106.4	3.3	3.2	8.10	8.1	0.07	0.07	<2	<2
			18		<0.1		10.08		106.5		3.1		8.10		0.07		<2	

Date	29-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:55	0.40	18.4	18.4	<0.1	<0.1	9.42	9.4	107.4	107.2	1.3	1.2	6.90	6.9	0.06	0.06	<2	<2
			18.4		<0.1		9.46		106.9		1.1		6.90		0.06		<2	



Date	31-Jan-19																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:50	0.40	19.7	19.7	<0.1	<0.1	9.11	9.1	106.4	106.3	1.6	1.5	6.80	6.8	0.06	0.06		#DIV/0!
			19.7		<0.1		9.14		106.2		1.3		6.80		0.06			


## **Appendix I**

### **Graphical Plots of Air Quality, Noise and Water Quality**






### Air Quality Impact Monitoring – 1-hour TSP

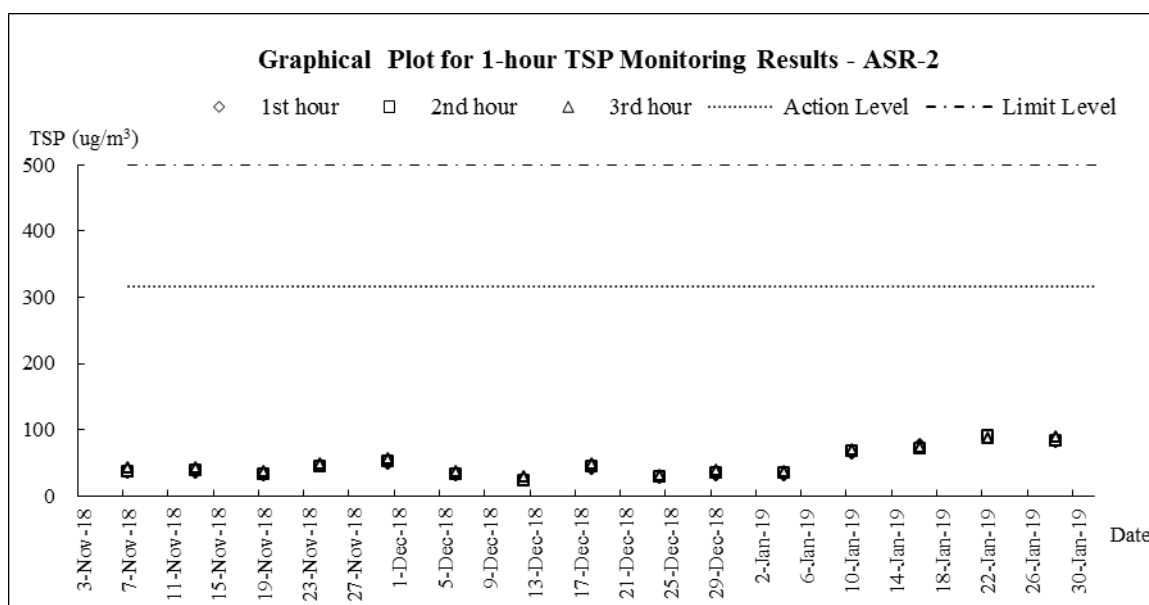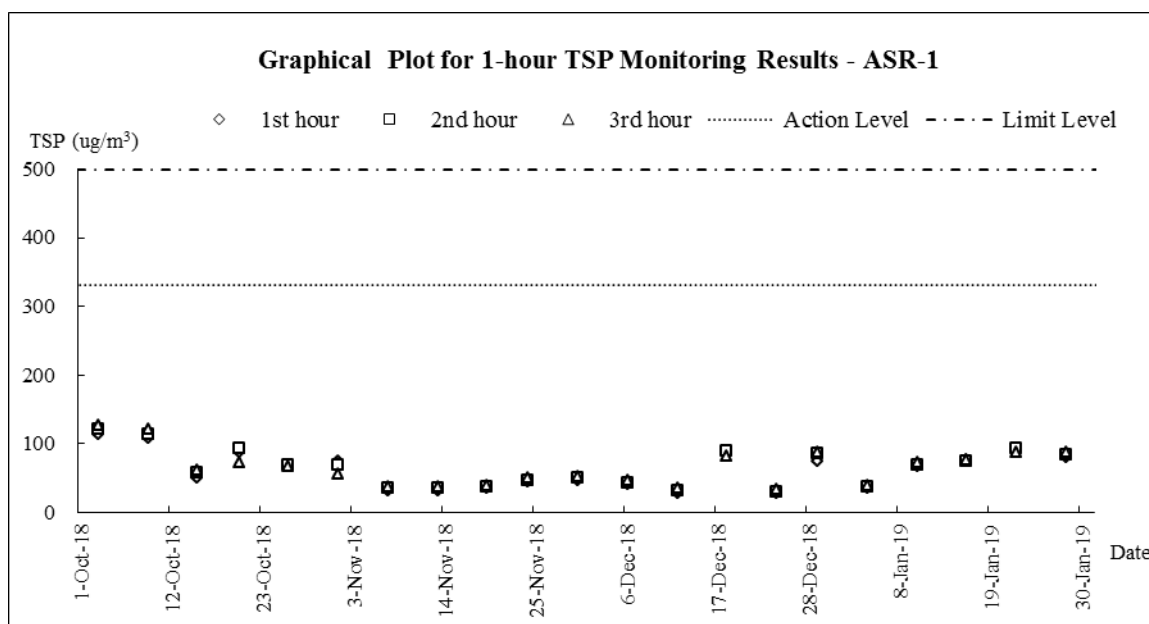

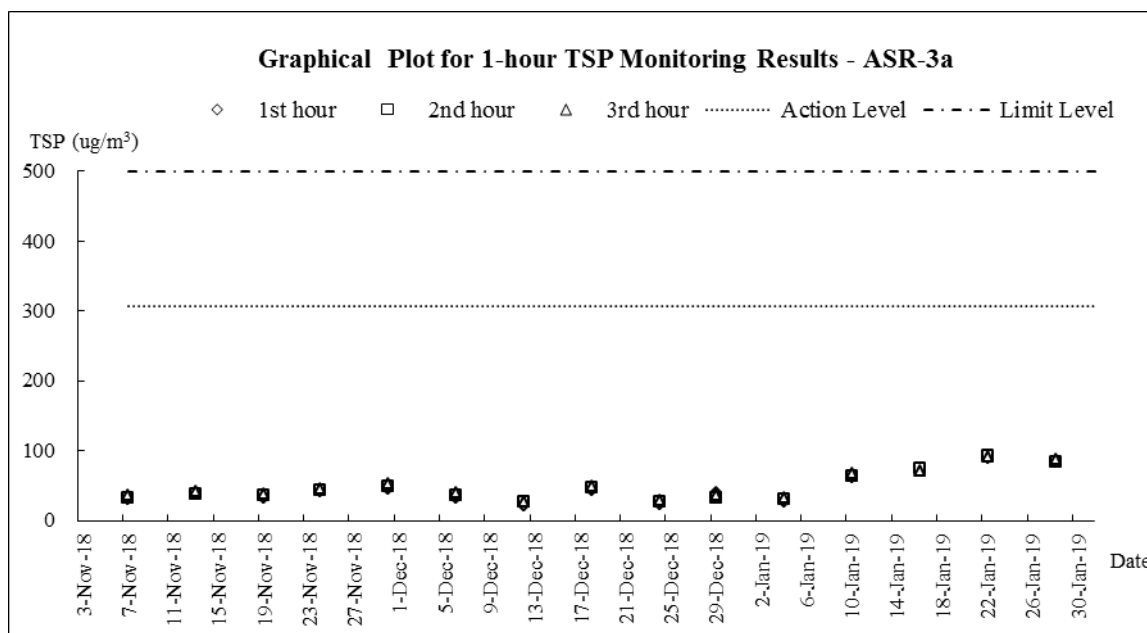



### Air Quality Impact Monitoring – 24-hour TSP

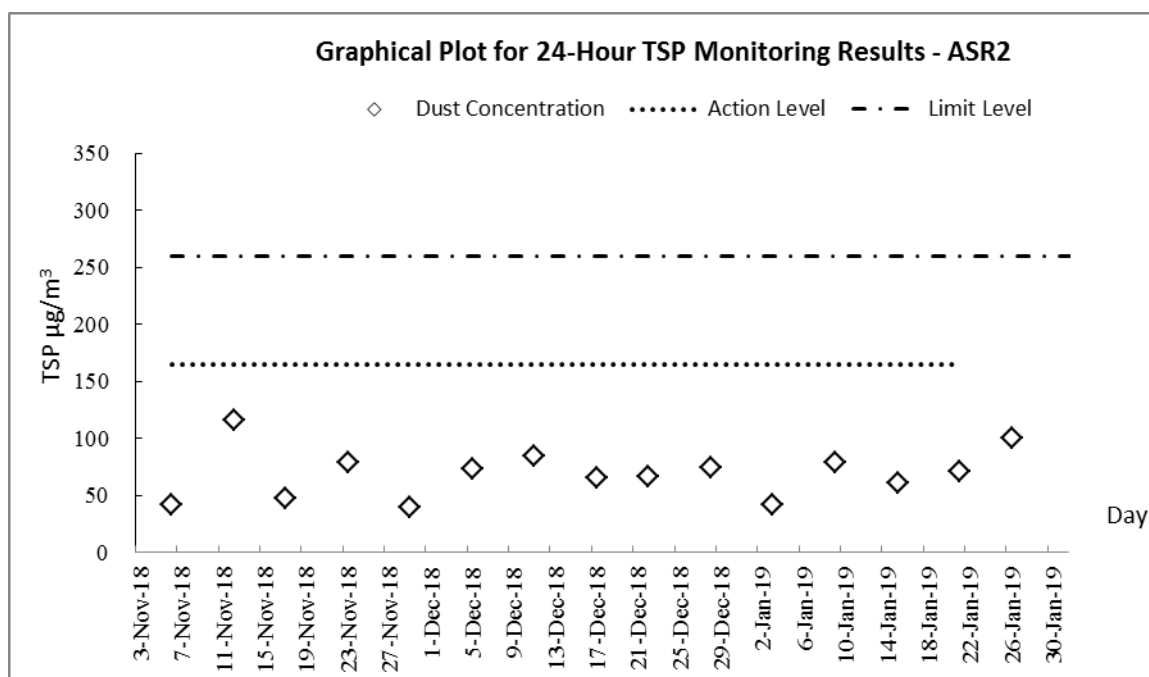
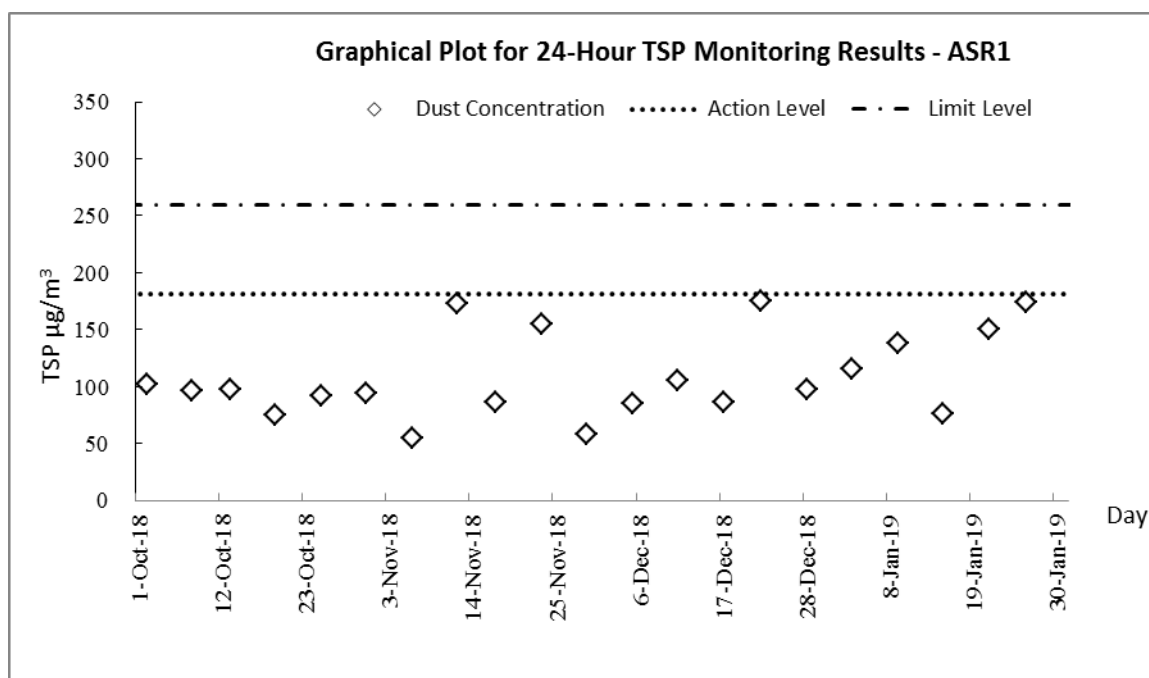


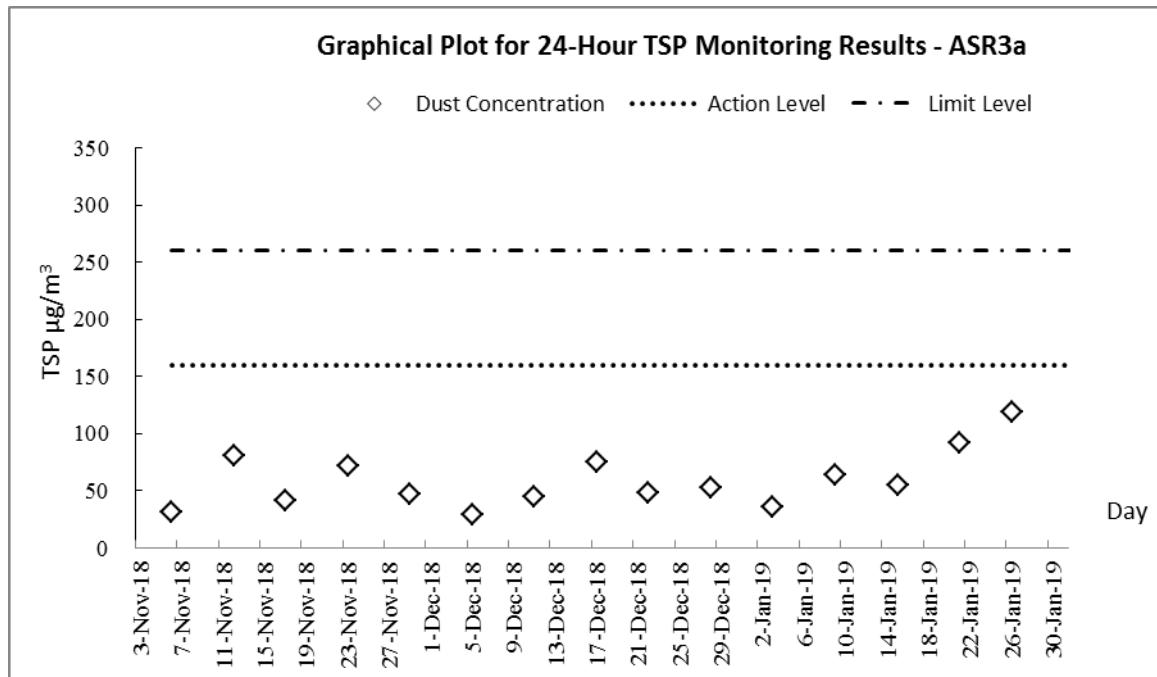







### Construction Noise Impact Monitoring

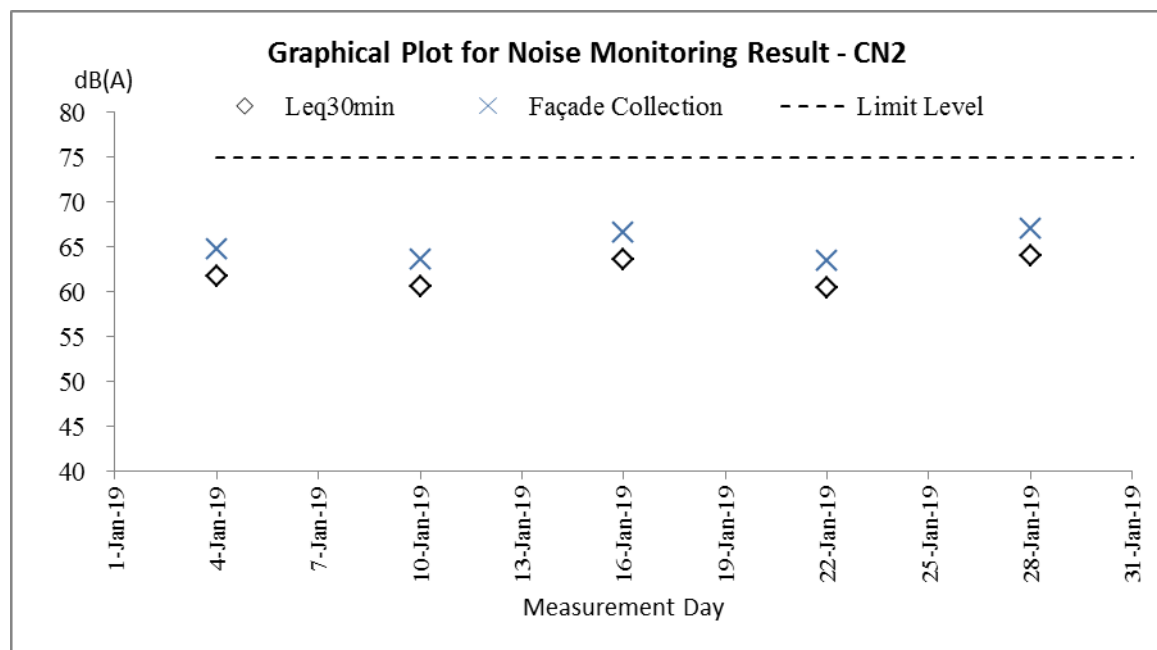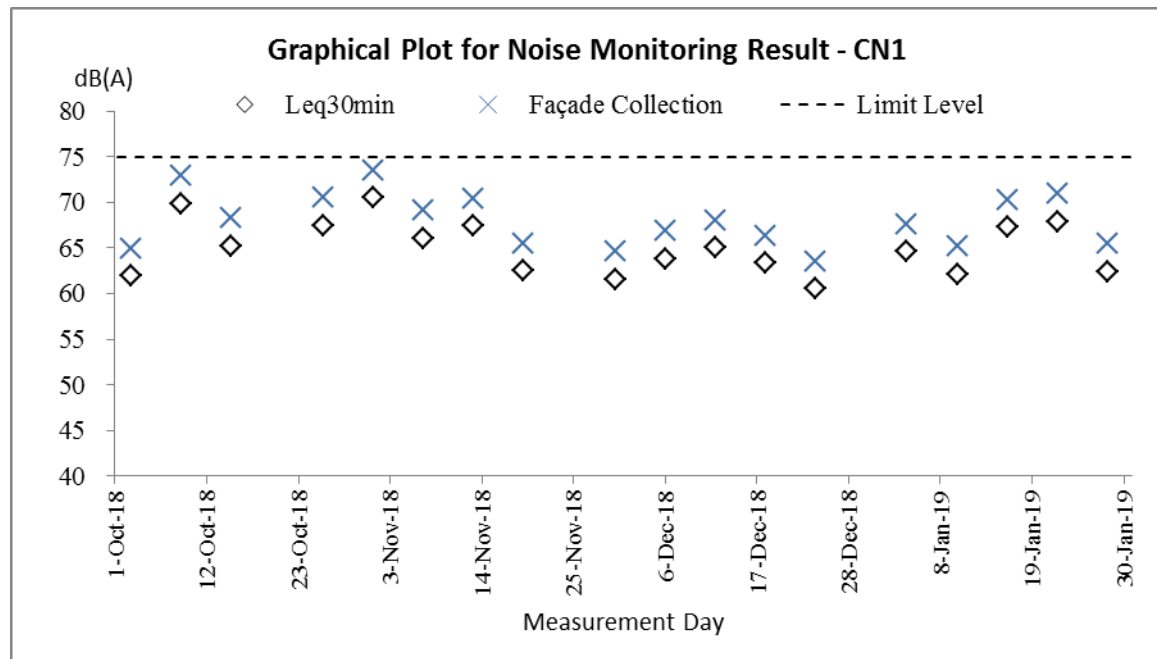


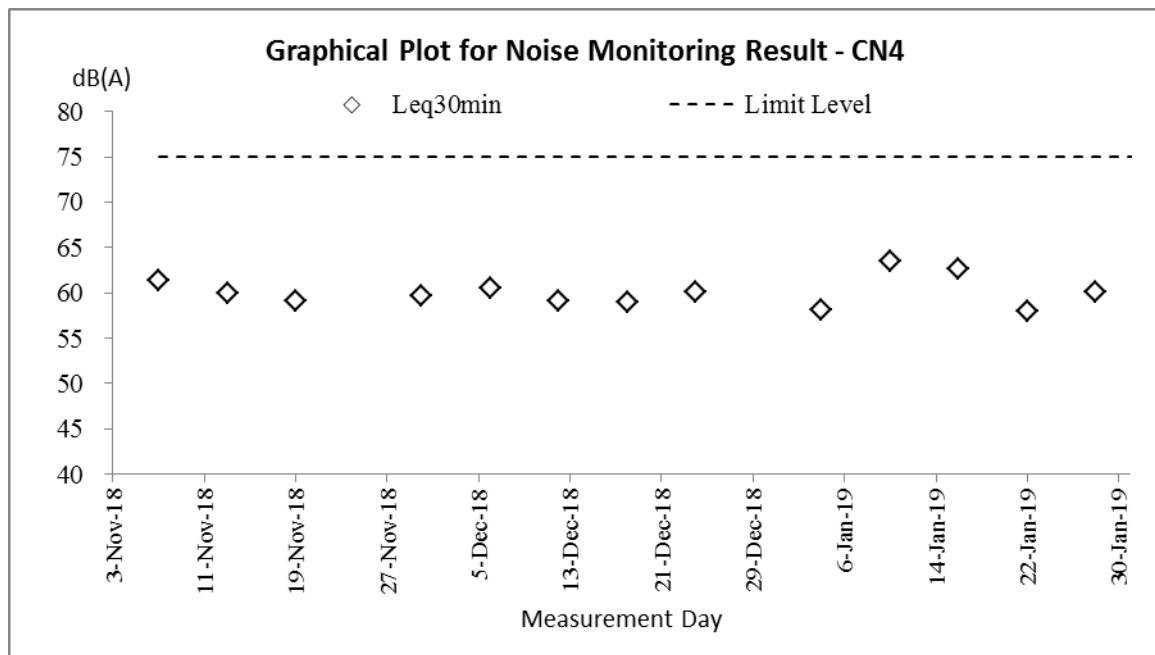
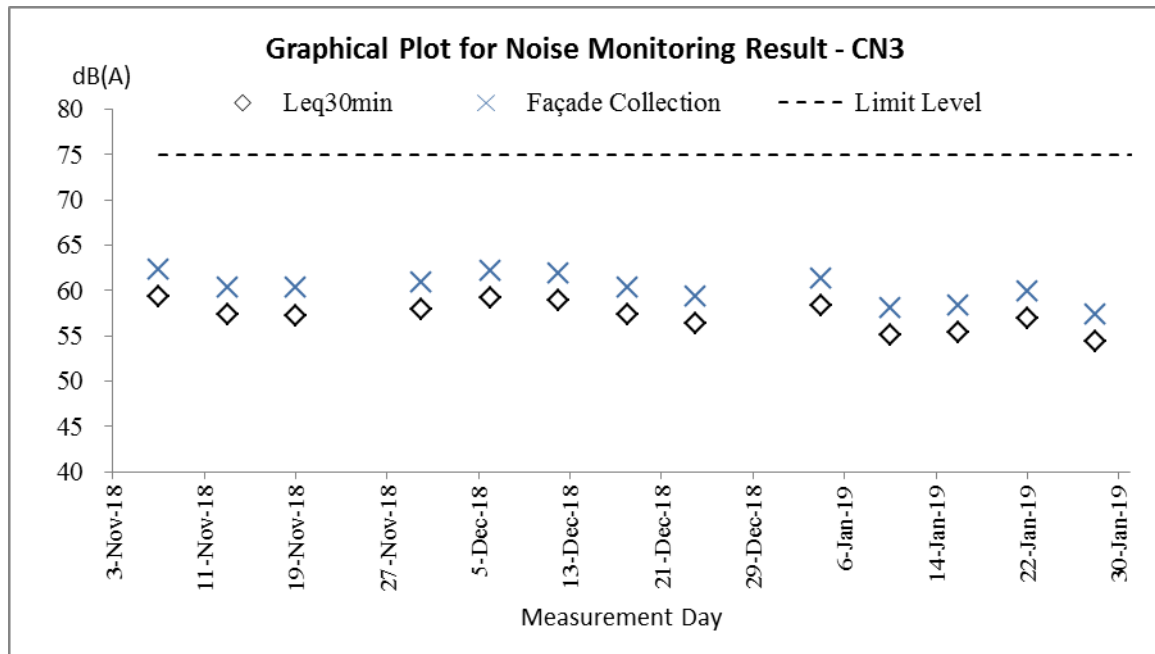





### Water Quality Impact Monitoring

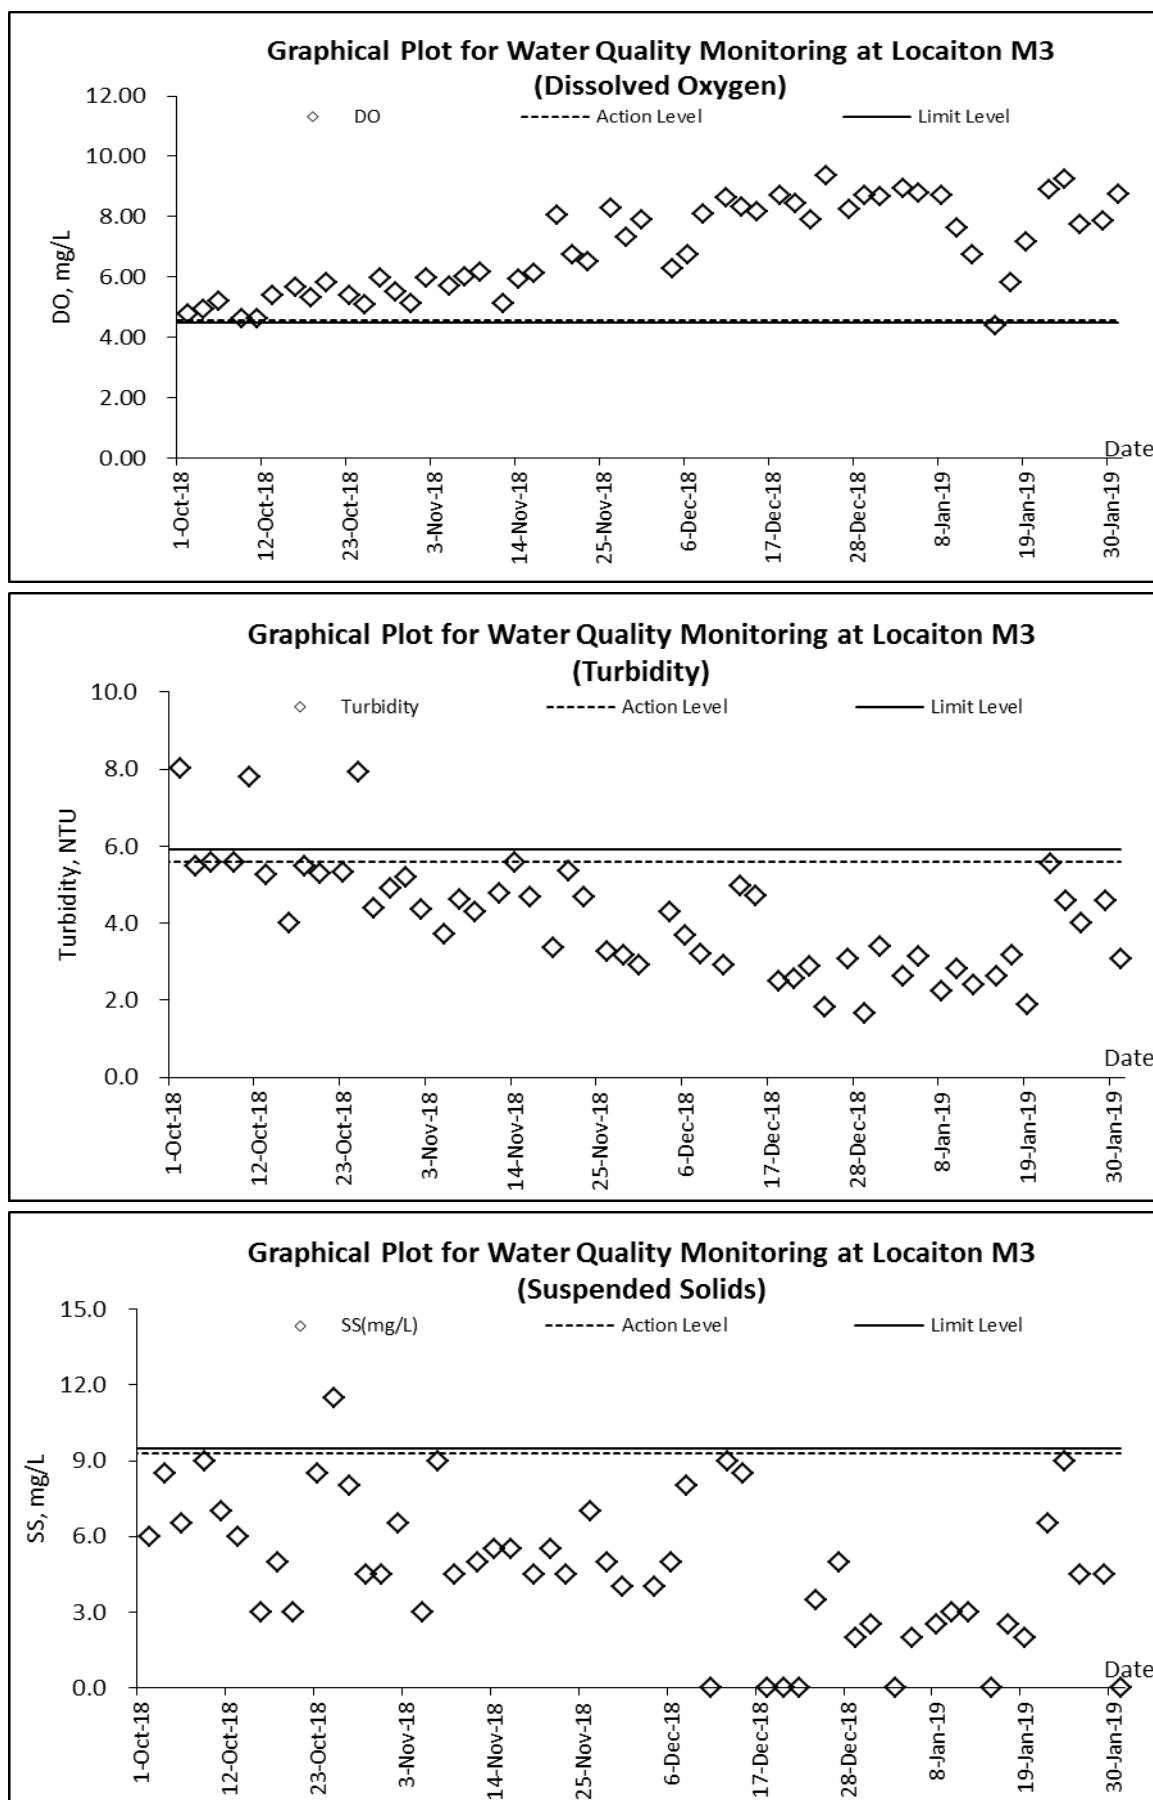

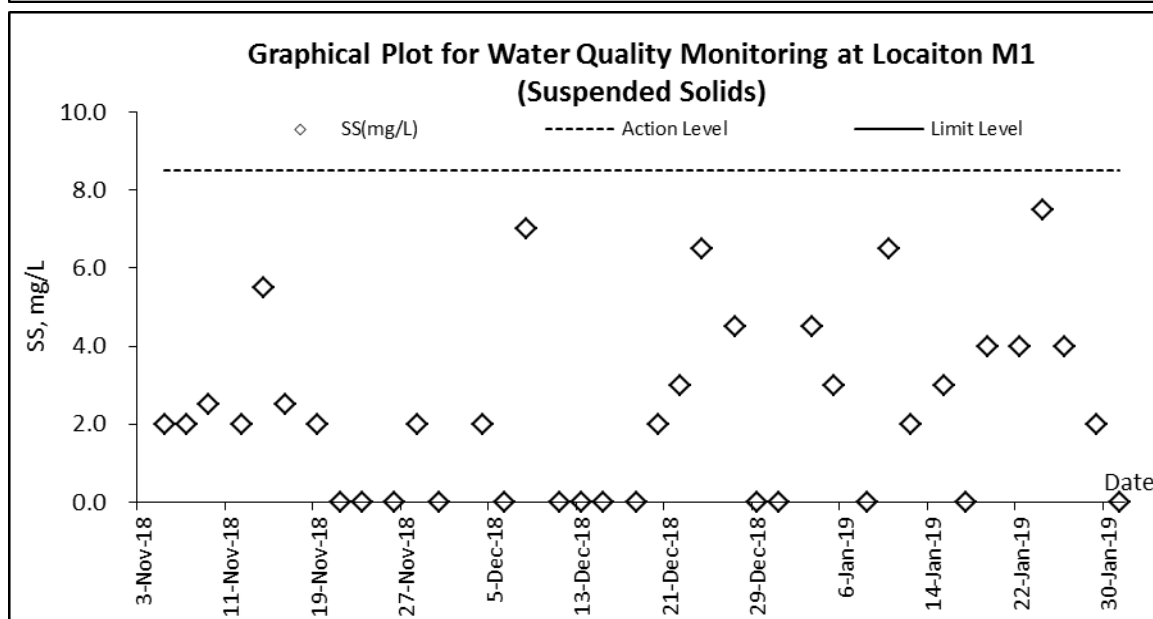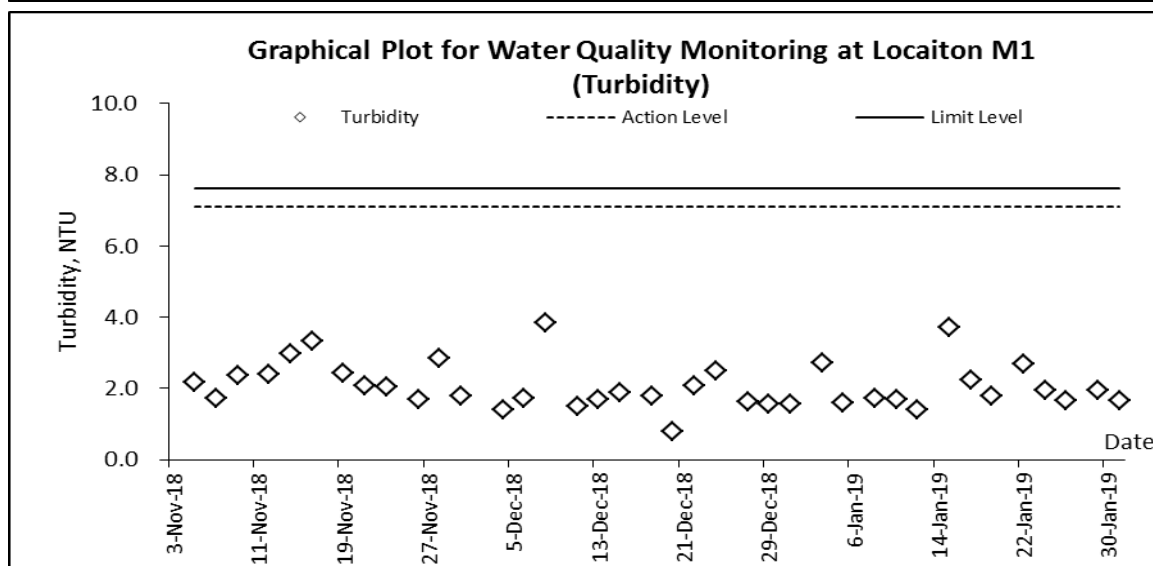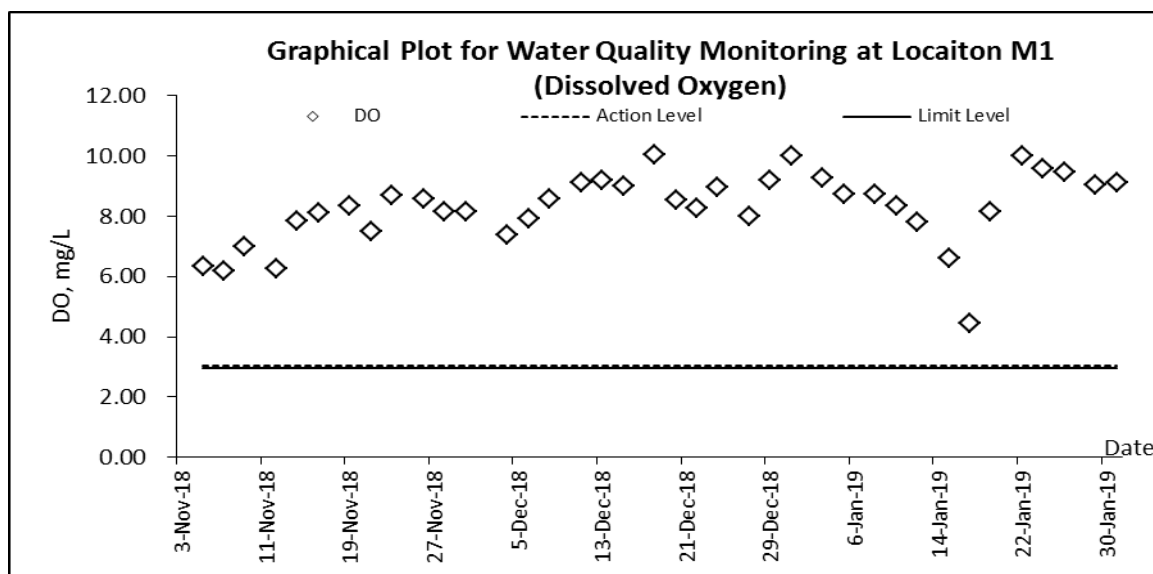



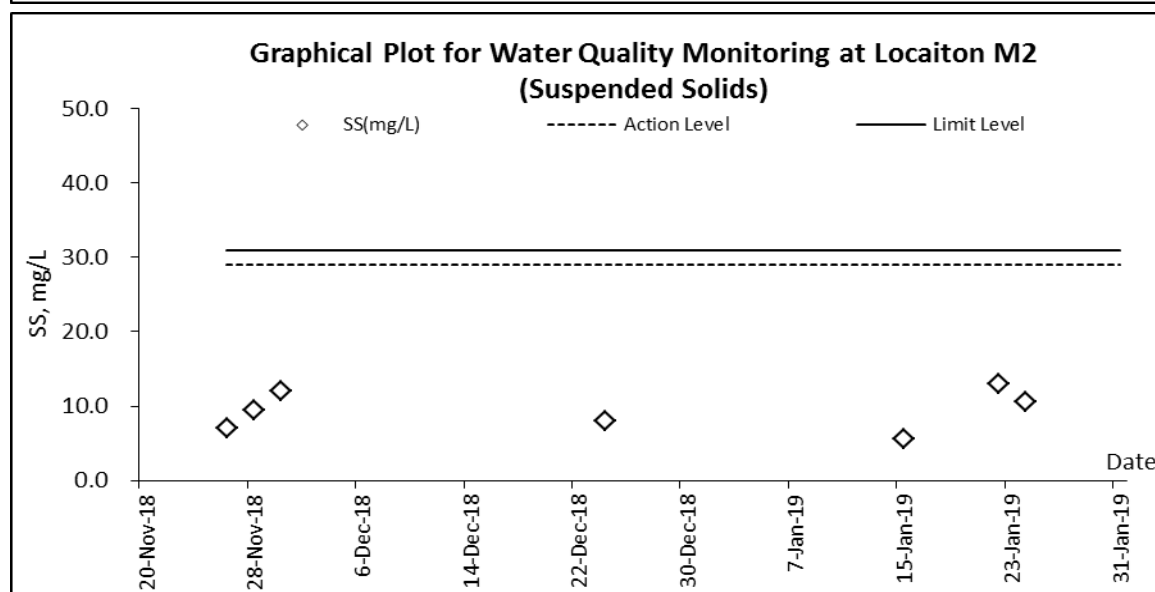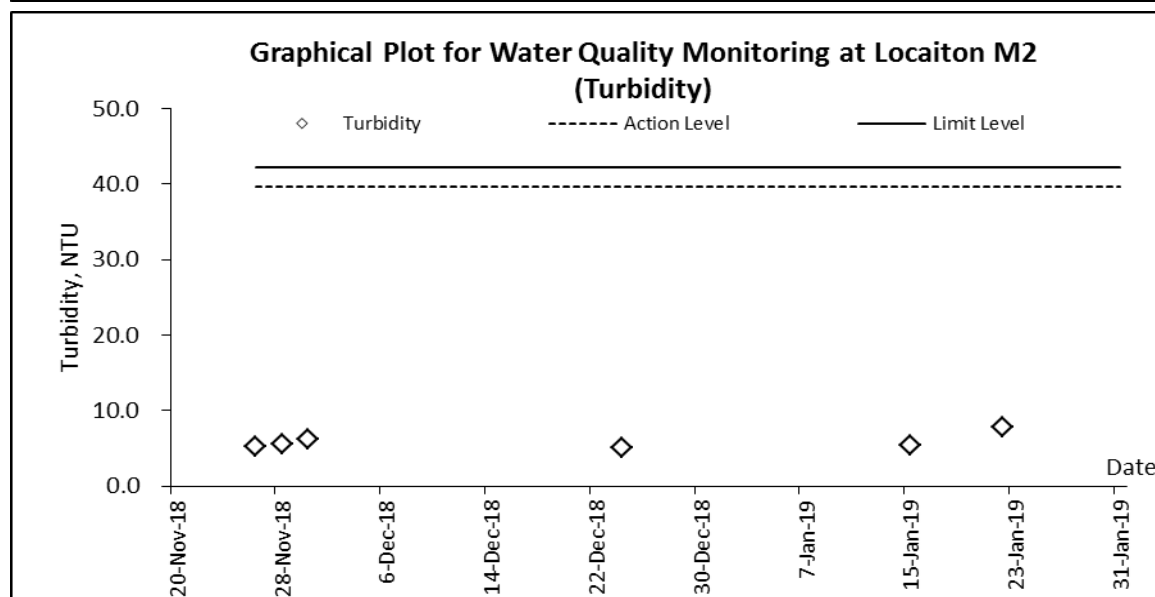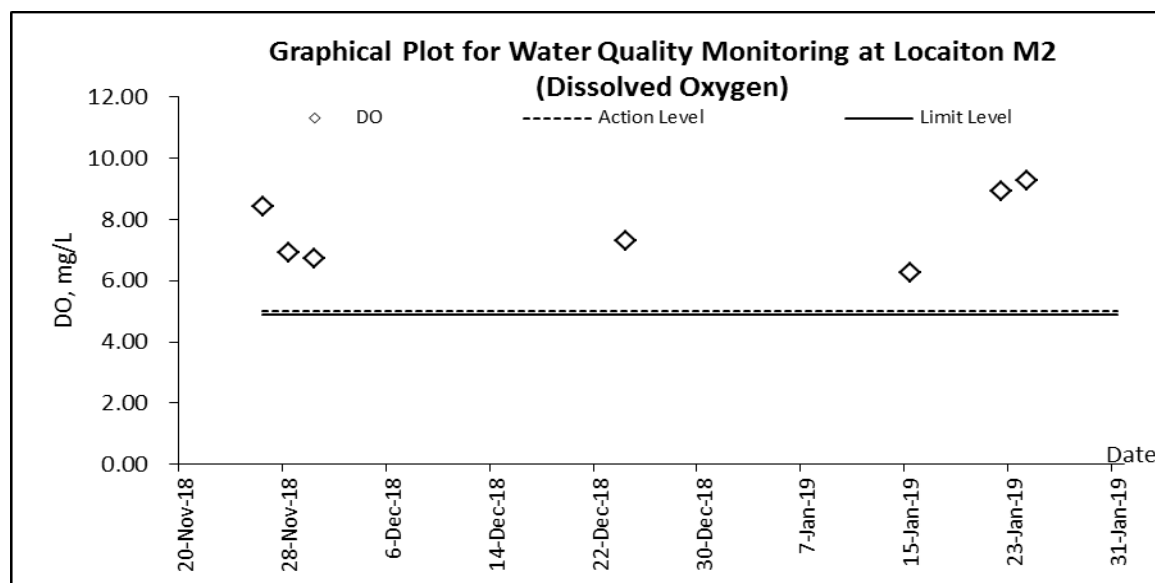

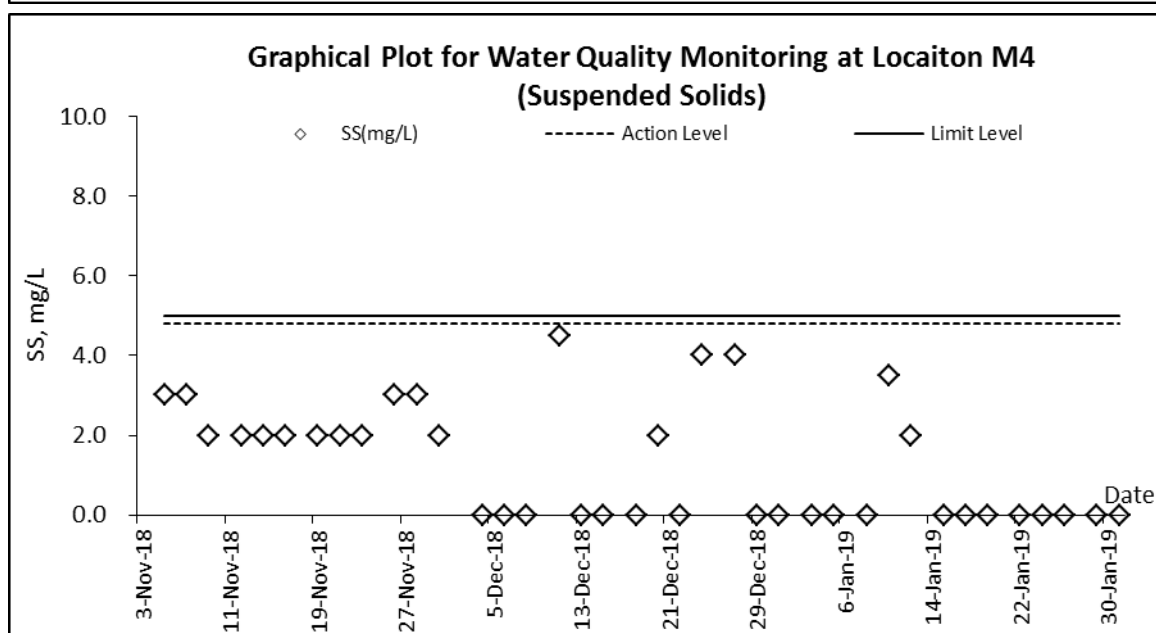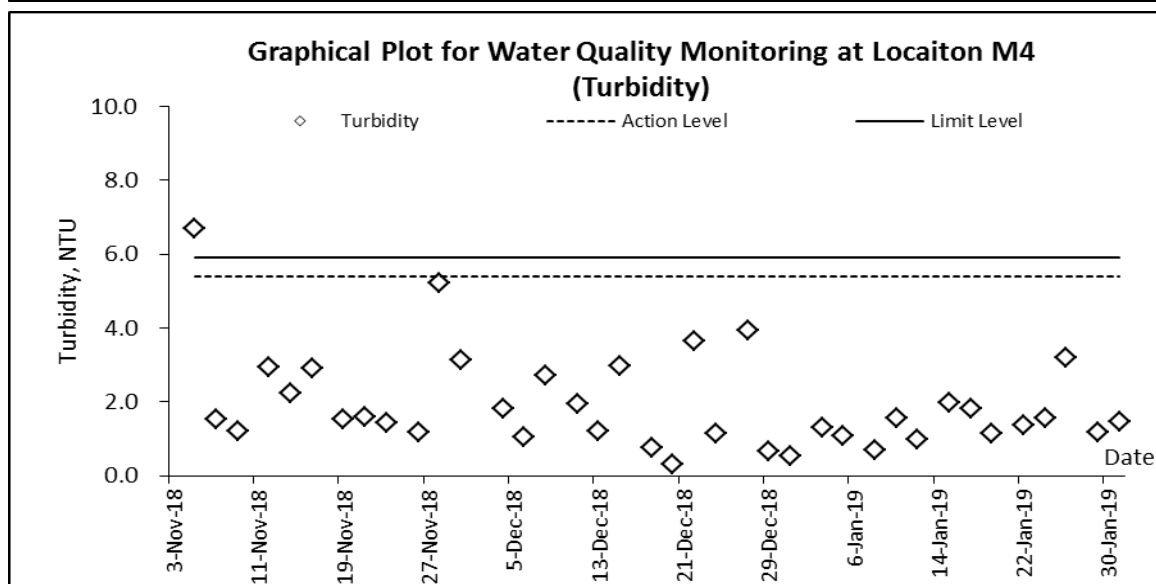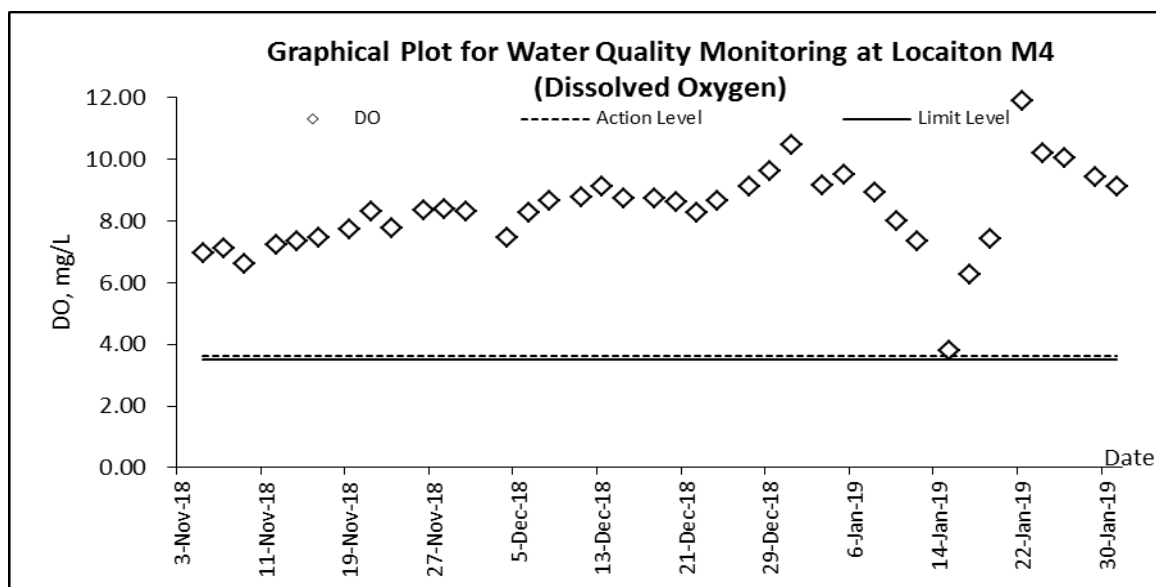

## **Appendix J**

### **Meteorological Data of the Reporting Period (Ta Kwu Ling Station)**

Date		Weather	Total Rainfall (mm)	Ta Kwu Ling Station			
				Mean Air Temp. (°C)	Wind Speed (km/h)	Mean Relative Humidity (%)	Wind Direction
1-Jan-19	Tue	Mainly cloudy. Visibility relatively low in some areas.	Trace	12.3	9.4	59.7	N/NW
2-Jan-19	Wed	Sunny periods in the afternoon.	Trace	13.3	12.4	60	N/NW
3-Jan-19	Thu	Moderate to fresh east to northeasterly winds.	0.1	13.5	5.1	78.2	N/NW
4-Jan-19	Fri	Mainly cloudy. Moderate to fresh east to northeasterly winds.	0.1	17.9	7.5	83	E/NE
5-Jan-19	Sat	Moderate easterly winds, fresh offshore.	0	23.4	4	84	W/NW
6-Jan-19	Sun	Mainly cloudy. Sunny intervals and relatively low visibility in some areas	Trace	17.4	7.5	76.5	N/NW
7-Jan-19	Mon	Sunny intervals. Moderate easterly winds, fresh offshore.	0	18.3	8	80	E
8-Jan-19	Tue	Mainly cloudy. Moderate to fresh easterly winds,	0.2	19.5	4.1	77.5	N/NW
9-Jan-19	Wed	Mainly cloudy. Moderate easterly winds.	0	18.5	8.9	74	E/NE
10-Jan-19	Thu	Mainly cloudy. Moderate to fresh easterly winds.	0	20.8	8	74.2	E
11-Jan-19	Fri	Mist patches at first. Sunny intervals in the afternoon.	0	22.1	8.5	76.7	E/SE
12-Jan-19	Sat	One or two light rain patches in the morning and at night.	Trace	22.2	6.7	77.5	W/SW
13-Jan-19	Sun	Visibility rather low in some areas at first.	Trace	18.6	6.6	89.7	E/SE
14-Jan-19	Mon	Mainly cloudy with a few light rain patches.	Trace	19	5.6	85.5	E/SE
15-Jan-19	Tue	Becoming cool tonight. Moderate northerly winds.	4	19.6	5.3	85.5	E/SE
16-Jan-19	Wed	Mainly cloudy. One or two light rain patches later.	0	16.2	9.6	68	N
17-Jan-19	Thu	Mainly cloudy with a few light rain patches.	0	15.9	10	60.5	N
18-Jan-19	Fri	There will be sunny periods. Moderate to fresh easterly winds.	0	15.1	5.7	72.5	N/NW
19-Jan-19	Sat	Fine and dry. Rather cool tomorrow morning.	0.2	20	5.9	71.5	N/NW
20-Jan-19	Sun	Mainly cloudy with a few light rain patches.	0.1	22	6.5	64.7	E/SE
21-Jan-19	Mon	Moderate north to northeasterly winds. Mainly fine and dry	4.7	17.1	9.7	58.7	N
22-Jan-19	Tue	Fine and dry. Rather cool tomorrow morning.	0	13.6	13.2	43.7	N
23-Jan-19	Wed	Fine and dry. Moderate easterly winds	0	13.4	5.5	63.5	E/NE
24-Jan-19	Thu	Fine and dry. Moderate easterly winds, occasionally fresh offshore.	0	15.8	7.3	65	E/NE
25-Jan-19	Fri	Fine and dry. Light winds,	0	17.5	6.8	66.2	E/SE
26-Jan-19	Sat	Cloudy periods overnight. Mainly fine tomorrow.	0	17.1	7	65	E/SE
27-Jan-19	Sun	Fine and dry. Moderate easterly winds	4.7	16.9	6.3	63.7	E/SE
28-Jan-19	Mon	Sunny intervals in the afternoon. Moderate easterly winds.	0	18.4	8	60	E/SE
29-Jan-19	Tue	Moderate easterly winds, occasionally fresh offshore at first.	0	18	8.9	65	E
30-Jan-19	Wed	Mainly cloudy with sunny intervals.	0	18.2	7.3	71	E
31-Jan-19	Thu	Warm with sunny periods. Visibility relatively low. Light winds,	0	21.3	6.5	72.5	N/NW



## **Appendix K**

### **Ecology Survey Report**

## **Contract No. CV/2016/10**

# **Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery**

---

## **Monthly Report of Ecologically Sensitive Habitats Monitoring – Jan 2019**

Revision	0	
Date of issue	29 Jan 2019	
Prepared by	Alan Lam	
Reviewed by	Edwina Yeung	
Verified by	Desmond Tang	

## Table of Contents

<b>1</b>	<b>INTRODUCTION</b>	<b>4</b>
1.1	BACKGROUND	4
1.2	OBJECTIVE	4
<b>2</b>	<b>ECOLOGICALLY SENSITIVE HABITATS</b>	<b>6</b>
2.1	DESCRIPTION OF HABITATS	6
2.2	MONITORING MEASURES OF WETLAND HABITATS	7
2.3	MONITORING MEASURES OF NON-WETLAND HABITATS	7
<b>3</b>	<b>METHODOLOGY</b>	<b>8</b>
3.1	MAMMAL SURVEY	8
3.2	BIRD SURVEY	8
3.3	HERPETOFAUNA SURVEY	8
3.4	DRAGONFLY SURVEY	8
3.5	BUTTERFLY SURVEY	9
3.6	AQUATIC FAUNA SURVEY	9
<b>4</b>	<b>RESULT</b>	<b>10</b>
	<b>Appendix I – Transect Routes at Sandy Ridge</b>	<b>15</b>

### **LIST OF TABLE**

Table 1	Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna
Table 2	Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna
Table 3	Survey Schedule
Table 4	Result of Avifauna in survey
Table 5	Result of reptile in survey
Table 6	Result of amphibian in survey
Table 7	Result of butterfly in survey
Table 8	Result of Odonate in survey
Table 9	Result of freshwater communities in survey

### **LIST OF APPENDIX**

Appendix I	Transect Routes at Sandy Ridge
------------	--------------------------------

# 1 INTRODUCTION

## 1.1 BACKGROUND

- 1.1.1 The main objective of the proposed site formation and associated infrastructural works for development of columbarium, crematorium (C&C) and related facilities at Sandy Ridge Cemetery is to increase the public cremation services and supply of public niches to meet the future demand.
- 1.1.2 The project includes site formation and associated works for development of C&C facilities at the Sandy Ridge Cemetery, road works within Sandy Ridge Cemetery, widening a section of Lin Ma Hang Road (from 6.5m to 7.3m), provision of off-site pick-up/drop-off points for shuttle buses as well as barging point at Siu Lam, Lok On Pai.
- 1.1.3 The Environmental Impact Assessment (EIA) report, including Environmental Monitoring and Audit Manual (EM&A Manual), was approved with conditions on 8 August 2016 (Register No.: AEIAR-198/2016). EPD issued an Environmental Permit (EP) for the Project (EP-534/2017) on 7 April 2017. A Further Environment Permit (FEP) for the Project (FEP-01/534/2017) was issued on 23 February 2018, variation of EP (EP-534/2017/A) and variation of FEP (FEP-01/534/2017/A) were issued on 24 December 2018.
- 1.1.4 According to Clause 3.1 of the FEP (FEP-01/534/2017/A), “The Permit Holder shall implement the EM&A programme in accordance with the procedures and requirements as set out in the EM&A Manual. Any changes to the programme shall be justified by the ET Leader and verified by the IEC as conforming to the information and requirements contained in the EM&A Manual before submission to the Director for approval”.
- 1.1.5 This Ecologically Sensitive Habitats Monitoring Methodology articulates the protocol of monitoring the ecology of concerned habitats as specified in EM&A Manual.

## 1.2 OBJECTIVE

- 1.2.1 According to approved EIA report (AEIAR-198/2016), habitat types within project boundary comprise of watercourse, grassland, upland grassland, plantation, woodland and developed area. Natural habitats were of moderate ecological value in terms of species diversity, species rarity, species abundance, ecological linkage as well as nursery. Moreover, 0.3ha of wet woodland on the northern side of Sandy Ridge was deemed habitat with high ecological value. Four types of habitats were regarded as ecologically sensitive habitats, namely wet woodland, watercourses, upland grassland and woodland. Considering human disturbance in upcoming construction and operation phases, ecologically sensitive habitats shall be monitored in accordance with EM&A Manual.
- 1.2.2 The objective of ecologically sensitive habitats monitoring is to evaluate the effectiveness of measures to minimize impacts on concerned habitats from disturbance and pollution.





## 2 ECOLOGICALLY SENSITIVE HABITATS

### 2.1 DESCRIPTION OF HABITATS

- 2.1.1 In order to monitor the effectiveness of the measures to the minimise impact on ecologically sensitive habitats from disturbance and pollution, monthly monitoring during construction and operation phases is required as specified in EM&A Manual. Standard faunal transect and sampling surveys cover both wetland and non-wetland habitats:

Wetland habitats	Non-wetland habitats
Wet Woodland	Upland Grassland
Watercourses	Woodland

- 2.1.2 Wet woodland is small patch present on northwest of the project boundary, and is confined by the marsh area to the north and the secondary woodland to the east, south and south-west parts. A number of mature trees *Cleistocalyx nervosum* and *Acronychia pedunculata* form the tree canopy, with other self-sown shrubs (including *Psychotria asiatica*, *Ligustrum sinense* and *Glochidion lanceolarium*) and trees (*Aporosa dioica* and *Litsea monopetala*). Whilst botanically it comprises of naturally regenerated secondary woodland and ground level are a series of small braided streams and weep points which even during the dry season remain wet. This creates a rather uncommon habitat in Hong Kong offering suitable conditions for a good assemblage of common wetland species. The wet woodland provides a good assemblage of micro-habitats, which is relatively undisturbed and has good linkages to other natural habitats. Several species of conservation importance were recorded in EIA report from this habitat: East Asian Porcupine, Leopard Cat, Red Muntjac, Two-striped Grass Frog, Small Snakehead, *Somanniathelphusa zanklon*, Dancing Shadow-emerald.
- 2.1.3 Seasonal watercourse running west to east in the eastern part of the area inside the Project boundary is shallower in gradient than those running off the hillside. This seasonal watercourse is heavily vegetated with wetland-associated herbs including *Commelina diffusa*, *Polygonum chinense*, *Colocasia esculenta* and *Dracaena sanderiana*. A mature tree of *Aquilaria sinensis* was recorded at the bank of the seasonal watercourse to the west of the Sandy Ridge Cemetery Office. Seasonal watercourses are restricted to the steeper slopes within the project boundary and are characterised by being entirely dry for much of the dry season. However, endemic crab *S. zanklon* population is supported by ephemeral watercourses close to the project boundary.
- 2.1.4 Upland grassland is the major habitat within the project boundary. The semi-natural habitat is dominated by typical upland grassland species: fern *Dicranopteris pedata*, grass *Neyraudia reynaudiana*, *Miscanthus floridulus*, climbing vines *Smilax china*, *Smilax glabra*, and shrubs such as *Rhodomertus tomentosa*, *Breynia fruticosa* and *Helicteres angustifolia*. Approximately 30 flowering spikes of two orchid species Bamboo Orchid and Toothed Habenaria were recorded near the hill top in the northern part of this upland grassland. Golden-headed Cisticola, which is considered as Local Concern by Fellowes *et al.* (2002), was also recorded in upland grassland on Sandy Ridge, including a proved breeding record of fledged young in September 2013. In addition, numerous species of conservation interest were recorded in EIA report, such as East Asian Porcupine, Leopard Cat, Red Muntjac, Great Swift, Tamil Grass Dart, Small Three-ring and Small Grass Yellow.

- 2.1.5 Scattered patches of woodland are present throughout the assessment area, with the largest contiguous block located immediately to the east of the project boundary. These woodlands are relatively young with single-layered of canopy dominants (~10 – 15m tall) including *A. dioica*, *Bridelia tomentosa*, *Cinnamomum burmannii*, *Daphniphyllum calycinum*, *Litsea glutinosa*, *Rhus succedanea*, and *Zanthoxylum avicennae*. Such areas comprise secondary woodland which is largely derived from natural regeneration and colonisation of trees as a result of seed dispersal by birds and/or bats. A mature tree of *A. sinensis* is located at the woodland edge at the central part of the Project according to EIA report.

## 2.2 MONITORING MEASURES OF WETLAND HABITATS

- 2.2.1 Wetland habitats include wet woodland and watercourses. Monitoring surveys using standardised quantitative methodology will be conducted at fixed points. For seasonal watercourse, survey shall be conducted whenever the habitat appears.
- 2.2.2 Measures to respond to decreases in numbers of aquatic fauna using the wetland habitats and action and limit levels to trigger these measures are detailed in Table 1.

Action Level	Response	Limit Level	Response
Reduction in taxa diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in taxa diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

Table 1 Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna

## 2.3 MONITORING MEASURES OF NON-WETLAND HABITATS

- 2.3.1 Non-wetland habitats consist of upland grassland and woodland. Monthly quantitative surveys of non-aquatic fauna will be conducted using standard route transect counts.
- 2.3.2 Measures to respond to decreases in numbers of non-aquatic fauna using the non-wetland habitats and action and limit levels to trigger these measures are detailed in Table 2.

Action Level	Response	Limit Level	Response
Reduction in species diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in species diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

Table 2 Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna

### 3 METHODOLOGY

The ecological survey includes all taxa being investigated in EIA report. Table 3 summarizes schedule of faunal surveys.

Month	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Mammals												
Birds (day)												
Birds (night)												
Herpetofauna												
Dragonflies												
Butterflies												
Aquatic fauna												

Table 3 Survey Schedule

#### 3.1 MAMMAL SURVEY

- 3.1.1 Mammal surveys will be conducted along the transects shown in Appendix 1 during both daytime and night time periods. Along with direct observations, other field signs, such as scats and tracks, will be searched and recorded if present.

#### 3.2 BIRD SURVEY

- 3.2.1 Bird surveys will be conducted along the transects shown in Appendix 1 during the surveys, species and their vocalizing individuals recorded will be enumerated and recorded according to the habitat(s) they are utilising.

#### 3.3 HERPETOFAUNA SURVEY

- 3.3.1 Reptile and amphibian surveys will be conducted along transects shown in Appendix 1 during surveys careful searches of appropriate microhabitats and refugia for reptiles and their vocalizing individuals will be undertaken and all reptiles observed will be identified and counted.

#### 3.4 DRAGONFLY SURVEY

- 3.4.1 Dragonfly surveys will be conducted along transects shown in Appendix 1 during surveys all dragonflies seen will be identified and counted as accurately as possible.

### **3.5 BUTTERFLY SURVEY**

- 3.5.1 Butterfly surveys will be conducted along transects shown in Appendix 1 during surveys all dragonflies seen will be identified and counted as accurately as possible.

### **3.6 AQUATIC FAUNA SURVEY**

- 3.6.1 Freshwater fishes and macro-invertebrates will be recorded by direct observation. All species trapped/recorded will be enumerated and identified (to the lowest taxonomic level possible), and the species of conservation importance photographed.



## 4 RESULT

This monitoring survey started on 29th January 2019. The weather was fine. The day survey covering wetland and non-wetland areas. The survey was conducted by transect and fixed points. All species seen will be identified and counted as accurately as possible.

- Mammal  
There were no mammal recorded in the monitoring area.
- Bird  
There were total of 28 bird individuals from 11 species recorded during the survey. One species of conservation interests were recorded in the monitoring area: *Milvus migrans*, Black Kite(黑鳶)
- Herpetofauna  
There was no reptile recorded in the monitoring area.  
There was no amphibian recorded in the monitoring area.
- Dragonfly  
There was one odonate individual in the monitoring area.
- Butterfly  
There were 5 butterfly individuals from 4 species recorded during the survey.
- Freshwater communities  
There were no freshwater community recorded in the monitoring area.

**Figure 1**  
Wetland in monitoring area.



**Figure 2**  
*Abisara echerius*  
Plum Judy  
(蛇目褐蛱蝶)



**Table 4 Result of Avifauna in survey**

Scientific Name	English Name	Chinese Name	Conservation Status	29-Jan-19	
				Non-wetland	Wetland
<i>Milvus migrans</i>	Black Kite	黑鳶	Fellowes et al. (2002): RC; Appendix 2 of CITES		2
<i>Spilopelia chinensis</i>	Spotted Dove	珠頸斑鳩			1
<i>Lanius schach</i>	Long-tailed Shrike	棕背伯勞			1
<i>Parus cinereus</i>	Cinereous Tit	蒼背山雀			1
<i>Pycnonotus jocosus</i>	Red-whiskered Bulbul	紅耳鵲		2	4
<i>Pycnonotus sinensis</i>	Chinese Bulbul	白頭鵲		4	
<i>Pycnonotus aurigaster</i>	Sooty-headed Bulbul	白喉紅臀鵲			2
<i>Hirundo rustica</i>	Barn Swallow	家燕			1
<i>Phylloscopus fuscatus</i>	Dusky Warbler	褐柳鶯			1
<i>Prinia flaviventris</i>	Yellow-bellied Prinia	黃腹鷦鶯			2
<i>Zosterops japonicus</i>	Japanese White-eye	暗綠繡眼鳥			7

**Table 5 Result of reptile in survey**

Table 3 Results of Reports in Survey				
Scientific Name	Common Name	Chinese Name	29-Jan-19	
			Non-wetland	Wetland
N/A				

**Table 6 Result of amphibian in survey**

Table 6 Result of amphibian in survey					
Scientific Name	Common Name	Chinese Name	Conservation Status	29-Jan-19	
				Non-wetland	Wetland
N/A					

**Table 7 Result of butterfly in survey**

Scientific Name	Common Name	Chinese Name	29-Jan-19	
			Non-wetland	Wetland
<i>Abisara echerius</i>	Plum Judy	蛇目褐蛱蝶		2
<i>Neptis hylas</i>	Common Sailer	中環蛱蝶		1
<i>Mycalesis mineus</i>	Dark Brand Bush Brown,	小眉眼蝶	1	
<i>Eurema hecabe</i>	Common Grass Yellow	寬邊黃粉蝶	1	

**Table 8 Result of Odonate in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	29-Jan-19	
				Non-wetland	Wetland
<i>Pantala flavescens</i>	Wandering Glider	黃蜻		1	

**Table 9 Result of freshwater communities in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	29-Jan-19
N/A				



## **Appendix I – Transect Routes at Sandy Ridge**




DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
© OVE ARUP & PARTNERS HONG KONG LIMITED.



## Legend

- Project Boundary
- Utilities Construction
- Sandy Ridge Works Area
- Lin Ma Hang Road Works Area
- 500m Assessment Area
- Survey Transect

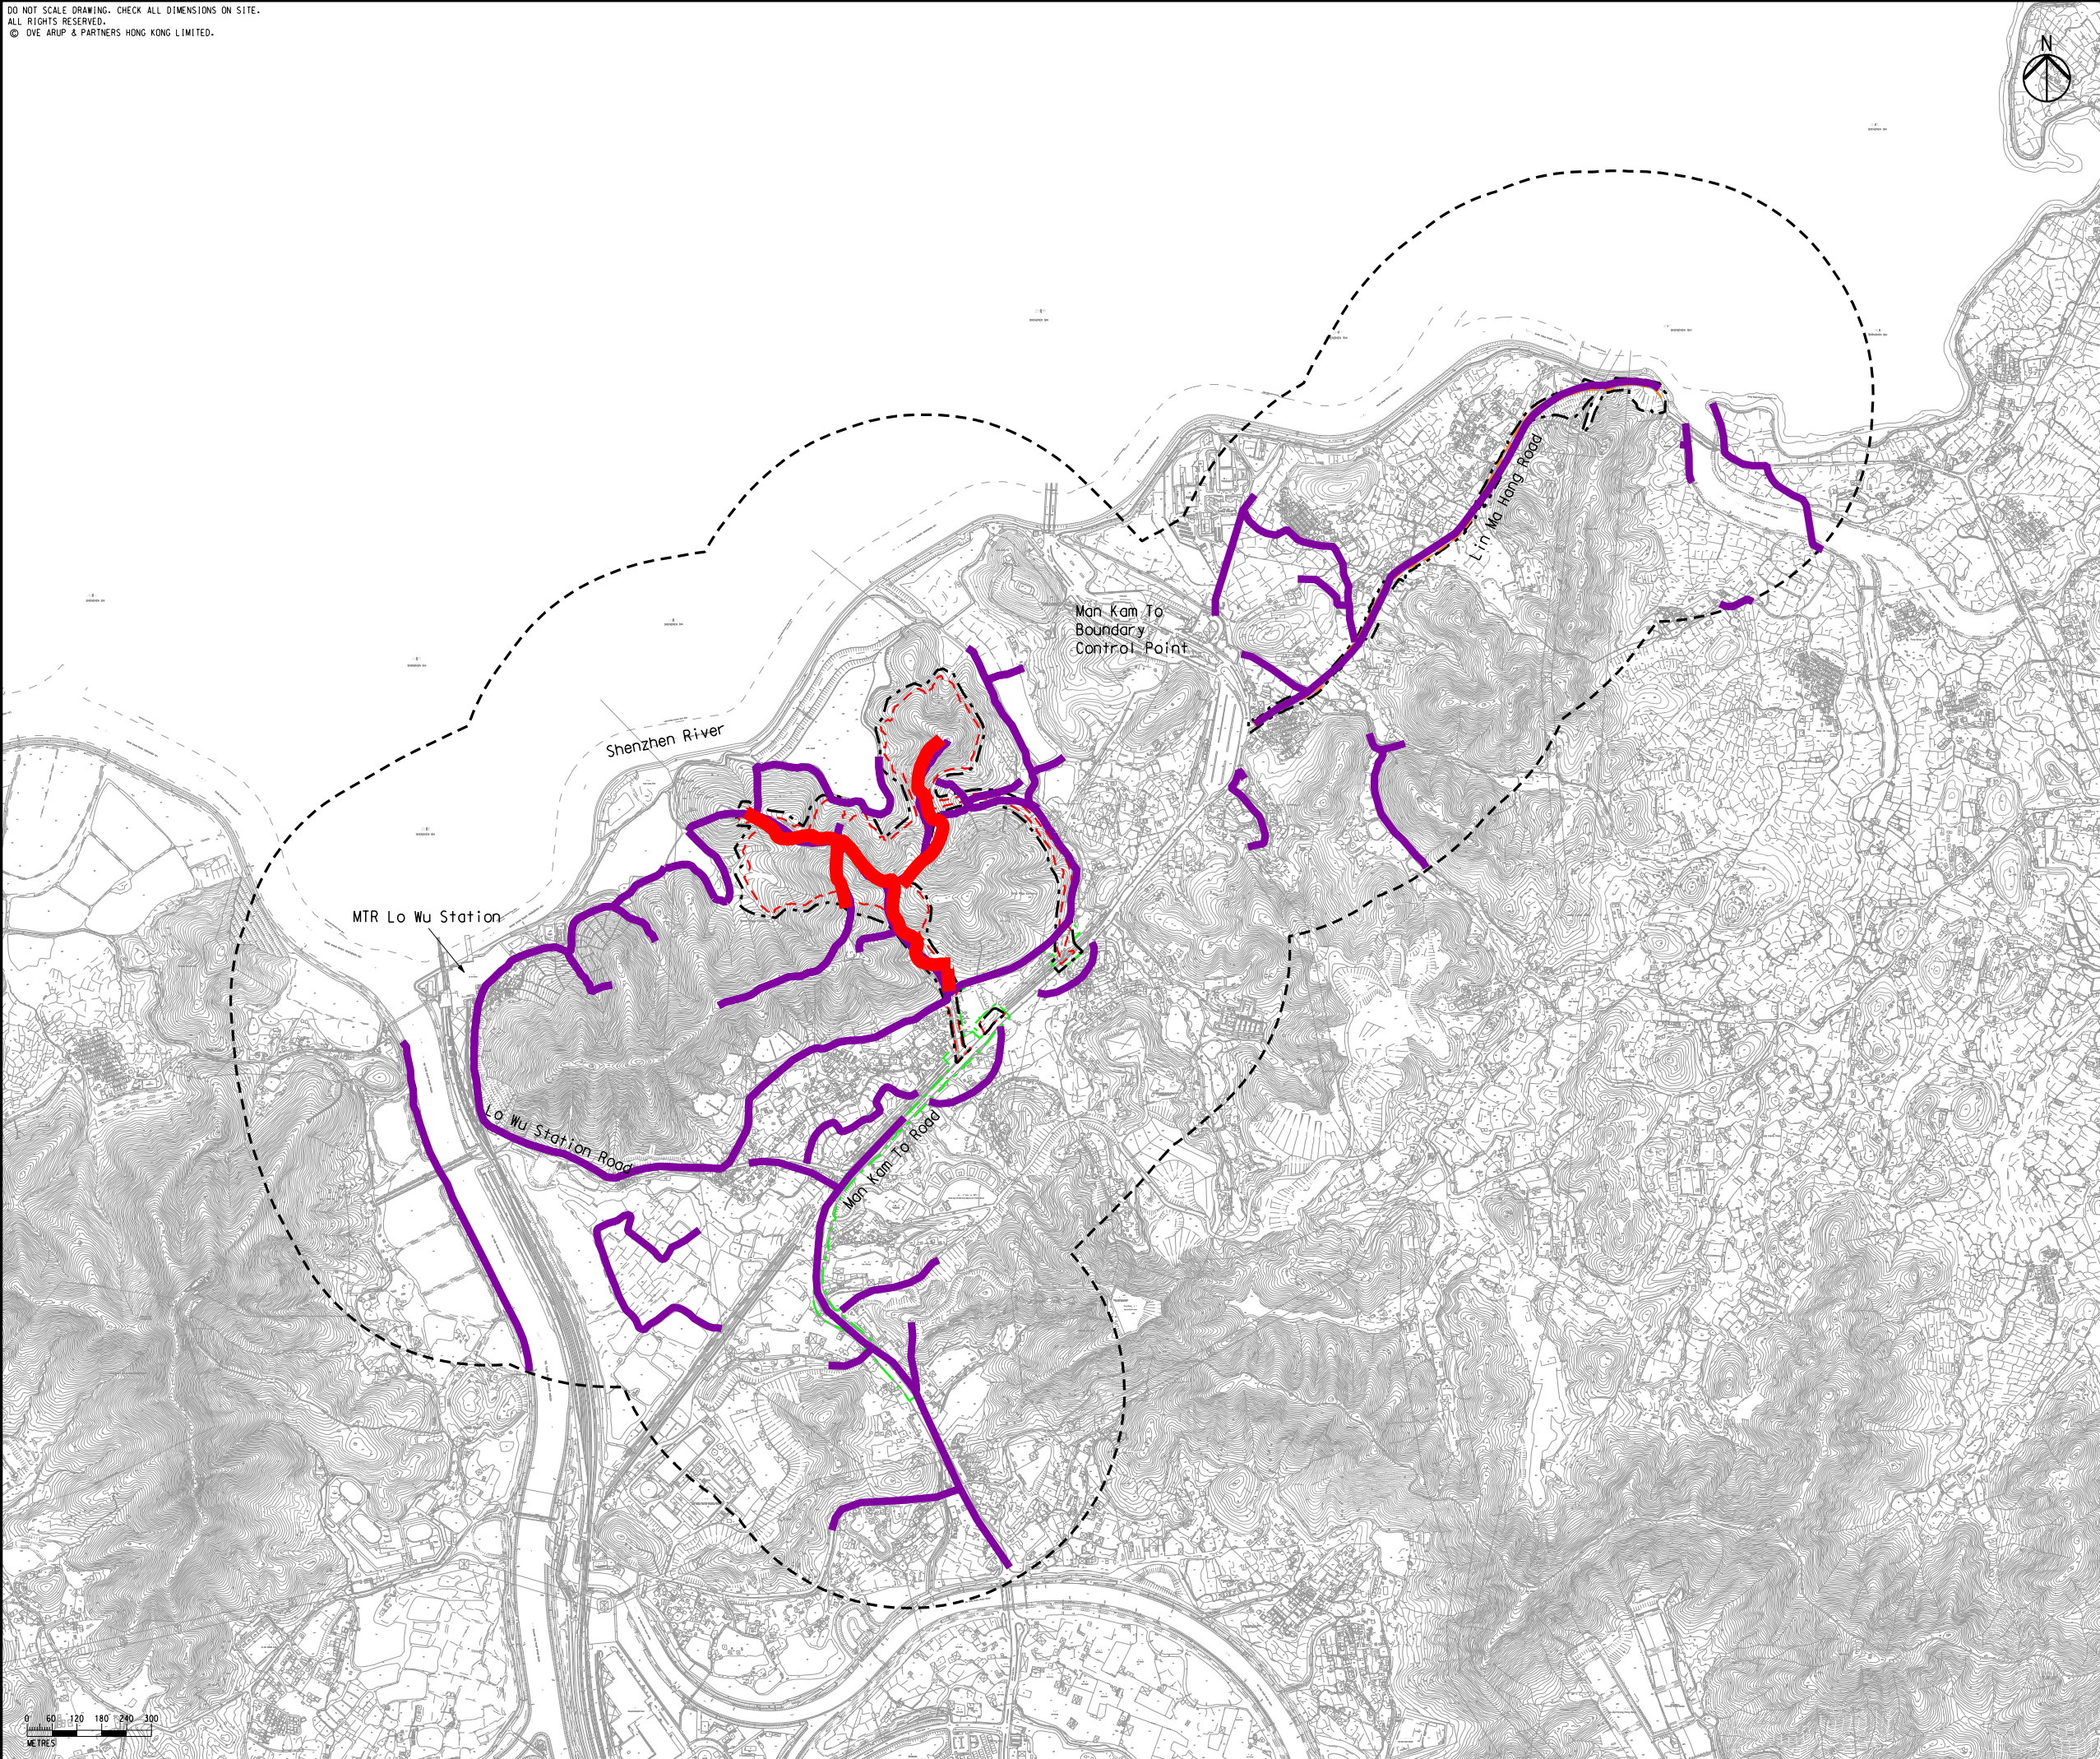

G	SEVENTH ISSUE	GL	02/16
F	SIXTH ISSUE	GL	01/16
E	FIFTH ISSUE	GL	12/15
D	FOURTH ISSUE	GL	10/15
Rev	Description	By	Date

Consultant

**ARUP**

Contract No. and Title:

Agreement No. CE 1/2013(CE)

Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery - Design and Construction

Drawing title

**Transect Routes at Sandy Ridge**

Drawing no.		Figure 9.2		Rev.	G
Drawn	Date	Checked	Approved		
GL	02/16	EL	ST		
Scale	AS SHOWN		Status	PRELIMINARY	

COPYRIGHT RESERVED








## **Contract No. CV/2017/02**

### **Development of Columbarium at Sandy Ridge Cemetery – Infrastructural Works at Man Kam To Road and Lin Ma Hang Road**

---

## **Monthly Report of Ecologically Sensitive Habitats Monitoring – Jan 2019**

Revision	0	
Date of issue	29 Jan 2019	
Prepared by	Alan Lam	
Reviewed by	Edwina Yeung	
Verified by	Desmond Tang	

## Table of Contents

<b>1</b>	<b>INTRODUCTION</b>	<b>4</b>
1.1	BACKGROUND	4
1.2	OBJECTIVE	4
<b>2</b>	<b>ECOLOGICALLY SENSITIVE HABITATS</b>	<b>5</b>
2.1	DESCRIPTION OF HABITATS	5
2.2	MONITORING MEASURES OF WETLAND HABITATS	6
2.3	MONITORING MEASURES OF NON-WETLAND HABITATS	6
<b>3</b>	<b>METHODOLOGY</b>	<b>7</b>
3.1	MAMMAL SURVEY	7
3.2	BIRD SURVEY	7
3.3	HERPETOFAUNA SURVEY	7
3.4	DRAGONFLY SURVEY	7
3.5	BUTTERFLY SURVEY	8
3.6	AQUATIC FAUNA SURVEY	8
<b>4</b>	<b>RESULT</b>	<b>9</b>
	<b>Appendix I – Transect Routes</b>	<b>14</b>

<b><u>LIST OF TABLE</u></b>	
Table 1	Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna
Table 2	Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna
Table 3	Survey Schedule
Table 4	Result of Avifauna in survey
Table 5	Result of reptile in survey
Table 6	Result of amphibian in survey
Table 7	Result of butterfly in survey
Table 8	Result of Odonate in survey
Table 9	Result of freshwater communities in survey

<b><u>LIST OF APPENDIX</u></b>	
Appendix I	Transect Routes



# **1 INTRODUCTION**

## **1.1 BACKGROUND**

- 1.1.1 The main objective of the proposed site formation and associated infrastructural works for development of columbarium, crematorium (C&C) and related facilities at Sandy Ridge Cemetery is to increase the public cremation services and supply of public niches to meet the future demand.
- 1.1.2 The project includes site formation and associated works for development of C&C facilities at the Sandy Ridge Cemetery, road works within Sandy Ridge Cemetery, widening a section of Lin Ma Hang Road (from 6.5m to 7.3m), provision of off-site pick-up/drop-off points for shuttle buses as well as barging point at Siu Lam, Lok On Pai.
- 1.1.3 The Environmental Impact Assessment (EIA) report, including Environmental Monitoring and Audit Manual (EM&A Manual), was approved with conditions on 8 August 2016 (Register No.: AEIAR-198/2016). EPD issued an Environmental Permit (EP) for the Project (EP-534/2017) on 7 April 2017, variation of EP (EP-534/2017/A) were issued on 24 December 2018.
- 1.1.4 According to Clause 3.1 of the EP (EP/534/2017/A), “The Permit Holder shall implement the EM&A programme in accordance with the procedures and requirements as set out in the EM&A Manual. Any changes to the programme shall be justified by the ET Leader and verified by the IEC as conforming to the information and requirements contained in the EM&A Manual before submission to the Director for approval”.
- 1.1.5 This Ecologically Sensitive Habitats Monitoring Methodology articulates the protocol of monitoring the ecology of concerned habitats as specified in EM&A Manual.

## **1.2 OBJECTIVE**

- 1.2.1 According to approved EIA report (AEIAR-198/2016), habitat types within project boundary comprise of watercourse, grassland, upland grassland, plantation, woodland and developed area. Natural habitats were of moderate ecological value in terms of species diversity, species rarity, species abundance, ecological linkage as well as nursery. Moreover, 0.3ha of wet woodland on the northern side of Sandy Ridge was deemed habitat with high ecological value. Four types of habitats were regarded as ecologically sensitive habitats, namely wet woodland, watercourses, upland grassland and woodland. Considering human disturbance in upcoming construction and operation phases, ecologically sensitive habitats shall be monitored in accordance with EM&A Manual.
- 1.2.2 The objective of ecologically sensitive habitats monitoring is to evaluate the effectiveness of measures to minimize impacts on concerned habitats from disturbance and pollution.

## 2 ECOLOGICALLY SENSITIVE HABITATS

### 2.1 DESCRIPTION OF HABITATS

- 2.1.1 In order to monitor the effectiveness of the measures to the minimise impact on ecologically sensitive habitats from disturbance and pollution, monthly monitoring during construction and operation phases is required as specified in EM&A Manual. Standard faunal transect and sampling surveys cover both wetland and non-wetland habitats:

Wetland habitats	Non-wetland habitats
Wet Woodland	Upland Grassland
Watercourses	Woodland

- 2.1.2 Wet woodland is small patch present on northwest of the project boundary, and is confined by the marsh area to the north and the secondary woodland to the east, south and south-west parts. A number of mature trees *Cleistocalyx nervosum* and *Acronychia pedunculata* form the tree canopy, with other self-sown shrubs (including *Psychotria asiatica*, *Ligustrum sinense* and *Glochidion lanceolarium*) and trees (*Aporosa dioica* and *Litsea monopetala*). Whilst botanically it comprises of naturally regenerated secondary woodland and ground level are a series of small braided streams and weep points which even during the dry season remain wet. This creates a rather uncommon habitat in Hong Kong offering suitable conditions for a good assemblage of common wetland species. The wet woodland provides a good assemblage of micro-habitats, which is relatively undisturbed and has good linkages to other natural habitats. Several species of conservation importance were recorded in EIA report from this habitat: East Asian Porcupine, Leopard Cat, Red Muntjac, Two-striped Grass Frog, Small Snakehead, *Somanniathelphusa zanklon*, Dancing Shadow-emerald.
- 2.1.3 Seasonal watercourse running west to east in the eastern part of the area inside the Project boundary is shallower in gradient than those running off the hillside. This seasonal watercourse is heavily vegetated with wetland-associated herbs including *Commelina diffusa*, *Polygonum chinense*, *Colocasia esculenta* and *Dracaena sanderiana*. A mature tree of *Aquilaria sinensis* was recorded at the bank of the seasonal watercourse to the west of the Sandy Ridge Cemetery Office. Seasonal watercourses are restricted to the steeper slopes within the project boundary and are characterised by being entirely dry for much of the dry season. However, endemic crab *S. zanklon* population is supported by ephemeral watercourses close to the project boundary.
- 2.1.4 Upland grassland is the major habitat within the project boundary. The semi-natural habitat is dominated by typical upland grassland species: fern *Dicranopteris pedata*, grass *Neyraudia reynaudiana*, *Miscanthus floridulus*, climbing vines *Smilax china*, *Smilax glabra*, and shrubs such as *Rhodomyrtus tomentosa*, *Breynia fruticosa* and *Helicteres angustifolia*. Approximately 30 flowering spikes of two orchid species Bamboo Orchid and Toothed Habenaria were recorded near the hill top in the northern part of this upland grassland. Golden-headed Cisticola, which is considered as Local Concern by Fellowes *et al.* (2002), was also recorded in upland grassland on Sandy Ridge, including a proved breeding record of fledged young in September 2013. In addition, numerous species of conservation interest

were recorded in EIA report, such as East Asian Porcupine, Leopard Cat, Red Muntjac, Great Swift, Tamil Grass Dart, Small Three-ring and Small Grass Yellow.

- 2.1.5 Scattered patches of woodland are present throughout the assessment area, with the largest contiguous block located immediately to the east of the project boundary. These woodlands are relatively young with single-layered of canopy dominants (~10 – 15m tall) including *A. dioica*, *Bridelia tomentosa*, *Cinnamomum burmannii*, *Daphniphyllum calycinum*, *Litsea glutinosa*, *Rhus succedanea*, and *Zanthoxylum avicennae*. Such areas comprise secondary woodland which is largely derived from natural regeneration and colonisation of trees as a result of seed dispersal by birds and/or bats. A mature tree of *A. sinensis* is located at the woodland edge at the central part of the Project according to EIA report.

## 2.2 MONITORING MEASURES OF WETLAND HABITATS

- 2.2.1 Wetland habitats include wet woodland and watercourses. Monitoring surveys using standardised quantitative methodology will be conducted at fixed points. For seasonal watercourse, survey shall be conducted whenever the habitat appears.
- 2.2.2 Measures to respond to decreases in numbers of aquatic fauna using the wetland habitats and action and limit levels to trigger these measures are detailed in Table 1.

Action Level	Response	Limit Level	Response
Reduction in taxa diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in taxa diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

Table 1 Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna

## 2.3 MONITORING MEASURES OF NON-WETLAND HABITATS

- 2.3.1 Non-wetland habitats consist of upland grassland and woodland. Monthly quantitative surveys of non-aquatic fauna will be conducted using standard route transect counts.
- 2.3.2 Measures to respond to decreases in numbers of non-aquatic fauna using the non-wetland habitats and action and limit levels to trigger these measures are detailed in Table 2.

Action Level	Response	Limit Level	Response
Reduction in species diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in species diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

Table 2 Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna

### 3 METHODOLOGY

The ecological survey includes all taxa being investigated in EIA report. Table 3 summarizes schedule of faunal surveys.

Month	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Mammals	√	√	√	√	√	√	√	√	√	√	√	√
Birds (day)	√	√	√	√	√	√	√	√	√	√	√	√
Birds (night)				√	√	√	√	√	√	√		
Herpetofauna				√	√	√	√	√	√	√		
Dragonflies			√	√	√	√	√	√	√	√		
Butterflies			√	√	√	√	√	√	√	√		
Aquatic fauna	√	√	√	√	√	√	√	√	√	√	√	√

Table 3 Survey Schedule

#### 3.1 MAMMAL SURVEY

- 3.1.1 Mammal surveys will be conducted along the transects shown in Appendix 1 during both daytime and night time periods. Along with direct observations, other field signs, such as scats and tracks, will be searched and recorded if present.

#### 3.2 BIRD SURVEY

- 3.2.1 Bird surveys will be conducted along the transects shown in Appendix 1 during the surveys, species and their vocalizing individuals recorded will be enumerated and recorded according to the habitat(s) they are utilising.

#### 3.3 HERPETOFAUNA SURVEY

- 3.3.1 Reptile and amphibian surveys will be conducted along transects shown in Appendix 1 during surveys careful searches of appropriate microhabitats and refugia for reptiles and their vocalizing individuals will be undertaken and all reptiles observed will be identified and counted.

#### 3.4 DRAGONFLY SURVEY

- 3.4.1 Dragonfly surveys will be conducted along transects shown in Appendix 1 during surveys all dragonflies seen will be identified and counted as accurately as possible.

### **3.5 BUTTERFLY SURVEY**

- 3.5.1 Butterfly surveys will be conducted along transects shown in Appendix 1 during surveys all dragonflies seen will be identified and counted as accurately as possible.

### **3.6 AQUATIC FAUNA SURVEY**

- 3.6.1 Freshwater fishes and macro-invertebrates will be recorded by direct observation. All species trapped/recorded will be enumerated and identified (to the lowest taxonomic level possible), and the species of conservation importance photographed.



## 4 RESULT

This monitoring survey started on 15<sup>th</sup> January 2019. A rainy day. The day survey covering wetland and non-wetland areas. The survey was conducted by transect and fixed point. All species seen will be identified and counted as accurately as possible.

- Mammal  
There was no mammal recorded in the monitoring area.
- Bird  
There were total of 32 bird individuals from 15 species recorded during the survey.
- Herpetofauna  
There was no reptile recorded in the monitoring area.  
There was no amphibian recorded in the monitoring area.
- Dragonfly  
There was a total of 1 odonate individual from 1 species.
- Butterfly  
There was no butterfly recorded in the monitoring area.
- Freshwater communities  
There were two species of freshwater fish were recorded

**Figure 1**  
**The woodland in monitoring area.**



**Figure 2**  
*Copera marginipes* Yellow Featherlegs 黃狹扇蟋



**Table 4 Result of Avifauna in survey**

Scientific Name	English Name	Chinese Name	Conservation Status	15-Jan-2019	
				Non-wetland	Wetland
<i>Spilopelia chinensis</i>	Spotted Dove	珠頸斑鳩		1	3
<i>Pericrocotus speciosus</i>	Scarlet Minivet	赤紅山椒鳥			1
<i>Parus cinereus</i>	Cinereous Tit	蒼背山雀		3	
<i>Pycnonotus jocosus</i>	Red-whiskered Bulbul	紅耳鸛		2	
<i>Pycnonotus sinensis</i>	Chinese Bulbul	白頭鸛		2	
<i>Phylloscopus inornatus</i>	Yellow-browed Warbler	黃眉柳鶯		1	
<i>Prinia flaviventris</i>	Yellow-bellied Prinia	黃腹鷦鶯		1	1
<i>Prinia inornata</i>	Plain Prinia	純色鷦鶯			1
<i>Orthotomus sutorius</i>	Common Tailorbird	長尾縫葉鶯		1	
<i>Garrulax perspicillatus</i>	Masked Laughingthrush	黑臉噪鵲		4	4

<i>Zosterops japonicus</i>	Japanese White-eye	暗綠繡眼鳥		3	
<i>Myophonus caeruleus</i>	Blue Whistling Thrush	紫嘯鶇		1	
<i>Phoenicurus aureus</i>	Daurian Redstart	北紅尾鴝		1	
<i>Saxicola stejnegeri</i>	Stejneger's Stonechat	黑喉石(即鳥)			1
<i>Anthus godlewskii</i>	Olive-backed Pipit	樹鵲		1	

**Table 5 Result of reptile in survey**

Table 3 Result of Reptile in Survey				
Scientific Name	Common Name	Chinese Name	15-Jan-2019	
			Non-wetland	Wetland
N/A				

**Table 6 Result of amphibian in survey**

Table 3 Result of amphibian in survey					
Scientific Name	Common Name	Chinese Name	Conservation Status	15-Jan-2019	
				Non-wetland	Wetland
N/A					

**Table 7 Result of butterfly in survey**

Table 1. Result of butterfly in survey				
Scientific Name	Common Name	Chinese Name	15-Jan-2019	
			Non-wetland	Wetland
N/A				

**Table 8 Result of Odonate in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	15-Jan-2019	
				Non-wetland	Wetland
<i>Copera marginipes</i>	Yellow Featherlegs	黃狹扇尾			1

**Table 9 Result of freshwater communities in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	15-Jan-2019
<i>Gambusia affinis</i>	Mosquito fish	食蚊魚		+
<i>Puntius semifasciolatus</i>	Chinese Barb	五線無鬚魮		+

+: Species appear but uncountable.



## **Appendix I – Transect Routes**




DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
© THE ARUP & PARTNERS HONG KONG LIMITED.

VSRs	TYPE	ID	KEY VSRs
R1			RESIDENTS OF VILLAGES ALONG MAN KAM TO ROAD
R2			RESIDENTS OF SAN UK LING
R3			RESIDENTS OF LO WU VILLAGE
R4			RESIDENTS OF MUK WU
R5			RESIDENTS OF VILLAGES ALONG FOOTHILL OF TAI SHEK MO
R6			RESIDENTS OF MUK WU NGA YIU
G1C1			WORKERS AT BORDER DISTRICT POLICE HEADQUARTER
G1C2			WORKERS AT WATER TREATMENT WORKS
G1C3			WORKERS AT MAN KAM TO PUMPING STATION
G1C4			WORKERS AT LO WU CORRECTIONAL INSTITUTION
T1			TRAVELLERS ALONG EAST RAIL LINE
T2			TRAVELLERS ALONG MAN KAM TO ROAD
I1			WORKERS AT STORAGE AREA ALONG MAN KAM TO ROAD



SHENZHEN SH1

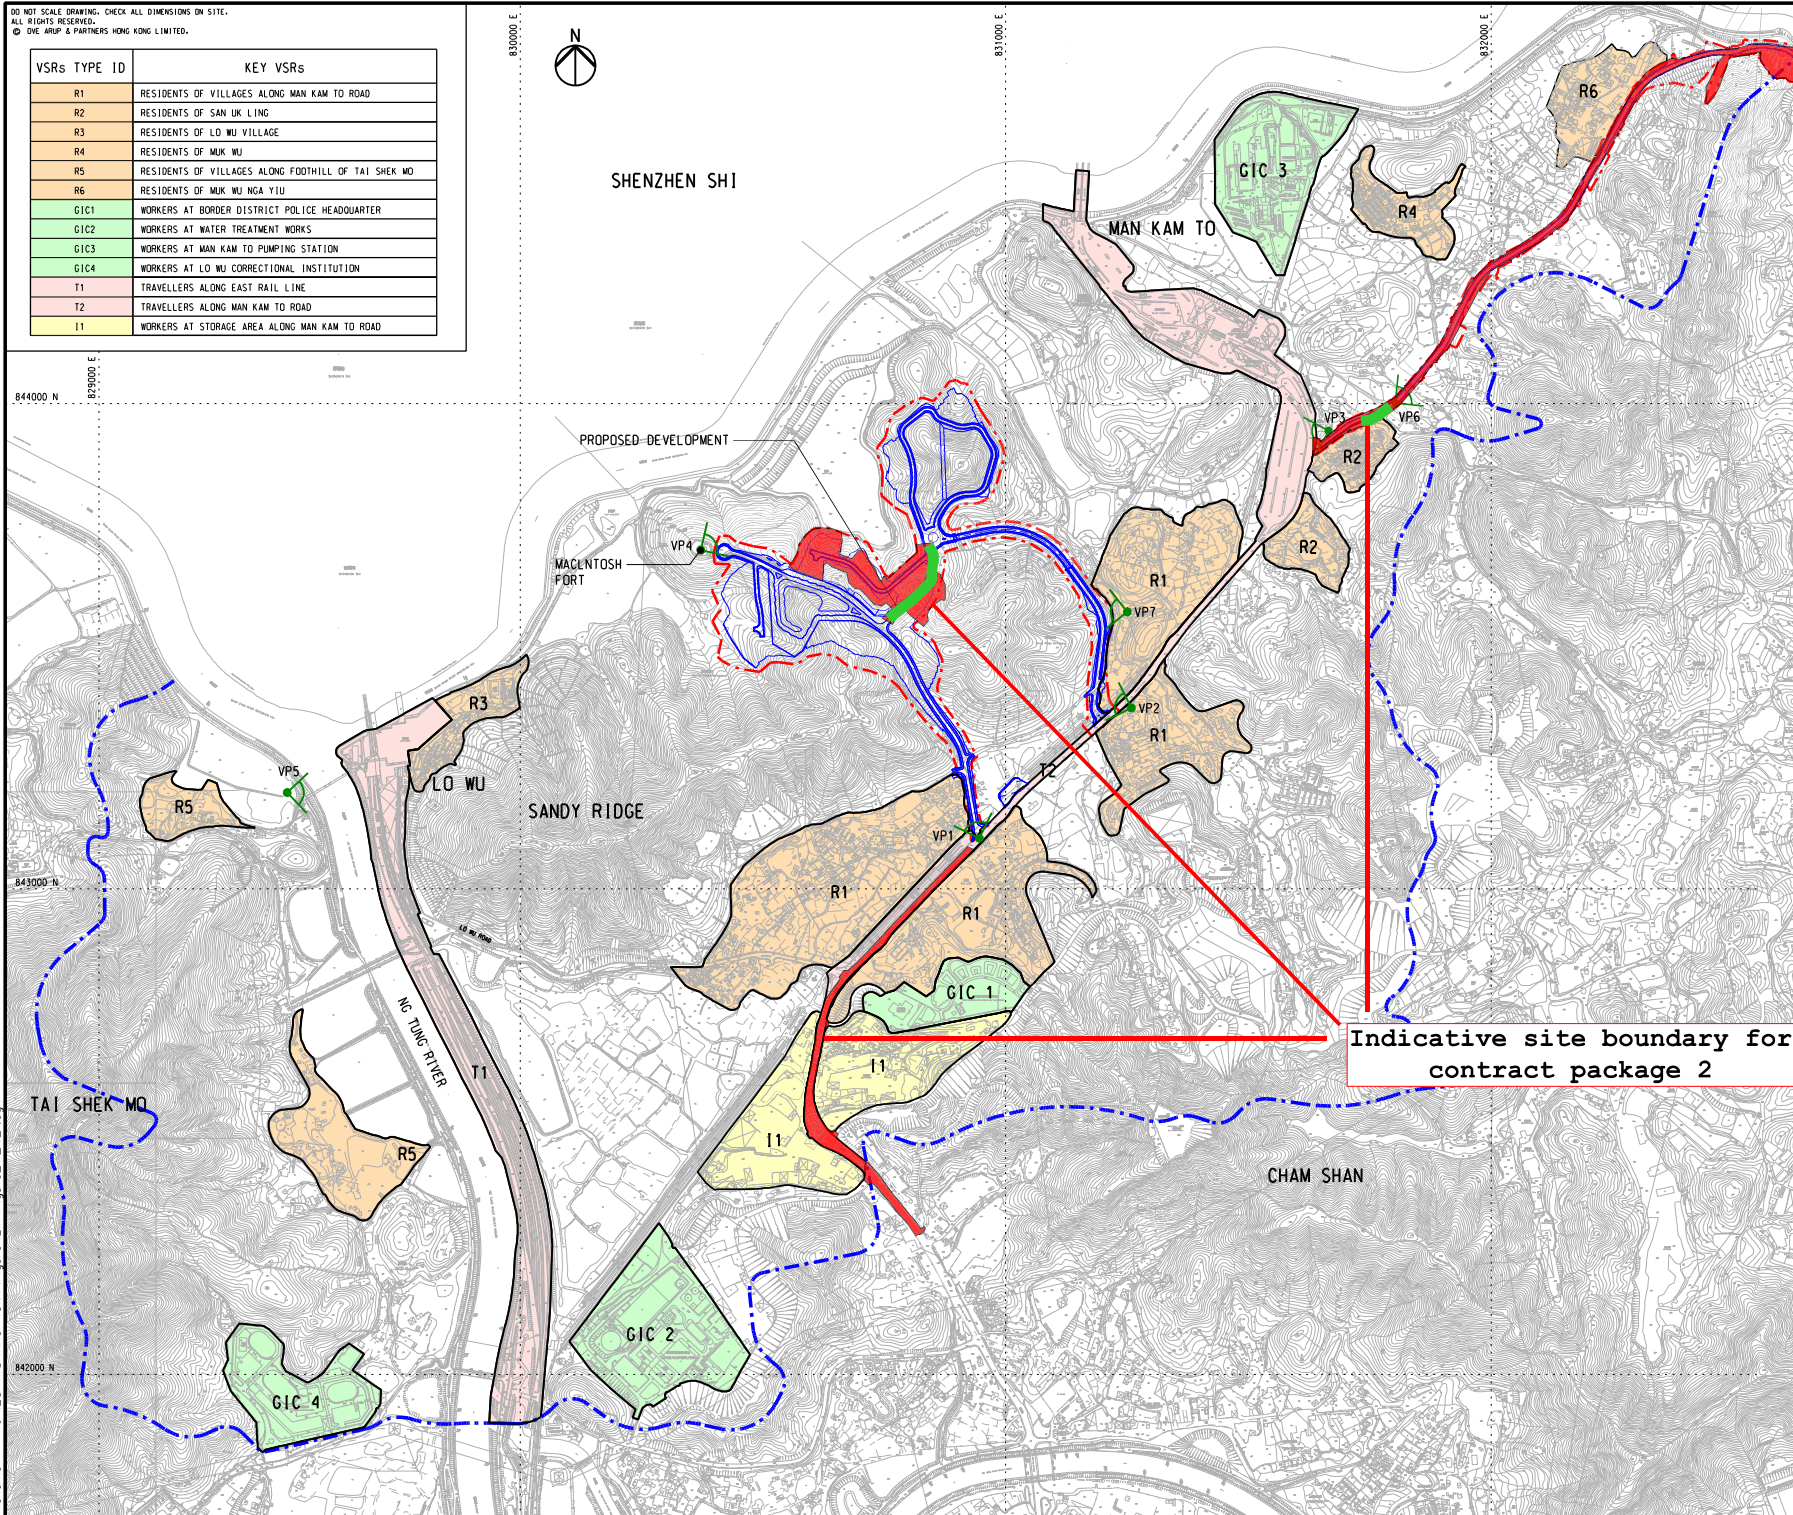

#### LEGEND:

- PROJECT BOUNDARY
- ZONE OF VISUAL ENVELOPE
- VANTAGE POINTS
- Transect of C2

Rev	Description	By	Date
A	REVISED SUBMISSION	WM	01/15

Consultant  
**ARUP**

Contract No. and Title:  
**Agreement No. CE 1/2013(CE)**  
**Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery - Design and Construction**

Drawing title  
**VISUAL ENVELOPE LOCATIONS OF VISUAL SENSITIVE RECEIVERS (VSRs) AND VANTAGE POINT (VPs)**

Drawing no.	FIGURE 11.4.1	Rev.	A
Drawn	Date	Checked	Approved
WM	08/13	PC	DL
Scale	N.T.S.	Status	PRELIMINARY

COPYRIGHT RESERVED  
 **土木工程拓展署**  
Civil Engineering and Development Department



## **Appendix L**

### **Landscape & Visual Inspection Checklist**

**Contract No. CV/2016/10**

**Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery**

**Landscape and Visual Impact Assessment Checklist for Site Audit**

**Date/ Time:** 25/01/2019 15:00 **Weather:** Fine/ Overcast/ Rain/ Windy

Item	Mitigation Measures	Implementation			Actions/ Remarks
		Yes	No	N/A	
<b>1</b>	<b>Landscape and Visual</b>				
1.1	Is the construction period become shortened?			✓	Under review.
1.2	Is the work site confined within site boundaries and without encroaching into the landscape resources offsite?	✓			
1.3	Is the site kept clean and tidy (E.g. storage of materials, location and appearance of site accommodation being well positioned)	✓			
1.4	Is the construction site screened properly by hoardings or noise barriers in visually unobstructed colours?	✓			
1.5	Is the erosion and dust control for exposed soil well performed during excavation work? (E.g. Exposed soil shall be covered or “camouflaged” and watered frequently. Areas that are expected to be left with bare soil for a long period of time should be hydro seeded and / or covered with suitable protective fabrics.)	✓			
1.6	Are the woodland, plantation and other vegetation being protected and preserved in accordance with DEVB TC(W) No. 07/2015(E.g. Set up Tree Protection Zone)?	✓			
1.7	Are the trees which are in direct conflict with the development proposal being transplanted as far as practical in accordance with and DEVB TC(W) No. 07/2015?	✓			
1.8	Are compensatory planting for trees being provided to compensate the trees felled in accordance with DEVB TC(W) No. 07/2015?			✓	Tree planting works have not yet been commenced.
1.9	Are precautionary control measures to protect natural streams and rivers from adverse impact being implemented in accordance with ETWWB TCW No. 5/2005? (E.g. Construction debris and spoil should be covered up and properly disposed)	✓			
1.10	Is light and glare control such as hooding being implemented during construction and operation to minimize light pollution and night time glare? (E.g. All security floodlights for construction sites should be equipped with adjustable shield, frosted diffusers and reflective covers)	✓			

## Summary / Remarks:

### Follow up actions taken by Contractor for previous comments:

1. Tree protection zones were provided for retained/transplant trees and some of the tree protection barrier was damaged or missing.

### New observation:

1. T2928 was transplanted to designated receptor site.

### Reminders:

1. Contractor is reminded to prevent the construction material pile within TPZ and ensure no works is allowed within the TPZ.
2. Contractor is reminded to provide proper maintenance for transplanted tree (T2928) according to approved method statement.

### Photo Record:

**Fig A.**



TPZ is missing

**Fig B.**



TPZ for retain trees

**Fig C.**



Debris and fallen trees near retain trees

**Fig D.**



General view



**Fig E.**



Transplanted tree (T2928)\_Wholeview

**Fig F.**



Transplanted tree (T2928)\_Root zone

**Contract No. CV/2017/02**

**Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery**

**Development of Columbarium at Sandy Ridge Cemetery –**

**Infrastructural Works at Man Kam To Road and Lin Ma Hang Road**

**Landscape and Visual Impact Assessment Checklist for Site Audit**



**Date/ Time: 25/01/2019 16:00 Weather: Fine/ Overcast/ Rain/ Windy**

Item	Mitigation Measures	Implementation			Actions/ Remarks
		Yes	No	N/A	
<b>1</b>	<b>Landscape and Visual</b>				
1.1	Is the construction period become shortened?			✓	Under review
1.2	Is the work site confined within site boundaries and without encroaching into the landscape resources offsite?	✓			
1.3	Is the site kept clean and tidy (E.g. storage of materials, location and appearance of site accommodation being well positioned)	✓			
1.4	Is the construction site screened properly by hoardings or noise barriers in visually unobstructed colours?	✓			
1.5	Is the erosion and dust control for exposed soil well performed during excavation work? (E.g. Exposed soil shall be covered or “camouflaged” and watered frequently. Areas that are expected to be left with bare soil for a long period of time should be hydro seeded and / or covered with suitable protective fabrics.)			✓	
1.6	Are the woodland, plantation and other vegetation being protected and preserved in accordance with DEVB TC(W) No. 07/2015(E.g. Set up Tree Protection Zone)?			✓	
1.7	Are the trees which are in direct conflict with the development proposal being transplanted as far as practical in accordance with and DEVB TC(W) No. 07/2015?	✓			
1.8	Are compensatory planting for trees being provided to compensate the trees felled in accordance with DEVB TC(W) No. 07/2015?			✓	
1.9	Are precautionary control measures to protect natural streams and rivers from adverse impact being implemented in accordance with ETWWB TCW No. 5/2005? (E.g. Construction debris and spoil should be covered up and properly disposed)			✓	
1.10	Is light and glare control such as hooding being implemented during construction and operation to minimize light pollution and night time glare? (E.g. All security floodlights for construction sites should be equipped with adjustable shield, frosted diffusers and reflective covers)			✓	

**Summary / Remarks:**

**Follow up actions taken by Contractor for previous comments:**

N/A

**New Observation:**

N/A

**Reminders:**

N/A

**Photo Record:**

**Fig A.**



General view (1)

**Fig B.**



General view (2)

**Fig C.**



General view (3)

**Signature:**

		Signature	Date
Recorded by	Registered Landscape Architect		 31 January 2019
Checked by	Environmental Team Leader		14 Feb 2019
	Independent Environmental Checker		14 Feb 2019



## **Appendix M**

### **Monthly Summary Waste Flow Table**



## Monthly Summary Waste Flow Table for Jan 2019

Department: Civil Engineering and Development Department      Contract No.: CV/2016/10  
 Contract Title: Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery  
 Commencement Date: 15-Dec-2017      Estimated completion Date 22-Dec-2023      Estimated Contract Sum: 780M

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m <sup>3</sup> )
Jan	44.444	0.000	10.431	0.000	34.013	0.000	0.000	0.000	0.000	0.332	0.088
Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
May	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
June	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
<b>Sub-total</b>	<b>44.444</b>	<b>0.000</b>	<b>10.431</b>	<b>0.000</b>	<b>34.013</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.332</b>	<b>0.088</b>
July	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Aug	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Sept	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Oct	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Nov	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Dec	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
<b>Total</b>	<b>44.444</b>	<b>0.000</b>	<b>10.431</b>	<b>0.000</b>	<b>34.013</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.332</b>	<b>0.088</b>

- Notes:
- (1) The waste flow table should cover the whole construction period of the Contract.
  - (2) The original estimates of the C&D materials should be the estimates at contract commencement and should not be altered during construction.
  - (3) Inert C&D materials that are specified in the Contract to be imported for use at the Site shall be separately indicated.
  - (4) The yearly estimates of the C&D materials should be updated as appropriate taking into account the latest works programme etc.
  - (5) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
  - (6) Broken concrete for recycling into aggregates.

## Monthly Summary Waste Flow Table for December 2018 (Revised)

Department: Civil Engineering and Development Department      Contract No.: CV/2016/10  
 Contract Title: Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery  
 Commencement Date: 15-Dec-2017      Estimated completion Date 22-Dec-2023      Estimated Contract Sum: 780M

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m <sup>3</sup> )
Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.134
Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.127
Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.005
Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.071
May	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.248
June	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.019
<b>Sub-total</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.604</b>
July	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.064
Aug	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	2.094
Sept	22.980	0.000	0.991	0.000	21.989	0.000	0.000	0.000	0.000	0.000	0.075
Oct	46.863	0.000	2.982	0.000	43.881	0.000	0.000	0.000	0.000	0.000	0.298
Nov	47.615	0.000	9.225	0.000	38.390	0.000	0.000	0.000	0.000	0.000	0.841
Dec	39.321	0.000	8.859	0.000	30.462	0.000	0.000	0.000	0.000	0.000	0.077
<b>Total</b>	<b>156.779</b>	<b>0.000</b>	<b>22.057</b>	<b>0.000</b>	<b>134.722</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>4.053</b>

- Notes:
- (1) The waste flow table should cover the whole construction period of the Contract.
  - (2) The original estimates of the C&D materials should be the estimates at contract commencement and should not be altered during construction.
  - (3) Inert C&D materials that are specified in the Contract to be imported for use at the Site shall be separately indicated.
  - (4) The yearly estimates of the C&D materials should be updated as appropriate taking into account the latest works programme etc.
  - (5) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
  - (6) Broken concrete for recycling into aggregates.

Name of Department: CEDD

## Monthly Summary Waste Flow Table for 2019

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m <sup>3</sup> )
JAN	0.000	13.050	13.050	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
FEB	--	--	--	--	--	--	--	--	--	--	--
MAR	--	--	--	--	--	--	--	--	--	--	--
APRIL	--	--	--	--	--	--	--	--	--	--	--
MAY	--	--	--	--	--	--	--	--	--	--	--
JUN	--	--	--	--	--	--	--	--	--	--	--
Sub Total	0.000	13.050	13.050	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
JUL	--	--	--	--	--	--	--	--	--	--	--
AUG	--	--	--	--	--	--	--	--	--	--	--
SEP	--	--	--	--	--	--	--	--	--	--	--
OCT	--	--	--	--	--	--	--	--	--	--	--
NOV	--	--	--	--	--	--	--	--	--	--	--
DEC	--	--	--	--	--	--	--	--	--	--	--
Total	0.000	13.050	13.050	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000

Notes:

## **Appendix N**

### **Implementation Schedule for Environmental Mitigation Measures (ISEMM)**

## Environmental Mitigation Implementation Schedule – Sandy Ridge

**Note:** Chapters 1 to 3 of the EIA report present the background information of the Project, identified concurrent projects, objectives and scope for various environmental aspects, and description on alternative options and construction description. Chapters 4 to 12 of the EIA report present the EIA findings and mitigation measures are described below with cross-reference to the EIA report. Chapters 13 to 15 describe the environmental monitoring requirements and conclusion.

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
<b>Common Mitigation Measures (Applicable to ALL Project Components, including DPs and Non-DPS)</b>						
<b>Construction Dust Impact</b>						
S4.4.5.2	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	Minimise dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>• APCO</li> <li>• To control the dust impact to meet HKAQO and TM-EIAO criteria</li> </ul>
S4.4.5.3	Water spraying every hour for all active works area.	Minimise dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>• APCO</li> <li>• To control the dust impact to meet HKAQO and TM-EIAO criteria</li> </ul>
S4.4.5.2	<ul style="list-style-type: none"> <li>• Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading;</li> <li>• Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads;</li> <li>• A stockpile of dusty material should not be extended beyond the pedestrian barriers, fencing or traffic cones;</li> <li>• The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle;</li> <li>• Vehicle wheel washing facilities should be provided at each construction</li> </ul>	Minimise dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>• APCO</li> <li>• To control the dust impact to meet HKAQO and TM-EIAO criteria</li> </ul>



## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<p>site exit. Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels;</p> <ul style="list-style-type: none"> <li>• When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period;</li> <li>• The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials;</li> <li>• Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously;</li> <li>• Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet;</li> <li>• Any skip hoist for material transport should be totally enclosed by impervious sheeting;</li> <li>• Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;</li> <li>• Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system;</li> <li>• Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shortcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.</li> </ul>					

### Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S4.4.5.1	Implement regular dust monitoring under EM&A programme during the construction stage.	Monitoring of dust impact	Contractor	Selected representative dust monitoring station	Construction phase	• TM-EIAO
S4.4.5.3	<ul style="list-style-type: none"> <li>All road surface within the barging facilities will be paved.</li> <li>Dust enclosures will be provided for the loading ramp, installation of 3-sided screen with top cover and the provision of water sprays at the discharge point would be provided.</li> <li>Vehicles will be required to pass through designated wheel wash facilities.</li> <li>Continuous water spray at the loading point.</li> </ul>	Minimise dust impact at the nearby sensitive receivers	Contractor	Barging point at Siu Lam	Construction phase	• TM-EIAO

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
<b>Construction Noise</b>						
S5.5.5.3	<p>Implement the following good site management practices:</p> <ul style="list-style-type: none"> <li>only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme;</li> <li>machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;</li> <li>plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs;</li> <li>silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works;</li> <li>mobile plant should be sited as far away from NSRs as possible and practicable;</li> <li>material stockpiles, mobile container site office and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities.</li> </ul>	Control construction noise	Contractor	All construction sites	Construction phase	• Annex 5, TM-EIAO
S5.5.5.5	Adopt quiet plants during the construction of viaduct, widening of Sha Ling Road, construction of platform for crematorium and widening of Lin Ma Hang Road. The quiet plants should be made reference to the PME listed in the TM or the QPME/ other commonly used PME listed in EPD web pages or taken from BS5228: Part 1: 2009 Noise Control on Construction and Open Sites as far as possible.	Reduce the noise levels of plant items	Contractor	Works area for construction of viaduct, widening of Sha Ling Road, construction of platform for crematorium and widening of Lin Ma Hang Road	Construction phase	• Annex 5, TM-EIAO

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S5.5.5.6	Install temporary noise barriers (in the form of site hoardings, approx. 2.4m high) located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level zone of NSRs through partial screening.	Contractor	All construction sites where practicable	Construction phase	• Annex 5, TM-EIAO
S5.5.5.7 – S5.5.5.12	Install movable noise barriers (typical design is wooden framed barrier with a small-cantilevered upper portion of superficial density no less than 7kg/m <sup>2</sup> on a skid footing with 25mm thick internal sound absorptive lining), acoustic mat or full enclosure, screen the noisy plants including air compressors, generators etc.	Screen the noisy plant items to be used at all construction sites	Contractor	All construction sites where practicable	Construction phase	• Annex 5, TM-EIAO
S5.5.5.13	Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction noise	Contractor	All construction sites where practicable	Construction phase	• Annex 5, TM-EIAO
S13.2.1.1 – S13.4.1.2	Implement a noise monitoring under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected representative noise monitoring station	Construction phase	• TM-EIAO
<b>Operational Noise (Road Traffic Noise)</b>						
S5.6.6.4	<p>Provide a series of noise mitigation measures including absorptive noise barriers and low noise road surfacing materials along Lin Ma Hang Road and Sha Ling Road before operation of the proposed project for existing and planned representative NSRs. Locations of noise mitigation measures are stated as following:</p> <p><i>For existing representative NSRs</i></p> <ul style="list-style-type: none"> <li>• Approx. 12m of absorptive noise barrier 2.5m above road level along Sha Ling Road (MM1);</li> <li>• Approx. 92m of absorptive noise barrier 2.5m above road level along Sha Ling Road (MM2);</li> </ul>	Reduce operation noise from road traffic	Contractor	Refer to <b>Figures 5.6.9 – 5.6.13</b> of the EIA Report	Prior to operation of the Project for existing representative NSRs. While for barriers to protect planned representative NSRs, it should be constructed before intake of planned representative NSRs.	• TM-EIAO

### Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<ul style="list-style-type: none"> <li>Approx. 28m of absorptive noise barrier 3m above road level along Project Road near Sha Ling Road (MM3);</li> <li>Approx. 51m of absorptive noise barrier 3m above road level along Project Road near Sha Ling Road (MM4);</li> <li>Approx. 25m of absorptive noise barrier 4m above road level along Lin Ma Hang Road near San Uk Ling (MM5);</li> <li>Approx. 21m of absorptive noise barrier 4m above road level along Lin Ma Hang Road near San Uk Ling (MM6);</li> <li>Approx. 14m of absorptive noise barrier 4m above road level along Lin Ma Hang Road near San Uk Ling (MM7);</li> <li>Approx. 18m of absorptive noise barrier 3m above road level along Lin Ma Hang Road near San Uk Ling (MM8);</li> <li>Approx. 42m of absorptive noise barrier 3m above road level along temporary pullover space opposite San Uk Ling (MM9);</li> <li>Approx. 93m of absorptive noise barrier 3m above road level along Lin Ma Hang Road opposite San Uk Ling (MM10);</li> <li>Approx. 185m of low noise surfacing materials along Lin Ma Hang Road near San Uk Ling (MM11);</li> </ul> <p><i>For planned representative NSRs</i></p> <ul style="list-style-type: none"> <li>Approx. 36m of absorptive noise barrier 5m above road level along Lin Ma Hang Road near Muk Wu Nga Yiu (MM12);</li> <li>Approx. 47m of absorptive noise barrier 5m above road level along Lin Ma Hang Road near Muk Wu Nga Yiu (MM13);</li> <li>Approx. 31m of absorptive noise barrier 5m above road level along Lin Ma Hang Road near Muk Wu Nga Yiu (MM14);</li> <li>Approx. 31m of absorptive noise barrier 5m above road level along Lin Ma Hang Road near Muk Wu Nga Yiu (MM15);</li> <li>Approx. 41m of absorptive noise barrier 5m above road level along Lin Ma Hang Road near Muk Wu Nga Yiu (MM16);</li> </ul>					



### Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<ul style="list-style-type: none"> <li>Approx. 340m of low noise surfacing materials along Lin Ma Hang Road near Muk Wu Nga Yiu (MM17).</li> </ul>					

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
<b>Water Quality (Construction Phase)</b>						
S6.4.4.1 – S6.4.4.3	<p>In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN1/94), construction phase mitigation measures shall include the following:</p> <p><u>General Site Operation</u></p> <ul style="list-style-type: none"> <li>At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction;</li> <li>Diversion of natural stormwater should be avoided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimise polluted runoff. Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m<sup>3</sup> capacities, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications where the influent is pumped;</li> <li>The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a site/sediment trap. The sediment/silt traps should be incorporated in the permanent drainage channels to enhance deposition rates;</li> <li>The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94. The detailed design of</li> </ul>	To minimise water quality impact from construction site runoff and general construction activities	Contractor	All construction sites where applicable	Construction phase	<ul style="list-style-type: none"> <li>Water Pollution Control Ordinance</li> <li>ProPECC PN1/94</li> <li>TM-EIAO</li> <li>TM-DSS</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<p>the sand/silt traps shall be undertaken by the contractor prior to the commencement of construction;</p> <ul style="list-style-type: none"> <li>Construction works should be programmed to minimise surface excavation works during the rainy seasons (April to September). All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means;</li> <li>If the excavation of trenches in wet periods is necessary, it should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities;</li> <li>All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas;</li> <li>All open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m<sup>3</sup> should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system;</li> <li>Manholes (including newly constructed ones) should always be covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers;</li> <li>Precautions be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes;</li> </ul>					

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<ul style="list-style-type: none"> <li>All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains;</li> <li>Oil interceptors should be provided in the drainage system downstream of any oil/fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain;</li> <li>Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts;</li> <li>All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby;</li> <li>Regular environmental audit on the construction site should be carried out in order to prevent any malpractices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the water bodies, marsh and ponds;</li> <li>Adopt best management practices.</li> </ul>					
S6.4.4.4 – S6.4.4.5	<p><u>Sewage from workforce</u></p> <ul style="list-style-type: none"> <li>Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance;</li> </ul>	To minimise water quality from sewage effluent	Contractor	All construction sites where practicable	Construction phase	<ul style="list-style-type: none"> <li>Water Pollution Control Ordinance</li> <li>TM-DSS</li> </ul>

### Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<ul style="list-style-type: none"> <li>Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project;</li> <li>Regular environmental audit on the construction site should be conducted in order to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site.</li> </ul>					
S6.4.4.6	<p><u>Operation of Barging Point at Siu Lam</u></p> <ul style="list-style-type: none"> <li>All barges should be fitted with tight bottom seals to prevent leakage of materials during transport;</li> <li>Barges or hoppers should not be filled to a level that will cause overflow of materials or polluted water during loading or transportation;</li> <li>All vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; and</li> <li>Loading of barges and hoppers should be controlled to prevent splashing of material into the surrounding water.</li> <li>Mitigation measures for land-based activities as outlined in Section 6.4.4 should be applied to minimise water quality impacts from site runoff and open stockpile spoils at the proposed barging facilities where appropriate.</li> </ul>	To minimise water quality from operation of barging point at Siu Lam	Contractor	All construction sites where practicable	Construction phase	<ul style="list-style-type: none"> <li>Water Pollution Control Ordinance</li> <li>TM-DSS</li> </ul>
<b>Water Quality (Operational Phase)</b>						
S6.5.4.1 – S6.5.4.6	<p>The following mitigation measures during operational phase are recommended:</p> <ul style="list-style-type: none"> <li>Sewage and wastewater discharge should be connected to foul sewerage system;</li> <li>Proper drainage systems with silt traps and oil interceptors should be installed;</li> </ul>	To minimise the road runoff, wastewater discharge and erosion of seasonal watercourse during the operational phase	Highways Department / Contractors	Whole alignment	Construction / Operational Phase	<ul style="list-style-type: none"> <li>Water Pollution Control Ordinance</li> <li>TM-DSS</li> </ul>



### Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<ul style="list-style-type: none"> <li>• The design of road gullies with silt traps should be incorporated especially for the catchment leading to the existing wet woodland area located at the north of the site;</li> <li>• The silt traps and oil interceptors should be cleaned and maintained regularly, especially before peak seasons of the visitors in Ching Ming Festival and Chung Yeung Festival;</li> <li>• Energy dissipaters should be installed at the seasonally wet watercourses to reduce the magnitude of the first flush in order to minimise the erosion impact to the wet woodland.</li> </ul>					

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
<b>Waste Management (Construction Waste)</b>						
S7.3.3.8	<u>Construction &amp; Demolition Material Management Plan (C&amp;DMMP)</u> <ul style="list-style-type: none"> <li>A C&amp;DMMP shall be submitted to the Public Fill Committee for approval in the case of C&amp;D materials disposal exceeding 50,000m<sup>3</sup>.</li> </ul>	To enhance the management of construction and demolition (C&D) material including rock in public works projects	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Project Administrative Handbook for Civil Engineering Works, 2012 Edition</li> </ul>
S7.3.4.2	<u>Good Site Practice</u> <p>The following good site practices are recommended throughout the construction activities:</p> <ul style="list-style-type: none"> <li>nomination of an approved personnel, such as a site manager, to be responsible for the implementation of good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site;</li> <li>training of site personnel in site cleanliness, appropriate waste management procedures and concepts of waste reduction, reuse and recycling;</li> <li>provision of sufficient waste disposal points and regular collection for disposal;</li> <li>appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers;</li> <li>regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors;</li> <li>a Waste Management Plan (WMP) should be prepared by the contractor and submitted to the Engineer for approval.</li> </ul>	Minimise waste generation during construction	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Waste Disposal Ordinance</li> </ul>
S7.3.4.3	<u>Waste Reduction Measures</u> <p>Waste reduction is best achieved at the planning and design phase, as well as by ensuring the implementation of good site practices. The following recommendations are proposed to achieve reduction:</p> <ul style="list-style-type: none"> <li>segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> </ul>	Reduce waste generation	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Waste Disposal Ordinance</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<ul style="list-style-type: none"> <li>proper storage and site practices to minimise the potential for damage and contamination of construction materials;</li> <li>plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste;</li> <li>sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable portions (i.e. soil, broken concrete, metal etc.);</li> <li>provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling.</li> </ul>					
S7.3.4.5	<p><u>Storage of Waste</u></p> <p>The following recommendation should be implemented to minimise the impacts:</p> <ul style="list-style-type: none"> <li>non-inert C&amp;D materials such as soil should be handled and stored well to ensure secure containment;</li> <li>stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away;</li> <li>different locations should be designated to stockpile each material to enhance reuse;</li> </ul>	Good site practice to minimise the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Land (Miscellaneous Provisions) Ordinance</li> <li>Waste Disposal Ordinance</li> <li>ETWB TCW No. 19/2005</li> </ul>
S7.3.4.6	<p><u>Collection and Transportation of Waste</u></p> <p>The following recommendation should be implemented to minimise the impacts:</p> <ul style="list-style-type: none"> <li>remove waste in timely manner;</li> <li>employ the trucks with cover or enclosed containers for waste transportation;</li> <li>obtain relevant waste disposal permits from the appropriate authorities; and</li> <li>disposal of waste should be done at licensed waste disposal facilities.</li> </ul>	Minimise waste impacts from storage	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Waste Disposal Ordinance</li> </ul>
S7.3.4.8 – S7.3.4.15	<p><u>Excavated and C&amp;D Materials</u></p> <p>Wherever practicable, C&amp;D materials should be segregated from other wastes to avoid contamination and ensure acceptability at public filling areas or reclamation sites. The following mitigation measures should be implemented in handling the excavated and C&amp;D materials:</p> <ul style="list-style-type: none"> <li>maintain temporary stockpiles and reuse excavated fill material for</li> </ul>	Minimise waste impacts from excavated and C&D materials	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Land (Miscellaneous Provisions) Ordinance</li> <li>Waste Disposal Ordinance</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<p>backfilling;</p> <ul style="list-style-type: none"> <li>carry out on-site sorting;</li> <li>make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; and</li> <li>implement a recording system for the amount of waste generated, recycled and disposed of for checking.</li> </ul> <p>The recommended C&amp;D materials handling should include:</p> <ul style="list-style-type: none"> <li>On-site sorting of C&amp;D materials;</li> <li>Reuse of C&amp;D materials; and</li> <li>Use of Standard Formwork and Planning of Construction Materials purchasing.</li> </ul>					<ul style="list-style-type: none"> <li>ETWB TCW No. 19/2005</li> <li>Project Administrative Handbook for Civil Engineering Works, 2012 Edition</li> </ul>
S7.3.4.17 – S7.3.4.18	<p><u>Chemical Waste</u></p> <p>If chemical wastes are produced at the construction site, the Contractors should register with EPD as chemical waste producer. Chemical wastes should be stored in appropriate containers and collected by a licensed chemical waste Contractor. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.</p>	Control the chemical waste and ensure proper storage, handling and disposal.	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Waste Disposal (Chemical Waste) (General) Regulation</li> <li>Code of Practice on the Packaging, Labelling and Storage of Chemical Waste</li> </ul>
S7.3.4.19	<p><u>General Refuse</u></p> <ul style="list-style-type: none"> <li>General refuse should be stored in enclosed bins separately from construction and chemical wastes. Recycling bins should also be placed to encourage recycling.</li> <li>Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should also be implemented to keep areas clean.</li> <li>A reputable waste collector should be employed to remove general refuse on a daily basis.</li> </ul>	Minimise production of the general refuse and avoid odour, pest and litter impacts	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Waste Disposal Ordinance</li> </ul>
S7.3.4.20	<p><u>Sewage</u></p> <ul style="list-style-type: none"> <li>The WMP should document the locations and number of portable chemical toilets depending on the number of workers, land availability,</li> </ul>	Minimise production of sewage impacts	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Waste Disposal Ordinance</li> </ul>

### Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<p>site condition and activities.</p> <ul style="list-style-type: none"> <li>Regularly collection by licensed collectors should be arranged to minimise potential environmental impacts.</li> </ul>					
<b>Waste Management (Operational Waste)</b>						
S7.4.4.1	<p><u>General Refuse</u></p> <p>A reputable waste collector should be employed to remove general refuse on a daily basis.</p>	Remove general refuse during routine road cleaning activities on the roads network and avoid odour, pest and litter impacts	Highways Department / Contractor	Roads network for the C&C facilities and Lin Ma Hang Road	Operational phase	<ul style="list-style-type: none"> <li>Waste Disposal Ordinance</li> </ul>



## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
<b>Land Contamination</b>						
S8.9.1.1	Re-appraisal of the potentially contaminated site (SRC-1)	Identify any hot spots for SI within the southeast and western portions of SRC-1	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	Once the works area for the Project is confirmed and site access is available (e.g. after land resumption)	<ul style="list-style-type: none"> <li>• Annex 19 of the TM-EIAO, Guidelines for Assessment of Impact On Sites of Cultural Heritage and Other Impacts (Section 3 : Potential Contaminated Land Issues);</li> <li>• Guidance Manual for Use of Risk-Based Remediation Goals (RBRGs) for Contaminated Land Management;</li> <li>• Guidance Notes for Contaminated Land Assessment and Remediation; and</li> <li>• Practice Guide for Investigation and Remediation of Contaminated Land</li> <li>• Recommendations in Health Risk Assessment</li> </ul>
S8.11.1.1	Preparation and submission of Contamination Assessment Plan (CAP) to EPD for review and approval, if required	Present the findings of the re-appraisal and strategy of the recommended SI, if required	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	After land resumption and prior to the construction phase	Ditto
S8.11.1.2	Preparation and submission of Contamination Assessment Report (CAR) to EPD for review and approval, if required	Present the findings of SI, if any, and evaluate the level and extent of potential contamination	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	Prior to the construction phase	Ditto

### Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S8.11.1.2	Preparation and submission of Remediation Action Plan (RAP) to EPD for review and approval if contamination is identified	Recommend appropriate mitigation measures for the contaminated soil and groundwater identified in the assessment if remediation is required	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	Prior to the construction phase	Ditto
S8.11.1.2	Preparation and submission of Remediation Report (RR) to EPD for review and approval following the completion of any necessary remediation works	Demonstrate that the decontamination work is adequate and is carried out in accordance with the endorsed CAR and RAP	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	Prior to the construction phase	Ditto

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
<i>Ecology ( Construction Phase)</i>						
S9.7.2.3	Preparation and submission of Upland Grassland Reinstatement Plan to EPD for agreement.	<p>An Upland Grassland Reinstatement Plan will be prepared by a qualified ecologist/botanist with full details of the findings of a baseline grassland survey, the practical details and methodology of the physical excavation, transport and storage or turves/topsoil and their subsequent reinstatement once the receptor sites have been established, along with an implementation programme of reinstatement, post- reinstatement monitoring and maintenance programme.</p> <p>A contingency plan should be proposed in the Grassland Reinstatement Plan so as to describe the action and limit levels and the action plan if certain performance criteria (such as area of preferred habitat) are not met during the monitoring and maintenance period.</p>	Project Proponent/ Detailed Design Consultant (qualified ecologist/ botanist) for Upland Grassland Reinstatement Plan	Engineered slopes of Crematorium  Indicative locations for Grassland Reinstatement should be referred to <b>Figure 9.11</b> of the EIA Report	Prior to construction phase	<ul style="list-style-type: none"> <li>• Reinstatement and establishment requirements to be detailed in Upland Grassland Reinstatement Plan</li> <li>• TM-EIAO</li> </ul>
S9.7.2.5 – S9.7.2.6	Preparation and submission of a Vegetation Survey Report and Transplantation Proposal (if needed as concluded in the Vegetation Survey Report) to EPD for agreement.	The Vegetation Survey will report the presence, as well as update the conditions, number, locations and habitat types of any identified floral species of conservation importance to be impacted by the development,	Project Proponent/ Detailed Design Consultant (qualified ecologist/ botanist) for	Within the Project Area where applicable	Prior to construction phase	<ul style="list-style-type: none"> <li>• Survey findings and transplantation methodology to be detailed in Vegetation Survey Report and Transplantation Plan</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		and evaluate suitability and/or practicality of transplantation.  The Transplantation Proposal will recommend locations of the receptor site(s), transplantation methodology, implementation programme of transplantation and post-transplantation monitoring and maintenance programme.	Vegetation Survey Report and Transplantation Proposal.			respectively.  • TM-EIAO.
S9.7.5.3 – S9.7.5.5, S9.8.1.6	Preparation and submission of Enhancement Woodland Proposal to EPD for agreement.	Recommend appropriate enhancement planting programme, planting and post-transplantation monitoring methodology, action plan for monitoring the enhancement planting and maintenance programme.	Project Proponent/ Detailed Design Consultant (qualified ecologist/ botanist) for Wooded Area Proposal.	Filled slope west of the platform, and north west of the platform in the valley below MacIntosh Fort  Indicative locations for Enhancement Woodland should be referred to <b>Figure 9.11</b> of the EIA Report	Prior to construction phase	• Enhancement planting and establishment requirements to be detailed in Wooded Enhancement Proposal.  • TM-EIAO
S9.7.3.1 – S9.7.3.3	Indirect impacts due to potential changes in water quality, hydrology and sedimentation could occur to a series of downstream watercourses and wetland systems (including the wet woodland, marsh and mitigation ponds) during both the construction (for the Platform and LMHR widening works) and operational stages.  Generally, indirect water impact to any aquatic fauna during the construction phase should easily be avoided by implementing water control measures (ETWB TCW No. 5/2005) to avoid direct or indirect impacts any watercourses and good site practices (further details are discussed in Section 6 of the EIA Report).	Minimise the indirect impacts to Water Quality and Hydrology	Contractor /detailed design consultant.	On the edge of any active works area, 30m from the watercourse	Prior to commencement and during construction phase	• ETWB TCW No. 5/2005  • TM-EIAO

### Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	In addition, construction phase impacts on the watercourses, riparian corridor and fauna using these areas will be minimised by erection of a 2m high, solid, dull green site boundary fence on the edge of any active works area, 30m from the watercourse. Where this is not practicable due to site constraints, demarcation fencing will need to be erected to prevent unauthorised encroachment into the riparian corridor by constructions works and traffic. Detailed mitigation measures will be designed at the detailed design stage.					
S9.7.3.4 – S9.7.3.6	<p>Mitigation for noise disturbance (details refer to S5.5.5 to S5.6.6 of this table). Site formation and construction are tentatively proposed to cover a 65-month period from mid 2017 to late 2022.</p> <p>As a precautionary approach, consideration should be given at the detailed design stage to avoid the use of highly reflective materials in the design and implementing the use of opaque materials, fritting, breaking up external reflections with stickers or plastic wrap and/or any other bird-friendly design for noise barriers.</p> <p>Works will be restricted to daytime and any construction lighting should be designed and positioned as to not impact on adjacent ecologically sensitive areas.</p>	The construction work and site formation will be phased in order to reduce overall noise disturbance impacts in particular areas. Collisions usually occurs as a result of birds perceiving a clear path through an object that is transparent or appears to be transparent at some distance, or if the noise barrier is highly reflective which would appear to be composed of the adjacent natural vegetation. Furthermore, mitigation measures to control noise disturbance during this phase will involve the selection of quieter plant, use of movable noise barriers and erection of hoarding and fencing to demarcate the site boundary	Contractor Project Proponent	All construction sites	Prior to commencement and during construction phase	• TM-EIAO.



### Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S.9.7.3.7	<p>In order to demonstrate ecological awareness and to minimise the risk of indirect impacts from water pollution and hill fires, a series of good site practices should be adopted by site staff throughout the construction phase at each works site. These are as follows:</p> <ul style="list-style-type: none"> <li>• Put up signs to alert site staff about any locations which are ecologically sensitive and measures to prevent accidental impacts;</li> <li>• Erection of temporary geotextile silt or sediment fences/oil traps around any earth-moving works to trap any sediments and prevent them from entering watercourses;</li> <li>• Prohibition of soil storage against trees or close to waterbodies;</li> <li>• Delineation of works site to prevent encroachment onto adjacent habitats and fence off areas which have some ecological value;</li> <li>• No smoking, hot works or sources of fire close to upland grassland;</li> <li>• No on-site burning of waste; and</li> <li>• Waste and refuse in appropriate receptacles.</li> </ul>	Minimise impacts on hydrological condition and water quality of hillside watercourses and reduce chances of hillfires.	Contractor	All construction sites	Prior to commencement and during construction phase	• TM-EIAO.
S.9.7.3.9	Precautionary checks by a suitably experienced ecologist of the vegetation for the presence of nesting birds should be carried out in the breeding season (February to July) before vegetation clearance. These impacts can be avoided by conducting vegetation clearance during the non-breeding season (tentatively August-January) and phased through the project period to minimise impacts.	Minimise the impacts to breeding birds within the works areas.	Contractor	All construction sites	Prior to site clearance	• TM-EIAO • WAPO
<b>Ecology (Operational Phase)</b>						

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S9.7.2	Establishment, maintenance and monitoring of a Upland Grassland Reinstatement Area	Reinstatement of upland grassland and to maintain connectivity in Sandy Ridge.	Project Proponent / Contractor / Maintenance Authority	Engineered slopes of Crematorium  Indicative locations for Grassland Reinstatement should be referred to <b>Figure 9.11</b> of the EIA Report	Operational phase	<ul style="list-style-type: none"> <li>Monitoring methodology and successfulness of survival of upland grassland should follow Upland Grassland Reinstatement Plan.</li> <li>TM-EIAO.</li> </ul>
S9.7.5.3 – S9.7.5.6	Establishment, maintenance and monitoring of an enhancement woodland	Recommend appropriate planting programme, planting and post-transplantation monitoring methodology, action plan for monitoring the enhancement planting and maintenance programme.	Project Proponent/ Detailed Design Consultant (qualified ecologist/ botanist) for Wooded Area Proposal.	Filled slope west of the platform, and north west of the platform in the valley below MacIntosh Fort  Indicative locations for Enhancement Woodland should be referred to <b>Figure 9.11</b> of the EIA Report	Operational phase	<ul style="list-style-type: none"> <li>Enhancement planting and establishment requirements to be detailed in Wooded Area Proposal.</li> <li>TM-EIAO.</li> </ul>
S9.7.4.1 – S9.7.4.5	<u>Mitigation for Impacts to Water Quality and Hydrology (Operational Phase)</u> <ul style="list-style-type: none"> <li>Stormwater drainage system will be further developed in detailed design stage to collect dusty materials from water collected from the platform and associated road system. Silt traps will be installed to ensure removal of dusty materials. Regular cleaning will be conducted to avoid debris entering downstream rivers during first flush; and</li> <li>The proposed small diameter bore pile system at the foundation of the proposed platform structure.</li> </ul>	Specific mitigation measures will be implemented to prevent indirect impacts wetland habitats and fauna. Mitigation measures are to be further developed in the detailed design stage to address any water quality impacts due to the drainage from the proposed platform, and any erosion issues due to the drainage from the	Detailed Design Consultant	Wet woodland (and further down the marsh and mitigation ponds) and the seasonal watercourse to the east of the Project boundary	Detailed Design phase/Operational phase	<ul style="list-style-type: none"> <li>TM-EIAO</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		<p>proposed platform.</p> <p>The surface runoff collected on the platform will be captured by a stormwater drainage system, which will be further developed at the detailed design stage</p> <p>The proposed small diameter bore pile system at the foundation of the proposed platform structure would allow a notional free area of about 87 – 91% for groundwater to pass through</p>				
S9.7.4.6 – S9.7.4.7	<p><u>Minimise the potential indirect light disturbance on the Street Lighting on fireflies surrounding the Project Site during operational phase</u></p> <ul style="list-style-type: none"> <li>It is considered that at the detailed design stage, street lighting of similar lux/light intensity as to what is currently present is utilised. Furthermore, as a precautionary measure, it is suggested that deflectors are fixed to the back of the street lights to prevent additional light reaching the marsh and causing adverse impacts to fireflies.</li> </ul>	Reduce light pollution and impact on the nearby habitats and their associated wildlife groups, particularly nocturnal fireflies.	Detailed Design/ Consultant/ Operator	The whole Project area	Detailed Design phase/Operational phase	• TM-EIAO
S9.7.4.9 – S9.7.4.9	<p>The increase in visitors to the columbarium allows greater public access to the upland grassland of Sandy Ridge and in turn, the potential for hill fires is also increased. Fires may emanate from discarded cigarettes and from specific practices during festivals or grave-sweeping.</p> <p>In order to reduce the risk of hill fires, sufficient educational signage should be displayed throughout the columbarium warning people of the risks of fire and strictly prohibits practices that could cause hill fires. This will require input in the detailed design phase.</p>	Minimise the risk of hill fires.	Detailed Design/ Consultant/ Operator	The whole Project area	Detailed Design phase/Operational phase	• TM-EIAO

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
<b>Fisheries</b>						
S10.5.1.1	<p>No loss of fish ponds is anticipated and no <i>in situ</i> mitigation is required.</p> <p>However, mitigation measures for water quality (S6.4.4 – S6.5.4 in this table) proposed are also pertinent in ensuring that fisheries impacts of the Project do not occur downstream of the Project area either locally or in Inner Deep Bay.</p>	-	-	-	-	-

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
<b>Landscape &amp; Visual</b>						
S11.8.1.3, Table 11.9	CM1 – The construction area and contractor's temporary works areas should be minimised to avoid impacts on adjacent landscape, and the reliance on off-site construction.	Minimise landscape impact and visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-
S11.8.1.3, Table 11.9	CM3 – Screening of construction works by hoardings/noise barriers around works area in visually unobtrusive colours and to screen construction works. It is proposed that screening be compatible with the surrounding environment and non-reflective, recessive colours be used. Hoarding should be taken down at the end of the construction period.	Minimise visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-
S11.8.1.3, Table 11.9	CM4 – Dust and Erosion Control for Exposed Soil - Excavation works and demolition of existing building blocks shall be well planned with precautions to suppress dust. Exposed soil shall be covered or watered often. Areas that are expected to be left with bare soil for a long period of time after excavation shall be properly covered with suitable protective fabric. Suitable drainage shall be provided around construction sites to avoid discharge of contaminants and sediments into sensitive water-based habitat.	Minimise indirect landscape impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-
S11.8.1.3, Table 11.9	CM5 – Control night-time lighting and glare by hooding all lights.	Minimise visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-



## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S11.8.1.3, Table 11.9	CM6 – Tree Protection and Preservation – Woodland, plantation and other vegetation within the Study Area will be protected and preserved as far as possible in accordance with ETWB TCW No. 29/2004 - Registration of Old and Valuable Trees, and Guidelines for their Preservation and DEVB TCW No.07/2015 – Tree Preservation. Detailed Design Considerations are made to avoid impacts to trees, e.g. proper viaduct/ bridge design routing to avoid majority of the woodland, locating the columbarium buildings in areas with less trees and ensuring design of the buildings has as small a footprint as practical.	Minimise landscape impact and visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	<ul style="list-style-type: none"> <li>• DEVB TC(W) 07/2015</li> <li>• Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DevB</li> </ul>
S11.8.1.3, Table 11.9	CM7 – Tree Transplantation – Tree(s) will be affected according to the Tree Preservation and Removal Proposal to be carried out in a later stage. Established trees of value are to be re-located where practically feasible.	Minimise landscape and visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Design and Construction phase	<ul style="list-style-type: none"> <li>• ‘Guidelines for Tree Risk Management and Assessment Arrangement on an Area Basis and on a Tree Basis’, issued January 2011, Greening, Landscape and Tree Management (GLTM) Section, DevB</li> <li>• Latest recommended horticultural practices from GLTM Section, DevB</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S11.8.1.3, Table 11.9	CM8 - Implementing precautionary control measures during construction stage accordingly to ETWB TCW No. 5/2005 – Protection of natural streams/rivers from adverse impacts arising from construction works to avoid direct or indirect impacts any watercourses and good site practices.	Minimize landscape impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Design and Construction phase	<ul style="list-style-type: none"> <li>• ETWB TCW No. 5/2005 – Protection of natural streams/rivers from adverse impacts arising from construction works</li> </ul>
S11.8.1.3, Table 11.9	OM1 – Compensatory Woodland Planting - The arrangement of compensatory planting (e.g. areas of woodland to be compensated and space to be allowed within the Project Site) will be subject to detailed engineering design, landscape design and planting plan, and is recommended to be implemented prior to the construction activities as far as practical.	Compensate the loss of landscape greenery and enhance the overall visual value of the site.	Funded by CEDD and implemented by Contractor	Within Project Site	Prior to Construction phase	<ul style="list-style-type: none"> <li>• DEVB TC(W) 07/2015 – Tree Preservation</li> <li>• Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DevB</li> <li>• DEVB TCW No. 06/2015 – Maintenance of Vegetation and Hard Landscape Features</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S11.8.1.3, Table 11.9	OM2 – Compensatory Tree Planting for Plantation and Other Vegetated Areas - Compensatory planting should be provided in accordance with DEVB TCW No. 07/2015 to compensate for those trees felled. According to the preliminary design, compensatory trees will be planted on the cut/fill slopes, along new roads and in car parks. The selection of planting species shall be made with reference to the species identified in the future Detailed Tree Survey and be native to Hong Kong or the South China region.	Compensate the loss of landscape greenery and enhance the overall visual value of the site.	Funded by CEDD and implemented by Contractor	Within Project Site	Construction phase	<ul style="list-style-type: none"> <li>• DEVB TC(W) 07/2015 – Tree Preservation</li> <li>• Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DevB</li> <li>• DEVB TCW No. 06/2015 – Maintenance of Vegetation and Hard Landscape Features</li> </ul>
S11.8.1.3, Table 11.9	OM3 – Amenity Planting and aesthetic streetscape design of hard landscaping for Pedestrian Walkway, Roadside - Roadside amenity planting should be provided along Sha Ling Road, Lin Ma Hang Road, as well as the internal road within Sandy Ridge columbarium and crematorium site; to enhance the landscape quality of the existing and proposed transport routes. Climbers are proposed to cover vertical, hard surfaces of the piers of the proposed viaducts, and also the newly formed retaining wall within the site. Shade tolerant plants will be planted, where light is sufficient, to improve aesthetic value of areas under viaducts.	Minimise visual impact and also enhance landscape.	Funded by CEDD and implemented by Contractor	Within Project Site	Construction phase	<ul style="list-style-type: none"> <li>• Guidelines on Greening of Noise Barriers, issued April 2012, GLTMS, DevB</li> <li>• DEVB TCW No. 06/2015 – Maintenance of Vegetation and Hard Landscape Features</li> </ul>
S11.8.1.3, Table 11.9	OM4 – Greening Works and Contour Grading Works on Cut/ Fill Slopes - Greening works such as hydroseeding/ terraces of shrub or tree planting will be provided where slope gradient allows, according to Geotechnical Engineering Office (GEO) Publication No.1/2011 Technical Guidelines on Landscape Treatment for Slopes.	Minimise landscape and visual impact	Funded by CEDD and implemented by Contractor	Within Project Site	Construction phase	Geotechnical Engineering Office (GEO) Publication No.1/2011 Technical Guidelines on Landscape Treatment for Slopes.

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S11.8.1.3, Table 11.9	OM5 – Landscape design treatment to be provided by relevant government department.	Mitigate the loss of greenery and enhance the overall landscape and visual value	Funded by FEHD and implemented by Contractor	Within Project Site	After handover to the relevant department	-
S11.8.1.3, Table 11.9	OM6 – Architectural and chromatic treatment of the hard architectural and engineering structures and facilities.	Mitigate the loss of greenery and enhance the overall landscape and visual value	Funded by FEHD and implemented by Contractor	Within Project Site	After handover to the relevant department	-
S11.8.1.3, Table 11.9	OM7 – Aesthetic design of the proposed noise barriers.	Mitigate the visual impact	Funded by CEDD and implemented by Contractor	Along Sha Ling Road and Lin Ma Hang Road	Construction phase	<ul style="list-style-type: none"> <li>• WBTC No. 36/2004 - ACABAS - submission is required to ACABAS for approval of any bridges and associated structures within the public highway system.</li> </ul>
S11.8.1.3, Table 11.9	OM8 - Silt traps should also be incorporated into design of road gullies for the natural water stream(s).	Minimise the landscape impact on natural stream	Funded by CEDD and implemented by Contractor	Within Project Site	Construction Phase	

**Notes:**

- (a) A detailed Tree Survey Report showing all identified valuable trees and OVT will be undertaken in a separate Tree Preservation and Removal Proposal.
- (b) Wood resulting from tree removal should be recycled as mulch or soil conditioner for re-use within the Project or in other projects as far as possible e.g. for the construction of soft landscape work, were practical.
- (c) Contractor is responsible for landscaping during the agreed establishment and maintenance period. Other designated management and maintenance agents to take up maintenance and management of landscaping after end of agreed period.
- (d) Highways Department (HyD) is responsible for maintenance and management of landscaping of public road side slope, Leisure and Cultural Services Department (LCSD) is responsible for the management and maintenance of soft landscapes along non-expressway public roads outside Country Park and Food and Environmental Hygiene Department (FEHD) is responsible for maintenance and management of landscaping of other areas allocated to FEHD.
- (e) The landscape mitigation treatment of the future development site shall follow the below frameworks:
  - Buffer planting shall be provided to soften the edge of the site.
  - Aesthetic landscape treatment including both soft and hard landscape features shall be provided.
  - Vertical greening shall be provided as far as practicable.
  - At-grade tree planting shall be provided as far as possible while planting space is allowed, to enhance the overall environment.
  - Architectural design shall blend in with the surrounding environment.
  - Overall greening ratio shall comply with TC(W) No.3/2012 Site coverage of Greenery for Government Building Projects.

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
The compensatory woodland planting shall be included woodland mixed whips, seeding, and shrubs. The principle of the location shall be the extension of the existing woodland, as well as the original lost woodland location. The proposal will be agreed with AFCD, the woodland enhancement planting shall refer to Chapter 9.						



## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
<b><i>Cultural Heritage Impact (Construction and Operational Phase)</i></b>						
S.12.4.8.1	<ul style="list-style-type: none"> <li>Archaeological Watching Brief (AWB) programme near the crossing at the south of the proposed connection road to Man Kam To Road as delineated on <b>Figure 12.3.13</b> needs to be undertaken by qualified archaeologist, who will apply for an archaeological licence to conduct the works.</li> </ul>	To further assess cultural soils recorded during the Archaeological field survey	Contractor	Location for AWB shown in <b>Figure 12.3.13</b> of the EIA Report	Prior to the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>Archaeological licence requirements</li> <li>AWB methodology guidelines</li> </ul>
S.12.4.8.2	<ul style="list-style-type: none"> <li>The contractor should be alerted during the construction along Lin Ma Hang Road on the possibility of locating archaeological remains and as a precautionary measure, AMO shall be informed immediately in case of discovery of antiquities or supposed antiquities in the subject sites.</li> </ul>	To preserve any cultural heritage items which may be removed and damaged by the excavation works.	Contractor	Along Lin Ma Hang Road	During the Construction phase	<ul style="list-style-type: none"> <li>Antiquities and Monuments Ordinance</li> </ul>
S.12.3.11.10 Table 12.4	<ul style="list-style-type: none"> <li>Monitoring of vibration levels will be undertaken during the construction phase and the Alert, Alarm and Action (AAA) vibration limit will be set at 5/6/7.5 mm/s. The monitoring proposal should be sent to AMO for comment;</li> <li>A condition survey should be undertaken by the project proponent to determine the present condition of graded historic building and to recommend protective measures to ensure that the building is not damaged by the construction works. A condition survey must be carried out by qualified building surveyor or engineer. A condition survey proposal will be submitted to AMO for comment before commencement of work;</li> <li>Regular site inspections and monitoring works will be carried out by the contractor and the monitoring results will be submitted to the resident site staff to ensure compliance.</li> </ul>	Protect the building from damage from construction works	Contractor	MacIntosh Fort at Nam Hang (GB-01)	Prior to commencement and during the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>AMO Proposed Vibration Limits</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S.12.3.11.10 Table 12.5	<ul style="list-style-type: none"> <li>A cartographic and photographic survey will be conducted for shrine that will require relocation prior to the construction works;</li> <li>The shrine will be relocation to a suitable locations in the close vicinity to allow for continuing worship by public.</li> </ul>	Protect the structure from damage from construction works	Contractor	Earth God Shrine on corner of Man Kam To and Sha Ling Road (HB-01)	Prior to commencement the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>AMO's guidelines for cartographic and photographic survey</li> </ul>
S.12.3.11.10 Table 12.5	<ul style="list-style-type: none"> <li>A condition survey will be undertaken to determine the present condition of graded historic building and to recommend protective measures to ensure that the building is not damaged by the construction works. A condition survey must be carried out by qualified building surveyor or engineer;</li> <li>Monitoring of vibration levels will be undertaken during the construction phase and the action vibration limit will be set at 25 mm/s;</li> <li>Regular site inspections and monitoring works will be carried out by the contractor and the monitoring results will be submitted to the resident site staff to ensure compliance.</li> </ul>	Protect the building from damage from construction works	Contractor	Tin Hau Temple (HB-02)	Prior to commencement and during the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>AMO Proposed Vibration Limits</li> </ul>
S.12.3.11.10 Table 12.5	<ul style="list-style-type: none"> <li>A condition survey will be undertaken to determine the present condition of graded historic building and to recommend protective measures to ensure that the building is not damaged by the construction works. A condition survey must be carried out by qualified building surveyor or engineer;</li> <li>Monitoring of vibration levels will be undertaken during the construction phase and the action vibration limit will be set at 25 mm/s;</li> <li>Protective covering should be provided for the structure in the form of plastic sheeting;</li> <li>A buffer zone measuring a minimum of 1 m or as appropriate needs to be set up and covering in the form of plastic sheeting on a moveable fence to protect the heritage building from works;</li> </ul>	Protect the building from damage from construction works	Contractor	San Uk Ling Village Entrance Gate (HB-03)	Prior to commencement and during the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>AMO Proposed Vibration Limits</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<ul style="list-style-type: none"> <li>Regular site inspections and monitoring works will be carried out by the contractor and the monitoring results will be submitted to the resident site staff to ensure compliance.</li> </ul>					
S.12.3.11.10 Table 12.5	<ul style="list-style-type: none"> <li>A condition survey will be undertaken to determine the present condition of graded historic building and to recommend protective measures to ensure that the building is not damaged by the construction works. A condition survey must be carried out by qualified building surveyor or engineer;</li> <li>Monitoring of vibration levels will be undertaken during the construction phase and the action vibration limit will be set at 25 mm/s;</li> <li>Regular site inspections and monitoring works will be carried out by the contractor and the monitoring results will be submitted to the resident site staff to ensure compliance.</li> </ul>	Protect the building from damage from construction works	Contractor	Cheung Ancestral Hall (HB-04)	Prior to commencement and during the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>AMO Proposed Vibration Limits</li> </ul>
S.12.3.11.10 Table 12.5	<ul style="list-style-type: none"> <li>A condition survey will be undertaken to determine the present condition of graded historic building and to recommend protective measures to ensure that the building is not damaged by the construction works. A condition survey must be carried out by qualified building surveyor or engineer;</li> <li>Monitoring of vibration levels will be undertaken during the construction phase and the action vibration limit will be set at 25 mm/s;</li> <li>Regular site inspections and monitoring works will be carried out by the contractor and the monitoring results will be submitted to the resident site staff to ensure compliance.</li> </ul>	Protect the building from damage from construction works	Contractor	No. 9 San Uk Ling Village House (HB-05)	Prior to commencement and during the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>AMO Proposed Vibration Limits</li> </ul>
S.12.3.11.10 Table 12.5	<ul style="list-style-type: none"> <li>A condition survey will be undertaken to determine the present condition of graded historic building and to recommend protective measures to ensure that the building is not damaged by the construction works. A condition survey must be carried out by qualified building surveyor or engineer;</li> <li>Monitoring of vibration levels will be undertaken during the construction phase and the action vibration limit will be set at 25 mm/s;</li> </ul>	Protect the structure from damage from construction works	Contractor	Buddhist Shrine (HB-06)	During the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>AMO Proposed</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	<ul style="list-style-type: none"> <li>Protective covering should be provided for the structure in the form of plastic sheeting;</li> <li>Buffer zones should be provided between the construction works and the shrine and should be as large as site restrictions allow and be marked out by temporary fencing or hoarding;</li> <li>Provision of safe public access.</li> </ul>					Vibration Limits
S.12.3.11.10 Table 12.5	<ul style="list-style-type: none"> <li>A condition survey will be undertaken to determine the present condition of graded historic building and to recommend protective measures to ensure that the building is not damaged by the construction works. A condition survey must be carried out by qualified building surveyor or engineer;</li> <li>Monitoring of vibration levels will be undertaken during the construction phase and the action vibration limit will be set at 25 mm/s;</li> <li>Protective covering should be provided for the structure in the form of plastic sheeting;</li> <li>Buffer zones should be provided between the construction works and the shrine and should be as large as site restrictions allow and be marked out by temporary fencing or hoarding;</li> <li>Provision of safe public access.</li> </ul>	Protect the structure from damage from construction works	Contractor	Buddhist Shrine (HB-07)	During the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>AMO Proposed Vibration Limits</li> </ul>
S.12.3.11.10 Table 12.6	<ul style="list-style-type: none"> <li>A condition survey will be undertaken to determine the present condition of graded historic building and to recommend protective measures to ensure that the building is not damaged by the construction works. A condition survey must be carried out by qualified building surveyor or engineer;</li> <li>Monitoring of vibration levels will be undertaken during the construction phase and the action vibration limit will be set at 25 mm/s;</li> <li>Protective covering should be provided for the structure in the form of plastic sheeting;</li> <li>Buffer zones should be provided between the construction works and the grave and should be as large as site restrictions allow and be marked out</li> </ul>	Protect the structure from damage from construction works	Contractor	Yuen Clan Urns and Plaque (G-01)	Prior to commencement and during the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>AMO Proposed Vibration Limits</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	by temporary fencing or hoarding; <ul style="list-style-type: none"> <li>Regular site inspections and monitoring works will be carried out by the contractor and the monitoring results will be submitted to the resident site staff to ensure compliance;</li> <li>Provision of safe public access.</li> </ul>					
S.12.3.11.10 Table 12.6	<ul style="list-style-type: none"> <li>A condition survey will be undertaken to determine the present condition of graded historic building and to recommend protective measures to ensure that the building is not damaged by the construction works. A condition survey must be carried out by qualified building surveyor or engineer;</li> <li>Monitoring of vibration levels will be undertaken during the construction phase and the action vibration limit will be set at 25 mm/s;</li> <li>Protective covering should be provided for the structure in the form of plastic sheeting;</li> <li>Buffer zones should be provided between the construction works and the grave and should be as large as site restrictions allow and be marked out by temporary fencing or hoarding;</li> <li>Regular site inspections and monitoring works will be carried out by the contractor and the monitoring results will be submitted to the resident site staff to ensure compliance;</li> <li>Provision of safe public access.</li> </ul>	Protect the structure from damage from construction works	Contractor	Cheung Clan Grave (G-02)	Prior to commencement and during the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>AMO Proposed Vibration Limits</li> </ul>
S.12.3.11.10 Table 12.6	<ul style="list-style-type: none"> <li>Provision of safe public access.</li> </ul>	Public access may be affected during the construction works.	Contractor	Yuen Clan Grave (G-10)	During the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> </ul>
S.12.3.11.10 Table 12.6	<ul style="list-style-type: none"> <li>Provision of safe public access.</li> </ul>	Public access may be affected during the construction works.	Contractor	Cheung Clan Grave (G-11)	During the Construction phase	<ul style="list-style-type: none"> <li>Guidelines for Cultural Heritage Impact Assessment</li> </ul>



### Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
						<ul style="list-style-type: none"> <li>• TM-EIAO Annex 10 and Annex 19</li> </ul>

## Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
<i>EM&amp;A Project</i>						
S13.1.1.1, S13.2.1.2	An Independent Environmental Checker needs to be employed as per the EM&A Manual.	Control EM&A Performance	Highways Department	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>• EIAO Guidance Note No.4/2010</li> <li>• TM-EIAO</li> </ul>
S13.2.1.1 – S13.4.1.2	1) An Environmental Team needs to be employed as per the EM&A Manual. 2) Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures. 3) An environmental impact monitoring needs to be implementing by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with.	Perform environmental monitoring & auditing	Highways Department / Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>• EIAO Guidance Note No.4/2010</li> <li>• TM-EIAO</li> </ul>
