

JOB NO.: TCS00881/18 & TCS00944/18

SITE FORMATION AND ASSOCIATED INFRASTRUCTURAL WORKS FOR DEVELOPMENT OF COLUMBARIUM, CREMATORIUM AND RELATED FACILITIES AT SANDY RIDGE CEMETERY

MONTHLY ENVIRONMENTAL MONITORING AND AUDIT REPORT (No.40) – NOVEMBER 2021

PREPARED FOR HSIN CHONG TSUN YIP JOINT VENTURE & SANG HING CIVIL CONTRACTORS CO., LTD

Date Reference No. Prepared By Certified By

13 December 2021 TCS00881/18/600/R0591v2

Nicola Hon Tam Tak Wing (Environmental Consultant) (Environmental Team Leader)

Version	Date	Remarks
1	9 December 2021	First Submission
2	13 December 2021	Amended according to the IEC's comments



Our Ref: TCS00881/18/300/L0592

Civil Engineering and Development Department

2/F, Civil Engineering and Development Building, 101 Princess Margaret Rd, Homantin, Kowloon

Attn: Mr. SHUM Ngai Hung, Steven

14 December 2021 By e-mail

Dear Sirs,

Re: Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery Monthly Environmental Monitoring & Audit Report (No.40) –November 2021

We confirmed that the captioned report has complied with the requirement set out in the EM&A Manual, we hereby certify the captioned report pursuant to Specific Condition 3.4 of the Environmental Permit No. FEP-01/534/2017/A and EP-534/2017/A.

Should you have any queries, please feel free to contact the undersigned at Tel: 2959-6059 or Fax: 2959-6079 or Email: twtam@fordbusiness.com.

Yours sincerely, For and on Behalf of

Action-United Environmental Services & Consulting (AUES)

T. W. Tam

Environmental Team Leader

TW/nh

cc	ARUP (RE of Contract 1)	Mr. Steven Tang	by e-mail
	ARUP (RE of Contract 2)	Mr. Anthony Lau	by e-mail
	HCTY-JV (Contractor of Contract 1)	Mr. Ho Man To	by e-mail
	Sang Hing (Contractor of Contract 2)	Mr. Elvin Lam	by e-mail
	Acuity (IEC)	Mr. Jacky Leung	by e-mail





(852) 2959-6059

Nos. 37-39 Wing Hong Street, Cheung Sha Wan, Kowloon

Tel.: (852) 2698 6833

Fax.: (852) 2698 9383



Our ref: PL-202112011

Hsin Chong Tsun Yip Joint Venture (CV/2016/10)
Hsin Chong Centre
107-109 Wai Yip Street
Kwun Tong, Kowloon
Hong Kong

Attention: Mr. HO Man-to

14 December 2021

Dear Sir,

Site formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery

Monthly Environmental Monitoring and Audit Report (No. 40) November 2021

I refer to the email of the ET dated on 13/12/2021 regarding the captioned Monthly Report. According to Section 3.4 of the EP-534/2017/A and the FEP-01/534/2017/A, I hereby verify the Monthly EM&A report for October 2021 with Ref. No. TCS00881/18/600/R0591v2.

You are required to follow up the comments from EPD and IEC on the relevant EPs requirement and provide supplementary information of this report for our further review as soon as possible.

Yours faithfully,

CH Leung

Leung CH Jacky Independent Environmental Checker

cc. CEDD-DPTL/Land Works – Mr. SHUM Steven ARUP – Mr. LEE Davis ET Leader – Mr. TAM



EXECUTIVE SUMMARY

ES.01. This is the 40th Monthly Environmental Monitoring and Audit (EM&A) Report summarizing the monitoring results and inspection findings under the Project for the period from 1st to 30th November 2021 (the Reporting Month).

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

ES.02. In the Reporting Month, the major construction works under the Project included Contract CV/2016/10 (hereinafter named "Contract 1") and Contract CV/2017/02 (hereinafter named "Contract 2"). Environmental monitoring activities under the EM&A programme in this Reporting Month are summarized in the following table.

Table ES-1 Summary of EM&A Programme in the Reporting Month

Issues	Environmental Monitoring	Monitorin	Total Occasions/	
Issues	Parameters / Inspection	CV/2016/10	CV/2017/02	dates
A in Onelita	1-hour TSP	ACD 1	ASR-2	45
Air Quality	24-hour TSP	ASR-1	ASR-3	15
Construction Noise	L _{eq (30min)} Daytime	CN-1 CN-2	CN-3 CN-4	16
Water Quality	In-situ measurement and Water sampling	M3	M1, M2 and M4	13 (#)
Ecology	Sensitive Habitat	Transect within site area of CV/2016/10		18 th Nov 2021
Landscape & Visual	Site Inspection	Site area of CV/2016/10	Site area of CV/2017/02	15 th Nov 2021
Inspection	Environmental Team (ET) Regular Environmental Site Inspection		Site area of	4
& Audit	Independent Environmental Checker (IEC) Monthly Environmental Site Audit		CV/2017/02	1

Remarks: (#) The channel of M2 was dried up / too shallow and representative water sampling was unable be carried out.

BREACH OF ACTION AND LIMIT (A/L) LEVELS

ES.03. In the Reporting Month, no exceedance of air quality, noise monitoring and water quality was recorded. The statistics of environmental exceedance, Notification of Exceedance (NOE) issued and investigation of exceedance are summarized in the following table.

Table ES-2 Breach of Action and Limit (A/L) Levels in the Reporting Month

Environmental	Monitoring	Action	Limit	Event & Action	
Issues	Parameters	Level	Level	Investigation Findings	Corrective Actions
Air Quality	1-hour TSP	0	0	-	-
Air Quality	24-hour TSP	0	0	-	-
Construction Noise	Leq _{30min} Daytime	0	0	-	-
	DO	0	0	-	-
Water Quality	Turbidity	0	0	-	-
water Quarty	Suspended Solids (SS)	0	0	-	1

Note: NOE – Notification of Exceedance

ES.04. Monthly ecological monitoring for sensitive habitat for area of Contract 1 and Contract 2 were undertaken on 18th November 2021. After analysing survey results in November from 2018 to 2021, there were a slight decrease in abundance and a drop in species richness for wetland habitat under Contract 1. Good site practice during construction, with reference to EM&A Manual, is required to prevent or alleviate environmental impacts. For instance, the size of work areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works.



Unnecessary site clearance should be avoided as well. For Contract 2, no significant drop in species richness and abundance is observed for wetland and non-wetland habitats. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.

ES.05. Landscape and visual inspection at both Contracts were undertaken on 15th November 2021. The Contractor was reminded to prevent the construction material pile within Tree Protection Zone and ensure no works is allowed within the TPZ.

ENVIRONMENTAL COMPLAINT

ES.06. No environmental complaint was received in this Reporting Period.

Table ES-3 Environmental Complaint Summaries in the Reporting Month

Reporting Month		Environmental Complaint Statistics			
		Frequency	Cumulative	Complaint Nature	
1 st – 30 th November	Contract 1	0	1	Air Quality	
2021	Contract 2	0	2	Air Quality	

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES.07. No environmental summons or successful prosecution was recorded in this Reporting Month. The statistics of summons or successful prosecutions are summarized in the following tables.

Table ES-4 Environmental Summons Summaries in the Reporting Month

Reporting Month		Environmental Summons Statistics			
		Frequency	Cumulative	Summons Nature	
1 st – 30 th November	Contract 1	0	0	NA	
2021	Contract 2	0	0	NA	

Table ES-5 Environmental Prosecution Summaries in the Reporting Month

Reporting Month		Environmental Prosecution Statistics			
		Frequency	Cumulative	Prosecution Nature	
1 st – 30 th November	Contract 1	0	0	NA	
2021	Contract 2	0	0	NA	

ES.08. In addition, no complaint and emergency event relating to violation of environmental legislation for illegal dumping and landfilling was received.

REPORTING CHANGE

ES.09. No reporting change was made in the Reporting Month.

SITE INSPECTION

ES.010. In the Reporting Month, joint site inspections for Contract 1 to evaluate the site environmental performance were carried out by the Resident Engineer, ET and the Contractor of the Contract 1 on 4th, 11th, 18th and 25th November 2021. Moreover, joint site inspections for Contract 2 by the RE, ET and the Contractor of Contract 2 were carried out on 4th, 11th, 18th and 25th November 20211. IEC attended the both Contract joint site inspection on 18th November 2021. No non-compliance was noted during the site inspections.

FUTURE KEY ISSUES

- ES.011. The Contractors are reminded to pay special attention on water quality mitigation measures and should fully implement the measures as recommended in the EM&A Manual, in particular to prevent surface runoff and other pollutants from flowing to local stream and Conservation Area.
- ES.012. During dry season, air quality mitigation measures such as wheel wash facilities, watering of haul roads, loose soil construction surface and covering of dusty materials with tarpaulin sheet should be implemented as far as practicable.



ES.013. Construction noise would be a key environmental issue during construction phase of the Project. Noise mitigation measures such as using quiet plants and mobile noise barriers should be implemented in accordance with the EM&A requirement.



Table of Contents

1.	INTRODUCTION	1
	1.1 PROJECT BACKGROUND	1
	1.2 REPORT STRUCTURE	2
2.	PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS	4
	2.1 CONSTRUCTION CONTRACT PACKAGING 2.2 CONSTRUCTION PROGRESS	4 4
	2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS	4
	2.4 SUMMARY OF SUBMISSION UNDER THE ENVIRONMENTAL PERMIT REQUIREMENTS	5
3.	SUMMARY OF IMPACT MONITORING REQUIREMENT	7
٥.	3.1 GENERAL	7
	3.2 MONITORING PARAMETERS	7
	3.3 MONITORING LOCATIONS	7
	3.4 MONITORING FREQUENCY AND PERIOD	9
	3.5 MONITORING EQUIPMENT 3.6 EQUIPMENT CALIBRATION	9 12
	3.7 DATA MANAGEMENT AND DATA QA/QC CONTROL	12
	3.8 DETERMINATION OF ACTION/LIMIT (A/L) LEVELS	12
4.	AIR QUALITY	14
••	4.1 MONITORING RESULTS	14
	4.2 AIR MONITORING EXCEEDANCE	14
5.	CONSTRUCTION NOISE	15
	5.1 MONITORING RESULTS	15
	5.2 Noise Monitoring Exceedance	15
6.	WATER QUALITY	16
	6.1 MONITORING RESULTS	16
	6.2 WATER QUALITY MONITORING EXCEEDANCE	17
7.	ECOLOGY MONITORING	18
	7.1 REQUIREMENT	18
	7.2 METHODOLOGY	18
	 7.3 ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 1) 7.4 ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 2) 	19 21
	7.5 Monitoring of Flora Species of Conservation Interest	22
	7.6 MEASURE FOR PROTECTION OF NESTING BIRD	23
8.	LANDSCAPE AND VISUAL	24
٠.	8.1 REQUIREMENT	24
	8.2 FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH	24
9.	WASTE MANAGEMENT	25
	9.1 GENERAL WASTE MANAGEMENT	25
	9.2 RECORDS OF WASTE QUANTITIES	25
10.	SITE INSPECTION	26
	10.1 REQUIREMENT	26
	10.2 FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH	26
11.	ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	28
	11.1 Environmental Complaint, Summons and Prosecution	28
12.	IMPLEMENTATION STATUS OF MITIGATION MEASURES	29
	12.1 GENERAL REQUIREMENTS	29
	12.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH	30
	12.3 KEY ISSUES FOR THE COMING MONTH	30
13.	CONCLUSIONS AND RECOMMENTATIONS	33
	13.1 CONCLUSIONS 13.2 RECOMMENDATIONS	33 33
	LD.4 DECUMENDATIONS	77



LIST OF TABLES

TABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS FOR CONTRACT 1
TABLE 2-2	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS FOR CONTRACT 2
TABLE 2-3	STATUS OF SUBMISSION AS UNDER FEP FOR CONTRACT 1
TABLE 2-4	STATUS OF SUBMISSION AS UNDER FEP FOR CONTRACT 2
TABLE 3-1	SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2	DESIGNATED AIR QUALITY MONITORING LOCATION UNDER THE PROJECT
TABLE 3-3	DESIGNATED CONSTRUCTION NOISE MONITORING LOCATION UNDER THE PROJECT
TABLE 3-4	DESIGNATED WATER QUALITY MONITORING STATIONS UNDER THE PROJECT
TABLE 3-5	AIR QUALITY MONITORING EQUIPMENT
TABLE 3-6	NOISE MONITORING EQUIPMENT
TABLE 3-7	WATER QUALITY MONITORING EQUIPMENT
TABLE 3-8	ACTION AND LIMIT LEVELS FOR AIR QUALITY MONITORING
TABLE 3-9	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 3-10	ACTION AND LIMIT LEVELS FOR WATER QUALITY
TABLE 4-1	SUMMARY OF AIR QUALITY MONITORING RESULTS AT ASR-1 UNDER CONTRACT 1
TABLE 4-2	SUMMARY OF AIR QUALITY MONITORING RESULTS AT ASR-2 UNDER CONTRACT 2
TABLE 4-3	SUMMARY OF AIR QUALITY MONITORING RESULTS AT ASR-3A UNDER CONTRACT 2
TABLE 5-1	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS UNDER CONTRACT 1
TABLE 5-2	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS UNDER CONTRACT 2
TABLE 6-1	SUMMARY OF WATER QUALITY MONITORING RESULTS – M3 UNDER CONTRACT 1
TABLE 6-2	Summary of Water Quality Monitoring Results (M1, M2 and M4) under Contract 2 $$
TABLE 6-3	SUMMARY OF FIELD MEASUREMENTS FOR WATER QUALITY
TABLE 6-4	ACTION AND LIMIT (A/L) LEVELS EXCEEDANCE RECORD
TABLE 6-5	SUMMARY OF INVESTIGATION OF WATER QUALITY EXCEEDANCE IN THE REPORTING MONTH
TABLE 7-1	ACTION AND LIMIT LEVELS FOR WET WOODLAND HABITATS MONITORING
TABLE 7-2	ACTION AND LIMIT LEVELS FOR NON-WET WOODLAND HABITATS MONITORING
TABLE 7-3	SCHEDULE OF FAUNAL SURVEYS IN EACH YEAR DURING CONSTRUCTION PHASE
TABLE 7-4	RESULT OF FAUNAL SURVEY UNDER CONTRACT 1
TABLE 7-5	RESULT OF FRESHWATER COMMUNITIES SURVEY UNDER CONTRACT 1
TABLE 7-6	RESULT OF FAUNAL SURVEY UNDER CONTRACT 2
TABLE 7-7	RESULT OF FRESHWATER COMMUNITIES SURVEY UNDER CONTRACT 2
TABLE 8-1	LANDSCAPE & VISUAL INSPECTION FINDING FOR CONTRACT 1
TABLE 8-2	LANDSCAPE & VISUAL INSPECTION FINDING FOR CONTRACT 2
TABLE 9-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 9-2	SUMMARY OF QUANTITIES OF C&D WASTES
TABLE 10-1	SITE OBSERVATIONS FOR THE WORKS OF CONTRACT 1
TABLE 10-2	SITE OBSERVATIONS FOR THE WORKS OF CONTRACT 2
TABLE 11-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 11-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 11-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 12-1	Environmental Mitigation Measures
TABLE 12-2	WORK UNDERTAKEN AND MITIGATION MEASURES FOR CONTRACT 1
TABLE 12-3	WORK UNDERTAKEN AND MITIGATION MEASURES FOR CONTRACT 2



LIST OF APPENDICES

APPENDIX A	LAYOUT PLAN OF THE PROJECT
APPENDIX B	ORGANIZATION STRUCTURE AND CONTACT DETAILS OF RELEVANT PARTIES
APPENDIX C	THREE MONTHS ROLLING PROGRAMME
APPENDIX D	DESIGNATED MONITORING LOCATIONS
APPENDIX E	CALIBRATION CERTIFICATES OF MONITORING EQUIPMENT AND LABORATORY CERTIFICATE
APPENDIX F	EVENT AND ACTION PLAN OF AIR QUALITY, NOISE AND WATER QUALITY
APPENDIX G	MONITORING SCHEDULES OF THE REPORTING MONTH AND COMING MONTH
APPENDIX H	MONITORING DATA OF 24-HOUR TSP AIR QUALITY, NOISE AND WATER QUALITY
APPENDIX I	GRAPHICAL PLOTS OF AIR QUALITY, NOISE AND WATER QUALITY
APPENDIX J	METEOROLOGICAL DATA OF THE REPORTING MONTH
APPENDIX K	ECOLOGICAL SURVEY REPORT
APPENDIX L	LANDSCAPE & VISUAL INSPECTION CHECKLIST
APPENDIX M	MONTHLY SUMMARY WASTE FLOW TABLE
APPENDIX N	COMPLAINT LOG
APPENDIX O	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM)
APPENDIX P	ILLUSTRATIONS OF SITE ACTIVITIES



1. INTRODUCTION

1.1 PROJECT BACKGROUND

1.1.1 Civil Engineering and Development Department (CEDD) is the Project Proponent for the Project "Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery". The Project is a Designated Project to be implemented under Environmental Permit No. EP-534/2017/A and FEP-01/534/2017/A. The layout plan of the Project is shown in Appendix A. Major works to be executed under the Project shall include to the following:

A Designated Works under EP-534/2017/A

- (i) Site formation of about 8 hectares of land and associated drainage, sewerage and landscape works for development of Columbarium and Crematorium facilities at the Sandy Ridge Cemetery;
- (ii) Construction of a new road (about 600m) including a section of viaduct connecting the platform for Crematorium and Man Kam To Road and the pick-up/drop-off point at Man Kam To Road;
- (iii) Widening of about 900m of the existing Sha Ling Road;
- (iv) Widening of about 1.4km of the existing Lin Ma Hang Road; and
- (v) Improvement works to the existing barging point at Siu Lam

Non-Designated Works

- (i) Construction of a sewage detention tank complete with odour and septicity control mechanism;
- (ii) Construction of noise barriers along Sha Ling Road;
- (iii) Construction of a new Refuse Collection Point (RCP) near the junction between Man Kam To Road and Sha Ling Road;
- (iv) Landscaping works (including both hard and soft landscape works);
- (v) Associated tree felling, transplanting and compensatory planting works;
- (vi) Associated street lighting, street furniture and road marking, etc.; and
- (vii) Other works which are specified in PS of the Contract.
- 1.1.2 To facilitate the Project management, the Project works were separated into three Contracts to be executed which are described in below sub-sections.
- 1.1.3 Contract No. CV/2016/10 Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery (hereinafter named "Contract 1"):-
 - Site formation of about 1.77 ha of land for the proposed pick-up and drop-off area for shuttle bus operation;
 - Upgrading of a section of 900m existing Sha Ling Road from 3m wide carriageway to 7.3m wide carriageway with footpath at both sides;
 - Construction of one EVA with a total length of about 160m;
 - Construction of noise barriers along Sha Ling Road;
 - Modification of junction between Man Kam To Road and Sha Ling Road;
 - Construction of a new pick up / drop off point at Man Kam To Road;
 - Relocation and construction of a new refuse collection point near junction between Man Kam To Road and Sha Ling Road;
 - Associated geotechnical works including cut and fill slopes, soil nailing works and retaining structures;
 - Associated drainage, sewerage and waterworks along Sha Ling Road; and
 - Associated landscaping works.
- 1.1.4 Contract No. CV/2017/02 Infrastructural Works at Man Kam To Road and Lin Ma Hang Road for Development of Columbarium at Sandy Ridge Cemetery (hereinafter named "Contract 2"):-
 - Construction of a new road connecting Columbarium site to Crematorium site;
 - Construction of one EVA with a total length of about 300m;
 - Widening of a section of 1.4 km long Lin Ma Hang Road (between Man Kam To Road and Ping Yuen River) from 6m wide carriageway to 7.3m with 2m width footpath on both sides;
 - Provision of a pair of lay-by at Lin Ma Hang Road;
 - Construction of a new vehicular access connecting the Sheung Shui Landmark North PTI and Lung Sum Avenue;



- Construction of covered walkway along Fanling Station Road;
- Removal of planters and central divider along Fanling Station Road and San Wan Road;
- Associated drainage, sewerage, waterworks and utility works along Man Kam To Road and Lin Ma Hang Road;
- Associated geotechnical works including cut and fill slopes, soil nailing works and retaining structures; and
- Associated landscaping works.
- 1.1.5 CEDD Contract No. (to be confirmed):-
 - Site Formation for the platform of the columbarium site;
 - Construction of two 2 at-grade access roads;
 - Construction of road junction between Man Kam To Road and the new access road;
 - Associated drainage, sewerage and waterworks along the two new access roads;
 - Associated geotechnical works including cut and fill slopes, soil nailing works and retaining structures; and
 - Associated landscaping works
- 1.1.6 Hsin Chong Tsun Yip Joint Venture (hereafter referred as "HCTYJV") has been awarded Contract 1 on 5 December 2017. According to the Contract requirement, HCTYJV shall take over the responsibility for part of the Environmental Permit No. EP-534/2017 for ease of management, therefore application for Further Environmental Permit was submitted by HCTYJV to EPD on 26 January 2018 and Further Environmental Permit No. FEP-01/534/2017 was granted to HCTYJV by EPD on 23 February 2018. Furthermore, EPD issued Environmental Permit No. FEP-01/534/2017/A on 24 December 2018.
- 1.1.7 Sang Hing Civil Contractors Company Limited (hereinafter referred as "Sang Hing") was awarded Contract 2 on 23 May 2018. The Contract Works is a Designated Project as under Environmental Permit (EP) No. EP-534/2017. Furthermore, EPD issued Environmental Permit No. EP-534/2017/A on 24 December 2018.
- 1.1.8 Action-United Environmental Services & Consulting (AUES) has been commissioned by the Contractors as an Environmental Team (ET) to implement the Environmental Monitoring and Audit (EM&A) programme in accordance with the approved EM&A Manual as well as the associated duties. As part of the EM&A programme, baseline monitoring to determine the ambient environmental conditions was completed before construction work commencement. The Baseline Monitoring Report (air, noise and water) certified by ET Leader (ETL) and verified by Independent Environmental Checker (IEC) was submitted to Environmental Protection Department (EPD) and it was approved by EPD on 25 October 2018.
- 1.1.9 Major construction work of Contract 1 and Contract 2 was commenced on 16 August 2018 and 5 November 2018 respectively.
- 1.1.10 This is the **40**th Monthly EM&A Report summarizing the monitoring results and inspection findings for the period from **1**st to **30**th November **2021**.

1.2 REPORT STRUCTURE

1.2.1 The Monthly EM&A Report is structured into the following sections:-

Section 1 *Introduction*

Section 2 *Project Organization and Construction Progress*

Section 3 *Summary of Monitoring Requirements*

Section 4 *Air Quality Monitoring Results*

Section 5 *Noise Monitoring Results*

Section 6 Water Quality Monitoring Results

Section 7 *Ecology Monitoring Results*

Section 8 *Landscape & Visual*

Section 9 *Waste Management*

Section 10 *Site Inspections*



Section 11 Environmental Complaints and Non-Compliance
 Section 12 Implementation Status of Mitigation Measures
 Section 13 Conclusions and Recommendation



2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

2.1 CONSTRUCTION CONTRACT PACKAGING

- 2.1.1 To facilitate the project management and implementation, the Project was divided by the following contracts:
 - Contract 1 (Contract No. CV/2016/10)
 - Contract 2 (Contract No. CV/2017/02)
 - Contract 3 (Contract No. TBA)
- 2.1.2 Organization structure and contact details of relevant parties with respect to on-site environmental management are shown in *Appendix B*.

2.2 CONSTRUCTION PROGRESS

2.2.1 The three-month rolling construction programme for Contract 1 and Contract 2 are enclosed in *Appendix C*. Construction activities of the Contract 1 and Contract 2 undertaken in the Reporting Month are presented below. The tentative construction activities are summarised in Section 12.2

Contract 1 (CV/2016/10)

- Bulk excavation
- Construction of cut slope, installation of soil nailing and construction of surface channel and planter wall
- Construction of pick-up and drop-off Point near Man Kam To Road
- Construction of storm/ sewer drain
- Laying of watermains
- Construction of Concrete/ Bituminous Pavement

Contract 2 (CV/2017/02)

- Construction of Manhole, gullies, drainage pipe at Lin Ma Hang Road between CH0-50 Northbound & CH780-890 Southbound
- Pipe Jacking works for DN400 watermain in approx. CH0-300 at Man Kam To Road
- DN400 DI Watermain works in approx. CH300-1040 at Man Kam To Road North Slow Lane
- Construction of Manhole, gullies, drainage pipe at Sandy Ridge Road E CH0-300 (~300m)
- Construction of Manhole, gullies, drainage pipe at Sandy Ridge Road F CH640-720 (~80m)
- Construction of Manhole, gullies, drainage pipe at Sandy Ridge Road F CH30-130 (~100m)
- Backfilling of Retaining Wall 12
- Fanling Station Road Covered Walkway
- Lung Sum Avenue road surface modification works

2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

2.3.1 Summary of the relevant permits, licenses, and/or notifications on environmental protection for the Project in this Reporting Month is presented in *Tables 2-1 and 2-2*.

Table 2-1 Status of Environmental Licenses and Permits for Contract 1

Item	Description	License/ Permit ref no.	License/ Permit Status
1	Air Pollution Control	Ref. no. 428909	Valid
	(Construction Dust) Regulation	Acknowledged by EPD on 20/12/2017	
2	Chemical waste Producer	WPN: 5231-641-H3937-01	Valid
	Registration	Issued by EPD on 27/03/2018	
3	Water Pollution Control	License no. WT00030795-2018	Valid
	Ordinance	Issued date: 9/5/2018	
		Expire Date: 31/5/2023	
4	Billing Account for Disposal	Account no.: 7029769	Valid
	of Construction Waste		



Table 2-2 Status of Environmental Licenses and Permits for Contract 2

Item	Description	License/ Peri	nit ref no.	License/ Permit Status
1	Air Pollution Control		Man Kam To Road	Valid
	(Construction Dust)	Acknowledged by EPD on		
	Regulation	14/12/2018	Kong Nga Po Road	
		Ref. no. 440405	Fanling Station Road	Valid
		Acknowledged by EPD on		
		14/12/2018		
			Sa Ling Road (Sandy	Valid
		Acknowledged by EPD on	Ridge Cemetery)	
		14/12/2018		
			Lin Ma Hang Road	Valid
		Acknowledged by EPD on		
		14/12/2018	Wu Nga Yiu)	
			Lung Sum Avenue	Valid
		Acknowledged by EPD on	(near Landmark North)	
	C1 1 1	14/12/2018		X 7 1' 1
2	Chemical waste	WPN: 5213-641-S4151-01		Valid
	Producer Registration	Issued by EPD on 04/02/20		X 7 1' 1
3	Water Pollution	License no:	Man Kam To Road &	Valid
	Control Ordinance	WT00032936-2018	Lin Ma Hang Road,	
		Issued date: 16/01/2019	Man Kam To	
		Expire Date: 31/01/2024	Columbarium at	Valid
		License no: WT00033335-2019	Sandy Ridge	v and
		Issued date: 29/03/2019	Cemetery	
		Expire Date: 31/03/2024	Cemetery	
		License no:	Fanling Station Road	Valid
		WT00034717-2019	anning Station Road	v and
		Issued date: 9/10/2019		
		Expire Date: 31/10/2024		
4	Billing Account for	Account no.: 7031098	L	Valid
	Disposal of			
	Construction Waste			
5	Construction Noise	GW-RN0226-21		Valid
	Permit	(1 May 2021 – 30 Oct 2021	1)	

2.4 SUMMARY OF SUBMISSION UNDER THE ENVIRONMENTAL PERMIT REQUIREMENTS

2.4.1 *Tables 2-3 to 2-4* summarized the submission status under the EP and/or FEP stipulation in the Reporting Month.

Table 2-3 Status of Submission as under FEP

Item	EP and / or FEP Stipulation	Description	Status	
1		Management organization of : i) the main construction companies; ii) ET;	Submitted and no approval is	
		and iii) IEC and the supporting team	required.	
2	Condition 2.11 of FEP	1 01 0	Submitted and no approval is	
		construction works; and ii) Location plan of all construction works	required.	
3	Condition 2.12 of FEP	Contamination Assessment Plan (CAP)	Approved by EPD on 27 May 2019	
4	Condition 2.13 of FEP	Grassland Reinstatement Plan	Pending approval	
5	Condition 2.14 to 2.16 of		Approved by EPD on 12	
	FEP		October 2018	
		for Contract 1		



Item	EP and / or FEP Stipulation	Description	Status	
6	Condition 2.17 of FEP	Woodland Compensation Plan (Rev.05)	Approved by EPD on 30 Jun 2020	
7	Condition 2.18 of FEP	Monitoring and Survey Plan for Golden-headed Cisticola for Contract 1 (Rev.02)	Approved by EPD on 22 Oct 2019	
8	Condition 2.20 of FEP	Landscape & Visual Mitigation and Tree Preservation Plan(s) Contract 1 (Rev.04)	Pending approval	
9	Condition 2.22 of FEP	Traffic Noise Mitigation Plan Contract 1 (Rev. 4)	Pending approval	
10	Condition 3.3 of the FEP	Baseline Monitoring Report (Air, Noise and Water)	Approved by EPD on 25 October 2018	
11	Condition 4.2 of the FEP	The Contract Internet website	Internet website address has notified EPD on 15 Jun 2018 and no approval is required.	

Table 2-4 Status of Submission as under EP

Item	EP and / or FEP Stipulation	Description	Status	
1	Condition 2.10 of EP	Management organization of: i) the main construction companies; ii) ET; and iii) IEC and the supporting team	Submitted and no approval is required.	
2	Condition 2.11 of EP	i) Detailed phasing programme of all construction works; and ii) Location plan of all construction works	Submitted and no approval is required.	
3	Condition 2.12 of EP	Layout Plan for the proposed footpath at Lin Ma Hang Road		
4	Condition 2.13 of EP	Contamination Assessment Plan (CAP)	Approved by EPD on 27 May 2019	
5	Condition 2.14 of EP	Grassland Reinstatement Plan	Pending approval	
6	Condition 2.15 to 2.17 of EP	Vegetation Survey Report and Vegetation Transplantation Proposal under Contract 2	Pending approval	
7	Condition 2.18 of EP	Woodland Compensation Plan (Rev.05)	Approved by EPD on 30 Jun 2020	
8	Condition 2.19 of EP	Monitoring and Survey Plan for Golden-headed Cisticola Contract 2	Pending approval	
9	EP	Landscape & Visual Mitigation and Tree Preservation Plan(s) Contract 2	Pending approval	
10	Condition 2.23 of EP	Traffic Noise Mitigation Plan Contract 2	Pending approval	
11	Condition 3.3 of the EP	Baseline Monitoring Report (Air, Noise and Water)	Approved by EPD on 25 October 2018	
12	Condition 4.2 of the EP	The Contract Internet website	Internet website address has notified EPD on 15 June 2018 and no approval is required.	



3. SUMMARY OF IMPACT MONITORING REQUIREMENT

3.1 GENERAL

- 3.1.1 The EM&A requirements are set out in the Approved EM&A Manual. Environmental issues such as air quality, construction noise, water quality and ecology were identified as the key issues during the construction phase of the Project.
- 3.1.2 A summary of construction phase EM&A requirements are presented in the sub-sections below.

3.2 MONITORING PARAMETERS

- 3.2.1 The EM&A impact monitoring shall cover the following environmental aspect:
 - Air quality;
 - Construction noise;
 - Water quality;
 - Ecology; and
 - Landscape and visual
- 3.2.2 A summary of the monitoring parameters is presented in *Table 3-1* below

Table 3-1 Summary of EM&A Requirements

Environmental Issue	Parameters		
Air Quality	1-hour TSP;24-hour TSP		
Noise	 Leq_(30min) during normal working hours.; and Leq_(15min) during the construction works undertaken in Restricted Hours 		
Water Quality	In-situ Measurements Dissolved Oxygen Concentration (mg/L) & Saturation (%); Temperature (°C); Turbidity (NTU); Salinity (ppm) pH unit; Water depth (m); and Stream Flow Velocity (m/sec). Laboratory Analysis Suspended Solids (mg/L)		
Ecology	Ecologically sensitive habitats (wetland habitats and non-wetland habitats)		

3.3 MONITORING LOCATIONS

- 3.3.1 According to the Approved EM&A Manual of the Project Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery, the designated monitoring locations for air quality, noise, water quality and ecology under the monitoring programme, is shown in Appendix D.
- 3.3.2 Since the Project was divided into three Works Contracts and all Contracts will be commenced at different time, the construction phase impact monitoring will only be performed at the Contract-related monitoring stations upon commencement of each Contract Works.

Air Quality

3.3.3 There were three (3) designated air quality monitoring stations recommended in the Approved EM&A Manual Section 5.6.1.1. There was proposed relocation of air quality monitoring location ASR-3 in October 2018 since the landlord refused to set up the HVS at his premises and nearby Conservation Area due to noise nuisance and Muk Wu Nga Yiu House No. 2A was proposed as alternative location ASR-3a. The proposal dated on 9 November 2018 which verified by IEC was submitted to EPD for approval. Based on rationale in Section 3.3.2, the Contract-related air quality monitoring location for construction phase were summarized in *Table 3-2* and illustrated in *Appendix D*.



Table 3-2 Designated Air Quality Monitoring Location under the Project

Location ID	Description in EM&A Manual	Location	Related Work Contract
ASR-1	Village House along Man Kam To	Sha Ling Village House No.6	Contract 1
	Road		
ASR-2	Village House at San Uk Ling	San Uk Ling Village House No.1	Contract 2
ASR-3	Village House at Muk Wu Nga Yiu	Muk Wu Nga Yiu House No.28	Contract 2
ASR-3a (#)	Village House at Muk Wu Nga Yiu	Muk Wu Nga Yiu House No.2A	Contract 2

Remark: (#) There was proposed relocation of air quality monitoring location ASR-3 in October 2018. The proposal dated on 9 November 2018 after verified by IEC was submitted to EPD for approval.

- 3.3.4 If the designated monitoring location is required to relocate, alternative monitoring location shall agree with IEC and seek for EPD approval which shall meet the following criteria:
 - i) Be at the site boundary or such locations close to the major dust emission source;
 - ii) Close to the sensitive receptors;
 - iii) Take into account the prevailing meteorological conditions;
 - iv) For monitoring location located in the vicinity of the ASRs, care shall be taken to cause minimal disturbance to the occupants during monitoring.
 - v) When positioning the HVS, the following points shall be noted:
 - a. a horizontal platform with appropriate support to secure the samples against gusty wind shall be provided;
 - b. no two samplers shall be placed less than 2m apart;
 - c. the distance between the HVS and an obstacle, such as buildings, must be at least twice the height that the obstacle protrudes above the HVS;
 - d. a minimum of 2 m separation from walls, parapets and penthouses is required for HVS at the rooftop;
 - e. a minimum of 2 m separation from any supporting structure, measures horizontally is required;
 - f. no furnace or incinerator flue is nearby;
 - g. airflow around the sampler is unrestricted;
 - h. the HVS is more than 20 m from the dripline;
 - i. any wire fence and gate to protect the HVS, shall not cause any obstruction during monitoring;
 - j. permission must be obtained to set up the HVS and to obtain access to the monitoring stations; and
 - k. a secured supply of electricity is needed to operate the HVS.

Construction Noise

3.3.5 There were four (4) designated noise monitoring locations recommended in the Approved EM&A Manual Section 6.5.1.1. Based on rationale in Section 3.3.2, the Contract-related noise quality monitoring location for construction phase were summarized in *Table 3-3* and illustrated in *Appendix D*.

Table 3-3 Designated Construction Noise Monitoring Location under the Project

Locatio n ID	Description in EM&A Manual	Location	Related Work Contract	
CN-1	Village house to the west of	Village house to the west of Sha Ling	Contract 1	
	Sha Ling Road	Road (free field condition)		
CN-2	Village house to the north of	Sha Ling Village House No. 25 (free	Contract 1	
	Man Kam To Road	field condition)	& 3	
CN-3	Village house near San Uk	San Uk Ling Village House No. 18 (free	Contract 2	
	Ling	field condition)		
CN-4	Village house of Muk Wu	Muk Wu Village House No. 267 (1m	Contract 2	
		façade from the building)		



Water Quality

3.3.6 There were four (4) water quality monitoring locations recommended in the Approved EM&A Manual Section 7.6.1.2. The locations and coordinates of water quality monitoring were listed in *Table 3-4*. Based on rationale in Section 3.3.2, the Contract-related water quality monitoring location for construction phase were summarized in *Table 3-4* and illustrated in *Appendix D*.

Table 3-4 Designated Water Quality Monitoring Stations under the Project

Proposed	Co-ordinates		Description	Related Work	
Location ID	North	East	Description	Contract	
M1	843 431	831 308	Midstream of Nam Hang Stream	Contract 2	
M2	843 840	831 101	Downstream of Nam Hang Stream	Contract 2	
M3	843 509	830 040	Wetland in the Conservation Area near Yuen Leng Chai	Contract 1	
M4	843 997	831 783	Watercourse across Lin Ma Hang Road, running from east of San Uk Ling to Man Kam To Boundary Control Point	Contract 2	

3.4 MONITORING FREQUENCY AND PERIOD

3.4.1 The requirements of impact monitoring were stipulated in *Sections 5.8.1.1*, *6.7.1.1* and *7.8.1.4* of the approved *EM&A Manual* and presented as follows.

Air Quality Monitoring

- 3.4.2 Monitoring frequency for air quality impact monitoring is as follows:
 - 1-Hour TSP 3 sets of 1-hour TSP monitoring shall be carried out once every six days during construction periods
 - 24-Hour TSP 24-hour TSP monitoring shall be carried out every six days during construction periods

Noise Monitoring

3.4.3 Noise impact monitoring shall be carried out once per week during construction periods. The noise measurement for the time period between 0700 and 1900 hours shall be measured in terms of L_{eq} (30 minutes) or 6 sets of L_{eq} (5mins).

Water Quality Monitoring

3.4.4 The monitoring frequency shall be 3 days per week during construction phase and the interval between two sets of monitoring shall not be less than 36 hours.

3.5 MONITORING EQUIPMENT

3.5.1 The monitoring equipment using for the EM&A program as proposed by the ET shall be verified by the IEC.

Air Quality Monitoring

- 3.5.2 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. If ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to IEC for approval.
- 3.5.3 The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.
- 3.5.4 All equipment used by ET for air quality monitoring is listed in *Table 3-5*.

Table 3-5 Air Quality Monitoring Equipment

Equipment	Model			
24-hour TSP				
High Volume Air Sampler (HVAS)	TISCH High Volume Air Sampler, HVS Model TE-5170			
Calibration Kit	TISCH Model TE-5025A			
1-Hour TSP				
Portable Dust Meter	Sibata LD-3 Laser Dust monitor Particle Mass Profiler & Counter			



Wind Data Monitoring Equipment

- 3.5.5 According to the approved EM&A Manual, wind data monitoring equipment shall also be provided and set up for logging wind speed and wind direction near the dust monitoring locations. The equipment installation location shall be proposed by the ET and agreed with the IEC. For installation and operation of wind data monitoring equipment, the following points shall be observed:
 - 1) The wind sensors should be installed 10 m above ground so that they are clear of obstructions or turbulence caused by buildings.
 - 2) The wind data should be captured by a data logger. The data shall be downloaded for analysis at least once a month.
 - 3) The wind data monitoring equipment should be re-calibrated at least once every six months.
 - 4) Wind direction should be divided into 16 sectors of 22.5 degrees each.
- 3.5.6 ET has liaised with the premises owners/ landlords to grant the permission for the HVS installation. However, they rejected to set up wind data monitoring equipment installation in their premises.
- 3.5.7 Under this situation, the ET proposed to obtain representative wind data from the Hong Kong Observatory Ta Kwu Ling Weather Station. Ta Kwu Ling Station is located near the Project site which situated at the sea level above 15mPD and the wind data monitoring equipment is installed 10 m above the existing ground.

Noise Monitoring

- 3.5.8 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in ms⁻¹ before each noise monitoring event. Noise measurements should not be made in fog, rain, wind with a steady speed exceeding 5 m s⁻¹ or wind with gusts exceeding 10 m s⁻¹.
- 3.5.9 Noise monitoring equipment used for impact monitoring is listed in *Table 3-6*.

Table 3-6 Noise Monitoring Equipment

Equipment	Model
Integrating Sound Level Meter	Rion NL-52 Sound Level Meter
Calibrator	Rion NC-73 Acoustical Calibrator
Portable Wind Speed Indicator	Testo Anemometer

3.5.10 Sound level meters listed above comply with the *International Electrotechnical Commission Publications 651: 1979 (Type 1)* and *804: 1985 (Type 1)* specifications, as recommended in TM issued under the NCO.

Water Quality Monitoring

3.5.11 Water quality parameters include dissolved oxygen, water temperature & depth, turbidity, salinity, pH and stream flow velocity shall be measured *in-situ*, and suspended solids shall be analyzed by a HOKLAS-accredited testing laboratory.

Dissolved Oxygen and Temperature Measurement

- 3.5.12 The dissolved oxygen (DO) measuring instruments should be portable and weatherproof. The equipment should also complete with cable and sensor, and DC power source. It should be capable of measuring:
 - A DO level in the range of 0 20 mg/L and 0 200% saturation; and
 - A temperature of 0 45 degree Celsius.
- 3.5.13 The equipment should have a membrane electrode with automatic temperature compensation complete with a cable.



3.5.14 Should salinity compensation not be built-in to the DO equipment, in-situ salinity should be measured to calibrate the DO measuring instruments prior to each measurement.

Turbidity Measurement

3.5.15 The turbidity measuring instruments should be a portable and weatherproof with DC power source. It should have a photoelectric sensor capable of measuring turbidity level between 0–1000 NTU (for example, Hach model 2100Q or an approved similar instrument).

Salinity Measurement

3.5.16 A portable salinometer capable of measuring salinity in the range of 0–40 parts per thousand (ppt) should be provided for measuring salinity of the water at each monitoring location.

pH Measurement

3.5.17 A portable pH meter capable of measuring a range between 0.0 and 14.0 should be provided to measure pH under the specified conditions accordingly to the APHA Standard Methods.

Water Depth Measurement

3.5.18 A portable, battery-operated echo sounder or an approved similar instrument should be used for water depths determination at each designated monitoring station.

Stream Flow Velocity Equipment

3.5.19 Since the EM&A Manuals do not specified instrument to use stream flow velocity measurement, the monitoring of stream flow velocity is therefore proposed to be conducted by using a flow probe which is a digital water velocity meter.

Water Sampling Equipment

- 3.5.20 A water sampler is required for suspended solid (SS) monitoring. A water sampler e.g. Kahlsico Water Sampler, which is a transparent PVC cylinder with capacity not less than 2 litres, will be used for water sampling if water depth over than 0.5m.
- 3.5.21 For sampling from very shallow water depths e.g. <0.5 m, water sample will be collected from water surface below 100mm using plastic bottle to avoid inclusion of bottom sediment or humus. Moreover, Teflon/stainless steel bailer or self-made sampling buckets maybe used for water sampling. The equipment used for sampling will be depended the sampling location and depth situations.

Sample Containers and Storage

- 3.5.22 Water samples for suspended solid should be stored in high density polythene bottles with no preservative added, packed in ice (cooled to 4° C without being frozen) and delivered to the laboratory within 24 hours of collection and be analyzed as soon as possible after collection.
- 3.5.23 Analysis of suspended solids should be carried out in a HOKLAS or other accredited laboratory. Water samples of about 1L should be collected at the monitoring stations for carrying out the laboratory suspended solids determination. The SS determination work should start within 24 hours after collection of the water samples. The SS analyses should follow the *APHA Standard Methods* 2540D with Limit of Reporting of 2 mg/L.
- 3.5.24 Details of the equipment used for water quality monitoring are listed in *Table 3-7* below.

Table 3-7 Water Quality Monitoring Equipment

Equipment	Model
Water Depth Detector	Tape measures
Water Sampler	A 2-litre transparent PVC cylinder with latex cups at both ends or Teflon/stainless steel bailer or self-made sampling bucket
Thermometer & DO meter	YSI Professional Plus/ YSI 550A
pH meter	AZ8685 pH meter / YSI Professional Plus / YSI Professional DSS



Equipment	Model		
Turbidimeter	Hach 2100Q/ YSI Professional Plus / YSI Professional DSS		
Salinometer	Atago refractometer Atago S Salinity Meter / YSI Professional Plus / YSI Professional DSS		
Stream Flow Velocity	FP211 Global Flow Probe		
Sample Container	High density polythene bottles (provided by laboratory)		
Storage Container	'Willow' 33-litter plastic cool box with Ice pad		

3.5.25 Furthermore, Suspended solids (SS) analysis was carried out by *ALS Technichem (HK) Pty Ltd*. Which is one a local HOKLAS-accredited laboratory

3.6 EQUIPMENT CALIBRATION

- 3.6.1 The HVAS is operated and calibrated on a regular basis in accordance with the manufacturer's instruction using Tisch Calibration Kit Model TE-5025A. Calibration would carry out at fortnightly interval. The calibration data are properly documented and the records are maintained by ET for future reference. Furthermore, Tisch Calibration Kit will be calibrated by the manufacturer in yearly basis.
- 3.6.2 The 1-hour TSP meter calibrated by a local HOKLAS-accredited laboratory would be undertaken in yearly basis. Zero response of the equipment was checked before and after each monitoring event.
- 3.6.3 The sound level meter and acoustic calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis.
- 3.6.4 The multi-parameter Water Quality Monitoring System is calibrated by HOKLAS accredited laboratory of three month intervals.
- 3.6.5 All updated calibration certificates of the monitoring equipment used for the impact monitoring program in this Reporting Month are attached in *Appendix E*.

3.7 DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.7.1 The impact monitoring data are handled by the ET's systematic data recording and management, which complies with in-house Quality Management System. Standard Field Data Sheets (FDS) are used in the impact monitoring program.
- 3.7.2 The monitoring data recorded in the equipment e.g. 1-hour TSP meter, noise meter and Multi-parameter Water Quality Monitoring System are downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data are input into a computerized database properly maintained by the ET. The laboratory results are input directly into the computerized database and QA/QC checked by personnel other than those who input the data. For monitoring activities require laboratory analysis, the local laboratory follows the QA/QC requirements as set out under the HOKLAS scheme for all laboratory testing.

3.8 DETERMINATION OF ACTION/LIMIT (A/L) LEVELS

3.8.1 The baseline monitoring results form the basis for determining the environmental acceptance criteria for the impact monitoring. The air quality, construction noise and water quality criteria, namely Action and Limit levels were established according to Approved EM&A Manual, and they are listed in *Tables 3-8, 3-9* and *3-10* below.

Table 3-8 Action and Limit Levels for Air Quality Monitoring

Monitoring Station	Action Level (μg /m³)		Limit Level (µg/m³)	
Monitoring Station	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
ASR-1	331	181	500	260
ASR-2	316	165	500	260
ASR-3	307	160	500	260



Table 3-9 Action and Limit Levels for Construction Noise

Monitoring Location	Action Level	Limit Level in dB(A)		
Monitoring Location	Time Period: 0700-1900 hours on normal weekdays			
CN-1,CN-2, CN-3, CN-4	When one or more documented complaints are received	75 dB(A)		

Note: * Reduces to 70 dB(A) for schools and 65 dB(A) during the school examination periods.

Table 3-10 Action and Limit Levels for Water Quality

Domomotor	Performance	Monitoring Location							
Parameter	criteria	M1	M2	M3	M4				
DO (ma/L)	Action Level	3.03	4.99	4.58	3.62				
DO (mg/L)	Limit Level	2.97	4.90	4.49	3.52				
Turbidity	Action Level	7.1	39.7	5.6	5.4				
(NTU)	Limit Level	7.6	42.2	5.9	5.9				
SS (mg/L)	Action Level	8.5	29.0	9.3	4.8				
	Limit Level	10.1	31.0	9.5	5.0				

Notes:

3.8.2 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan enclosed in Appendix F.

[•] For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits

[•] For turbidity and SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.



4. AIR QUALITY

4.1 MONITORING RESULTS

- 4.1.1 In the Reporting Month, air quality monitoring was performed at all designated locations. Impact monitoring schedule provided to all relevant parties was shown in Appendix G.
- 4.1.2 In this Reporting Month, there were 5 sessions of 24-hour TSP and 15 sessions of 1-hour TSP undertaken at each designated station for air quality monitoring. The air quality monitoring results are summarized in *Tables 4-1* to 4-3. The database of 24-hour TSP is shown in *Appendix H* and the graphical plots of monitoring result are shown in *Appendix I*.

Table 4-1 Summary of Air Quality Monitoring Results at ASR-1 under Contract 1

	24-hour	\\ \\ \\ \\ \\ \\ \\ \\ \\ \\ \\ \\ \\					
Date	$TSP (\mu g/m^3)$	Date	Start Time	1 st hour measured	2 nd hour measured	3 rd hour measured	
5-Nov-21	79	2-Nov-21	13:04	84	78	74	
11-Nov-21	77	8-Nov-21	10:13	74	76	79	
17-Nov-21	38	13-Nov-21	9:24	71	84	78	
23-Nov-21	140	19-Nov-21	9:27	75	71	77	
29-Nov-21	137	25-Nov-21	13:19	81	79	83	
Average	94	Average			78		
(Range)	(38 - 140)	(Range	a)	(71 - 84)			

Table 4-2 Summary of Air Quality Monitoring Results at ASR-2 under Contract 2

	24-hour	24-hour 1-hour TSP (μg/m³)					
Date	$TSP (\mu g/m^3)$	Date	Start Time	1 st hour measured	2 nd hour measured	3 rd hour measured	
5-Nov-21	17	2-Nov-21	13:12	83	87	78	
11-Nov-21	24	8-Nov-21	10:18	77	75	74	
17-Nov-21	30	13-Nov-21	9:31	84	80	77	
23-Nov-21	33	19-Nov-21	9:34	66	68	64	
29-Nov-21	19	25-Nov-21	13:11	78	82	74	
Average	25	Average			76		
(Range)	(17 - 33)	(Range	e)		(64 - 87)		

Table 4-3 Summary of Air Quality Monitoring Results at ASR-3a under Contract 2

	24-hour	1-hour TSP (μg/m³)						
Date	TSP $(\mu g/m^3)$	Date	Start Time	1 st hour measured	2 nd hour measured	3 rd hour measured		
5-Nov-21	15	2-Nov-21	13:18	94	78	84		
11-Nov-21	32	8-Nov-21	10:26	76	77	74		
17-Nov-21	72	13-Nov-21	9:38	84	81	79		
23-Nov-21	43	19-Nov-21	9:41	71	66	68		
29-Nov-21	43	25-Nov-21	13:04	82	81	87		
Average	41	Average			79			
(Range)	(15 - 72)	(Range	()	(66 - 94)				

4.2 AIR MONITORING EXCEEDANCE

4.2.1 As shown in *Tables 4-1 to 4-3*, the monitoring results of 24-hour and 1-hour TSP monitoring in the Reporting Month were below the Action/ Limit Level. No Notification of Exceedance (NOE) of air quality monitoring criteria was issued and therefore corrective action was not required. The meteorological data during the impact monitoring days are summarized in *Appendix J*.



5. CONSTRUCTION NOISE

5.1 MONITORING RESULTS

- 5.1.1 In the Reporting Month, noise monitoring was performed at all designated locations. Impact monitoring schedule provided to all relevant parties was shown in *Appendix G*.
- 5.1.2 In this Reporting Month, 4 sessions of noise monitoring were undertaken at each designated noise monitoring location. The sound level were set in a free field situation for CN1, CN2 and CN3 and therefore a façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines. The monitoring result of noise monitoring is show in *Tables 5-1 and 5-2* and the graphical plots are shown in *Appendix I*.

Table 5-1 Summary of Construction Noise Monitoring Results under Contract 1

	Construction Noise Level (L _{eq30min}), dB(A)								
Date	Start Time	CN1(*)	Start Time	CN2(*)					
2-Nov-21	13:00	69	13:33	60					
8-Nov-21	10:15	67	10:55	63					
19-Nov-21	9:25	66	11:39	64					
25-Nov-21	13:00	62	13:36	62					
Limit Level		7	75 dB(A)						

^(*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

Table 5-2 Summary of Construction Noise Monitoring Results under Contract 2

	Construction Noise Level $(L_{eq30min})$, $dB(A)$								
Date	Start Time	CN3 (*)	Start Time	CN4					
2-Nov-21	14:06	50	14:41	58					
8-Nov-21	13:00	56	13:45	60					
19-Nov-21	15:15	58	15:52	58					
25-Nov-21	14:11	14:11 55 14.47 67							
Limit Level		7	75 dB(A)						

 $^{(*) \} A \ façade \ correction \ of \ +3dB(A) \ has \ been \ added \ according \ to \ acoustical \ principles \ and \ EPD \ guidelines.$

5.1.3 Prior and after noise monitoring, the accuracy of the sound level meter has been checked by an acoustic calibrator to ensure the measurement within acceptance range of ± 0.5 dB. Moreover, wind speed checked by portable wind speed meter has been performed before noise monitoring. No noise measurement was performed in fog, rain, wind with a steady speed exceeding 5 m s⁻¹ or wind with gusts exceeding 10 m s⁻¹.

5.2 Noise Monitoring Exceedance

5.2.1 As shown in *Tables 5-1 and 5-2*, no Limit Level exceedance for noise monitoring exceedance was recorded in the Reporting Month. Moreover, no noise complaint (which triggered Action Level) was received. No Notification of Exceedance (NOE) of construction noise criterion was issued and no corrective action was therefore required.



6. WATER QUALITY

6.1 MONITORING RESULTS

- 6.1.1 In the Reporting Month, water quality monitoring was performed at all designated locations. Impact monitoring schedule provided to all relevant parties was shown in *Appendix G*.
- 6.1.2 In the Reporting Month, a total of *13* monitoring days were carried out for water quality impact monitoring. During the Reporting Month, the channel of M2 was dried up / too shallow and representative water sampling was unable be carried out and notification was provided to relevant parties in the following days of the events.
- 6.1.3 The monitoring result of key parameters including Dissolved Oxygen, Turbidity and Suspended Solids are summarized in *Tables 6-1* and *6-2*. Detailed monitoring results including in-situ measurements and laboratory analysis data are shown in *Appendix H* and graphical plots for monitoring result are shown in *Appendix I*.

Table 6-1 Summary of Water Quality Monitoring Results – M3 under Contract 1

		Parameters	
Date	DO (Averaged) (mg/L)	Turbidity (Averaged) (NTU)	Suspended Solids (Averaged) (mg/L)
1-Nov-21	7.47	1.3	<2
3-Nov-21	7.54	1.3	2.0
5-Nov-21	7.47	0.9	<2
8-Nov-21	7.86	1.1	<2
10-Nov-21	7.95	0.6	<2
12-Nov-21	7.43	1.7	3.0
15-Nov-21	7.85	2.1	2.0
17-Nov-21	7.51	1.5	2.5
19-Nov-21	7.53	1.0	<2
22-Nov-21	7.67	1.9	2.0
24-Nov-21	7.68	1.4	2.0
26-Nov-21	8.02	2.1	<2
29-Nov-21	7.85	2.2	<2

Table 6-2 Summary of Water Quality Monitoring Results (M1, M2 and M4) under Contract 2

				Pa	rameter	`S				
Date		(Average (mg/L)	d)		Turbidity (Averaged) (NTU)			Suspended Solids (Averaged) (mg/L)		
	M1	M2	M4	M1	M2	M4	M1	M2	M4	
1-Nov-21	7.78	#	7.97	3.3	#	4.4	4.0	#	3.5	
3-Nov-21	7.74	#	7.88	2.7	#	2.1	4.0	#	<2	
5-Nov-21	7.68	#	7.84	2.4	#	1.6	4.5	#	<2	
8-Nov-21	7.87	#	7.88	2.9	#	1.4	3.0	#	<2	
10-Nov-21	8.18	#	8.12	0.6	#	1.2	4.0	#	<2	
12-Nov-21	7.83	#	8.13	1.2	#	1.3	3.5	#	<2	
15-Nov-21	8.04	#	8.34	2.8	#	1.3	3.5	#	<2	
17-Nov-21	8.06	#	7.50	2.4	#	1.2	3.5	#	<2	
19-Nov-21	7.81	#	7.35	1.2	#	1.1	2.5	#	<2	
22-Nov-21	7.92	#	7.21	2.3	#	1.2	3.5	#	<2	
24-Nov-21	8.27	#	6.98	1.9	#	1.0	3.5	#	<2	
26-Nov-21	8.32	#	7.78	2.1	#	1.5	<2	#	<2	
29-Nov-21	8.25	#	8.55	3.0	#	0.9	<2	#	<2	

Remarks: (#) The channel of M2 was dried up / too shallow and representative water sampling was unable be carried out.



6.1.4 During the Reporting Month, field measurements including temperature of stream water, salinity concentrations, pH values and the stream flow velocity for all monitoring locations are summarized in *Table 6-3*.

Table 6-3 Summary of Field Measurements for Water Quality

		Parameters of field measurements											
Monitoring Location	pH (Averaged)				Temp (Averaged)		Water Flow (Averaged) (m/s)						
Location	min	max	(ppt) min max		min max		min	max					
M1	6.9	8.3	0.03	0.06	15.6	23.6	<0.1	<0.1					
M2													
M3	6.9	8.2	0.02	0.02	16.3	24.0	< 0.1	< 0.1					
M4	6.9	8.2	0.02	0.05	16.2	24.1	< 0.1	< 0.1					

6.2 WATER QUALITY MONITORING EXCEEDANCE

6.2.1 In this Reporting Month, there were no exceedances of water quality parameters recorded. The summary of non-compliance of water quality performance is shown in *Table 6-4*.

Table 6-4 Action and Limit (A/L) Levels Exceedance Record

Station	D	DO		Turbidity		SS	To Excee	tal dance	Project excee	Related dance
	Action	Limit	Action	Limit	Action	Limit	Action	Limit	Action	Limit
M1	0	0	0	0	0	0	0	0	0	0
M2	0	0	0	0	0	0	0	0	0	0
M3	0	0	0	0	0	0	0	0	0	0
M4	0	0	0	0	0	0	0	0	0	0

6.2.2 Notification of Exceedance (NOE) and the investigation for exceedance in the Reporting Month is summarized in *Table 6-5*.

Table 6-5 Summary of Investigation of Water Quality Exceedance in the Reporting Month

Date of Exceedance	Exceeded Parameter	Cause of Water Quality Exceedance



7. ECOLOGY MONITORING

7.1 REQUIREMENT

- 7.1.1 According to approved EIA report (AEIAR-198/2016), habitat types within project boundary comprise of watercourse, grassland, upland grassland, plantation, woodland and developed area. Natural habitats were of moderate ecological value in terms of species diversity, species rarity, species abundance, ecological linkage as well as nursery. Moreover, 0.3ha of wet woodland on the northern side of Sandy Ridge was deemed habitat with high ecological value. Four types of habitats were regarded as ecologically sensitive habitats, namely wet woodland, watercourses, upland grassland and woodland. Considering human disturbance in upcoming construction and operation phases, ecologically sensitive habitats shall be monitored in accordance with EM&A Manual.
- 7.1.2 The objective of ecologically sensitive habitats monitoring is to evaluate the effectiveness of measures to minimize impacts on concerned habitats from disturbance and pollution. In order to monitor the effectiveness of the measures to the minimize impact on ecologically sensitive habitats from disturbance and pollution, monthly monitoring during construction and operation phases is required as specified in EM&A Manual. Standard faunal transect and sampling surveys cover both wetland habitats (wet woodland and watercourse) and non-wetland habitats (upland grassland and woodland).

7.2 METHODOLOGY

7.2.1 Wetland habitats include wet woodland and watercourses. Monitoring surveys using standardized quantitative methodology will conduct at fixed points. For seasonal watercourse, the survey will be conducted whenever the habitat appears. Measures to respond to decreases in numbers of aquatic fauna using the wetland habitats and Action/Limit levels to trigger these measures are detailed in *Table 7-1*.

Table 7-1 Action and Limit Levels for Wet Woodland Habitats Monitoring

Action Level	Response	Limit Level	Response
Reduction in	Investigate cause and if	Reduction in	Investigate cause and if cause
taxa diversity by	cause identified as related	taxa diversity by	identified as related to the
30%	to the project instigate	50%	project instigate remedial
	remedial action to remove		action.
	or reduce source of		
	disturbance.		

Remarks: Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna

7.2.2 Non-wetland habitats consist of upland grassland and woodland. Monthly quantitative surveys of non-aquatic fauna will be conducted using standard route transect counts. Measures to respond to decreases in numbers of non-aquatic fauna using the non-wetland habitats and Action/Limit levels to trigger these measures are detailed in *Table 7-2*.

Table 7-2 Action and Limit Levels for Non-Wet Woodland Habitats Monitoring

Action Level	Response	Limit Level	Response
Reduction in	Investigate cause and if	Reduction in	Investigate cause and if cause
species diversity	cause identified as related	species diversity	identified as related to the
by 30%	to the project instigate	by 50%	project instigate remedial
	remedial action to remove		action.
	or reduce source of		
	disturbance.		

Remarks: Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna

7.2.3 The ecological survey includes all taxa being investigated in accordance with EIA report. Schedule of faunal surveys in each year during construction phase is presented in *Table 7-3*.

Table 7-3 Schedule of Faunal Surveys in each year During Construction Phase

Month	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Mammals						V	V		V	V		V
Birds (day)				V		V	V		V	V	V	V



Month	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Birds (night)												
Herpetofauna						√	V					
Dragonflies					V		√					
Butterflies												
Aquatic fauna												

Mammal Survey

7.2.4 Mammal surveys will be conducted along the proposed transects (shown in *Appendix K* - Ecological Survey Reports) in during both daytime and night time periods. Along with direct observations, other field signs, such as scats and tracks, will be searched and recorded if present.

Bird Survey

7.2.5 Bird surveys will be conducted along the transects (shown in *Appendix K* - Ecological Survey Reports) during the surveys, species and their vocalizing individuals recorded will be enumerated and recorded according to the habitat(s) they are utilizing.

Herpetofauna Survey

7.2.6 Reptile and amphibian surveys will be conducted along transects (shown in *Appendix K* - Ecological Survey Reports) during surveys careful searches of appropriate microhabitats and refugia for reptiles and their vocalizing individuals will be undertaken and all reptiles observed will be identified and counted.

Dragonfly and Butterfly Survey

7.2.7 Dragonfly and Butterfly surveys will be conducted along transects (shown in *Appendix K* - Ecological Survey Reports) during surveys all dragonflies and Butterflies seen will be identified and counted as accurately as possible.

Aquatic Fauna Survey

- 7.2.8 Freshwater fishes and macro-invertebrates will be recorded by direct observation. All species trapped/recorded will be enumerated and identified (to the lowest taxonomic level possible), and the species of conservation importance photographed.
- 7.2.9 After each ecological monitoring survey, a monthly report of the survey result and data collected will be provided with reference to EM&A Manual. An annual analysis of data will be carried out in order to study if there is any significant reduction in taxa diversity and abundance.

7.3 ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 1)

7.3.1 In the Reporting Month, ecological monitoring was undertaken on 18th November 2021 at work area of Contract 1. A sunny day. The day and night survey covered wetland and non-wetland areas. The survey was conducted by transect and at fixed points. All species seen will be identified and counted as accurately as possible. Results of the monitoring survey are presented below:

Monitoring Result for Contract 1

Mammal

7.3.2 There was no mammal recorded in the monitoring area

Birds

7.3.3 There were a total of 24 bird individuals from 12 species recorded in the monitoring area. No Golden-headed Cisticola was observed during the bird survey. One species of conservation interests was recorded in the monitoring area: *Milvus migrans* Black Kite 黑意.

<u>Herpetofauna</u>

7.3.4 There was no reptile species recorded in monitoring area. There was no amphibian species recorded in the monitoring area.



Butterfly

7.3.5 There were a total of 12 butterfly individuals from 5 species recorded in the monitoring area.

<u>Dragonfly</u>

7.3.6 There were a total of 4 odonate individuals from 1 species recorded in the monitoring area.

Aquatic Fauna Survey (Freshwater communities)

- 7.3.7 There was no freshwater community recorded in the monitoring area.
- 7.3.8 The summaries of faunal survey result are shown in *Tables 7-4* and *7-5*.

Table 7-4 Result of Faunal Survey under Contract 1

Scientific Name	Common /	Chinese Name	Conservation	Non-w	etland	W	etlan	d
Scientific Name	Engineer Name	Chinese Name	Status	UG	WL	MA	ww	WC
Mammal Survey								
Avifauna Survey Milvus migrans	Black Kite	黑鳶	Fellowes et al. (2002): RC; Appendix 2 of CITES	1				
Amaurornis	White-breasted	白胸苦惡鳥			1			
phoenicurus	Waterhen			1				
Spilopelia chinensis	Spotted Dove	珠頸斑鳩		2				
Dicrurus macrocercus	Black Drongo	黑卷尾					1	
Parus cinereus	Cinereous Tit	蒼背山雀		2				
Pycnonotus jocosus	Red-whiskered Bulbul	紅耳鵯		4				
Phylloscopus inornatus	Yellow-browed Warbler	黃眉柳鶯		2				
Prinia flaviventris	Yellow-bellied Prinia	黃腹鷦鶯			2			
Prinia inornata	Plain Prinia	純色鷦鶯			1			
Orthotomus sutorius	Common Tailorbird	長尾縫葉鶯			2			
Garrulax perspicillatus	Masked Laughingthrush	黑臉噪鶥						4
Motacilla alba	White Wagtail	白鶺鴒		2				
Reptile Survey						-		
Amphibian Survey						-		
Butterfly Survey								
Jamides bochus	Dark Cerulean	雅灰蝶		4				
Rapala manea	Slate Flash	燕灰蝶		1		1		
Parathyma sulpitia	Five-dot Sergeant	殘鍔線蛺蝶		2				
Neptis hylas	Common Sailer	中環蛺蝶		3				
Abisara echerius	Plum Judy	蛇目褐蜆蝶		2				
Odonate Survey								
Pantala flavescens	Wandering Glider	黄蜻		2				2

^{*}UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

Table 7-5 Result of Freshwater Communities Survey under Contract 1

Scientific Name	Common	Chinese	Conservation	Non-wet	tland	V	Vetlai	nd
Scientific Name	Name	Name	Status	UG	WL	MA	WW	WC



Discussion

7.3.9 After analysing survey results in November from 2018 to 2021, there were a slight decrease in abundance and a drop in species richness for wetland habitat. These reductions could be due to natural fluctuation. Yet, good site practice during construction, with reference to EM&A Manual, is required to prevent or alleviate environmental impacts. For instance, the size of work areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works. Unnecessary site clearance should be avoided as well. In addition, implementing proper waste disposal is necessary to reduce contamination to water and soil. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.

7.4 ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 2)

7.4.1 In the Reporting Month, ecological monitoring was undertaken on 18th November 2021 at work area of Contract 2. A sunny day. The day and night survey covered wetland and non-wetland areas. The survey was conducted by transect and at fixed point. All species seen will be identified and counted as accurately as possible. Results of the monitoring survey are presented below:

Monitoring Result for Contract 2

Mammal

7.4.2 There was no mammal recorded in the monitoring area

Birds

7.4.3 There were a total of 20 bird individuals from 6 species recorded in the monitoring area. No Golden-headed Cisticola was observed during the bird survey.

Herpetofauna

7.4.4 There was no reptile recorded in the monitoring area. There was no amphibian recorded in the monitoring area.

Butterfly

7.4.5 There were a total of 7 butterfly individuals from 5 species recorded in the monitoring area.

Dragonfly

7.4.6 There were a total of 7 odonate individuals from 2 species recorded in the monitoring area.

Aquatic Fauna Survey (Freshwater communities)

- 7.4.7 There were 2 species of freshwater fish were recorded in the monitoring area.
- 7.4.8 The summaries of faunal survey result are shown in *Tables 7-6* and 7-7.

Table 7-6 Result of Faunal Survey under Contract 2

Scientific Name	Common / Engineer Name	Chinese Name	Conservation Status		on- land	V	Vetlar	ıd
	Name	Name	Status	UG	WL	MA	WW	WC
Mammal Survey								
								-
Avifauna Survey								
Hypothymis	Black	黑枕王鶲		1				
azurea	Black-naped Monarch			1				
Parus cinereus	Cinereous Tit	蒼背山雀		2				
Phylloscopus	Pallas's Leaf Warbler	黃腰柳鶯		1				
proregulus				1				
Phylloscopus	Yellow-browed	黄眉柳鶯		2			1	
inornatus	Warbler			2			1	
Pycnonotus	Red-whiskered Bulbul	紅耳鵯		5			3	
jocosus				3			3	
Garrulax	Masked	黑臉噪鶥			5			
perspicillatus	Laughingthrush				3			



Scientific Name	Common / Engineer Name	Chinese Name	Conservation Status		on- land	V	Vetlar	ıd
	Name		Status	UG	WL	MA	WW	WC
Reptile Survey								
Amphibian Survey	T							
Butterfly Survey								
Neptis hylas	Common Sailor	中環蛺蝶		1				
Mycalesis mineus	Dark Brand Bush Brown	小眉眼蝶					2	
Papilio polytes	Common Mormon	玉帶鳳蝶					1	
Delias pasithoe	Red-base Jezebel	報喜斑粉蝶		2				
Abisara echerius	Plum Judy	蛇目褐蜆蝶		1				
Odonate Survey								
Orthetrum pruinosum	Common Red Skimmer	赤褐灰蜻				1		
Pantala flavescens	Wandering Glider	黄蜻				6		

^{*}UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

Table 7-7 Result of Freshwater Communities Survey under Contract 2

Scientific Name	Common Name	Chinese Name	Conservation Status	Non- wetland		Wetland		
	Name		Status	UG	WL	MA	WW	WC
Gambusia affinis	Mosquito fish	食蚊魚						+
Puntius	Chinese Barb	五線無鬚舥						+
semifasciolatus								T

^{*}UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

Discussion

- 7.4.9 After analysing survey results in November 2018 to 2021, no significant drop in species richness and abundance is observed for wetland and non-wetland habitats. Maintaining good site practice during construction, with reference to EM&A Manual, is still required to prevent or alleviate environmental impacts. For instance, the size of work areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works. Unnecessary site clearance should be avoided as well. In addition, implementing proper waste disposal is necessary to reduce contamination to water and soil. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.
- 7.4.10 The detailed Ecological Survey Reports for Contract 1 and Contract 2 are attached in *Appendix K*.
- 7.4.11 The tentative ecology inspection and monitoring in the next Reporting Month (November 2021) is scheduled on 13th December 2021.

7.5 MONITORING OF FLORA SPECIES OF CONSERVATION INTEREST UNDER CONTRACT 1

- 7.5.1 According to the approved vegetation survey report and transplantation proposal under FEP-01/534/2017/A, an individual of flora species of conservation interest (the transplanted T-2928) was identified and transplanted to the receptor site.
- 7.5.2 According to approved vegetation survey report and transplantation proposal, post-transplantation monitoring was conducted once per week in the first three months after the transplantation in Oct 2018 and once in each of the following month in the remaining establishment period for 12 month. During the remaining construction phase of the project, the transplanted T-2928 would be monitored on quarterly basis.

^{+:} Species appeared but uncountable.



7.5.3 A landscape sub-contractor was employed by the Contractor to monitor the health condition of transplanted species and provide advice on necessary weeding, fertilizing and pest control. The monitoring records were submitted to ET and IEC for review and record. Moreover, inspection of the transplanted T-2928 was undertaken by ET as part of the weekly site inspection. No construction activity and disturbance were observed at the location of the transplanted T-2928. The health condition of the transplanted T-2928 was fair with normal foliage color and density.

7.6 MEASURE FOR PROTECTION OF NESTING BIRD

- 7.6.1 Pursuant to FEP-01/534/2017/A condition 2.19 and EP-534/2017/A condition 2.20, precautionary checks for the presence of nesting birds shall be carried out in the breeding season (February to July) before vegetation clearance.
- 7.6.2 Precautionary checks for the presence of nesting birds were not required in the Reporting Period as it is outside the concerned breeding season.



8. LANDSCAPE AND VISUAL

8.1 REQUIREMENT

- 8.1.1 The EIA has recommended EM&A for landscape and visual resources to be undertaken during the design, construction and operational stages of the project. The design, implementation and maintenance of landscape mitigation measures is a key aspect of this and should be checked to ensure that they are fully realized and that potential conflicts between the proposed landscape measures and any other project works let its are resolved at the earliest possible date and without compromise to the intention of the mitigation measures. In addition, implementation of the mitigation measures recommended by the EIA will be monitored through the site audit programme.
- 8.1.2 A number of mitigation measures to ameliorate the landscape and visual impacts of the Project implementation is summarized in the EMIS of *Appendix 13.1* of the EIA Report.
- 8.1.3 The landscape and visual mitigation measures proposed should be incorporated in the landscape and engineering design. Mitigation measures to be implemented during construction should be adopted from the start of construction and be in place throughout the entire construction period. Mitigation measures to be implemented during operation should be integrated into the detailed design and built as part of the construction works so that they are in place on commissioning of the Project. Tree transplantation and compensatory planting should be carried out as early as possible in the Project with transplantation carried out prior to construction starting in any particular area.
- 8.1.4 During construction phase, Landscape & Visual Monitoring of the contractor's operations should be conducted monthly and reported by ET, and countersigned by IEC.

8.2 FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH

8.2.1 In the Reporting Month, landscape & visual inspection was carried out by the Registered Landscape Architect (RLA) for works area of Contract 1 and Contract 2 on 15th November 2021. The findings / reminders recorded during the inspection are presented in Tables 8-1 and 8-2.

Table 8-1 Landscape & Visual Inspection Finding for Contract 1

Date	Findings and Reminder	Follow-Up Status
15 th November 2021	1. The Contractor is reminded to set up TPZ of proper size and with appropriate material around retain trees according to approved method statement.	Reminder only
	2. The Contractor is reminded to prevent the construction material pile within TPZ and ensure no works is allowed within the TPZ.	Reminder only
	3. Transplanted trees T2465, T2468 and T2928 were in fair health condition with normal foliage color and density. Contractor is reminded to provide proper maintenance according to approved method statement.	Reminder only

Table 8-2 Landscape & Visual Inspection Finding for Contract 2

Date	Findings and Reminder	Follow-Up Status
15 th November 2021	1. Contractor is reminded to set up TPZ of proper size and with appropriate material around retain trees according to approved method statement. Contractor should prevent any construction material pile within	
	TPZ and ensure no works is allowed within the TPZ.	

8.2.2 Inspection checklist of Landscape & Visual signed by RLA is attached in *Appendix L*.



9. WASTE MANAGEMENT

9.1 GENERAL WASTE MANAGEMENT

9.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time in accordance with the Waste Management Plan (WMP).

9.2 RECORDS OF WASTE QUANTITIES

- 9.2.1 All types of waste arising from the construction work are classified into the following:
 - Construction & Demolition (C&D) Material;
 - Chemical Waste;
 - General Refuse; and
 - Excavated Soil.
- 9.2.2 The quantities of waste for disposal in this Reporting Month are summarized in *Table 9-1* and *9-2* and the Monthly Summary Waste Flow Table is shown in *Appendix M*. Whenever possible, materials were reused on-site as far as practicable.

Table 9-1 Summary of Quantities of Inert C&D Materials

	Cont	ract 1	Cont	ract 2
Type of Waste	Quantity	Disposal Location	Quantity	Disposal Location
Total generated C&D Materials (Inert) ('000m³)	5.166		547.910 (#)	
Reused in this Contract (Inert) ('000m ³)	0		0	
Reused in other Projects (Inert) ('000m³)	0.250		0	1
Disposal as Public Fill (Inert) ('000m ³)	4.166	Tuen Mun Area 38	547.910 (#)	Tuen Mun Area 38

Remark: the unit is '000kg

Table 9-2 Summary of Quantities of C&D Wastes

	Contract 1		Contract 2	
Type of Waste	Quantity	Disposal Location	Quantity	Disposal Location
Recycled Metal ('000kg)	0		0	
Recycled Paper / Cardboard Packing	0		0.09	Licensed
('000kg)	U			collector
Recycled Plastic ('000kg)	0		0	
Chemical Wastes ('000kg)	0		0	
General Refuses ('000m³)	0.035	NENT Landfill	8.240	NENT
General Keruses (000III)	0.033		(#)	Landfill

Remark: the unit is '000kg

9.2.3 Since canteen and/or kitchen are not allowed setting on the Project site, no domestic wastewater was generated from the Project.



10. SITE INSPECTION

10.1 REQUIREMENT

10.1.1 According to the approved EM&A Manual, environmental site inspection should be led by RE and attended by the Contractor and ET at least once per week. Regular environmental site inspections shall be carried out to assess the environmental performance.

10.2 FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH Contract 1

- 10.2.1 In the Reporting Month, joint site inspections for Contract 1 to evaluate the site environmental performance were carried out by the RE, ET and the Contractor on 4th, 11th, 18th and 25th November 2021 and IEC attended joint site inspection on 18th November 2021. No non-compliance was noted.
- 10.2.2 The findings / deficiencies that observed during the weekly site inspection are listed in *Table 10-1*.

Table 10-1 Site Observations for the Works of Contract 1

Date	Findings / Deficiencies	Follow-Up Status		
4 th Nov 2021 11 th Nov 2021	 Accumulation of construction waste was observed at CS13. The Contactor was advised to dipose of it regularly The Contractor was reminded to spray water regularly at exposed work area to avoid dust emission. 	 Construction waste was disposed regularly within site area. Reminder only. 		
18 th Nov 2021	• Chemical containers were observed on the ground within site area. The Contractor was advised to place chemical containers inside drip tray.	Chemical containers were removed from site area.		
	• Open stockpiles was observe at CS1. The Contractor was advised to provide proper mitigation measure to avoid dust emission.	 Open stockpiles was covered with tarpaulin sheet. 		
	• Scattered waste was observed within site area. The Contractor was advised to enhance house keeping within site area.	• Scattered waste was removed.		
	 Hole was observed on the drip tray underneath generator at CS13. The Contactor was advised to plug it to avoid land contamination. 	Hole at drip tray was plugged.		
	 Muddy water from wheel washing facility was observed at site entrance. The Contactor was advised to treat the muddy water prior to discharge. 	• Regularly maintenance was performed for the desilting facilities at site entrance.		
	• The Contractor was reminded to spray water regularly at exposed work area to avoid dust emission.	Reminder only.		
	• The Contractor was reminded to treat the oil stains on the plank.	Reminder only.		
25 th Nov 2021	• The chemical container was observed on the ground. The contractor was reminded to put it inside drip tray.	Reminder only.		
	• The contractor was reminded to spray water regularly in site area.	Reminder only.		

Contract 2

- 10.2.3 In the Reporting Month, joint site inspections for Contract 2 to evaluate the site environmental performance carried out by the RE, ET and the Contractor was on 4th, 11th, 18th and 25th November 2021 and IEC attended joint site inspection on 19th November 2021 non-compliance was noted.
- 10.2.4 The findings / deficiencies that observed during the weekly site inspection are listed in *Table 10-2*.



Table 10-2 Site Observations for the Works of Contract 2

Date	Findings / Deficiencies	Follow-Up Status
4 th Nov 2021	No adverse environmental issue was observed.	• N/A
11 th Nov 2021	No adverse environmental issue was observed.	• N/A
18 th Nov 2021	• Tree without proper potection zone was observed at Jacking Pit. The Contractor was advised to provide proper tree potection for retained trees.	Proper tree protection zone was provided for retained trees.
	 Hole was observed at drip tray underneath air compressor. The Contractor was advised to plug the hole to avoid oil leakage. 	Hole at drip tray was plugged.
	 Hole was observed at drip tray underneath air compressor. The Contractor was advised to plug the hole to avoid oil leakage. 	 Stagnent water at drip tray was cleaned and dispose of as chemical waste.
	 Chemical containers on the ground was observed at Jacking Pit. The Contractor was advised to dispose of it as chemical waste. 	• The chemical containers was disposed of as chemical waste.
	• Gully without proper covering was observed at Lin Ma Hang Road TTA. The Contractor was advised to place sandbags along gully to avoid potential surface run-off of site boundary.	• Sandbags was provided for gully.
25 th Nov 2021	No adverse environmental issue was observed.	• N/A



11. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

11.1 Environmental Complaint, Summons and Prosecution

11.1.1 In the Reporting Month, no environmental complaint was received for the project. No summons and prosecution was lodged for the Contract. The statistical summary table of the environmental complaint, summons and prosecution are presented in *Tables 11-1*, *11-2* and *11-3*. The complaint log for the Project is shown in *Appendix N*.

Table 11-1 Statistical Summary of Environmental Complaints

Donouting Mon	4h	Envir	onmental Complai	int Statistics
Reporting Mon	uı	Frequency	Cumulative	Complaint Nature
$1^{\text{st}} - 30^{\text{th}}$ November 2021	Contract 1	0	1	Air Quality
1 st – 30 th November 2021	Contract 2	0	2	(1) Water (1) Air Quality

Table 11-2 Statistical Summary of Environmental Summons

Donouting Mon	4h	Environmental Summons Statistics						
Reporting Mon	un	Frequency	Cumulative	Complaint Nature				
$1^{\text{st}} - 30^{\text{th}}$ November 2021	Contract 1	0	0	NA				
1 st – 30 th November 2021	Contract 2	0	0	NA				

Table 11-3 Statistical Summary of Environmental Prosecution

Donostina Mon	41L	E	nvironmental Prosecut	ion Statistics
Reporting Mon	ın	Frequency	Cumulative	Complaint Nature
$1^{\text{st}} - 30^{\text{th}}$ November 2021	Contract 1	0	0	NA
$1^{\text{st}} - 30^{\text{th}}$ November 2021	Contract 2	0	0	NA

11.1.2 In addition, no complaints received and emergency event relating to violation of environmental legislation for illegal dumping and landfilling were received.



12. IMPLEMENTATION STATUS OF MITIGATION MEASURES

12.1 GENERAL REQUIREMENTS

- 12.1.1 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the approved EM&A Manual covered the issues of dust, noise, water and waste.
- 12.1.2 The Works of Contract 1 and Contract 2 under the Project shall be implementing the required environmental mitigation measures according to the approved EM&A Manual subject to the site condition. Environmental mitigation measures implemented in this Reporting Month is summarized in *Table 12-1*. The status of the Environmental mitigation measures are presented in *Appendix O*.

Table 12-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Water	• Provided efficient silt removal facilities to reduce SS level before effluent
Quality	discharge.
	• Provided ditches, earth bunds or sand bag barriers to minimize polluted runoff.
	• Temporary drainage was provided to prevent runoff going through site surface
	and minimize polluted runoff.
	 Provided perimeter cut-off drains at site boundaries to intercept storm runoff from crossing the site.
	 Exposed slopes surface were compacted and covered with tarpaulin or similar
	means.
	Provided portable chemical toilets on site.
Air Quality	Maintain damp / wet surface on access road.
	Maintain low vehicular speed within the works areas.
	 Provided vehicle wheel washing facilities at each construction site exit;
	 Provided water spraying for all active works area.
	Stockpiles of dusty material were covered with impervious sheeting.
	• Provided workers to clear dusty materials at the vehicle entrance or exit regularly.
	• Stockpile more than 20 bags of cement or dry pulverized fuel ash (PFA) has been accorded entirely by improvious cheeting or placed in an area chaltered on the top
	covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.
Noise	• Restricted operation time of plants from 07:00 to 19:00 on any working day
TVOISE	except for Public Holiday and Sunday.
	Keep good maintenance of plants.
	 Placed noisy plants away from residence and school.
	 Provided noise barriers or hoarding to enclose the noisy plants or works.
	Shut down the plants when not in used.
Waste and	Provided on-site sorting prior to disposal. The state of the sta
Chemical	Followed requirements and procedures of the "Trip-ticket System"
Management	• Predicted required quantity of concrete accurately.
	 Collected the unused fresh concrete at designated locations in the sites for subsequent disposal.
Ecology	 Implementing water control measures (ETWB TCW No. 5/2005) to avoid direct
Leology	or indirect impacts any watercourses and impact to any aquatic fauna during the
	construction phase.
	• Demarcation fencing has been erected to prevent unauthorised encroachment into
	the riparian corridor by constructions works and traffic.
	• The construction work and site formation have been phased in order to reduce
	overall noise disturbance impacts in particular areas.
	Works have been restricted to daytime and any construction lighting was designed
	and positioned as to not impact on adjacent ecologically sensitive areas.
General	The site was generally kept tidy and clean.



12.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

- 12.2.1 According to the information provided by HCTYJV, the forthcoming construction activities for Contract 1 are listed below:
 - Bulk Excavation
 - Construction of cut slope, installation of soil nailing and construction of surface channel and planter wall
 - Construction of pick-up and drop-off point near Man Kam To Road
 - Construction of sewer and storm drain
 - Construction of watermains
 - Construction of Concrete/ Bituminous Pavement
- 12.2.2 According to the information provided by Sang Hing, the forthcoming construction activities for Contract 2 are listed below:
 - Construction of Manhole, gullies, drainage pipe at Lin Ma Hang Road between CH0-50 Northbound & CH505-560 Northbound & CH890-960 Northbound.
 - Pipe Jacking works for DN400 watermain in approx. CH0-300 at Man Kam To Road
 - DN400 DI Watermain works in approx. CH700-1040 at Man Kam To Road North Slow Lane
 - Construction of road works at Sandy Ridge Road E CH0-300 (~300m), Road F CH640-720 (~80m), Road B CH30-130 (~100m)
 - Fanling Station Road Covered Walkway
 - Lung Sum Avenue road surface modification works

12.3 KEY ISSUES FOR THE COMING MONTH

12.3.1 The construction activities are illustrated in *Appendix P*. Key issues to be considered in the coming month for the works of Contract 1 and 2 shown in *Table 12-2* and *Table 12-3*.

Table 12-2 Work Undertaken and Illustrations of Mitigation Measures for Contract 1

1 abie 12-2	work Underta	ken and mustrations of whitigation Measures for Contract 1
Description of Construction Activities	Used on PME	Environmental Mitigation Measures
Construction of Concrete Pavement	ExcavatorDump truckCrane lorry	 Provided efficient silt removal facilities to reduce SS level before effluent discharge. Provided ditches, earth bunds or sand bag barriers to minimize polluted runoff.
Bulk excavation, cut slope work with Sail Nail works	 Drilling machine Excavtor Crane lorry	 Exposed slopes surface were compacted and covered with tarpaulin or similar means. Maintain damp / wet surface on access road. Maintain low vehicular speed within the works areas. Provided vehicle wheel washing facilities at each construction site exit;
Construction of watermain, sewer and drainage works	Dump truckExcavatorCrane lorry	 Provided water spraying for all active works area, in particular for the soil nail works. Stockpiles of dusty material were covered with impervious sheeting. Provided workers to clear dusty materials at the vehicle entrance



Description of Construction Activities	Used on PME	Environmental Mitigation Measures
Construction of concrete and Bituminous pavement	 Dump truck Excavator Crane lorry 	 Stockpile more than 20 bags of cement or dry PFA has been covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides. Restricted operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday. Keep good maintenance of plants. Placed noisy plants away from residence and school. Provided noise barriers or hoarding to enclose the noisy plants or works. Shut down the plants when not in used. Provided on-site sorting prior to disposal. Followed requirements and procedures of the "Trip-ticket System" Predicted required quantity of concrete accurately. Collected the unused fresh concrete at designated locations in the sites for subsequent disposal. Implementing water control measures (ETWB TCW No. 5/2005) to avoid direct or indirect impacts any watercourses and impact to any aquatic fauna during the construction phase. Demarcation fencing has been erected to prevent unauthorised encroachment into the riparian corridor by constructions works and traffic. The construction work and site formation have been phased in order to reduce overall noise disturbance impacts in particular areas. Works have been restricted to daytime and any construction lighting was designed and positioned as to not impact on adjacent ecologically sensitive areas. The site was generally kept tidy and clean.

Table 12-3 Work Undertaken and Illustrations of Mitigation Measures for Contract 2

		and mast attoms of mangation measures for contract
Construction Activities	Used on PME	Environmental Mitigation Measures
Construction	 Dump truck 	• Provided efficient silt removal facilities to reduce SS level before
	• Excavator	effluent discharge.
gullies,		• Provided ditches, earth bunds or sand bag barriers to minimize
drainage pipe		polluted runoff.
at Lin Ma		• Exposed slopes surface were compacted and covered with
Hang Road		tarpaulin or similar means.
Pipe Jacking	• Pipe jacking	 Maintain damp / wet surface on access road.
works for	drilling	 Maintain low vehicular speed within the works areas.
DN400	machine	 Provided vehicle wheel washing facilities at each construction site
watermain at		exit;
Man Kam To		 Provided water spraying for all active works area, in particular for
Road		the soil nail works.
Construction	 Excavator 	• Stockpiles of dusty material were covered with impervious
of road works		sheeting.
	 Dump truck 	• Provided workers to clear dusty materials at the vehicle entrance
Ridge Road		or exit regularly.
		• Stockpile more than 20 bags of cement or dry PFA has been
		covered entirely by impervious sheeting or placed in an area
		sheltered on the top and the 3 sides.
		• Restricted operation time of plants from 07:00 to 19:00 on any



Construction Activities	Used on PME	Environmental Mitigation Measures
		 working day except for Public Holiday and Sunday. Keep good maintenance of plants. Placed noisy plants away from residence and school. Provided noise barriers or hoarding to enclose the noisy plants or works.
		 Shut down the plants when not in used. Provided on-site sorting prior to disposal. Followed requirements and procedures of the "Trip-ticket System"
		 Predicted required quantity of concrete accurately. Collected the unused fresh concrete at designated locations in the sites for subsequent disposal. Implementing water control measures (ETWB TCW No. 5/2005)
		 Implementing water control measures (ETWB TCW No. 3/2003) to avoid direct or indirect impacts any watercourses and impact to any aquatic fauna during the construction phase. Demarcation fencing has been erected to prevent unauthorised
		encroachment into the riparian corridor by constructions works and traffic.
		• The construction work and site formation have been phased in order to reduce overall noise disturbance impacts in particular areas.
		 Works have been restricted to daytime and any construction lighting was designed and positioned as to not impact on adjacent ecologically sensitive areas.
		• The site was generally kept tidy and clean.

12.3.1 The Contractors are reminded to pay special attention on water quality mitigation measures and should fully implement the measures as recommended in the EM&A Manual, in particular to prevent surface runoff and other pollutants from flowing to local stream and Conservation Area.



13. CONCLUSIONS AND RECOMMENTATIONS

13.1 CONCLUSIONS

- 13.1.1 This is the **40**th Monthly EM&A Report presenting the monitoring results and inspection findings for the period of **1**st to **30**th **November 2021**.
- 13.1.2 No 24-hour or 1-hour TSP monitoring result that triggered the Action or Limit Levels was recorded. No NOEs or the associated corrective action was therefore required.
- 13.1.3 No noise complaint (which is an Action Level exceedance) was received and no construction noise measurement result that exceeded the Limit Level was recorded in this Reporting Month. No NOEs or the associated corrective actions were therefore issued.
- 13.1.4 In the Reporting Month, no Action Level and Limit level water quality exceedances were recorded.
- 13.1.5 Monthly ecological monitoring for sensitive habitat for area of Contract 1 and Contract 2 were undertaken on 18th November 2021. After analysing survey results in November from 2018 to 2021, there were a slight decrease in abundance and a drop in species richness for wetland habitat under Contract 1. Good site practice during construction, with reference to EM&A Manual, is required to prevent or alleviate environmental impacts. For instance, the size of work areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works. Unnecessary site clearance should be avoided as well. For Contract 2, no significant drop in species richness and abundance is observed for wetland and non-wetland habitats. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.
- 13.1.6 As advised by both Contractors, there were no vegetation clearance conducted within the site in the Reporting Month and therefore precautionary check for the presence of nesting birds was not required.
- 13.1.7 Landscape and visual inspection at both Contracts were undertaken on *15th November 2021*. The Contractor was reminded to prevent the construction material pile within Tree Protection Zone and ensure no works is allowed within the TPZ.
- 13.1.8 In the Reporting Month, no environmental complaints, summons and prosecution were received. In addition, no complaints received and emergency events relating to violation of environmental legislation for illegal dumping and landfilling were received.
- 13.1.9 In the Reporting Month, joint site inspections for Contract 1 to evaluate the site environmental performance were carried out by the Resident Engineer, ET and the Contractor of the Contract 1 on 4th, 11th, 18th and 25th November 2021.. Moreover, joint site inspections for Contract 2 by the RE, ET and the Contractor of Contract 2 were carried out on 4th, 11th, 18th and 25th November 2021.. IEC attended the both Contract joint site inspection on 18th November 2021. No non-compliance was noted during the site inspections.

13.2 RECOMMENDATIONS

- 13.2.1 The Contractors are reminded to pay special attention on water quality mitigation measures and should fully implement the measures as recommended in the EM&A Manual, in particular to prevent surface runoff and other pollutants from flowing to local stream and Conservation Area.
- 13.2.2 During dry season, air quality mitigation measures such as wheel wash facilities, watering of haul roads, loose soil construction surface and covering of dusty materials with tarpaulin sheet should be implemented as far as practicable.
- 13.2.3 Construction noise would be a key environmental issue during construction phase of the Project. Noise mitigation measures such as using quiet plants and mobile noise barriers should be implemented in accordance with the EM&A requirement.




Appendix A

Layout Plan of the Project



Layout Plan of Contract CV/2016/10

Environmental Permit No.: FEP-01/534/2017/A 環境許可證編號: FEP-01/534/2017/A

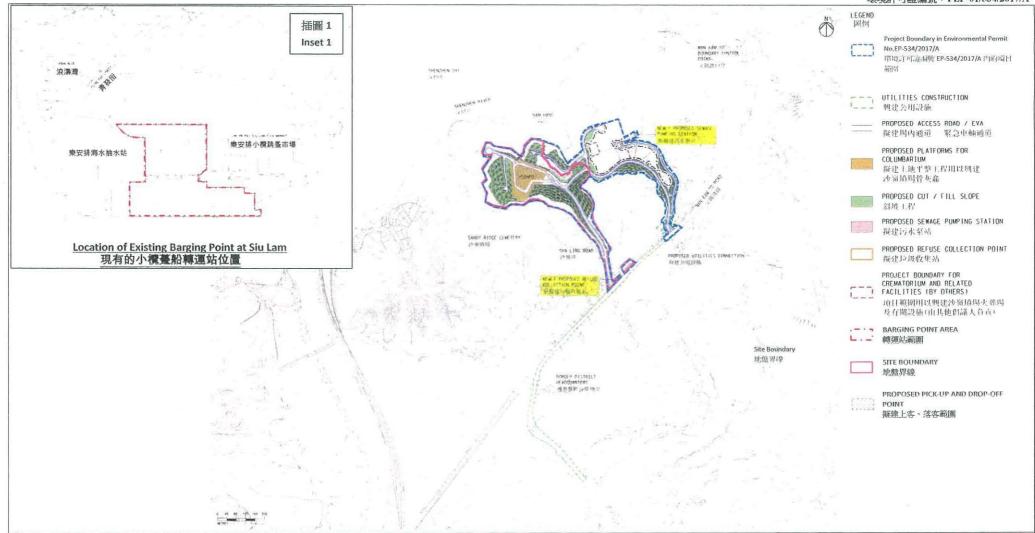

Project Title: Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery 工程名稱:沙嶺墳場興建骨灰龕的工地平整及相關基建工程

Figure 1: Project Location Plan

圖 1:項目位置圖


(This figure was prepared based on Figure 1 attached to the VEP Application No. VEP-555/2018 and Figures 1.3 of the Approved EIA Report No. AEIAR-198/2016)


(本圖是根據更改環境許可証申請文件編號: VEP-555/2018 所隨附的圖 1 和環境影響評估報告編號 AEIAR-198/2016 圖 1.3 編制)


Environmental Permit No.: FEP-01/534/2017/A 環境許可證編號:FEP-01/534/2017/A



FIAO

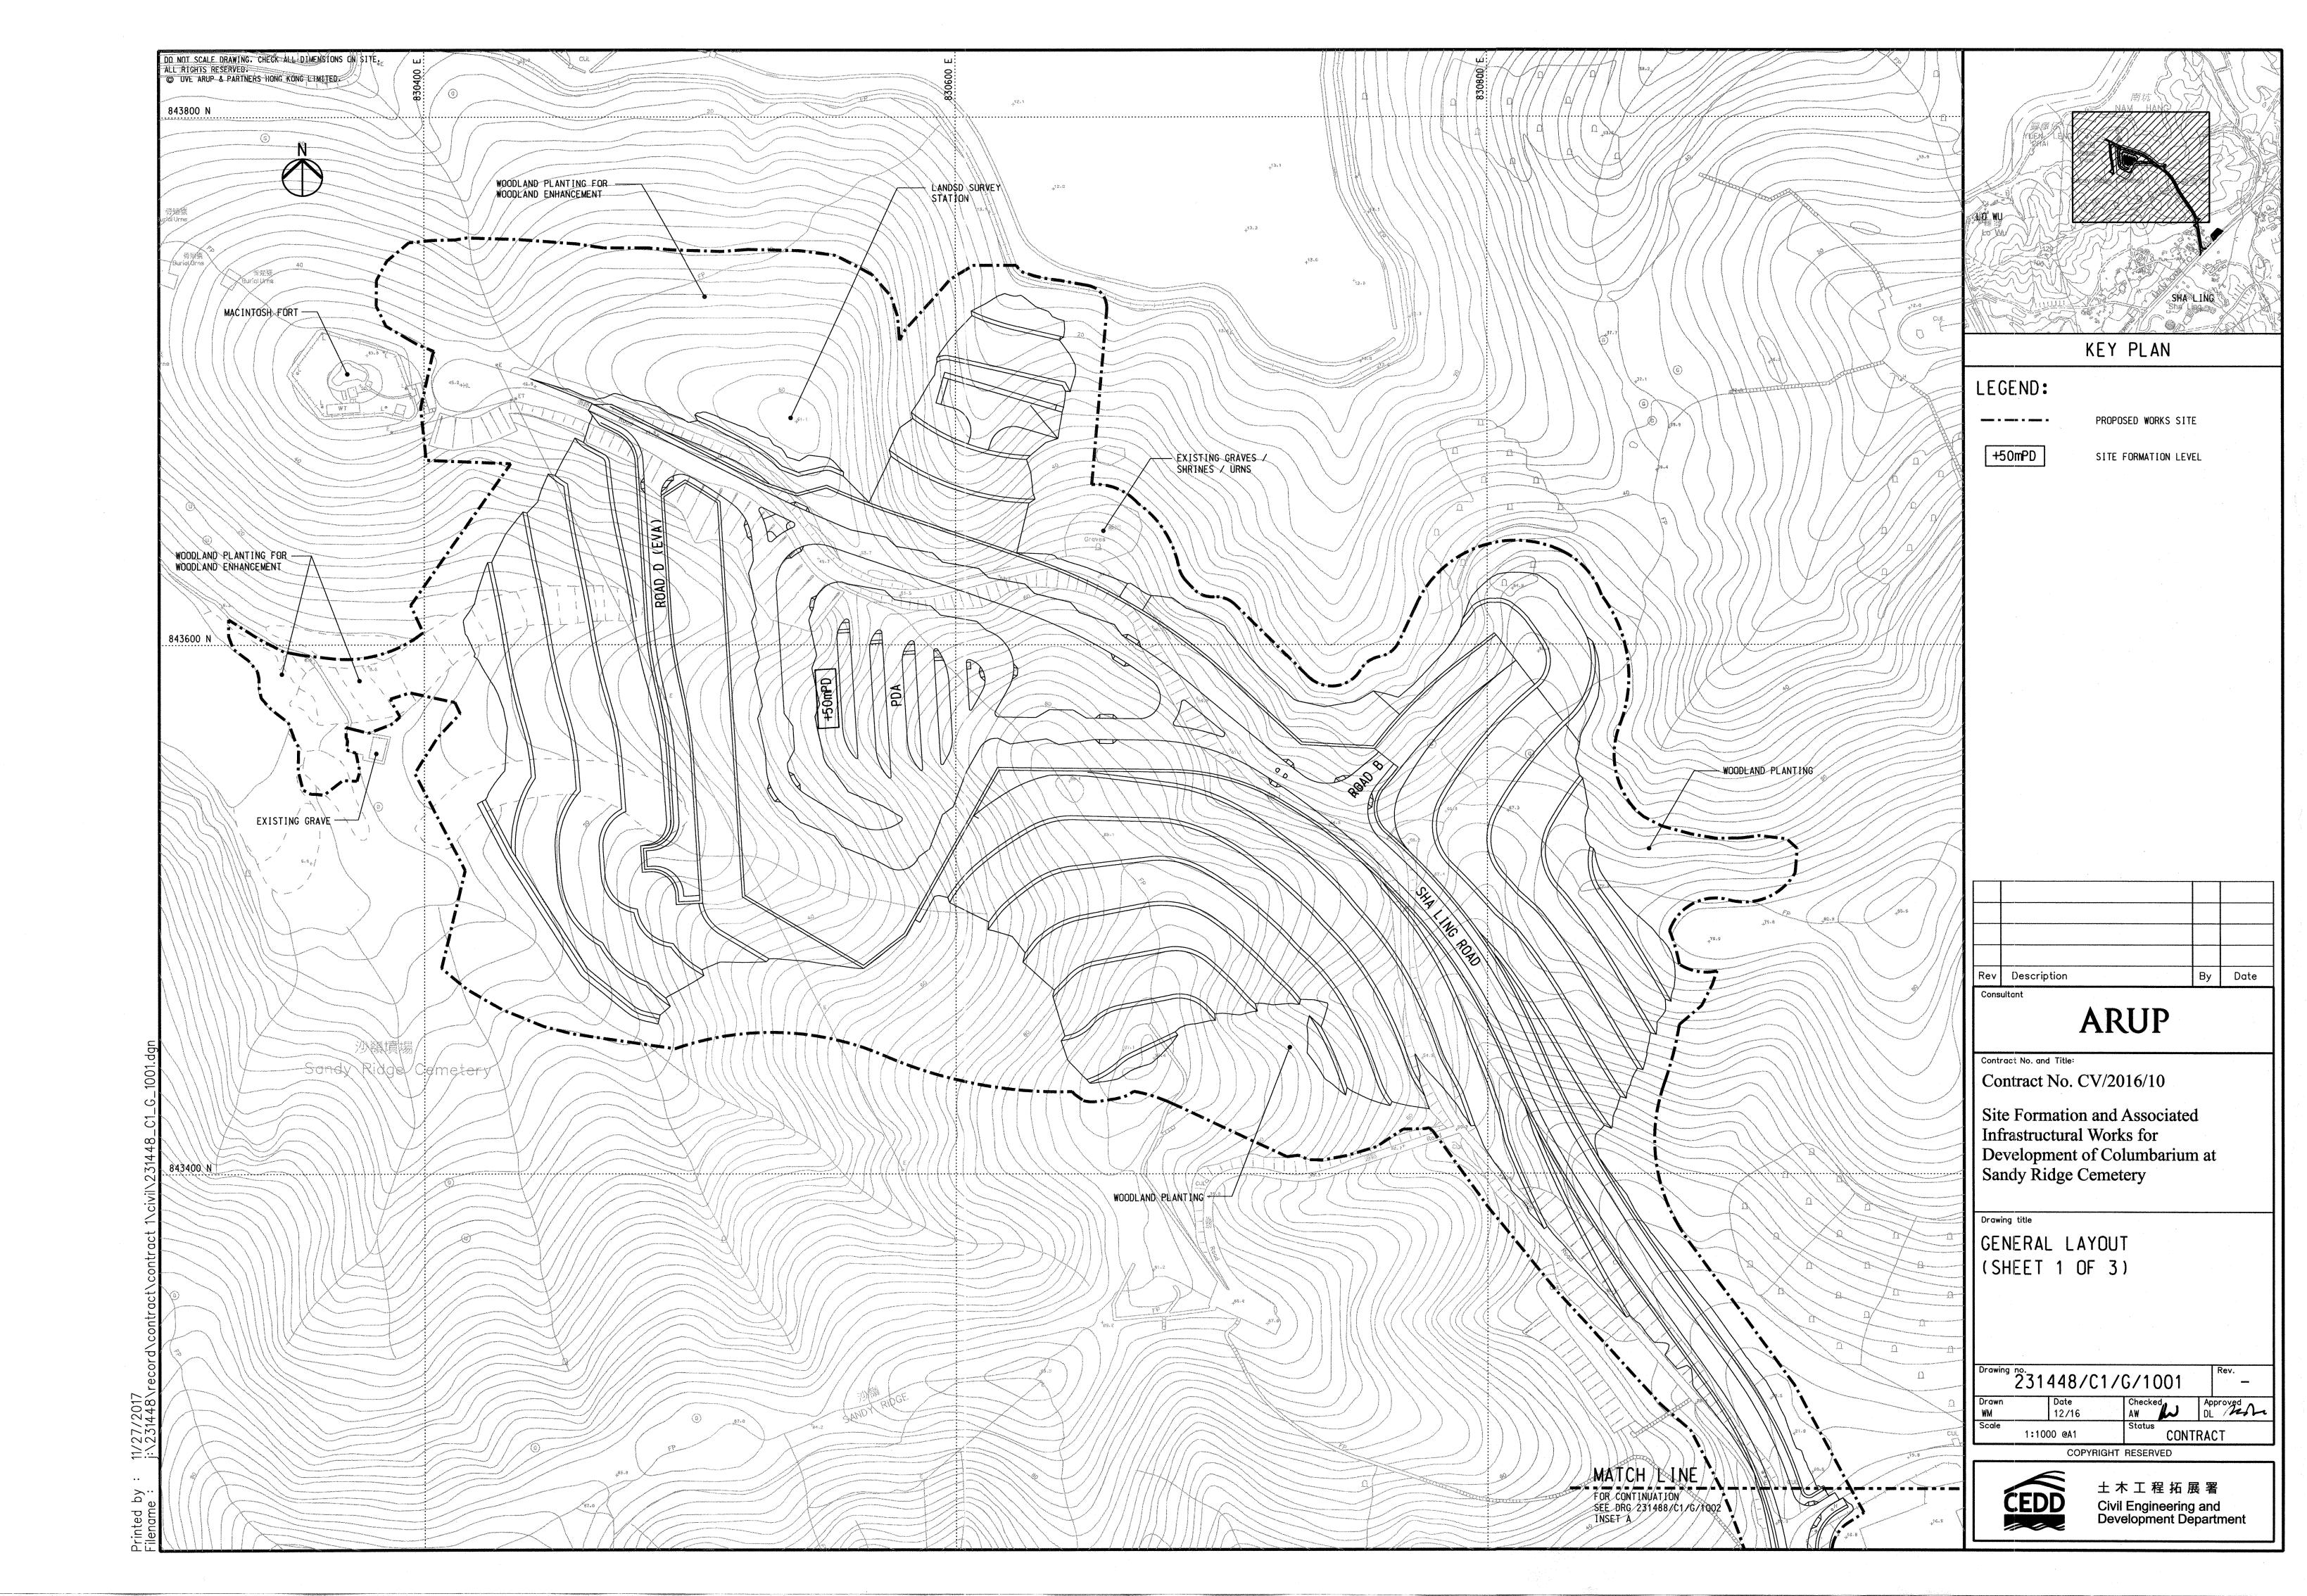


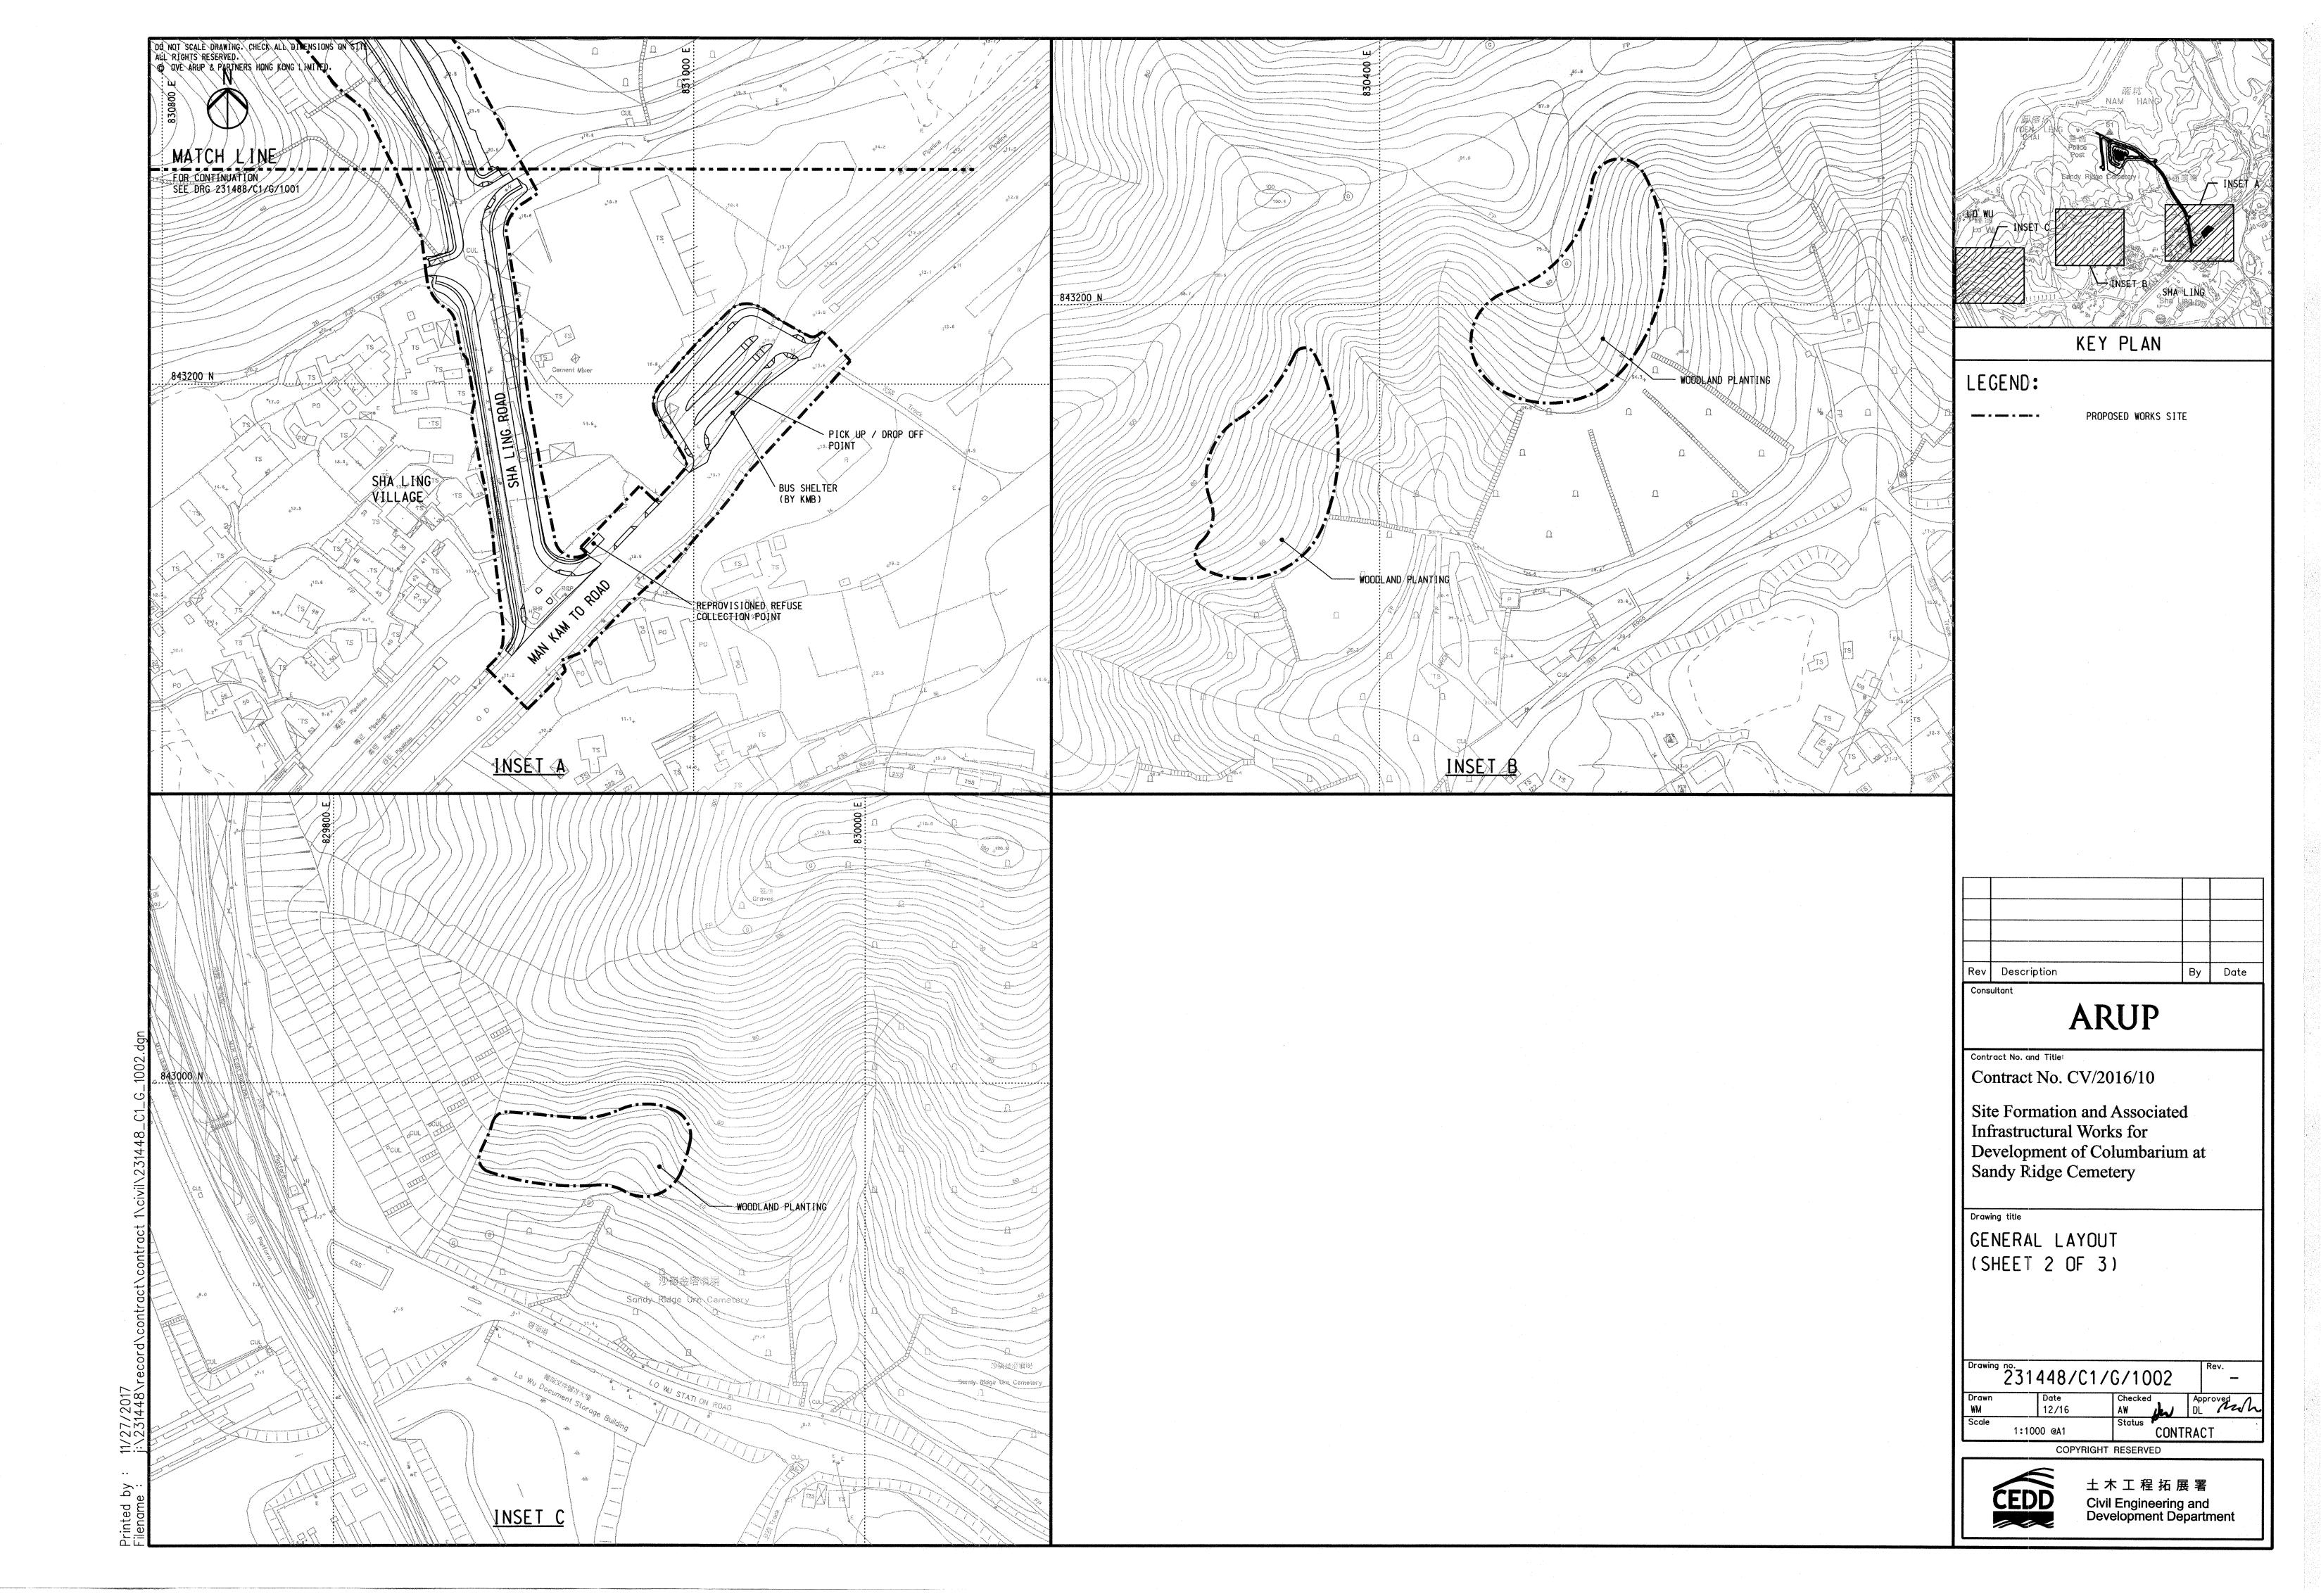

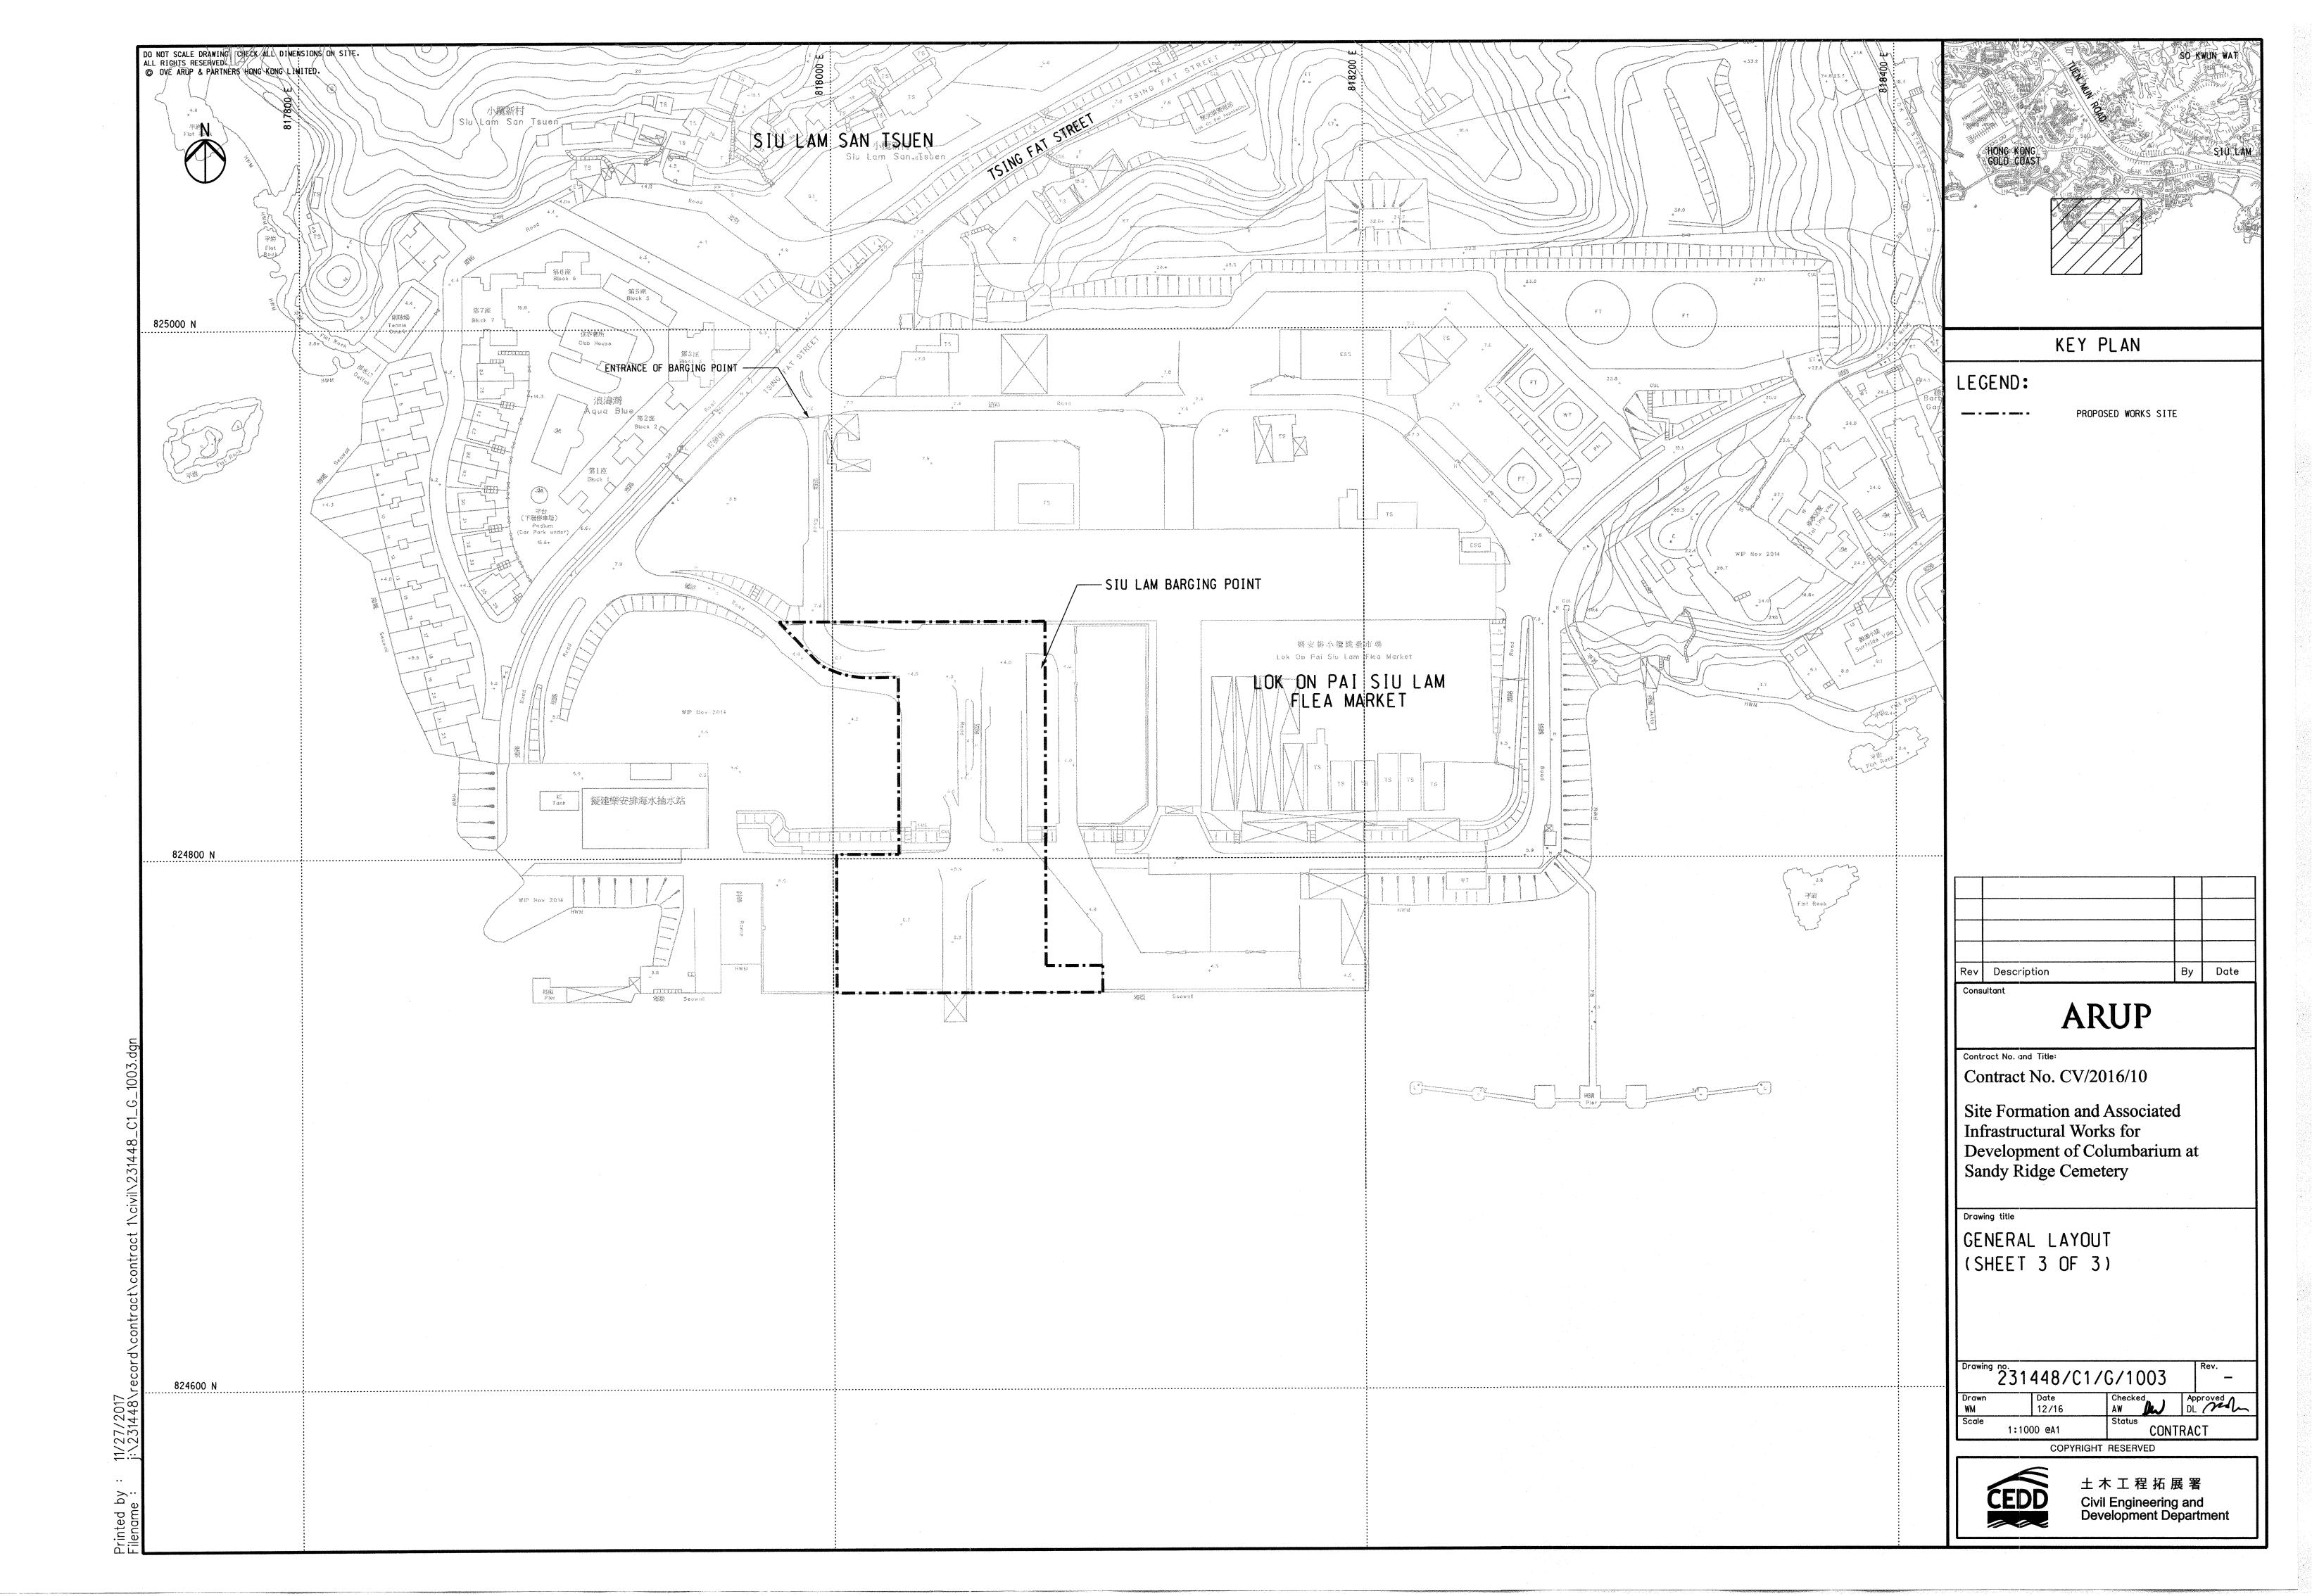






Layout Plan of Contract CV/2017/02

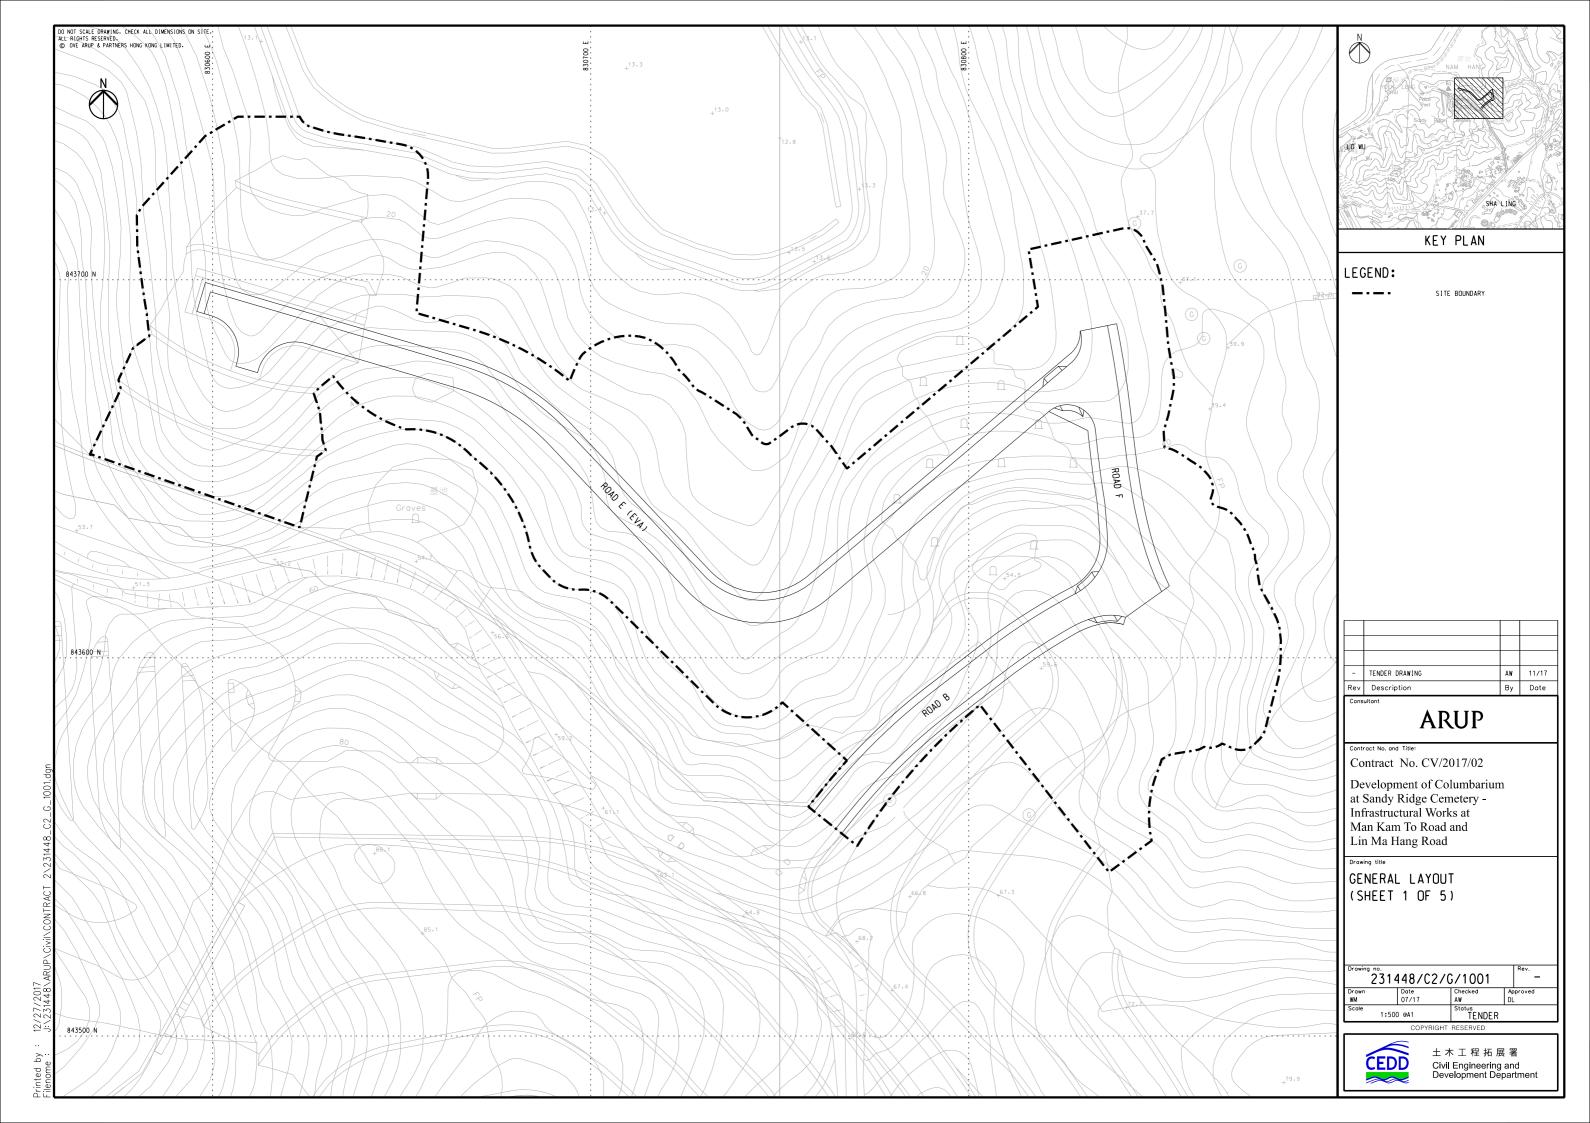



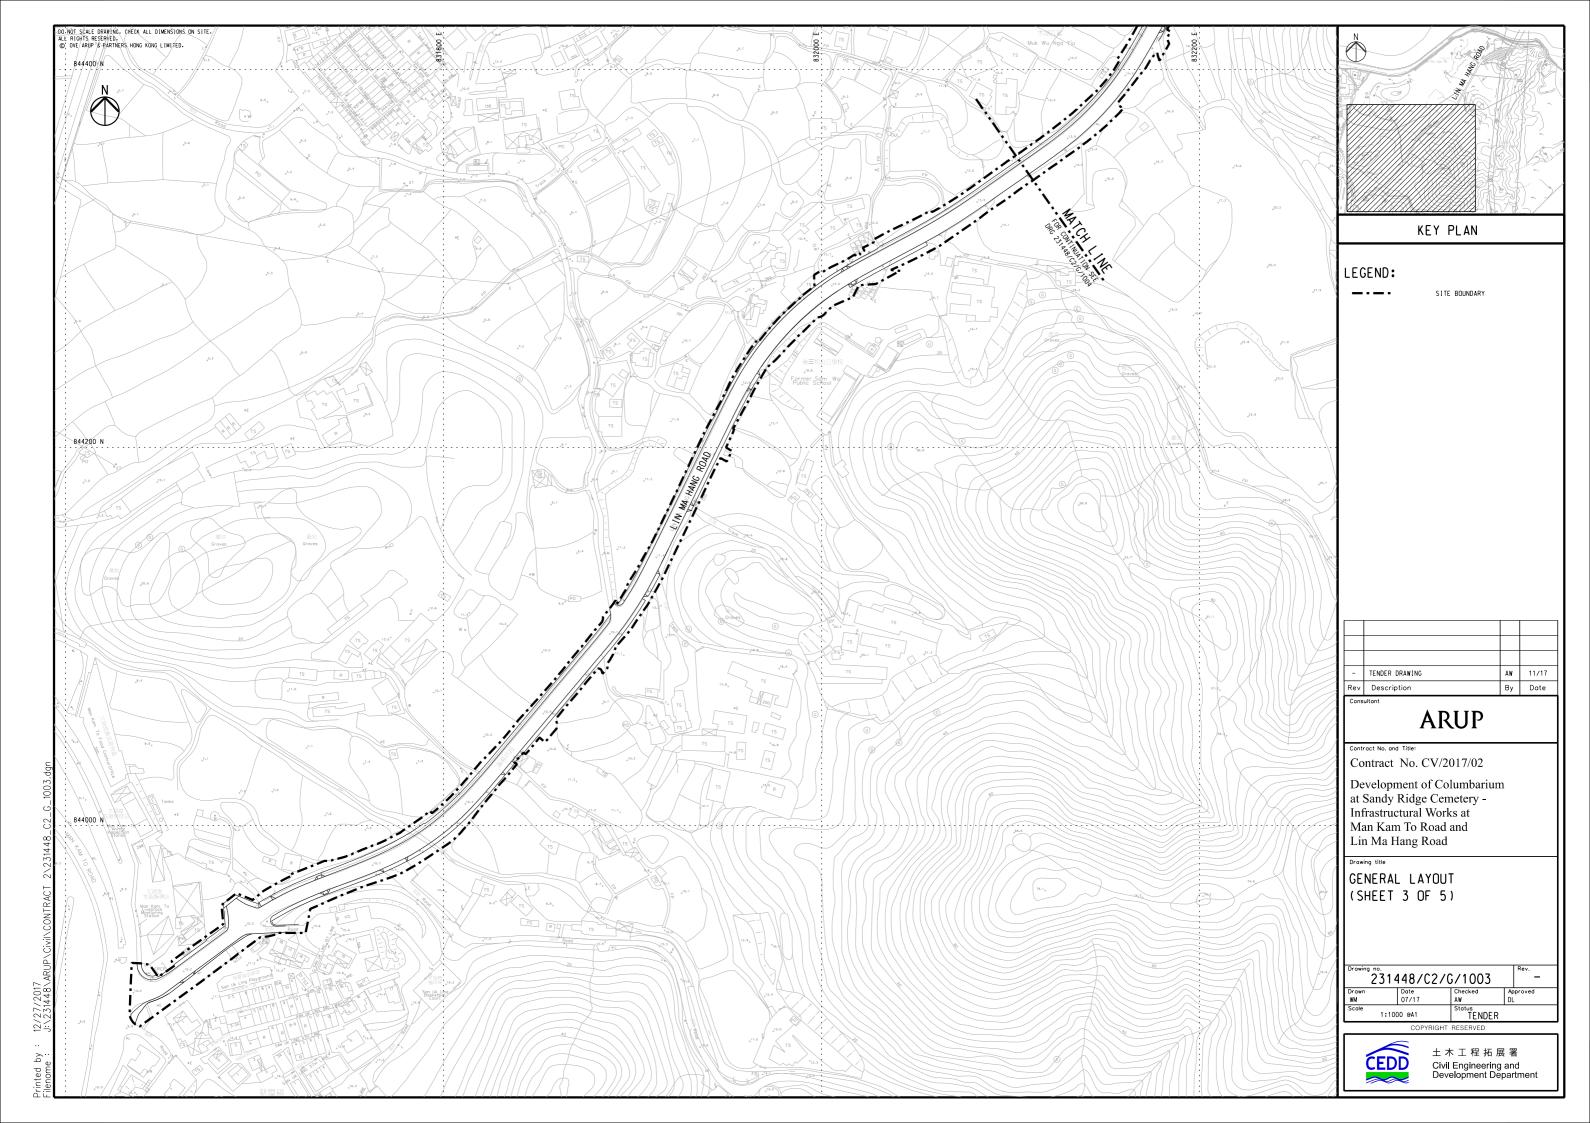

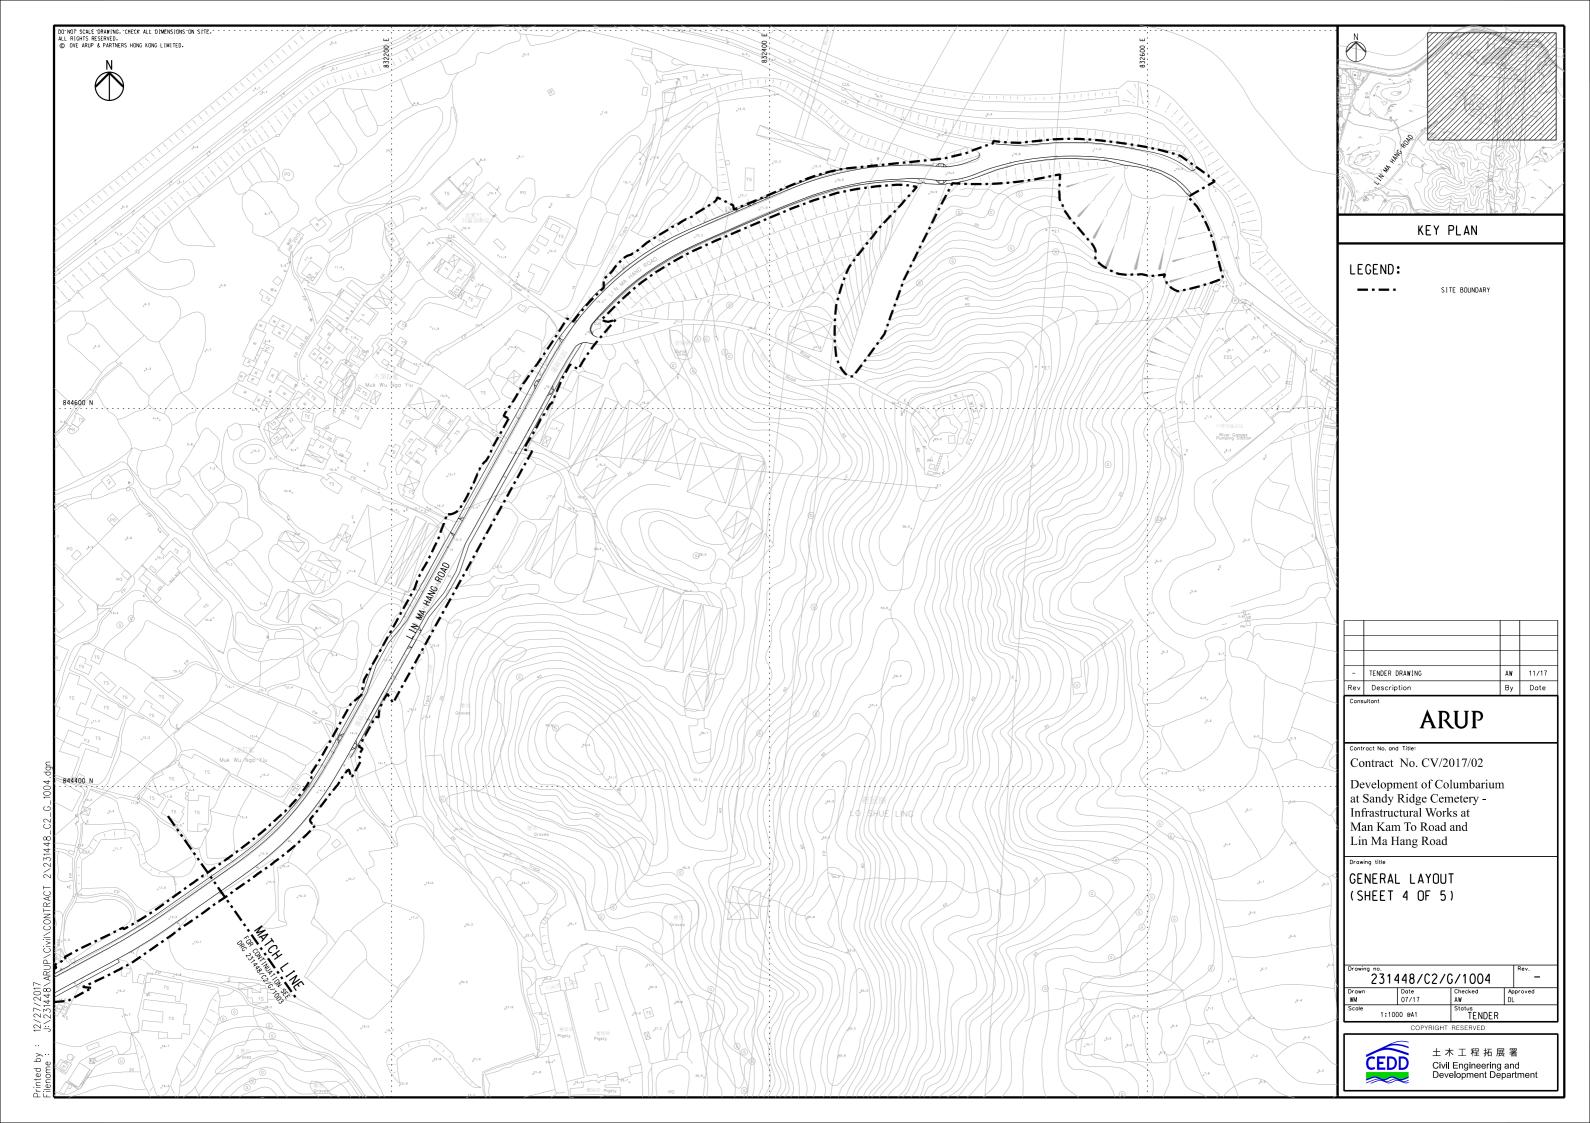

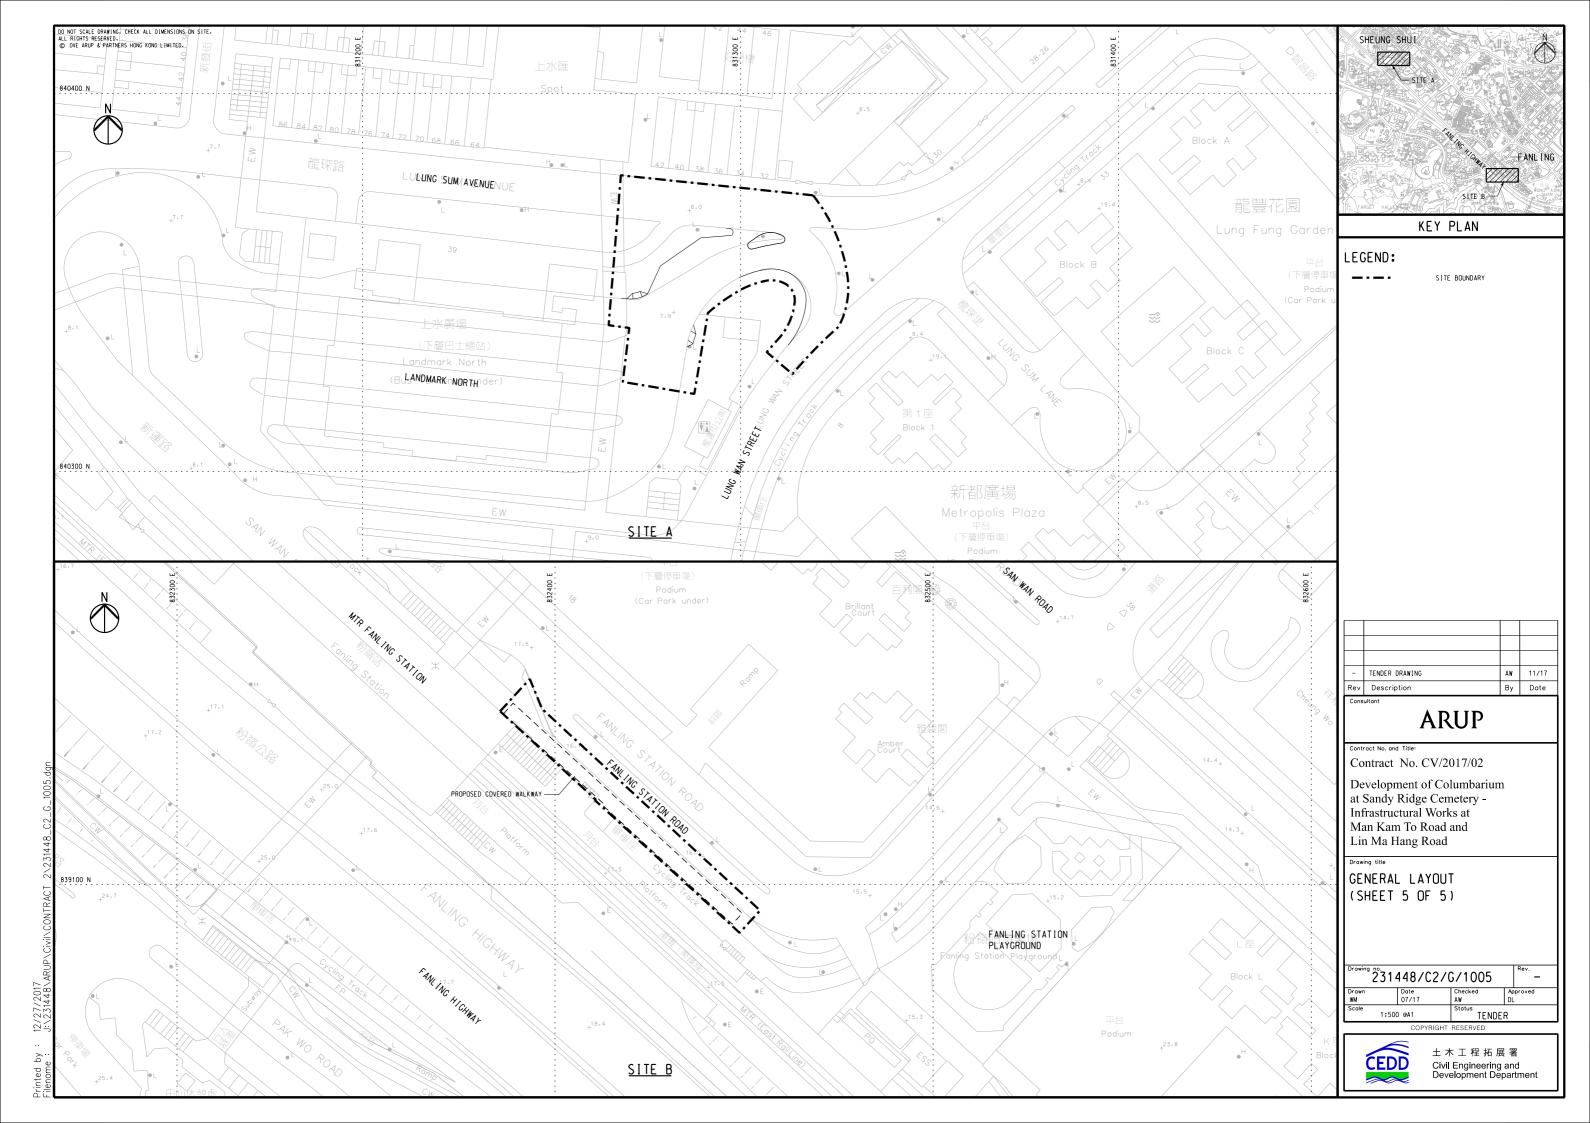




Appendix B

Organization Structure and Contact Details of Relevant Parties



The Contract's Environmental Management Organization

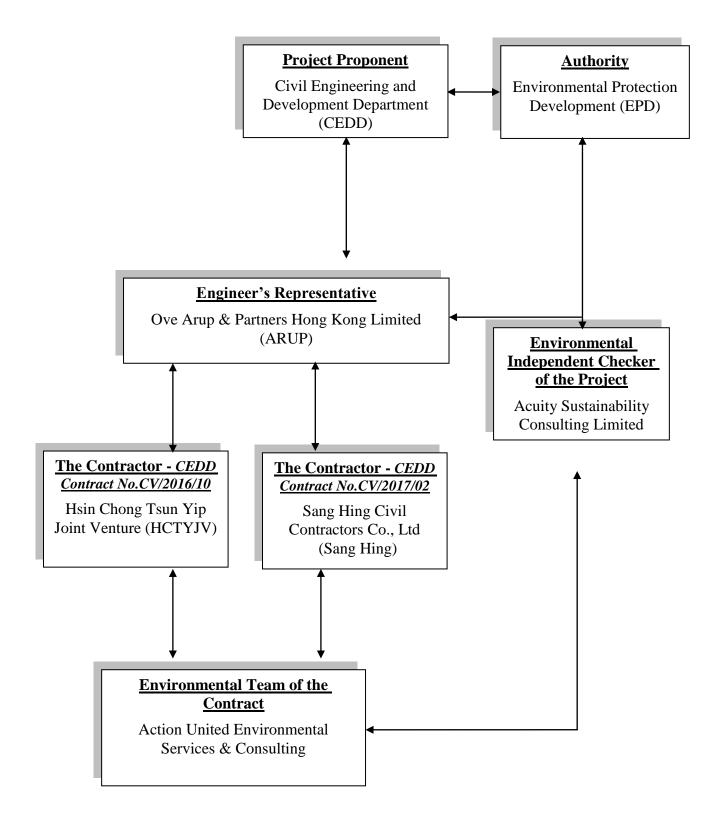



Contact Details of Key Personnel for CV/2016/10 (Contract 1)

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
CEDD	Employer	CHOI Wing-hing	2762-5620	2714-0695
ARUP	Engineer's Representative	Steve Tang	6190-1513	2268-3950
ACUITY	Independent Environmental Checker	Mr. Leung CH Jacky	2698-6833	2698-9383
HCTYJV	Project Director	Mr. Kan Kwok Cheung	9495-2408	2633-4691
HCTYJV	Construction Manager	Mr. Keniel Kwong	9863-0020	2633-4691
HCTYJV	Site Agent	Mr. Ho Man To	9507-9634	2633-4691
HCTYJV	Environmental Officer	Mr. Chan Ming Tai	9358-7007	2633-4691
AUES	Environmental Team Leader	Mr. T.W. Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Mr. Ben Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959-6059	2959-6079
AUES	Environmental Site Inspector	Mr. Martin Li	2959-6059	2959-6079

Legend:

CEDD (Employer) - Civil Engineering and Development Department

ARUP (Engineer) - Ove Arup & Partners Hong Kong Limited

HCTYJV (Main Contractor) – Hsin Chong Tsun Yip Joint Venture

ACUITY (IEC) – Acuity Sustainability Consulting Limited

AUES (ET) – Action-United Environmental Services & Consulting



Contact Details of Key Personnel for CV/2017/02 (Contract 2)

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
CEDD	Employer	CHOI Wing-hing	2762-5620	2714-0695
ARUP	Engineer's Representative	Anthony Lau	6190-1513	2268-3950
ACUITY	Independent Environmental Checker	Ir. Leung CH Jacky	2698-6833	2698-9383
SANG HING	Project Director	Edwin Au	9208-7329	2403-1162
SANG HING	Construction Manager	Raymond Wong	9272-1831	2403-1162
SANG HING	Site Agent	Elvin Lam	6285-0803	2403-1162
SANG HING	Environmental Officer	Keibi Chan	6090-0183	2403-1162
SANG HING	Environmental Supervisor	Kenny Chan	6115-0120	2403-1162
AUES	Environmental Team Leader	Mr. T.W. Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Mr. Ben Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959-6059	2959-6079
AUES	Environmental Site Inspector	Mr. Martin Li	2959-6059	2959-6079

Legend:

CEDD (Employer) – Civil Engineering and Development Department

ARUP (Engineer) - Ove Arup & Partners Hong Kong Limited

Sang Hing (Main Contractor) – Sang Hing Civil Contractors Co., Ltd

ACUITY (IEC) – Acuity Sustainability Consulting Limited

AUES (ET) – Action-United Environmental Services & Consulting



Appendix C

Three Months Rolling Programme



Three Months Rolling Programme of Contract CV/2016/10

Contract No. CV/2016/10 **Hsin Chong Tsun Yip Joint Venture** 3 Month Rolling Programme (Nov 2021 to Jan 2022) Site Formation and Associated Infrastructural Works for Updated Date: Nov 2021 Development of Columbarium at Sandy Ridge Cemetery % Complete Remaining Duration Predecessors 1 Key Dates 1071 days Fri 15/12/17 Fri 30/7/21 1071 days Contract Starting Date Fri 15/12/17 Fri 15/12/17 0% 0 davs 0 days Contract Completion Date for Section 1 Sat 29/8/20 Sat 29/8/20 0% 1 day 1 day Fri 30/7/21 Contract Completion Date for Section 2 1 day Fri 30/7/21 0% 1 day Contract Completion Date for Section 3 Thu 21/11/19 Thu 21/11/19 0% 1 day 1 day Scheduled Completion Date 644 days Tue 10/12/19 Mon 14/2/22 0% 644 days Section 1 0 days Sat 2/10/21 Sat 2/10/21 0% 0 days 13FF Section 2 0 days Mon 14/2/22 Mon 14/2/22 0% 0 days 133FF **∮**14/2 0 days 412FF Section 3 Tue 10/12/19 Tue 10/12/19 0 days 0% 10 Preliminary Works 144 days Tue 20/2/18 Wed 15/8/18 100% 0 days Submission and Approval Required at Environmental Permit for Commencement of Construction 128 days Tue 20/3/18 Wed 15/8/18 100% 0 days Tue 20/2/18 Fri 22/6/18 Other Submission (Initial Survey /Tree Survey/ Condition Survey) 106 days 100% 0 days 13 Section 1 of the Works (Parts A1, A2 & A3) 1041 days Thu 29/3/18 Sat 2/10/21 71% 305.84 days Ground Investigation and Geotechnical instrumentation for Commencement of Slopework 112 days Thu 29/3/18 Wed 15/8/18 100% 0 days Verification Drillholes (8 Nos., VDH1, 2, 7-9,8-16) / Inspection Pits and Preliminary Results Submission 114 days Wed 8/8/18 Thu 29/3/18 100% 0 days Thu 5/7/18 Design Review 36 days Wed 15/8/18 100% 0 days Retaining Wall RW1 280 days Thu 16/8/18 Sat 27/7/19 100% 0 days General Excavation to Formation Level Thu 16/8/18 37 days Thu 27/9/18 100% 0 days Plate Load Test and Blinding Layer for Retaining Wall Bays 1-4 3 days Fri 28/9/18 Mon 1/10/18 100% 0 days Plate Load Test and Blinding Layer for Retaining Wall Bays 5-8 3 days Tue 2/10/18 Thu 4/10/18 100% 0 days Plate Load Test and Blinding Layer for Retaining Wall Bays 9-13 15 days Wed 10/10/18 Fri 26/10/18 100% 0 days Plate Load Test and Blinding Laver for Retaining Wall Bays 14-17 100% 7 davs Sat 6/10/18 Sat 13/10/18 0 days Base slab of Retaining Wall RW1 Bay 1-4 8 days Tue 2/10/18 Wed 10/10/18 100% 0 days Base slab of Retaining Wall RW1 Bay 5-8 Mon 8/10/18 Mon 22/10/18 100% 13 days 0 days Base slab of Retaining Wall RW1 Bay 9-13 17 days Mon 22/10/18 Fri 9/11/18 100% 0 days Base slab of Retaining Wall RW1 Bay 14-17 17 days Mon 22/10/18 Fri 9/11/18 100% 0 days Wall Stem of Retaining Wall RW1 Bay1-4 Thu 25/10/18 Wed 5/12/18 100% 36 days 0 days Wall Stem of Retaining Wall RW1 Bay 5-8 26 davs Tue 11/12/18 Wed 9/1/19 100% 0 days Wall Stem of Retaining Wall RW1 Bay 10-13 30 days Wed 14/11/18 Tue 18/12/18 100% 0 days Wall Stem of Retaining Wall RW1 Bay 14-17 Mon 26/11/18 Fri 21/12/18 100% 23 days 0 days 100% Protective Coating / Subsoil Drain / Filter Laver 5 davs Thu 14/2/19 Tue 19/2/19 0 days Drainage and Maintenance Access in front of RW1 75 days Tue 26/3/19 Thu 20/6/19 100% 0 days Construction CP1X & CP7X 102 days Mon 1/4/19 Sat 27/7/19 100% 0 days Filling Works behind Retaining Wall and Fill Slope FS1 South (Section 12 at Drawing C1/GE/1030) 50% 351.98 days 705 days Mon 1/4/19 Tue 17/8/21 Behind Retaining Wall RW1, Filling Stage 1 (up to +25mPD) 95 days Mon 1/4/19 Fri 19/7/19 100% 0 days FS1 South , Filling (Rolling by Pass) (+25 to +27.8mPD) Wed 31/7/19 100% 10 days Sat 20/7/19 0 days FS1 South Filling Stage 2 (~2.5m, +25.0 to +27.5 mPD) Wed 1/4/20 100% 56 days Thu 4/6/20 0 days Filling (Rolling by Pass) 1 day Wed 1/4/20 Wed 1/4/20 100% 0 days Filling in 3m Zone 28 days Thu 2/4/20 Mon 11/5/20 100% 0 days Benching Works for Rolling by Pass Surface Thu 2/4/20 Mon 6/4/20 100% 3 davs 0 days 38 Lay Rockfill Layer (4.5/1m per 5 days) 25 days Tue 7/4/20 Mon 11/5/20 100% 0 days 40 Tue 12/5/20 Drainage and Maintenance Access (+25 to +27.5 mpD) 21 days Thu 4/6/20 100% 0 days 41 FS1 South Filling Stage 3 (~7.5m height, +27.5 to +35mPD) Sat 1/2/20 Mon 8/2/21 53% 150.8 days 320 days Filling (Rolling by Pass)(~7.5m, 0.5m per day) 130 days Sat 1/2/20 Tue 1/9/20 5% 123 days 38 Filling in 3m Zone 103 days Wed 2/9/20 Wed 6/1/21 100% 0 days Benching Works for Rolling by Pass Surface Fri 4/9/20 100% 3 days Wed 2/9/20 0 days 44 Lav Rockfill Laver (7.5/1m per 5 days) 100 days Sat 5/9/20 Wed 6/1/21 100% 0 days 46 Drainage and Maintenance Access (+27.5 to +35 mpD) Thu 7/1/21 Mon 8/2/21 100% 28 days 0 days 47 FS1 South Filling Stage 4 (~7.5m height, +35 to +42.5mPD) Wed 2/9/20 Thu 8/4/21 20% 188 davs 150.81 days Filling (Rolling by Pass)(~7.5m, 0.5m per day) 15 days Wed 2/9/20 Fri 18/9/20 100% 0 days 44 Filling in 3m Zone Thu 7/1/21 Fri 26/2/21 38 days 41 days Benching Works for Rolling by Pass Surface 3 days Thu 7/1/21 Sat 9/1/21 100% 0 days 50,47 Lay Rockfill Layer (7.5/1m per 5 days) 38 days Mon 11/1/21 Fri 26/2/21 0% 38 days 52 Drainage and Maintenance Access (+35 to +42.5mpD Sat 27/2/21 Thu 8/4/21 0% 35 days 53 35 days FS1 South Filling Stage 5 (~7.5m height, +42.5 to +50mPD) Mon 2/12/19 Tue 17/8/21 17% 443.59 days 536 days Construction of BW11 Mon 2/12/19 Wed 8/1/20 100% 30 davs 0 days 36 Filling in 3m Zone 109 days Sat 27/2/21 Mon 12/7/21 0% 109 days Benching Works for Rolling by Pass Surface 3 days Sat 27/2/21 Tue 2/3/21 0% 3 days 53 Lay Rockfill Layer (7.5/1m per 5 days) Wed 3/3/21 Wed 7/7/21 0% 102 days 58 102 days Additional Plate Load Test at FS1 4 days Thu 8/7/21 Mon 12/7/21 0% 4 days 59 Tue 17/8/21 Drainage and Maintenance Access (+42.4 to +50 mpD) Thu 8/7/21 35 days 59 Fill Slope FS1 Middle (Section 13 at Drawing C1/GE/1030) 386 days Mon 10/2/20 Sat 29/5/21 100% 0 davs Drainage and Maintenance Access at toe (+13 mpD) 10 days Mon 10/2/20 Thu 20/2/20 100% 0 days FS1 middle Filling Stage 1 (~7.0m max, +13.0 mPD to +20 mPD) 22 days Fri 21/2/20 Tue 17/3/20 100% 0 days

Fri 21/2/20

Wed 26/2/20

Wed 26/2/20

Wed 26/2/20

Wed 26/2/20

Sat 14/3/20

Sat 14/3/20

Sat 29/2/20

Fri 6/3/20

4 days

8 days

3 days

5 davs

10 days

53 days

15 days

23 days

3 days

Critic al

Summary 🛡

Filling (Rolling by Pass)(~2m, 0.5m per day)

Benching Works for Rolling by Pass Surface

FS1 middle Filling Stage 2 (~7.5m, +20.0 to +27.5 mPD)

Benching Works for Rolling by Pass Surface

Filling (Rolling by Pass)(~7.5m, 0.5m per day)

Task

Drainage and Maintenance Access (at and below+20 mpD)

■ Milestone ◆

Filling in 3m Zone

Filling in 3m Zone

Lav Filter Laver

Tue 25/2/20

Thu 5/3/20

Fri 28/2/20

Thu 5/3/20

Tue 17/3/20

Mon 4/5/20

Fri 13/3/20

Tue 14/4/20

Tue 17/3/20

Progress =

100%

100%

100%

100%

100%

100%

100%

100%

100%

0 days

0 days

0 davs

0 davs

0 days

0 days 65

0 days 68

0 days 65

0 days 71,68

Contract No. CV/2016/10 Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery

3 Month Rolling Programme (Nov 2021 to Jan 2022)

Hsin Chong Tsun Yip Joint Venture Updated Date : Nov 2021

4	ask Name									
74	ask ivalic	Duration	Start	Finish	% Complete Re	emaining Duration Predecessors		10		_
_	Lay Rockfill Layer (7.5m/1m per 5 day)	20 days	Wed 18/3/20	Tue 14/4/20	100%	0 days 73	11	12	1	_
5	Drainage and Maintenance Access (at and below+27.5 mpD)	15 days	Wed 15/4/20	Mon 4/5/20	100%	0 days 74				
6	FS1 middle Filling Stage 3 (~7.5m height, +27.5 to ~+35mPD)	283 days	Sat 14/3/20	Fri 26/2/21	100%	0 days				
7	Filling (Rolling by Pass)(~7.5m, 0.5m per day)	130 days	Sat 14/3/20	Fri 21/8/20	100%	0 days 71				
8	Filling in 3m Zone	133 days	Sat 22/8/20	Sat 30/1/21	100%	0 days				
9	Benching Works for Rolling by Pass Surface	3 days	Sat 22/8/20	Tue 25/8/20	100%	0 days 77,75	7			
)	Lay Rockfill Layer (7.5m/1m per 5 day)	130 days	Wed 26/8/20	Sat 30/1/21	100%	0 days 79				
	Drainage and Maintenance Access (at and below +35 mpD)	20 days	Mon 1/2/21	Fri 26/2/21	100%	0 days 80	_			
2	FS1 middle Filling Stage 4 (~7.5m height, +35 to +42.5mPD)	241 days	Sat 22/8/20	Sat 29/5/21	100%	0 days	—			
\dashv	Filling (Rolling by Pass)(~7.5m, 0.5m per day)	15 days	Sat 22/8/20	Tue 8/9/20	100%	0 days 77	—			
4	Filling in 3m Zone	41 days	Sat 27/2/21	Mon 19/4/21	100%	0 days	—			
;	Benching Works for Rolling by Pass Surface	3 days	Sat 27/2/21	Tue 2/3/21	100%	0 days 81	\dashv			
5	Lay Rockfill Layer (7.5/1m per 5 days)	38 days	Wed 3/3/21	Mon 19/4/21	100%	0 days 85	\dashv			
7	Drainage and Maintenance Access (+35 to +42.5mpD)	35 days	Tue 20/4/21	Sat 29/5/21	100%	0 days 86	\dashv			
3	FS1 middle Filling Stage 5 below +42.5mPD and +50mPD)	30 days	Tue 20/4/21	Wed 26/5/21	100%	0 days	\dashv			
\dashv	Filling (Rolling by Pass)(~15m, 0.5m per day)	30 days	Tue 20/4/21	Wed 26/5/21	100%	0 days 86	\dashv			
┪	Slope Surface forming/ Drainage and Maintenance Access	20 days	Tue 20/4/21	Thu 13/5/21	100%	0 days 86	_			
┪	Fill Slope FS1 North (Section 14 at Drawing C1/GE/1030)	900 days	Wed 11/7/18	Thu 22/7/21	80%	179.24 days	_			
\dashv	CE16	264 days	Wed 11/7/18 Wed 11/7/18	Fri 31/5/19	38%	164 days	-			
J	FS1 North Filling Works Stage 1 (+15 to+19.7mPD)	204 days	Sat 1/6/19	Fri 24/1/20	100%	0 days 92				
J	Drainage and Maintenance Access (+15 to +20 mpD)	28 days	Sat 1/6/19 Sat 25/1/20	Wed 26/2/20	100%	0 days 92 0 days 93	\dashv			
4	Construction of Outfall CP2X	-	Thu 27/2/20	Fri 13/3/20	100%		_			
\dashv		14 days		Mon 6/4/20		0 days 94	-			
4	FS1North , Filling (Rolling by Pass) (+19.7 to +22.4mPD) ES1 North Filling Stage 2 (+20 to +27.5 mPD)	20 days	Sat 14/3/20		100%	0 days 95	_			
-	FS1 North Filling Stage 2 (+20 to +27.5 mPD)	100 days	Tue 7/4/20	Fri 31/7/20	100%	0 days 94	_			
\dashv	Drainage and Maintenance Access (+20 to +27.5 mpD)	65 days	Sat 1/8/20	Thu 15/10/20	100%	0 days 97	_			
\exists	Filling in 3m Zone (below +27.5mPD)	58 days	Mon 9/3/20	Thu 21/5/20	100%	0 days	_			
-	Benching Works for Rolling by Pass Surface	3 days	Mon 9/3/20	Wed 11/3/20	100%	0 days 98	_			
,	Lay Filter Layer	5 days	Thu 12/3/20	Tue 17/3/20	100%	0 days 100	_			
-	Filling by SRT (7.5m/ 3 day per 5 day)	50 days	Wed 18/3/20	Thu 21/5/20	100%	0 days 101	_			
-	Filling in 3m Zone (below +27.5mPD) (Rockfill)	23 days	Mon 9/3/20	Fri 3/4/20	100%	0 days	_			
1	Benching Works for Rolling by Pass Surface	3 days	Mon 9/3/20	Wed 11/3/20	100%	0 days	_			
	Lay Rockfill Layer (7.5m/1m per 5 day)	20 days	Thu 12/3/20	Fri 3/4/20	100%	0 days 104				
Ĺ	Drainage and Maintenance Access	22 days	Sat 2/5/20	Wed 27/5/20	100%	0 days 105				
1	FS1 North Filling Stage 3 (+27 to +35 mPD)	171 days	Tue 26/11/19	Thu 11/6/20	100%	0 days				
I	Filling (Rolling by Pass)(~3m, 0.5m per day)	6 days	Tue 26/11/19	Mon 2/12/19	100%	0 days 97	_			
Ū	Drainage and Maintenance Access (+27.5 to +35 mpD)	30 days	Fri 8/5/20	Thu 11/6/20	100%	0 days 108				
Γ	FS1 North Filling Stage 4 (+35 to +42.5 mPD), Upgrading of Existing Slope Feature 3NW-C/F37	229 days	Fri 12/6/20	Fri 5/3/21	100%	0 days				
ſ	Filling (Rolling by Pass)(~3m, 0.5m per day)	20 days	Fri 12/6/20	Tue 7/7/20	100%	0 days 109				
ſ	Drainage and Maintenance Access (+35 to +42.5 mpD)	30 days	Sat 30/1/21	Fri 5/3/21	100%	0 days 111				
(FS1 North Filling Stage 5 (+42.5 to +50mPD), Upgrading of Existing Slope Feature 3NW-C/F37	62 days	Wed 12/5/21	Thu 22/7/21	60%	24.8 days				
ĺ	Filling (Rolling by Pass)(~3m, 0.5m per day)	30 days	Wed 12/5/21	Thu 17/6/21	70%	9 days 112				
٦	Drainage and Maintenance Access (+42.5 to +50 mpD)	30 days	Fri 18/6/21	Thu 22/7/21	50%	15 days 114				
1	Civil Works for Pick-up/Drop-off area (Part A1, M011 CH020 to CH140)	162 days	Sat 6/3/21	Sat 18/9/21	0%	162 days				
i		131 days	Sat 6/3/21	Fri 13/8/21	0%	131 days				
1	Waterworks / Drainage / Sewerage/ Utilities Works					-				
L	Sewerage Works / Drainage Works Sewerage Works / Drainage Works	90 days	Sat 6/3/21	Fri 25/6/21	0%	90 days 112				
ļ		90 days 20 days	Sat 6/3/21 Wed 31/3/21	Fri 25/6/21 Mon 26/4/21	0% 0%	20 days 112 20 days 118SS+21 days	\dashv			
	Sewerage Works / Drainage Works					-				
]	Sewerage Works / Drainage Works Watermain FW1a (CH29-100)	20 days	Wed 31/3/21	Mon 26/4/21	0%	20 days 118SS+21 days				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision	20 days 20 days	Wed 31/3/21 Thu 22/7/21	Mon 26/4/21 Fri 13/8/21	0% 0%	20 days 118SS+21 days 20 days 118FS+21 days				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others)	20 days 20 days 10 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21	0% 0% 0%	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway	20 days 20 days 10 days 72 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21	0% 0% 0% 0%	20 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level	20 days 20 days 10 days 72 days 30 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21	0% 0% 0% 0% 0%	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway	20 days 20 days 10 days 72 days 30 days 30 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21	0% 0% 0% 0% 0%	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture	20 days 20 days 10 days 72 days 30 days 30 days 12 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21	0% 0% 0% 0% 0% 0%	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works	20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21 Sat 2/10/21	0% 0% 0% 0% 0% 0% 0% 0%	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1	20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days 30 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21 Sat 2/10/21 Tue 21/9/21	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0%	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3	20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days 30 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21 Sat 2/10/21 Tue 21/9/21 Sat 28/8/21	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0%	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope	20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days 30 days 10 days 80 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Sat 6/3/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21 Sat 2/10/21 Tue 21/9/21 Sat 28/8/21 Sat 12/6/21	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 115				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off	20 days 20 days 10 days 72 days 30 days 12 days 172 days 172 days 40 days 10 days 10 days 24 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Sat 6/3/21 Fri 23/7/21 Mon 2/8/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 2/10/21 Tue 21/9/21 Sat 28/8/21 Sat 12/6/21 Tue 3/8/21	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 124 days 123				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works	20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days 30 days 10 days 80 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Sat 6/3/21 Fri 23/7/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 2/10/21 Tue 21/9/21 Sat 12/6/21 Tue 3/8/21 Sat 2/8/21 Sat 2/8/21 Sat 2/8/21	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 115				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection)	20 days 20 days 10 days 72 days 30 days 12 days 172 days 30 days 172 days 30 days 10 days 80 days 10 days 24 days 10 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Fri 23/7/21 Mon 2/8/21 Mon 2/8/21 Mon 2/9/21	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 2/10/21 Sat 2/10/21 Tue 21/9/21 Sat 12/6/21 Tue 3/8/21 Sat 2/8/21 Sat 2/8/21 Sat 28/8/21 Sat 28/8/21 Sat 28/8/21 Sat 28/8/21 Sat 28/8/21 Sat 28/8/21	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 123 10 days 123 10 days 123				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2)	20 days 20 days 10 days 72 days 30 days 12 days 172 days 172 days 172 days 30 days 10 days 10 days 40 days 10 days 10 days 10 days 110 days 1232 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Sat 6/3/21 Fri 23/7/21 Mon 2/8/21 Mon 2/8/21 Fri 15/12/17	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 2/10/21 Tue 21/9/21 Sat 28/8/21 Sat 12/6/21 Tue 3/8/21 Sat 28/8/21 Sat 28/8/21 Sat 28/8/21 Mon 14/2/22	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 115 24 days 123 10 days 125			—————	
Se	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works ction 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1	20 days 20 days 10 days 72 days 30 days 12 days 172 days 10 days 12 days 10 days 10 days 10 days 10 days 10 days 110 days 12 days 13 days 14 days 15 days 16 days 17 days 18 days 19 days 19 days 10 days 10 days 10 days 110 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Wed 18/8/21 Fri 23/7/21 Mon 2/8/21 Mon 2/8/21 Fri 15/12/17 Sat 28/4/18	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 21/0/21 Tue 21/9/21 Sat 28/8/21 Tue 3/8/21 Sat 28/8/21 Sat 28/8/21 Sat 21/0/21 Mon 14/2/22 Thu 13/1/22	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 115 24 days 123 10 days 125 487.25 days 337.58 days			———	
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework	20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days 10 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Wed 18/8/21 Fri 23/7/21 Mon 2/8/21 Mon 2/8/21 Fri 15/12/17 Sat 28/4/18 Sat 28/4/18	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21 Sat 21/0/21 Tue 21/9/21 Sat 12/6/21 Tue 3/8/21 Sat 28/8/21 Sat 28/8/21 Sat 21/0/21 Mon 14/2/22 Thu 13/1/22 Wed 22/8/18	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 115 24 days 123 10 days 125 487.25 days 337.58 days 0 days 0 days				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework Verification Drillholes (10 Nos., VDH3, 6, 10-15,19-20) and Preliminary Results Submission Design Review	20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days 10 days 110 days 124 days 110 days 1292 days 1103 days 96 days 95 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Fri 23/7/21 Mon 20/9/21 Fri 15/12/17 Sat 28/4/18 Sat 28/4/18 Thu 12/7/18	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 2/10/21 Tue 21/9/21 Sat 28/8/21 Sat 12/6/21 Tue 3/8/21 Sat 28/8/21 Sat 27/10/21 Mon 14/2/22 Thu 13/1/22 Wed 22/8/18 Tue 21/8/18	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 115 24 days 123 10 days 125 487.25 days 337.58 days 0 days 0 days 0 days				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework Verification Drillholes (10 Nos., VDH3, 6, 10-15,19-20) and Preliminary Results Submission Design Review Cut Slopes CS1 & CS2	20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days 30 days 10 days 110 days 1232 days 1103 days 96 days 95 days 170 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Fri 23/7/21 Mon 2/8/21 Fri 25/7/21 Mon 2/8/21 Sat 6/3/21 Fri 15/12/17 Sat 28/4/18 Sat 28/4/18 Thu 12/7/18 Fri 12/10/18	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 31/7/21 Sat 4/9/21 Sat 2/10/21 Tue 21/9/21 Sat 28/8/21 Sat 12/6/21 Tue 3/8/21 Sat 28/8/21 Sat 27/10/21 Mon 14/2/22 Thu 13/1/22 Wed 22/8/18 Tue 21/8/18 Wed 22/8/18 Mon 13/5/19	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 115 24 days 123 10 days 125 487.25 days 337.58 days 0 days 0 days 0 days 0 days 0 days			————	
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework Verification Drillholes (10 Nos., VDH3, 6, 10-15,19-20) and Preliminary Results Submission Design Review Cut Slopes CS1 & CS2 Excavation (crest to +55mPD)	20 days 20 days 10 days 10 days 72 days 30 days 12 days 172 days 10 days 10 days 10 days 10 days 10 days 110 days 24 days 110 days 1103 days 1103 days 95 days 36 days 170 days 4 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Wed 18/8/21 Fri 23/7/21 Mon 20/9/21 Fri 15/12/17 Sat 28/4/18 Sat 28/4/18 Thu 12/7/18 Fri 12/10/18	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 31/7/21 Sat 4/9/21 Sat 21/0/21 Tue 21/9/21 Sat 28/8/21 Sat 12/6/21 Tue 3/8/21 Sat 28/8/21 Sat 27/10/21 Mon 14/2/22 Thu 13/1/22 Wed 22/8/18 Tue 21/8/18 Wed 22/8/18 Mon 13/5/19 Tue 16/10/18	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 115 24 days 123 10 days 125 487.25 days 337.58 days 0 days 0 days 0 days 0 days 0 days 0 days				_
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework Verification Drillholes (10 Nos., VDH3, 6, 10-15,19-20) and Preliminary Results Submission Design Review Cut Slopes CS1 & CS2 Excavation (crest to +55mPD) Excavation (+55 to+50mPD)	20 days 20 days 10 days 10 days 72 days 30 days 12 days 172 days 172 days 10 days 10 days 10 days 10 days 10 days 10 days 110 days 1232 days 1103 days 96 days 170 days 4 days 170 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Wed 18/8/21 Fri 23/7/21 Mon 2/8/21 Mon 20/9/21 Fri 15/12/17 Sat 28/4/18 Sat 28/4/18 Sat 28/4/18 Fri 12/10/18 Fri 12/10/18	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 2/10/21 Sat 2/10/21 Tue 21/9/21 Sat 28/8/21 Sat 12/6/21 Tue 3/8/21 Sat 2/10/21 Mon 14/2/22 Wed 22/8/18 Tue 21/8/18 Wed 22/8/18 Mon 13/5/19 Tue 16/10/18 Wed 24/10/18	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 123 10 days 125 487.25 days 337.58 days 0 days				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework Verification Drillholes (10 Nos., VDH3, 6, 10-15,19-20) and Preliminary Results Submission Design Review Cut Slopes CS1 & CS2 Excavation (crest to +55mPD) Excavation (+55 to+50mPD) Drainage and Maintenance Access (at +55mPD berm)	20 days 20 days 10 days 10 days 72 days 30 days 30 days 12 days 172 days 10 days 1103 days 1103 days 1103 days 170 days 170 days 170 days 170 days 170 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Wed 18/8/21 Fri 23/7/21 Mon 2/8/21 Mon 20/9/21 Fri 15/12/17 Sat 28/4/18 Sat 28/4/18 Thu 12/7/18 Fri 12/10/18 Fri 12/10/18 Tue 16/10/18	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21 Sat 2/10/21 Sat 2/10/21 Sat 28/8/21 Sat 12/6/21 Tue 3/8/21 Sat 28/8/21 Sat 2/10/21 Mon 14/2/22 Thu 13/1/22 Wed 22/8/18 Tue 21/8/18 Wed 22/8/18 Mon 13/5/19 Tue 16/10/18 Wed 24/10/18 Tue 18/12/18	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 34 10 days 34 10 days 34 80 days 110 10 days 115 24 days 123 10 days 125 487.25 days 337.58 days 0 days			-	
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Fill Slope Shrubs Planting Works Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework Verification Drillholes (10 Nos., VDH3, 6, 10-15,19-20) and Preliminary Results Submission Design Review Cut Slopes CS1 & CS2 Excavation (crest to +55mPD) Excavation (+55 to+50mPD) Drainage and Maintenance Access (at +55mPD berm) Drainage and Maintenance Access (+55 to +50 slope surface)	20 days 20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days 10 days 10 days 10 days 10 days 24 days 110 days 1232 days 1103 days 95 days 170 days 4 days 11 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Wed 18/8/21 Fri 23/7/21 Mon 2/8/21 Mon 2/9/21 Fri 15/12/17 Sat 28/4/18 Sat 28/4/18 Thu 12/7/18 Fri 12/10/18 Fri 12/10/18 Tue 16/10/18 Tue 16/10/18	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21 Sat 2/10/21 Tue 21/9/21 Sat 12/6/21 Tue 3/8/21 Sat 2/8/21 Sat 2/10/21 Mon 14/2/22 Thu 13/1/22 Wed 22/8/18 Tue 21/8/18 Wed 22/8/18 Tue 16/10/18 Wed 24/10/18 Tue 18/12/18 Mon 13/5/19 Tue 18/12/18 Mon 13/5/19	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 115 24 days 123 10 days 125 487.25 days 337.58 days 0 days				
1 5 6 7 8 8 0 0 1 1 2	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework Verification Drillholes (10 Nos., VDH3, 6, 10-15,19-20) and Preliminary Results Submission Design Review Cut Slopes CS1 & CS2 Excavation (crest to +55mPD) Excavation (+55 to+50mPD) Drainage and Maintenance Access (at +55mPD berm) Drainage and Maintenance Access (+55 to +50 slope surface)	20 days 20 days 10 days 10 days 72 days 30 days 30 days 12 days 172 days 30 days 10 days 40 days 10 days 10 days 10 days 10 days 10 days 10 days 110 days 1232 days 1103 days 95 days 36 days 170 days 4 days 11 days 55 days 180 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Wed 18/8/21 Fri 23/7/21 Mon 2/8/21 Mon 20/9/21 Fri 15/12/17 Sat 28/4/18 Sat 28/4/18 Thu 12/7/18 Fri 12/10/18 Fri 12/10/18 Tri 12/10/18 Tri 16/10/18 Tue 16/10/18 Tue 16/10/18 Wed 4/11/20	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21 Sat 2/10/21 Tue 21/9/21 Sat 28/8/21 Sat 12/6/21 Tue 3/8/21 Sat 2/10/21 Mon 14/2/22 Thu 13/1/22 Wed 22/8/18 Tue 21/8/18 Wed 22/8/19 Tue 16/10/18 Wed 24/10/18 Tue 18/12/18 Mon 13/5/19 Tue 18/12/18 Mon 13/5/19 Tue 18/12/18 Mon 13/5/19 Tue 18/12/18	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 72 days 30 days 118 30 days 123 12 days 124,131 172 days 30 days 34 10 days 34 80 days 110 10 days 123 10 days 125 487.25 days 125 487.25 days 0 days				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework Verification Drillholes (10 Nos., VDH3, 6, 10-15,19-20) and Preliminary Results Submission Design Review Cut Slopes CS1 & CS2 Excavation (crest to +55mPD) Drainage and Maintenance Access (at +55mPD berm) Drainage and Maintenance Access (+55 to +50 slope surface) Cut Slope CS3 Excavation (crest to toe)	20 days 20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days 30 days 10 days 10 days 10 days 24 days 110 days 1232 days 1103 days 95 days 170 days 170 days 170 days 170 days 180 days 11 days 15 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Mon 2/8/21 Mon 2/8/21 Fri 23/7/21 Mon 2/8/21 Fri 23/7/21 Mon 2/8/21 Fri 15/12/17 Sat 28/4/18 Sat 28/4/18 Sat 28/4/18 Thu 12/7/18 Fri 12/10/18 Fri 12/10/18 Tue 16/10/18 Tue 16/10/18 Tue 16/10/18 Wed 4/11/20 Wed 4/11/20	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21 Sat 2/10/21 Tue 21/9/21 Sat 28/8/21 Sat 12/6/21 Tue 3/8/21 Sat 2/10/21 Mon 14/2/22 Thu 13/1/22 Wed 22/8/18 Tue 21/8/18 Wed 22/8/18 Mon 13/5/19 Tue 16/10/18 Wed 24/10/18 Tue 18/12/18 Mon 13/5/19 Tue 18/12/18 Mon 13/5/19 Tue 7/9/21 Fri 20/11/20	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 30 days 118SS+21 days 30 days 118 30 days 123 12 days 34 10 days 34 80 days 34 80 days 110 10 days 115 24 days 123 10 days 125 487.25 days 337.58 days 0 days				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework Verification Drillholes (10 Nos., VDH3, 6, 10-15,19-20) and Preliminary Results Submission Design Review Cut Slopes CS1 & CS2 Excavation (crest to +55mPD) Excavation (r+55 to+55mPD) Drainage and Maintenance Access (at +55mPD berm) Drainage and Maintenance Access (155 to +50 slope surface) Cut Slope CS3 Excavation (crest to toe) Drainage and Maintenance Access	20 days 20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days 30 days 10 days 10 days 10 days 10 days 10 days 110 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Wed 18/8/21 Mon 20/9/21 Fri 23/7/21 Mon 2/8/21 Mon 20/9/21 Fri 15/12/17 Sat 28/4/18 Sat 28/4/18 Sat 28/4/18 Fri 12/10/18 Fri 12/10/18 Tue 16/10/18 Tue 16/10/18 Wed 4/11/20 Wed 4/11/20 Sat 21/11/20	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21 Sat 18/9/21 Sat 2/10/21 Tue 21/9/21 Sat 28/8/21 Sat 12/6/21 Tue 3/8/21 Sat 28/8/21 Sat 2/10/21 Mon 14/2/22 Thu 13/1/22 Wed 22/8/18 Tue 21/8/18 Wed 22/8/18 Mon 13/5/19 Tue 16/10/18 Wed 24/10/18 Tue 18/12/18 Mon 13/5/19 Tue 7/9/21 Fri 20/11/20 Thu 24/12/20	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 30 days 118 30 days 123 12 days 34 10 days 34 10 days 34 80 days 110 10 days 115 24 days 123 10 days 125 487.25 days 337.58 days 0 days 144				
	Sewerage Works / Drainage Works Watermain FW1a (CH29-100) Road Lighting Civil Works Provision Utilities (by others) Carriageway and Footway Backfilling to Formation Level Carriageway Footpath, Road Marking and Street Furniture Landscape Works Shrubs Planting at RW1 Woodland Planting at Site 3 Hydroseeding at Fill Slope Shrubs Planting at Pick-up/ Drop Off Irrigation System and Water Points (Except Water Connection) Tree Planting Works Section 2 of the Works (Parts B1, B2, C, D, F, G1 & G2) Part B1 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework Verification Drillholes (10 Nos., VDH3, 6, 10-15,19-20) and Preliminary Results Submission Design Review Cut Slopes CS1 & CS2 Excavation (crest to +55mPD) Drainage and Maintenance Access (at +55mPD berm) Drainage and Maintenance Access (+55 to +50 slope surface) Cut Slope CS3 Excavation (crest to toe)	20 days 20 days 20 days 10 days 72 days 30 days 30 days 12 days 172 days 30 days 10 days 10 days 10 days 24 days 110 days 1232 days 1103 days 95 days 170 days 170 days 170 days 170 days 180 days 11 days 15 days	Wed 31/3/21 Thu 22/7/21 Wed 31/3/21 Sat 26/6/21 Sat 26/6/21 Mon 2/8/21 Mon 6/9/21 Sat 6/3/21 Wed 18/8/21 Wed 18/8/21 Mon 2/8/21 Mon 2/8/21 Fri 23/7/21 Mon 2/8/21 Fri 23/7/21 Mon 2/8/21 Fri 15/12/17 Sat 28/4/18 Sat 28/4/18 Sat 28/4/18 Thu 12/7/18 Fri 12/10/18 Fri 12/10/18 Tue 16/10/18 Tue 16/10/18 Tue 16/10/18 Wed 4/11/20 Wed 4/11/20	Mon 26/4/21 Fri 13/8/21 Wed 14/4/21 Sat 18/9/21 Sat 31/7/21 Sat 4/9/21 Sat 18/9/21 Sat 2/10/21 Tue 21/9/21 Sat 28/8/21 Sat 12/6/21 Tue 3/8/21 Sat 2/10/21 Mon 14/2/22 Thu 13/1/22 Wed 22/8/18 Tue 21/8/18 Wed 22/8/18 Mon 13/5/19 Tue 16/10/18 Wed 24/10/18 Tue 18/12/18 Mon 13/5/19 Tue 18/12/18 Mon 13/5/19 Tue 7/9/21 Fri 20/11/20	0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0	20 days 118SS+21 days 20 days 118FS+21 days 10 days 118SS+21 days 30 days 118SS+21 days 30 days 118 30 days 123 12 days 34 10 days 34 80 days 34 80 days 110 10 days 115 24 days 123 10 days 125 487.25 days 337.58 days 0 days				_

Contract No. CV/2016/10 Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery

3 Month Rolling Programme (Nov 2021 to Jan 2022)

Hsin Chong Tsun Yip Joint Venture Updated Date : Nov 2021

	Columbia and the Columb	les ::	la.	les co	[m. m] n	and the second second				
Task Nam		Duration	Start	Finish	% Complete Ren	aining Duration Predecessors	11	12	+ , , , , , ,	
18	Construction of toe wall (5 bays, approx. 66m) (4 days/ bay)	20 days	Thu 29/7/21	Fri 20/8/21	100%	0 days 147		12		
	, , , , , , , , , , , , , , , , , , ,	-					_			
	Backfilling and drainage	15 days	Sat 21/8/21	Tue 7/9/21	100%	0 days 148	_			
_	•	880 days	Thu 23/8/18	Wed 11/8/21	84%	140.71 days				
1	Slope Cutting (crest to+94.5mPD)	31 days	Thu 23/8/18	Fri 28/9/18	100%	0 days	·			
	Drainage and Maintenance Access (at crest)	29 days	Tue 2/10/18	Mon 5/11/18	100%	0 days				
_		40 days	Sat 6/10/18	Thu 22/11/18	100%	0 days	_			
		-					_			
		7 days	Fri 26/10/18	Fri 2/11/18	100%	0 days				
	Drainage and Maintenance Access (+94.5 to +87mPD slope surface)+ GI Works	24 days	Fri 26/10/18	Thu 22/11/18	100%	0 days	·			
	Slope Cutting and Soil Nail (+87 to+79.5mPD, 84Nos. of Soil Nail)	40 days	Thu 8/11/18	Mon 24/12/18	100%	0 days	7			
		33 days	Fri 26/10/18	Mon 3/12/18	100%	0 days	-			
	,					•	_			
	RFI50 (Waiting Instruction / Abortive Works / Additional Earthwork+25m Uchannel at CS13crest)	61 days	Thu 22/11/18	Mon 4/2/19	100%	0 days	·			
	RFI(Slope Cutting and Soil Nail - additional 24 Nos. of Soil Nail)	39 days	Fri 11/1/19	Thu 28/2/19	100%	0 days	·]			
	RFI50(Additional Drainage and Mantenance Access (at 87mPD berm)	13 days	Fri 1/2/19	Tue 19/2/19	100%	0 days	–			
-	· · · · · · · · · · · · · · · · · · ·	-				-	_			
	• • • • • • • • • • • • • • • • • • • •	10 days	Fri 8/2/19	Tue 19/2/19	100%	0 days				
	Slope Cutting and Soil Nail (+72 to +79.5,115+21Nos. of Soil Nail)	90 days	Mon 21/1/19	Wed 15/5/19	100%	0 days	·			
	Drainage and Maintenance Access (at +79.5mPD berm)	42 days	Fri 1/2/19	Mon 25/3/19	100%	0 days	¬			
	Drainage and Maintenance Access (+72 to +79.5mPD slope surface, CS13 crest)+ GI Works	13 days	Thu 2/5/19	Fri 17/5/19	100%	0 days	-			
		-				-	_			
		67 days	Mon 8/4/19	Tue 2/7/19	100%	0 days				
	Drainage and Maintenance Access (at +72mPD berm)	29 days	Sat 13/4/19	Wed 22/5/19	100%	0 days	·			
1	Drainage and Maintenance Access (+64.5 to +72mPD slope surface)+ GI Works	17 days	Wed 3/7/19	Mon 22/7/19	100%	0 days 165	7			
		180 days	Tue 2/7/19	Thu 6/2/20	100%		<u> </u>			
	1 0 ,	•				0 days	⊣			
	Drainage and Maintenance Access (at +64.5mPD berm)	40 days	Tue 6/8/19	Sat 21/9/19	100%	0 days 168SS+30 days				
	Drainage and Maintenance Access (+57 to +64.5mPD slope surface)+ GI Works	17 days	Fri 7/2/20	Wed 26/2/20	100%	0 days 168	7			
		38 days	Thu 12/3/20	Wed 29/4/20	100%	0 days 195	<u> </u>			
	Chape Guitting and Got i van lot Got i (+37 to +45.5 lin*D, of ilos. of Soli Ivali, 13 ilos. of naking Dialit)	oo days	111u 12/3/20	VV Cu 25/4/20	100%	u uays 133	·			
	Drainage and Maintenance Access for CS11 (at +57mPD berm)	20 days	Thu 26/3/20	Wed 22/4/20	100%	0 days 171SS+12 days	⊣			
	, ,	-					⊣			
	Drainage and Maintenance Access for CS11 (below57 mPD slope surface/ on RW11)+ GI Works	17 days	Sat 2/5/20	Thu 21/5/20	100%	0 days 171	· [
							_			
	Slope Cutting and Soil Nail for CS12/CS13 (+57 to +49.5 mPD, 497 nos. of Soil Nail, 80 nos. of Raking Drain)	85 days	Fri 7/2/20	Fri 22/5/20	100%	0 days 168,169,170FS-28 days	· [
	Drainage and Maintenance Access for CS12/13 (at +57mPD berm)	35 days	Wed 11/3/20	Fri 24/4/20	100%	0 days 174SS+28 days	·			
	Drainage and Maintenance Access for CS12/CS13 (+49.5 to + 57mPD slope surface)+ GI Works	20 days	Sat 23/5/20	Mon 15/6/20	100%	0 days 174	–			
	Drainage and maintenance records to the desire (rises to risem 1 dispersional action). At the maintenance records	20 dayo	Out 20/0/20	11.011 10/0/20	10070	o dayo	·			
	Slope Cutting and Soil Nail for CS12/CS13 (+42 to +49.5 mPD, 383 nos. of Soil Nail, 87 nos. of Raking Drain)	170 days	Tue 2/6/20	Tue 22/12/20	44%	96 days 174,175,176FS-12 days	-			
	cope during and contrained do 12/00/10 (142 to 140.0 mile), cooling, or not. of realing brains	170 days	1 40 2/0/20	100 22/12/20	1170	00 days 174,170,1701 0 12 days	·			
	Drainage and Maintenance Access for CS12/13 (at +49.5mPD berm)	42 days	Fri 3/7/20	Thu 20/8/20	100%	0 days 177SS+25 days	<u> </u>			
	, ,						_			
	Drainage and Maintenance Access for CS12/CS13 (+42 to +49.5mPD slope surface)+ GI Works	17 days	Sat 29/8/20	Thu 17/9/20	100%	0 days 177	•			
							<u> </u>			
	Slope Cutting and Soil Nail for CS13 (+42 to +34.5 mPD, 126 nos. of Soil Nail, 55 nos. of Raking Drain)	59 days	Wed 23/12/20	Mon 8/3/21	100%	0 days 177,178,179FS-20 days	·			
	Drainage and Maintenance Access for CS13 (at +42mPD berm)	28 days	Tue 19/1/21	Tue 23/2/21	100%	0 days 180SS+20 days	·			
	Drainage and Maintenance Access for CS13 (+34.5 to +42mPD slope surface)+ GI Works	25 days	Tue 9/3/21	Fri 9/4/21	100%	0 days 180	_			
	• • • • • • • • • • • • • • • • • • • •	100 days	Tue 16/3/21	Sat 17/7/21	0%	100 days 180,181,182FS-19 days	-			
	Slope Cutting and Soli Ivali for CS13 (+34.3 IIIF Dto toe, 73 flos. or Soli Ivali, 27 flos. or having Drain)	100 days	Tue 10/3/21	3al 17/1/21	0 76	100 days 160,161,162F3-19 days				
	Drainage and Maintenance Access for CS13 (at +34.5mPD berm)	27 days	Mon 12/4/21	Thu 13/5/21	0%	27 days 183SS+20 days	⊣			
	, ,						_			
	Drainage and Maintenance Access for CS13 (below+34.5 mPD slope surface)+ GI Works	21 days	Mon 19/7/21	Wed 11/8/21	0%	21 days 183				
	letaining Wall RW11	98 days	Tue 12/11/19	Wed 11/3/20	100%	0 days				
	General Excavation with ELS to Formation Level RW11 Bay 1-4	30 days	Tue 12/11/19	Mon 16/12/19	100%	0 days 168	<u> </u>			
	•	-				•	—			
	, ,	5 days	Tue 17/12/19	Sat 21/12/19	100%	0 days 187				
	Base slab of Retaining Wall RW11 Bay 1-4	10 days	Sun 22/12/19	Mon 6/1/20	100%	0 days 188	·			
	·	20 days	Mon 13/1/20	Fri 7/2/20	100%	0 days 189	7			
	,	-					_			
		5 days	Tue 17/12/19	Sat 21/12/19	100%	0 days 187	_			
		10 days	Sun 22/12/19	Mon 6/1/20	100%	0 days 191				
	Wall Stem of Retaining Wall RW11 Bay 5-6	20 days	Tue 7/1/20	Sat 1/2/20	100%	0 days 192	·			
	,	5 days	Sat 8/2/20	Thu 13/2/20	100%	0 days 190,193	<u> </u>			
	· ·	-				-	_			
		23 days	Fri 14/2/20	Wed 11/3/20	100%	0 days 194				
	xisting Slope Upgrading Works	210 days	Tue 1/12/20	Tue 17/8/21	65%	73.2 days	· [
	- 1 1	150 days	Tue 1/12/20	Mon 24/5/21	32%	102 days 174SS+110 days	7			
	11 0						-			
	1 11 1	200 days	Mon 28/12/20	Tue 17/8/21	90%	20 days	_			
	Slope Cutting and Soil Nail (Crest to To, 29 Nos. of Soil Nail)	100 days	Mon 28/12/20	Thu 22/4/21	100%	0 days 174SS+110 days	·			
	Drainage and Maintenance Access (Crest)	100 days	Fri 23/4/21	Tue 17/8/21	80%	20 days 199	7			
	· /	753 days	Thu 16/8/18	Mon 1/3/21	100%	0 days	<u> </u>			
	•	-				-	⊣			
		36 days	Thu 16/8/18	Thu 27/9/18	100%	0 days				
	Drainage and Maintenance Access (at crest)	15 days	Mon 20/8/18	Wed 5/9/18	100%	0 days	· I			
		62 days	Mon 3/9/18	Fri 16/11/18	100%	0 days	7			
						-	_			
		49 days	Mon 3/9/18	Thu 1/11/18	100%	0 days				
	Drainage and Maintenance Access (+62 to +69.5mPD slope surface)+ GI Works	36 days	Fri 26/10/18	Thu 6/12/18	100%	0 days	· [
	Slope Cutting and Soil Nail (+54.5 to +62mPD, 237 nos. of Soil Nail, 58 nos. of Raking Drain)	66 days	Wed 7/11/18	Fri 25/1/19	100%	0 days	7			
		-	Wed 7/11/18	Thu 6/12/18	100%	•	<u> </u>			
	· · · · · · · · · · · · · · · · · · ·	26 days				0 days	⊣			
	Drainage and Maintenance Access (+54.5 to +62mPD slope surface)+ GI Works	38 days	Sat 29/12/18	Fri 15/2/19	100%	0 days	· I			
	Slope Cutting and Soil Nail (+47 to +54.5mPD, 548 nos. of Soil Nail, 86 nos. of Raking Drain)	155 days	Mon 7/1/19	Thu 18/7/19	100%	0 days	7			
		61 days	Sat 19/1/19	Wed 3/4/19	100%	0 days	-			
	Drainage and Maintenance Access (at ±54.5mPD herm)	or uays				-	⊣			
			Mad 0/4/40	Thu 25/7/19	100%	0 days				
		90 days	Wed 3/4/19				¬	•		
	Drainage and Maintenance Access (+54.5 to +47mPD slope surface)+ GI Works	90 days 94 days	Mon 6/5/19	Mon 26/8/19	100%	0 days	- I			
	Drainage and Maintenance Access (+54.5 to +47mPD slope surface)+ GI Works Slope Cutting and Soil Nail (+39.5 to +47mPD, 490 nos. of Soil Nail, 107 nos. of Raking Drain)	94 days	Mon 6/5/19			-	<u> </u>			
	Drainage and Maintenance Access (+54.5 to +47mPD slope surface)+ GI Works Slope Cutting and Soil Nail (+39.5 to +47mPD, 490 nos. of Soil Nail, 107 nos. of Raking Drain) Drainage and Maintenance Access (at +47mPD berm)	94 days 38 days	Mon 6/5/19 Tue 2/7/19	Wed 14/8/19	100%	0 days				
	Drainage and Maintenance Access (+54.5 to +47mPD slope surface)+ GI Works Slope Cutting and Soil Nail (+39.5 to +47mPD, 490 nos. of Soil Nail, 107 nos. of Raking Drain) Drainage and Maintenance Access (at +47mPD berm) Drainage and Maintenance Access (+39.5 to +47mPD slope surface)+ GI Works	94 days 38 days 23 days	Mon 6/5/19 Tue 2/7/19 Tue 27/8/19	Wed 14/8/19 Mon 23/9/19	100% 100%	0 days 0 days 213				
	Drainage and Maintenance Access (+54.5 to +47mPD slope surface)+ GI Works Slope Cutting and Soil Nail (+39.5 to +47mPD, 490 nos. of Soil Nail, 107 nos. of Raking Drain) Drainage and Maintenance Access (at +47mPD berm) Drainage and Maintenance Access (+39.5 to +47mPD slope surface)+ GI Works	94 days 38 days	Mon 6/5/19 Tue 2/7/19	Wed 14/8/19	100%	0 days				

Task Name 7 Drainage and Maintenance Access (at +39.5mPD berm and Slope Surface) + Gl Works	Duration	Start	Finish		emaining Duration Predecessors	11	12	1	2	工
	30 days	Tue 5/1/21	Mon 1/3/21	100%	0 days					
Fill Slope FS17	52 days	Fri 2/7/21	Tue 31/8/21	0%	52 days					
Drainage and Maintenance Access at toe	28 days	Fri 2/7/21	Tue 3/8/21	0%	28 days 217					
FS17 Filling Stage 1 (~2.5m max) Civil Works for Sha Ling Road (M001 CH710 to CH825, MO11 CH00 to CH20, M014)	24 days	Wed 4/8/21	Tue 31/8/21 Tue 28/9/21	0% 0%	24 days 219					
Civil Works for Sha Ling Road (M001 CH710 to CH825, M011 CH00 to CH20, M014) Waterworks / Drainage / Sewerage/ Utilities Works	224 days 27 days	Mon 28/12/20 Mon 28/12/20	Thu 28/1/21	0%	224 days 27 days					
3 Sewerage Works / Drainage Works	18 days	Mon 28/12/20	Mon 18/1/21	0%	18 days 138,145	—			Ē	
Watermain FW1 (CH532-637), FW1a (CH000-029) and FW2 (CH530-618)	15 days	Tue 12/1/21	Thu 28/1/21	0%	15 days 223SS+12 days					
5 Road Lighting Civil Works Provision	8 days	Tue 12/1/21	Wed 20/1/21	0%	8 days 223SS+12 days					
Utilities (by others)	3 days	Tue 12/1/21	Thu 14/1/21	0%	3 days 223SS+12 days					
Carriageway and Footway	57 days	Fri 23/7/21	Tue 28/9/21	0%	57 days					
8 Backfilling to Formation Level	11 days	Fri 23/7/21	Wed 4/8/21	0%	11 days 222,115					
Carriageway	28 days	Thu 5/8/21	Mon 6/9/21	0%	28 days 228				-	
Footpath, Road Marking and Street Furniture	18 days	Tue 7/9/21	Tue 28/9/21	0%	18 days 229				1	
Civil Works for PDA (PT04, PT05, PT06, PT07 and PT08)	381.1 days	Fri 5/6/20	Tue 14/9/21	87%	51.22 days					
Waterworks / Drainage / Sewerage/ Utilities Works	238 days	Fri 5/6/20	Mon 22/3/21	100%	0 days				-	
Drainage Works (with Petrol Interceptor)	200 days	Fri 5/6/20	Tue 2/2/21	100%	0 days 444				1	
Road Lighting Civil Works Provision	10 days	Thu 11/3/21	Mon 22/3/21	100%	0 days 233FS+28 days				Ē	
Carriageway and Footway	143.1 days	Tue 23/3/21	Tue 14/9/21	69%	44.17 days					
Backfilling to Formation Level	80 days	Tue 23/3/21	Wed 30/6/21	80%	16 days 232					
7 Carriageway	60 days	Sat 10/4/21	Thu 19/8/21	80%	12 days 236					
Footpath, Road Marking and Street Furniture	22 days	Thu 19/8/21	Tue 14/9/21	0%	22 days 237					
9 Civil Works for PDA (M011 CH140-215,M08 CH70-102)	161 days	Tue 9/3/21	Mon 20/9/21	21%	126.67 days					
0 Waterworks / Drainage / Sewerage/ Utilities Works	90 days	Tue 9/3/21	Mon 28/6/21	40%	53.78 days					
Sewerage Works / Drainage Works	60 days	Tue 9/3/21	Sat 22/5/21	30%	41.8 days 180					
2 Road Lighting Civil Works Provision	10 days	Mon 29/3/21	Wed 16/6/21	70%	3 days 241FS+17 days					
3 Utilities (by others)	10 days	Thu 17/6/21	Mon 28/6/21	70%	3 days 242					
4 Carriageway and Footway	71 days	Tue 29/6/21	Mon 20/9/21	0%	71 days					
5 Backfilling to Formation Level	30 days	Tue 29/6/21	Tue 3/8/21	0%	30 days 240					
Carriageway Footpath, Road Marking and Street Furniture	30 days	Wed 4/8/21	Tue 7/9/21	0%	30 days 245					
7 Footpath, Road Marking and Street Furniture 8 Civil Works for Sha Ling Road (M001 CH610-710)	11 days	Wed 8/9/21	Mon 20/9/21 Tue 27/7/21	0% 53%	11 days 246					
9 Waterworks / Drainage / Sewerage/ Utilities Works	114 days 44 days	Tue 9/3/21 Tue 9/3/21	Mon 3/5/21	100%	53.2 days 0 days				Ē	
Sewerage Works / Drainage Works Sewerage Works / Drainage Works	30 days	Tue 9/3/21	Thu 15/4/21	100%	0 days 440,180					
Watermain FW1 (CH433-532) and FW2 (CH433-530)	30 days	Thu 25/3/21	Mon 3/5/21	100%	0 days 250SS+14 days				1	
Road Lighting Civil Works Provision	10 days	Thu 25/3/21	Thu 8/4/21	100%	0 days 250SS+14 days					
Utilities (by others)	10 days	Thu 25/3/21	Thu 8/4/21	100%	0 days 250SS+14 days				Ē	
Garriageway and Footway	70 days	Tue 4/5/21	Tue 27/7/21	0%	70 days					
55 Backfilling to Formation Level	30 days	Tue 4/5/21	Tue 8/6/21	0%	30 days 249					
Carriageway	30 days	Wed 9/6/21	Thu 15/7/21	0%	30 days 255				1	
Footpath, Road Marking and Street Furniture	10 days	Fri 16/7/21	Tue 27/7/21	0%	10 days 256				1	
Civil Works for Sha Ling Road (M001 CH480-610, M08 CH00-70)	555 days	Tue 3/3/20	Thu 13/1/22	19%	447.85 days					
Sewage Detention Tank Civil and Structural Works	549 days	Tue 3/3/20	Thu 6/1/22	25%	413.7 days					
Civil and Structural Works	74 days	Tue 3/3/20	Wed 3/6/20	80%	15 days				1	
Excavation by open cut	25 days	Tue 3/3/20	Tue 31/3/20	40%	15 days					
Blinding layer concreting	1 day	Wed 1/4/20	Wed 1/4/20	100%	0 days 261					
Construction of base slab	7 days	Thu 2/4/20	Tue 14/4/20	100%	0 days 262					
Construction of wall and top slab	20 days	Wed 15/4/20	Sat 9/5/20	100%	0 days 263					
Construction of manhole	7 days	Mon 11/5/20	Mon 18/5/20	100%	0 days 264					
Backgilling	14 days	Tue 19/5/20	Wed 3/6/20	100%	0 days 265					
VDS and AMS for Sewage Detention Tank (Permanment Design and Submission Approval)	350 days	Mon 18/5/20	Tue 20/7/21	23%	270 days 266					
VDS and AMS for Sewage Detention Tank	140 days	Wed 21/7/21	Thu 6/1/22	0%	140 days 267					
Waterworks / Drainage / Sewerage/ Utilities Works	146 days	Tue 4/5/21	Wed 27/10/21	0%	146 days					
0 Sewerage Works / Drainage Works	40 days	Wed 8/9/21	Wed 27/10/21	0%	40 days 260,256,246					
Watermain FW1 and FW2 (CH310-433)	17 days	Tue 4/5/21	Mon 24/5/21	0%	17 days 251					
2 Road Lighting Civil Works Provision	18 days	Tue 25/5/21	Tue 15/6/21	0%	18 days 271					
3 Utilities (by others)	17 days	Wed 16/6/21	Tue 6/7/21	0%	17 days 272					
Carriageway and Footway Backfilling to Formation Level	64 days 12 days	Thu 28/10/21 Thu 28/10/21	Thu 13/1/22 Wed 10/11/21	0 %	64 days 12 days 269					
5 Backfilling to Formation Level 6 Carriageway	32 days	Thu 11/11/21	Fri 17/12/21	0%	32 days 275					
7 Footpath, Road Marking and Street Furniture	20 days	Sat 18/12/21	Thu 13/1/22	0%	20 days 276		<u> </u>			
Civil Works for Sha Ling Road (M001 CH360-480)	104 days	Wed 28/7/21	Mon 29/11/21	26%	76.47 days					
9 Waterworks / Drainage / Sewerage/ Utilities Works	67 days	Wed 28/7/21	Sat 16/10/21	36%	42.83 days					
Sewerage Works / Drainage Works	28 days	Wed 28/7/21	Sat 28/8/21	80%	5.6 days 257					
1 Watermain FW1 and FW2 (CH175-310)	18 days	Thu 19/8/21	Wed 8/9/21	80%	3.6 days 280SS+19 days					
Additional rising main (CE No. 181)	30 days	Thu 9/9/21	Sat 16/10/21	0%	30 days 281					
Road Lighting Civil Works Provision	15 days	Thu 19/8/21	Sat 4/9/21	0%	15 days 280SS+19 days					
Utilities (by others)	11 days	Thu 19/8/21	Tue 31/8/21	0%	11 days 280SS+19 days					
Carriageway and Footway	37 days	Mon 18/10/21	Mon 29/11/21	0%	37 days	-				
6 Backfilling to Formation Level	7 days	Mon 18/10/21	Mon 25/10/21	0%	7 days 279					
7 Carriageway	18 days	Tue 26/10/21	Mon 15/11/21	0%	18 days 286					
Footpath, Road Marking and Street Furniture	12 days	Tue 16/11/21	Mon 29/11/21	0%	12 days 287	<u> </u>				
Civil Works for Sha Ling Road (M001 CH180-360)	109 days	Fri 6/8/21	Tue 14/12/21	0%	109 days					
Waterworks / Drainage / Sewerage/ Utilities Works	59 days	Fri 6/8/21	Sat 16/10/21	0%	59 days				1	
- ·			1		- 1		•		-	

Contract No. CV/2016/10 **Hsin Chong Tsun Yip Joint Venture** 3 Month Rolling Programme (Nov 2021 to Jan 2022) Site Formation and Associated Infrastructural Works for Updated Date: Nov 2021 Development of Columbarium at Sandy Ridge Cemetery Remaining Duration Predecessors Duration 6 Complete Drainage and Sewerage Works 40 days Fri 6/8/21 Tue 21/9/21 40 days 316 292 Watermain FW1 and FW2 (CH000-175) 23 days Tue 7/9/21 Tue 5/10/21 0% 23 days 291SS+27 days Road Lighting Civil Works Provision 22 days 291SS+27 days 293 22 days Tue 7/9/21 Mon 4/10/21 0% 294 Utilities (by others) 32 days Tue 7/9/21 Sat 16/10/21 0% 32 days 291SS+27 days Carriageway and Footway 50 days Mon 18/10/21 Tue 14/12/21 0% 50 days Backfilling to Formation Level 10 days Thu 28/10/21 Mon 18/10/21 0% 10 days 290 Carriageway 24 days Fri 29/10/21 Thu 25/11/21 0% 24 days 296 Footpath, Road Marking and Street Furniture 16 days Fri 26/11/21 Tue 14/12/21 0% 16 days 297 298 1232 days Part B2. G1 and G2 Fri 15/12/17 Mon 14/2/22 67% 404.47 days 300 Access Date for Part G1 and G2 0 days Tue 5/2/19 Tue 5/2/19 Land Decontamination Works 293 days Tue 2/10/18 Thu 26/9/19 100% 0 days Re-appraisal and Contamination Assessment Plan (CAP) Submission to EPD 302 Tue 2/10/18 Fri 12/10/18 100% 10 days 0 days 303 EPD Review and Acceptance for CAP 195 days Fri 12/10/18 Wed 12/6/19 100% 0 days Environmental SI for Determination of Decontamination and SI Testing 100% 304 Tue 28/5/19 0 days 70 days Contamination Assessment Report (CAR) Submission to EPD Tue 20/8/19 Mon 9/9/19 100% 0 days 304 18 days 306 EPD Review and Acceptance for CAR 14 days Tue 10/9/19 Thu 26/9/19 100% 0 days 305 Civil Works for Sha Ling Road (M001 CH40-110) 717 days Tue 21/5/19 Sat 16/10/21 83% 120.49 days 308 Objection from Local Village (EW16 & 18) 355 days Tue 21/5/19 Wed 29/7/20 100% 300 Application for Road Closure / Road Divertion 17 days Thu 30/7/20 Tue 18/8/20 100% 0 days 308 Noise Barrier Bay 5 to Bay 8 322 days Wed 19/8/20 Thu 16/9/21 89% 35.78 days General Excavation with ELS to Formation Level Bay 5 to Bay 8 Wed 19/8/20 Fri 4/9/20 15 days 100% 0 days 309 Base slab of Noise Barrier Bay 5 to Bay 8 30 days Thu 20/8/20 Wed 23/9/20 100% 0 days 311 Wall Stem of Noise Barrier Bay 5 to Bay 8 30 days Thu 24/9/20 Sat 31/10/20 100% 0 days 312 Mon 2/11/20 Fri 6/11/20 Protective Coating /Temp Fill 100% 314 0 days 313 5 days 315 Installation of panel 10 days Mon 6/9/21 Thu 16/9/21 0% 10 days 382 Waterworks / Drainage / Sewerage/ Utilities Works Thu 13/5/21 Thu 5/8/21 60% 70 days 28 days Sewerage Works / Drainage Works 35 days Thu 13/5/21 Thu 24/6/21 80% 7 days 373 Watermain FW3 (CH045-105) Thu 5/8/21 0% 318 20 days Wed 14/7/21 20 days 320 Road Lighting Civil Works Provision 10 days Fri 25/6/21 Wed 7/7/21 80% 2 days 317 320 Utilities (by others) Fri 25/6/21 Tue 13/7/21 80% 3 days 317 15 days 321 Carriageway and Footway 59 days Fri 6/8/21 Sat 16/10/21 0% 59 days 322 Backfilling to Formation Level 10 days Fri 6/8/21 Tue 17/8/21 0% 10 days 316 323 Carriageway 42 days Wed 18/8/21 Thu 7/10/21 0% 42 days 322 Footpath, Road Marking and Street Furniture 324 7 davs Fri 8/10/21 Sat 16/10/21 0% 7 days 323 Ground Investigation and Geotechnical instrumentation for Commencement of Slopework 45 days Fri 8/2/19 Mon 1/4/19 100% 0 days Trial Pit Excavation / Installation of Instruments and Preliminary Results Submission Fri 8/2/19 100% 0 days 11,300 Fill Slope FS13 and FS14 56 days Fri 6/8/21 Tue 12/10/21 0% 56 days Drainage and Maintenance Access at toe 32 days Fri 6/8/21 Sat 11/9/21 0% 32 days 325,316 FS13 and FS14 Filling Stage 1 (~2.5m max) 24 days Mon 13/9/21 Tue 12/10/21 24 days 328 Cut Slope CS14 20 days 20 days Wed 13/10/21 Fri 5/11/21 0% 330 Slope Cutting (crest totoe) 3 days Wed 13/10/21 Sat 16/10/21 0% 3 days 327 Drainage and Maintenance Access (at crest) Mon 18/10/21 17 days Fri 5/11/21 17 days 331 Civil Works for Sha Ling Road (M001 CH110-180 104 days Fri 8/10/21 Mon 14/2/22 0% 104 days Waterworks / Drainage / Sewerage/ Utilities Works 45 days Fri 8/10/21 Tue 30/11/21 0% 45 days Sewerage Works / Drainage Works 335 30 days Fri 8/10/21 Fri 12/11/21 30 days 323 Watermain FW3 (CH105-175) 12 days Sat 13/11/21 Fri 26/11/21 0% 12 days 335 Road Lighting Civil Works Provision 10 days Sat 13/11/21 Wed 24/11/21 0% 10 days 335 338 Utilities (by others) 15 days Sat 13/11/21 Tue 30/11/21 15 days 335 Carriageway and Footway Wed 1/12/21 Mon 14/2/22 0% 59 days 59 days 329 Backfilling to Formation Level 10 days Wed 1/12/21 Sat 11/12/21 0% 10 days 334 Mon 13/12/21 42 days 340 42 days Sat 5/2/22 342 Footpath, Road Marking and Street Furniture 7 days Mon 7/2/22 Mon 14/2/22 0% 7 days 341 Man Kam To Road Bus Shelter (PT01, PT02 and PT03) Fri 15/12/17 343 1175 days Thu 2/12/21 71% 339.29 days Used as Temporary Site Office / Storage Area 340 days Fri 15/12/17 Mon 11/2/19 100% 0 days 2SS Investigation for DongJiang Watermain(CE23) Thu 10/1/19 100% Tue 23/4/19 82 davs 0 davs 346 Works Area Handing Over to WSD as Reques 198 days Mon 15/4/19 Thu 12/12/19 0 days Interface Issue with C2 (As request by Arup to delay XP application) (Including Temp. Road 290 days Tue 19/5/20 188.75 days Tue 28/5/19 TTA and XP Application at Man Kam To Road 14 days Wed 20/5/20 Thu 4/6/20 0% 14 days 347 Works Area Handling to WSD for Dong liang Wa Wed 25/11/20 Sat 9/1/21 Waterworks / Drainage / Sewerage/ Utilities Works 180 days Mon 11/1/21 Thu 19/8/21 77% 41.77 days Sewerage Work (Petrol Interceptor) Fri 16/7/21 0 days 352 15 days Mon 2/8/21 100% Sewerage Works / Drainage Works 150 days Mon 11/1/21 Thu 15/7/21 90% 15 days 349 353 Road Lighting Civil Works Provision Fri 16/7/21 Wed 28/7/21 8.8 days 352 11 days Fri 16/7/21 Utilities (by others) Thu 19/8/21 20% 24 days 352 354 30 days Carriageway and Footway 117 days Fri 16/7/21 Thu 2/12/21 17% 96.65 days Backfilling to Formation Level 12 days Fri 20/8/21 Thu 2/9/21 7.2 days 350 Fri 3/9/21 Wed 10/11/21 20% 44.8 days 356 Carriageway 56 days Footpath, Road Marking and Street Furniture 19 days Thu 11/11/21 Thu 2/12/21 0% 19 days 357 Reinstatement to existing Man Kam To Road 5 days Fri 16/7/21 Wed 21/7/21 5 days 352 Civil Works for Sha Ling Road (M001 CH00-40) Thu 30/8/18 Wed 22/12/21 55% 445.63 days 985 davs TTA and XP Application at Man Kam To Road Fri 15/1/21 Sat 30/1/21 0% 14 days 364 Works Area Handing Over to WSD as Request Thu 26/9/19 120 days Mon 6/5/19 Work Area Handling to Sang Hing for Turn Around 190 days Tue 24/11/20 0% 190 days Mon 6/4/20 Milestone 🔷 Summary -Critic al

5

6

Contract No. CV/2016/10 Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery

Milestone 🔷

Critical =

3 Month Rolling Programme (Nov 2021 to Jan 2022)

Hsin Chong Tsun Yip Joint Venture Updated Date : Nov 2021

-	Task Name	Duration	Start	Finish	% Complete	Remaining Duration	Dradacassors	٠	T									
	I ask I valid	Dui ation	Start	1 1111511	% Complete	Kemaning Duranon	I redecessors	Н	11	11 12	11 12 1	11 12 1 2	11 12 1 2	11 12 1 2	11 12 1 2	11 12 1 2	11 12 1 2	11 12 1 2
438	Protective Coating / Subsoil Drain / Filter Layer	5 days	Sat 9/11/19	Thu 14/11/19	100%	0 days	436,437	1				: · · · · · · · · · · · · · · · · · · ·						
439	Backfilling behind RW4 and Fill Slop FS4 (~8m up to +35.5 mPD)	22 days	Fri 15/11/19	Tue 10/12/19	95%	1 day	438	1										
440	Fill Slope FS2	47 days	Thu 17/10/19	Tue 10/12/19	100%	0 days		1										
441	Drainage and Maintenance Access (+35.5 to +43.0 mpD)	19 days	Thu 17/10/19	Thu 7/11/19	100%	0 days	435	1										
442	FS2 Filling Stage 1 (~7.5m, +35.5 to +43 mPD)	20 days	Fri 8/11/19	Sat 30/11/19	100%	0 days	441											
443	Drainage and Maintenance Access (+43.0 to +50 mpD)	30 days	Thu 17/10/19	Wed 20/11/19	100%	0 days	435	1										
444	FS2 Filling Stage 2 (~7.5m, +43 to +50 mPD)	18 days	Wed 20/11/19	Tue 10/12/19	100%	0 days	443	1										
445	Cut Slope CS18 and CS19	235 days	Mon 25/2/19	Sat 7/12/19	100%	0 days		1										
446	Slope Cutting (+54.5 to crest)	30 days	Wed 27/2/19	Tue 2/4/19	100%	0 days		1										
447	Confirmation of Interface Details at CS18/19 (NCE29)	30 days	Wed 27/2/19	Tue 2/4/19	100%	0 days	5											
448	Drainage and Maintenance Access (crest)+ GI Works	8 days	Wed 3/4/19	Fri 12/4/19	100%	0 days	8	1										
449	Slope Cutting and Raking Drain (+47 to +54.5mPD, 13 nos. of Raking Drain)	113 days	Mon 25/2/19	Mon 15/7/19	100%	0 days												
450	Drainage and Maintenance Access (+54.5 to +62mPD slope surface/berm)+ GI Works	30 days	Thu 4/4/19	Wed 15/5/19	100%	0 days		1										
451	Slope Cutting and Raking Drain (+47mPD to toe, 18 nos. of Raking Drain)	110 days	Mon 6/5/19	Fri 13/9/19	100%	0 days	450FS-30 days,213SS	1										
452	Drainage and Maintenance Access (below +47mPD slope surface/berm)+ GI Works	70 days	Sat 14/9/19	Sat 7/12/19	100%	0 days	451	1										
453	Landscape Works	67 days	Mon 16/9/19	Wed 4/12/19	86%	9.14 day:		1										
454	at Fill Slope FS2, FS3	50 days	Tue 8/10/19	Wed 4/12/19	70%	15 days	425	1										
455	at Cut Slope CS18, CS19	60 days	Mon 16/9/19	Tue 26/11/19	100%	0 days	451											


7



Three Months Rolling Programme of Contract CV/2017/02

3 Month Rolling Programme (from 26/11/2021 to 25/2/2022)

Accepted Initial Works Programme (06)

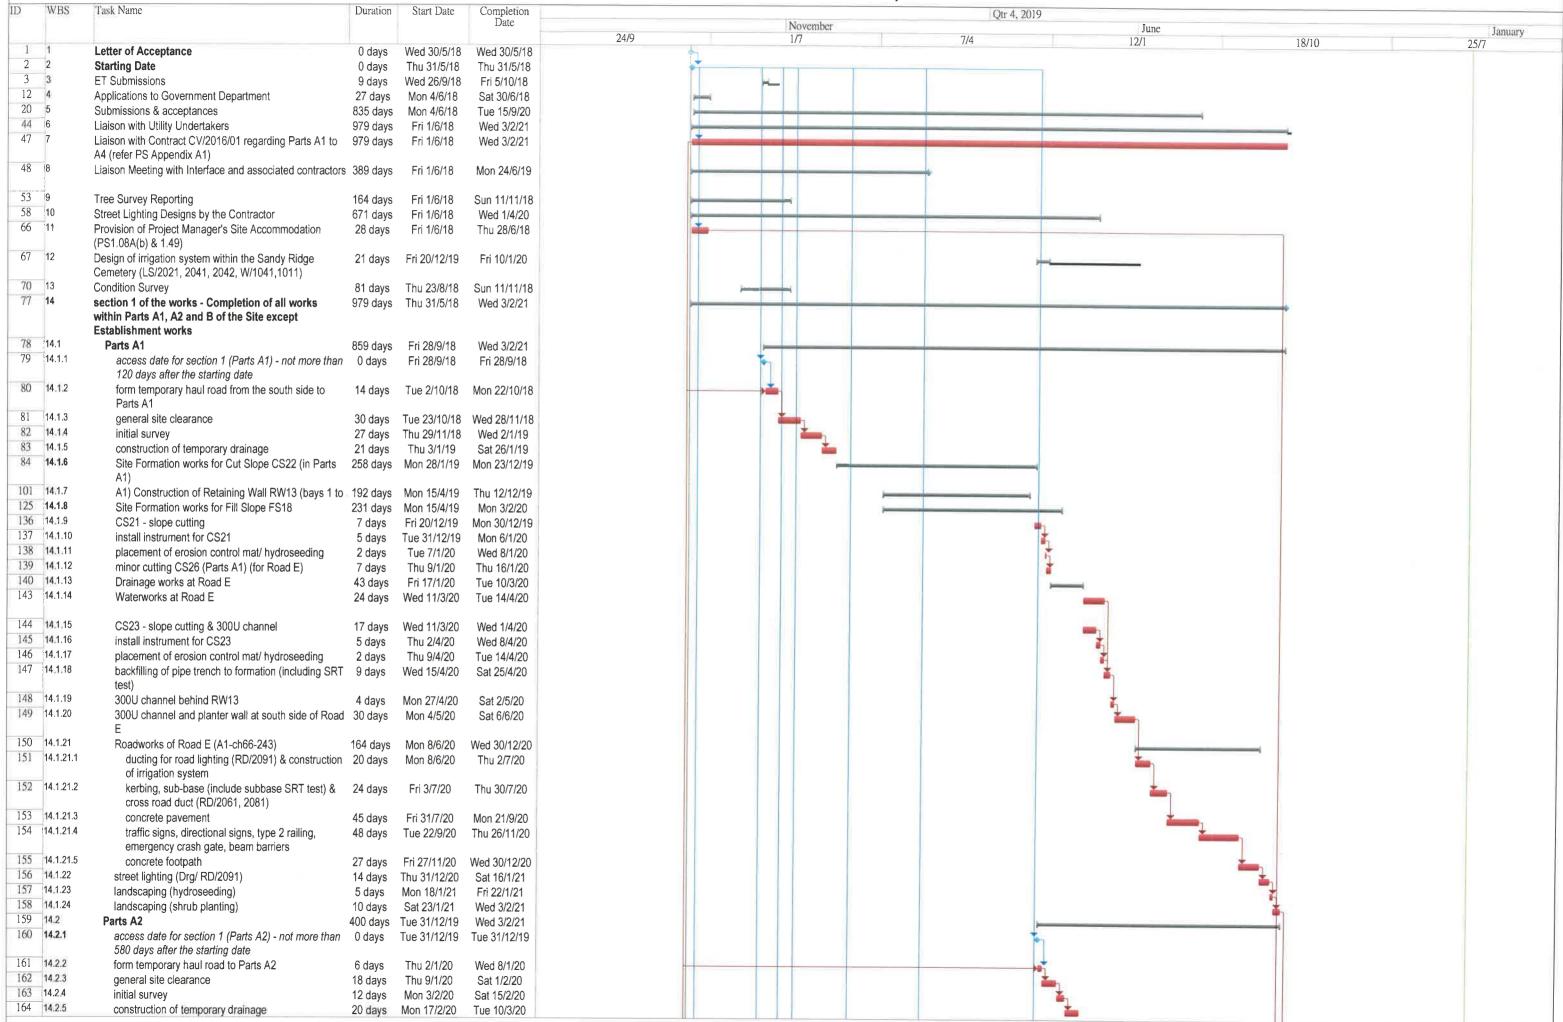

Sang Hing Civil Contractors Company Limited

3 Month Rolling Programme (from 26/11/2021 to 25/2/2022)

Accepted Initial Works Programme (06)

3 month rolling programme 20211126(26 Nov 21-25 Feb 22)

		vorks at Man Kam To Road and Lin Ma Hang Road Task Name	Duration	Start Date	Completion		(1rom 26/1	1/202	1 10 23/2	LI ZUZZ)	0. 1.00	10			
1.0	17.440		Duration	Guit Date	Date				November		Qtr 4, 201	June			January
165	1426	Cita Formation works for Cut Class COCCO (in D. 4. A.	1 1E de	10107 4410100	Man 20/0/00	24/9	1100		/7		7/4	12/1		18/10	25/7
174		Site Formation works for Cut Slope CS22 (in Parts A: Construction of Retaining Wall RW13 Bay 6 to Bay 8			Mon 30/3/20							j-man)			
199		(west) drainage works at Road E (ch250 to 300)	16 days		Mon 10/8/20 Wed 26/8/20										
1		(west) diditiage works at fload E (Ch200 to 500)	10 days	Jat 0/0/20	AACO 50/0/50							=	1		
200	14.2.9	(west) waterworks at Road E (ch250 to 300)	15 days	Thu 27/8/20	Sat 12/9/20										
		()	. 5 44,0	2170720	OG. IZIOIZO								-		
201	14.2.10	construction of Irrigation System	5 days	Sat 12/9/20	Thu 17/9/20								*		
	14.2.11	U channel for Road E	3 days	Thu 17/9/20	Sat 19/9/20								6		
	14.2.12	Roadworks of Road E (A2-ch243-300)	42 days	Sat 19/9/20	Tue 17/11/20								juga juga juga juga juga juga juga juga		
	14.2.12.1	kerbing & sub-base (include sub-base SRT test)	7 days	Sat 19/9/20	Sat 26/9/20										
	14.2.12.2	ducting for road lighting & water point	4 days	Sat 26/9/20	Wed 30/9/20								ř.		
	14.2.12.3	concrete pavement	15 days		Thu 22/10/20								*		
	14.2.12.4	traffic signs, beam barriers	-										*		
	14.2.12,5	concrete footpath	12 days		Tue 17/11/20								-		
209	14.2.13	street lighting for Road E (Drg/ RD/2091)	-										a di		
210		landscaping (shrub planting)	4 days	Fri 27/11/20	Tue 1/12/20		P						4		
212		site formation works for Cut Slope CS26 (A2) site formation works for Cut Slope CS25 (A2)	24 days		Fri 4/9/20								1		
213		placement of erosion control mat/ hydroseeding	12 days 2 days	Sat 5/9/20 Sat 19/9/20	Fri 18/9/20 Mon 21/9/20										
213		drainage works at Road B & sewerage works at	2 days 28 days		Wed 28/10/20								į.		
, D. T		Road B	20 udys	Sat 18/8/20	vveu 20/10/20										
215	14.2.19	waterworks at Road B	25 days	Thu 29/10/20	Mon 30/11/20								<u> </u>		
		natorno de Noda B	20 dayo	1110 20/10/20	141011 00/11/20										
216		backfill formation for Road B	3 days	Tue 1/12/20	Thu 3/12/20								+		
217		street lighting ducts and drawpits at Road B	9 days		Thu 10/12/20		10						1		
218	14.2.22	arrange Town Gas to lay cables (NOT YET			Wed 16/12/20		1						*		
		AGREED)					1								
219		planter wall for Road B		Thu 17/12/20									T.		
220	14.2.24	arrange HKT to lay PCCW cables (NOT YET	5 days	Wed 23/12/20	Wed 30/12/20								*		
201	440.00	AGREED)			_,,,										
	14.2.25	Roadworks of Road B (A2-ch28.5-90)		Thu 31/12/20	Fri 22/1/21								-		
	14.2.25.1	kerbing & sub-base (include sub-base SRT test)	-		Sat 9/1/21								*		
	14.2.25.2	DBM (Roadbase)	2 days	Mon 11/1/21	Tue 12/1/21								*		
	14.2.25.3 14.2.25.4	base course and wearing course	2 days	Wed 13/1/21	Thu 14/1/21								5		
17	14.2.26	directional sign, roadmarkings & footpath landscaping (hydroseeding)	7 days	Fri 15/1/21 Wed 13/1/21	Fri 22/1/21 Mon 1/2/21								i i		
227		landscaping (nydroseeding) landscaping (shrub planting)	-	Mon 1/2/21	Wed 3/2/21								-	J	
228			3 days		Wed 3/2/21									F	
		MKTR01B	or o days	1114 3 173/10	YYGU JIZIZ I									1	
229	14.3.1	access date for section 1 (Parts B) - the starting date	0 davs	Thu 31/5/18	Thu 31/5/18		*								
) -	37. 1											
230	14.3.2		104 days	Fri 1/6/18	Thu 4/10/18		4								1
231		utility detection and submit reports	30 days		Fri 9/11/18			-							
232	14.3.4		134 days	Fri 1/6/18	Fri 9/11/18		-								
226	140 5	Man Kam Road	055												
236	14.3.3	Construction of Fresh Water Mains (DN400)-refer to	352 days	Sat 10/11/18	Fri 17/1/20			ju ju							
237	14.3.5.1	Drawings No. MKTR Programme/W/001 & 002 Phase 1: TTA 1s	50 days	Cot 10/14/40	Cot 40/4/40			100							
246				Sat 10/11/18 Wed 14/11/18				ja ,							
255 1		Phase 1: TTA 0s Phase 1: TTA 15s		Tue 20/11/18	Sat 12/1/19 Sat 12/1/19			,							
264		Phase 2: TTA 2s		Tue 15/1/19	Mon 4/3/19					_					
273 1				Tue 15/1/19	Mon 4/3/19										
282	14.3.5.6			Mon 14/1/19	Mon 4/3/19										1
291 1			39 days		Tue 23/4/19		11 1								
300 1			39 days	Tue 5/3/19	Tue 23/4/19					—					
309 1		Phase 3: TTA17s	39 days	Tue 5/3/19	Tue 23/4/19										
	14.3.5.10	Phase 4: TTA4s	38 days		Fri 14/6/19										
	14.3.5.11				Fri 14/6/19										
	14.3.5.12			Wed 24/4/19	Fri 14/6/19								,		
	14.3.5.13			Wed 19/6/19	Wed 7/8/19					-					
	14.3.5.14			Sat 15/6/19	Wed 7/8/19					1					
372	14.3.5.15		-	Sat 15/6/19	Wed 7/8/19					1					
	14.3.5.16 14.3.5.17		46 days		Thu 3/10/19										
	14.3.5.17 14.3.5.18			Wed 14/8/19	Thu 3/10/19						-				
	14.3.5.18		47 days		Thu 3/10/19						—				
0	-386.0.10	FIIdSC F. LIMFS	44 days	Tue 8/10/19	vveu 2//11/19						ji				

Page 2/9

3 Month Rolling Programme (from 26/11/2021 to 25/2/2022)

Accepted Initial Works Programme (06)

WBS	Task Name	Duration	Start Date	Completion Date			16. 11		Qtr 4, 20	19			
				Date	24/9		November 1/7		7/4	Jun 12/1	е	10/10	Januar
)8 14.3.5.20		46 days		Wed 27/11/19	2 11 /			T	//4	12/1		18/10	25/7
7 .14.3,5.21		29 days	Thu 24/10/19						_				
7 14.3.5.22	additional Phase 8: additional TTA 0s	41 days	Wed 27/11/19	Fri 17/1/20					⊢				
7 14.3.6	Construction of Sewerage (DN630) - refer to	311 days	Sat 18/1/20	Wed 3/2/21									
	Drawing No. MKTR Programme/DR/001												
8 14.3.6.1	Phase A: TTA 1n		Tue 21/1/20	Sat 21/3/20						<u> </u>			
7 14.3.6.2	Phase A: TTA 7n	52 days	Sat 18/1/20	Sat 21/3/20									
6 14.3.6.3	Phase B: TTA 2n	52 days		Thu 28/5/20									
5 14.3.6.4	Phase B: TTA 8n	52 days	Mon 23/3/20	Thu 28/5/20						-			
4 14.3.6.5	Phase C: TTA 3n	52 days	Fri 29/5/20	Thu 30/7/20									
14.3.6.6	Phase C: TTA 9n	52 days	Fri 29/5/20	Thu 30/7/20						<u> </u>	-		
2 14.3.6.7	Phase D: TTA 4n	52 days	Fri 31/7/20	Tue 29/9/20		HIII							
1 14.3.6.8	Phase D: TTA 10n	52 days	Fri 31/7/20	Tue 29/9/20		11.11							
0 14.3.6.9 9 14.3.6.10	Phase E: TTA 5n	52 days		Wed 2/12/20									
8 14.3.6.10		52 days	Wed 30/9/20	Wed 2/12/20									
7 14.3.6.12		51 days		Wed 3/2/21							j		
6 14.3.6.13		38 days	Fri 18/12/20	Wed 3/2/21							H		
5 15		38 days	Fri 18/12/20	Wed 3/2/21							H		
6 16	Planned Completion for section 1 of the works	0 days	Wed 3/2/21	Wed 3/2/21								*1	
7 17	Completion Date for section 1 of the works section 2 of the works - Completion of all works	0 days	Wed 3/2/21 Thu 31/5/18	Wed 3/2/21 Wed 3/2/21								*	
ý. II	within Parts C1 and C2 of the Site except Establishment works	979 days	TNU 31/5/18	Wed 3/2/21								_	
8 17.1	access date for section 2 (Part C1)	0 days	Thu 31/5/18	Thu 31/5/18		+							
9 17.2	Temporary Traffic Arrangement (TTA) Scheme for Lin Ma Hang Road			Fri 9/11/18		-	-						
5 17.3	works at Lin Ma Hang Road (section 2 Part C1) refer Appendice LMHR01a to d	817 days	Sat 10/11/18	Wed 3/2/21			-					→	
6 17.3.1	Phase I (stage 1)-south lane (chainage 240-283)	23 days	Sat 10/11/18	Thu 6/12/18			parasi .						
7 17.3.2	Phase I (stage 2)-north lane (chainage 240-283)	16 days		Thu 27/12/18			1						
7 17.3.3	Phase I (stage 3)-south lane (chainage 283-335)		Fri 28/12/18	Mon 28/1/19			-						
8 17.3.4	Phase I (stage 4)-north lane (chainage 283-335)	17 days		Wed 20/2/19			<u></u>						
8 17.3.5	Phase I (stage 5)-south lane (chainage 335-380)	18 days		Wed 13/3/19				_					
8 17.3.6	Phase I (stage 6)-north lane (chainage 335-380)	16 days		Mon 1/4/19				H					
7 17.3.7	Phase I (stage 7)-south lane (chainage 380-435)	23 days	Tue 2/4/19	Fri 3/5/19				—					
8 17.3.8	Phase I (stage 8)-north lane (chainage 380-435)	15 days	Sat 4/5/19	Wed 22/5/19				H					
8 17.3.9	Phase I (stage 9)-south lane (chainage 190-240)	18 days	Thu 23/5/19	Thu 13/6/19				—					
9 17.3.10	Phase I (stage 10)-north lane (chainage 190-240)	16 days	Fri 14/6/19	Wed 3/7/19				-	i.				
9 17:3.11	Phase II (stage 1)-south lane (chainage 32-85)-Noise Barrier MM6 (bays 1-3) & MM7 (bays	95 days	Thu 4/7/19	Fri 25/10/19				1					
3 17.3.12	1-2) Phase II (stage 2)-north lane (chainage 32-85)-Noise Barrier MM9 (bays 1-4)	84 days	Sat 26/10/19	Fri 7/2/20					j				
5 17.3.13	Phase II (stage 3)-south lane (chainage 85-138)	38 days	Sat 8/2/20	Mon 23/3/20									
6 17.3.14	Phase II (stage 4)-north lane (chainage			Wed 17/6/20									
	85-138)-Noise Barrier MM10 (bays 1-4)	oo aayo	100 27/0/20	1100 1110120									
6 17.3.15	Phase II (stage 5)-south lane (chainage 138-190)	36 days	Thu 18/6/20	Fri 31/7/20									
7 17.3.16	Phase II (stage 6)-north lane (chainage		Sat 1/8/20	Wed 11/11/20									
	138-190)-Noise Barrier MM10 (bays 5-9)			· · · · - ·									
8 17.3.17	Phase II (stage 7)-south lane (chainage 0-32)-Noise	53 days	Thu 12/11/20	Fri 15/1/21								_	
	Barrier MM5 (bays 1-2)											7	
1 17.3.18	Phase II (stage 8)-north lane (chainage 0-32)	16 days	Sat 16/1/21	Wed 3/2/21								-	
2 17.3.19	Noise Barrier MM8 (bays 1-3)		Sat 1/8/20	Mon 18/1/21								2	
1 17.3.20	Street lighting (drawpits, abandon existing public lighting & cable, 100uPVC ducts) (ch0-435)		Mon 14/12/20	Sat 9/1/21									
0 47.0.04	Local de Co			144 146									
2 17.3.21	tree planting		Mon 11/1/21	Wed 13/1/21								*	
3 17.3.22	Street furniture & construction of footpath (ch0-435)	22 days	Sat 9/1/21	Wed 3/2/21									
47.0.00	Dis. 1.7.1 404) 11.1 (1.1 0.2 0.2 0.2 0.2 0.2 0.2 0.2 0.2 0.2 0.2	00.1	0										
4 17.3.23	Phase Ia (stage 101)-south lane (chainage 633-685)						J						
4 17.3.24	Phase la (stage 102)-north lane (chainage 633-685)			Fri 21/12/18			H						
4 17.3.25	Phase la (stage 103)-south lane (chainage 685-740)			Wed 23/1/19			-						
5 17.3.26	Phase la (stage 104)-north lane (chainage 685-740)			Fri 15/2/19			<u> </u>						
4 17.3.27	Phase Ia (stage 105)-south lane (chainage 740-790)		Sat 16/2/19	Fri 15/3/19			-	⊣					
17.3.28	Phase la (stage 106) north lane (chainage 740-790)		Sat 16/3/19 Sat 6/4/19	Thu 4/4/19 Sat 4/5/19				-					
5 17.3.29	Phase la stage 107)-south lane (chainage 790-840)												

3 Month Rolling Programme (from 26/11/2021 to 25/2/2022)


Accepted Initial Works Programme (06)

	vorks at Man Kam To Road and Lin Ma Hang Road Task Name	Duration	Start Date	Completion	\ \	20/11/2021 to 25/2/	Qtr 4, 2019			
		A CONTRACTOR OF THE CONTRACTOR		Date	24/9	November 1/7		June		Janua
6 17.3.30	Phase la (stage 108)-north lane (chainage 790-840)			Mon 10/6/19	2417	HI	7/4	12/1	18/10	25/7
6 17.3.31	Phase la (stage 109)-south lane (chainage 840-890)			Wed 17/7/19	1111		-			
17.3.32 17.3.33	Phase la (stage 110)-north lane (chainage 840-890)	18 days		Wed 7/8/19			jump()			
	Phase III (stage 1)-south lane (chainage 435-490)	20 days	Thu 8/8/19	Fri 30/8/19			- Paranti			
17.3.34	Phase III (stage 2)-north lane (chainage 435-490)	16 days		Thu 19/9/19			<u></u>			
17.3.35	Phase III (stage 3)-south lane (chainage 490-540)	34 days	Fri 20/9/19	Thu 31/10/19			jamenta)			
17.3.36	Phase III (stage 4)-north lane (chainage 490-540)	17 days	Fri 8/11/19	Wed 27/11/19			jump			
9 17.3.37 9 17.3.38	Phase III (stage 5)-south lane (chainage 540-590)	29 days					 4			
9 17.3.36	Phase III (stage 6)-north lane (chainage 540-590)	22 days	Sat 4/1/20	Sat 1/2/20	1			mi .		
17.3.40	Phase III (stage 7)-south lane (chainage 590-633)	29 days	Tue 4/2/20	Sat 7/3/20				-		
17.3.40	Phase III (stage 8)-north lane (chainage 590-633) Street lighting (drawpits, abandon existing public	25 days	Mon 9/3/20	Tue 7/4/20 Sat 18/4/20				passed.		
17.0.41	lighting & cable, 100uPVC ducts) (ch435-890)	7 days	Wed 8/4/20	Sat 10/4/20				-		
17.3.42	tree planting	5 days	Tue 14/4/20	Sat 18/4/20						
17.3.43	Street furniture & construction of footpath	23 days	Mon 20/4/20	Mon 18/5/20				4		
	(ch435-890)	20 dayo	101011 2014720	141011 10/0/20			1	China		
17.3.44	Phase IV (stage 1)-south lane (chainage 890-940)	22 days	Fri 20/9/19	Thu 17/10/19			<u> </u>			
17.3.45	Phase IV (stage 2)-north lane (chainage 890-940)	17 days		Wed 6/11/19			-			
17.3.46	Phase IV (stage 3)-south lane (chainage 940-983)	31 days	Thu 7/11/19	Thu 12/12/19			jamen j			
17.3.47	Phase IV (stage 4)-north lane (chainage 940-983)	16 days		Fri 3/1/20			—			
17.3.48	Phase V (stage 1)-south lane (chainage 983-1035)	17 days	Sat 4/1/20	Thu 23/1/20			-	í		
2 17.3.49	Phase V (stage 2)-north lane (chainage 983-1035)	16 days		Fri 14/2/20				i-i		
17.3.50	Phase V (stage 3)-south lane (chainage 1035-1087)		Sat 15/2/20	Sat 7/3/20						
17.3.51	Phase V (stage 4)-north lane (chainage 1035-1087)		Mon 9/3/20	Sat 21/3/20				H		
17.3.52			Mon 23/3/20	Sat 18/4/20				<u> </u>		
17.3.53	Phase V (stage 6)-north lane (chainage 1087-1139)		Mon 20/4/20	Fri 8/5/20				H		
17.3.54 17.3.55	Phase V (stage 7)-south lane (chainage 1139-1190)		Sat 9/5/20	Mon 1/6/20				-		
7 17.3.55 3 17.3.56	Phase V (stage 8)-north lane (chainage 1139-1190)		Tue 2/6/20	Thu 18/6/20				jenej		
17.3.56	Phase VI (stage 1)-south lane (chainage 1190-1240)		Fri 19/6/20	Wed 15/7/20				-		
7 17.3.58	Phase VI (stage 2)-north lane (chainage 1190-1240) Phase VI (stage 3)-south lane (chainage 1240-1286)		Thu 16/7/20 Mon 3/8/20	Sat 1/8/20 Thu 10/9/20				H_		
8 17.3.59	Phase VI (stage 4)-north lane (chainage 1240-1266)		Fri 11/9/20	Mon 28/9/20						
17.3.60	Phase VI (stage 4)-north lane (chainage 1240-1260)		Tue 29/9/20	Fri 23/10/20				janej		
7 17.3.61	Phase VI (stage 6) - north lane (chainage 1286 -133)			Sat 7/11/20				1000		
4 17.3.62	Phase VI (stage 7)-south lane (chainage 1332-1377)	,		Wed 9/12/20				T		
6 17.3.63	Phase VI (stage 8)-north lane (chainage 1332-1377)			Tue 29/12/20						
75 17.3.64	Street lighting (drawpits, abandon existing public								.	
	lighting & cable, 100uPVC ducts) (ch890-1377)									
5 17.3.65	tree planting	1 day	Wed 6/1/21	Wed 6/1/21					Ļ.	
7 17.3.66	Street furniture & construction of footpath		Wed 6/1/21	Wed 3/2/21						
	(ch890-1377)									
3 17.4	Noise Barrier works above the concrete substructure of	674 days	Mon 29/10/18	Wed 3/2/21						
	the noise barrier (section 2 Part C1)									
9 17.4.1			Mon 29/10/18				1			
77.4.2	propose specialist subcontractor to PM for	0 days	Sun 26/5/19	Sun 26/5/19			<u>~</u>			
1 4749	acceptance	0 1	0 10/0::-				Ţ			
17.4.3		0 days	Sun 16/6/19	Sun 16/6/19			41			
17.4.4	Project Manager	100 4	Mon 47/0/40	Mon 444040			1			
3 17.4.5	prepare design & liaise with designer & PM submit a proposal detailing the changes to PM's		Mon 17/6/19				1			
e man	design, if any	14 days	Tue 15/10/19	WIUTI 28/10/19						
17.4.6	submit 1st design for PM's comment	0 dave	Mon 28/10/19	Mon 28/10/10			.			
17.4.7	PM's comments		Tue 29/10/19				<u> </u>			
17.4.8	revise design		Tue 19/11/19				<u></u>			
17.4.9	re-submit design for PM's acceptance		Mon 16/12/19							
17.4.10	submit 3 sample panels for each type & colour for		Tue 17/12/19				1			
	acceptance	. days	100 17/12/10	MO11 20/12/10						
17.4.11	PM's & relevant authorities' acceptance	0 days	Mon 13/1/20	Mon 13/1/20						
17.4.12	ordering of noise barrier panel		Wed 15/1/20							
17.4.13	- ,		Thu 16/1/20				1			
17.4.14			Tue 14/7/20				-	<u> </u>		
3 17.4.15	completion of concrete curing of substructure of		Mon 14/10/19							
17 4.13		,								
	Nosie Barriers									
17.4.16	Nosie Barriers construction works above the concrete substructure of the noise barrier MM6, MM7 & MM9 (app. 77m)	48 days	Mon 28/9/20	Wed 25/11/20				-		

Contract No. CV/2017/02 Development of Columbarium at Sandy Ridge Cemetery - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

3 Month Rolling Programme (from 26/11/2021 to 25/2/2022)

Accepted Initial Works Programme (06)

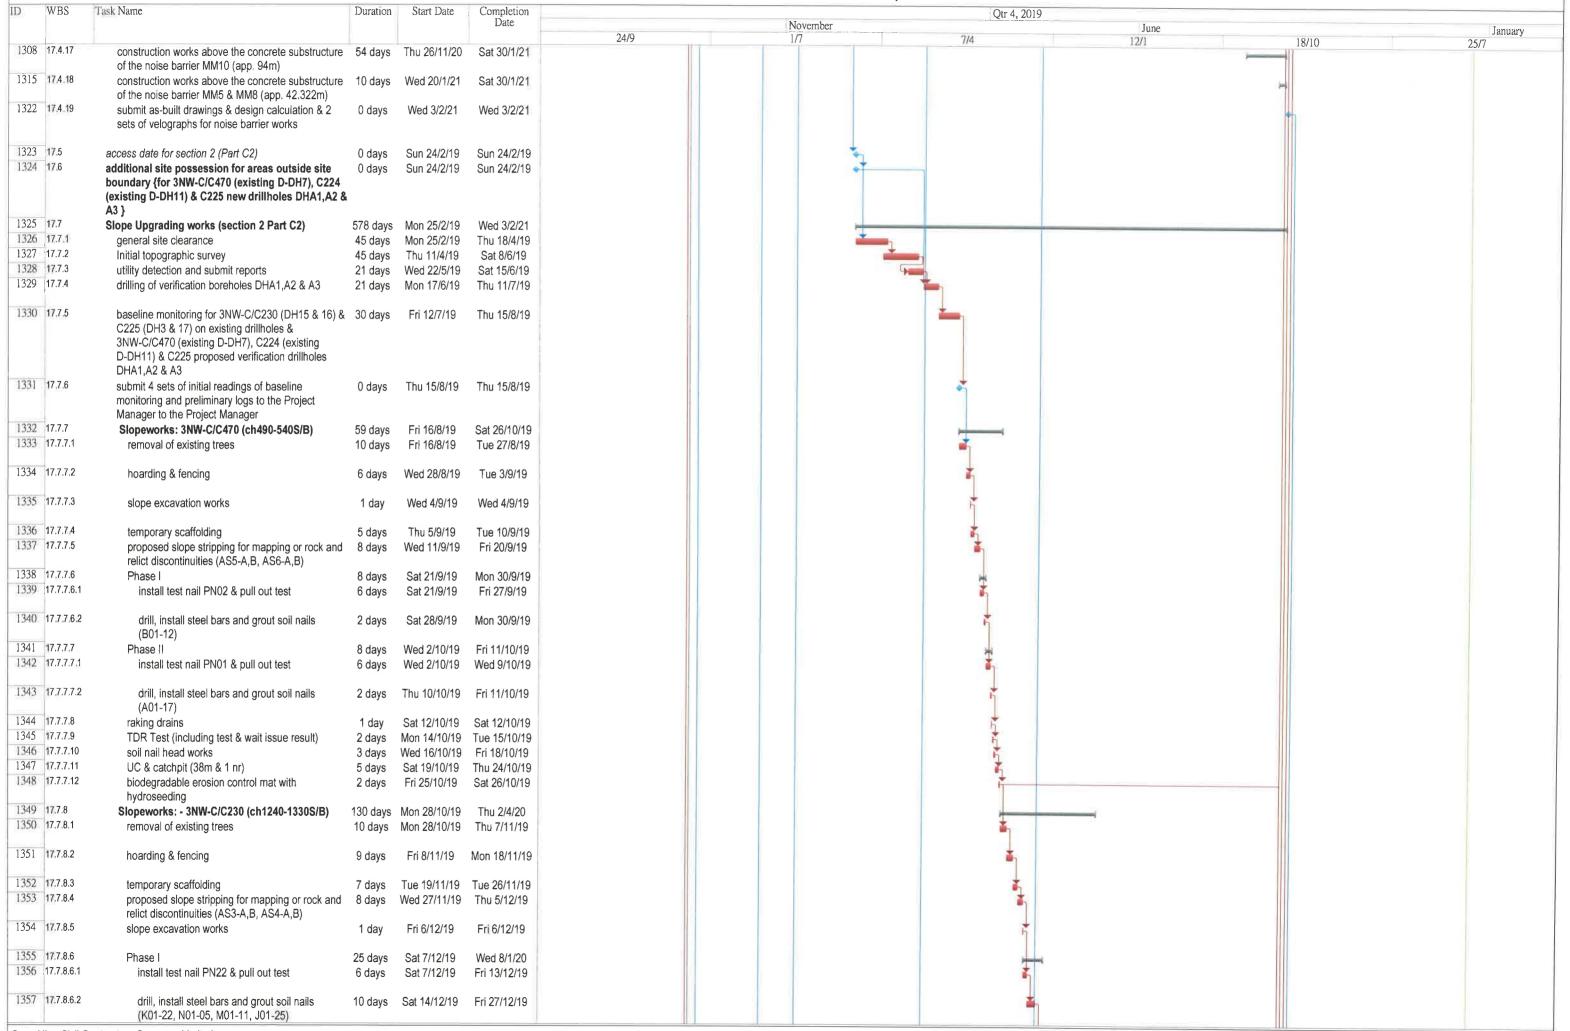

Contract No. CV/2017/02 Development of Columbarium at Sandy Ridge Cemetery - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road


3 Month Rolling Programme (from 26/11/2021 to 25/2/2022)

Accepted Initial Works Programme (06)

WBS	Task Name	Duration	Start Date	Completion					Qtr 4, 20	19		
				Date	24/9		November			June		Januar
358 17.7.8.6.3	TDR Test (including test & wait issue result)	2 days	Sat 28/12/19	Mon 30/12/19	24/9	11	1/7		7/4	12/1	18/10	25/7
359 17.7.8.6.4			Tue 31/12/19	Wed 8/1/20						*		
360 17.7.8.7	Phase II	22 days	Thu 9/1/20	Thu 6/2/20								
361 17.7.8.7.1	install test nail PN21 & pull out test	6 days	Thu 9/1/20	Wed 15/1/20						\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\		
17.7.8.7.2	·	8 days	Thu 16/1/20	Fri 24/1/20								
363 17.7.8.7.3		2 days	Wed 29/1/20	Thu 30/1/20						*		
364 17.7.8.7.4		2 days	Fri 31/1/20	Sat 1/2/20						1		
365 17.7.8.7.5		4 days	Mon 3/2/20	Thu 6/2/20						£		
366 17.7.8.8	225UC, 300SC & catchpits	21 days	Fri 7/2/20	Mon 2/3/20						<u> </u>		
367 17.7.8.9	600mm width concrete maintenance staircase	9 days	Tue 3/3/20	Thu 12/3/20								
	with handrailing											
368 17.7.8.10	soil replacement by no-fines concrete	6 days	Fri 13/3/20	Thu 19/3/20						b		
369 17.7.8.10.1	olago .	2 days	Fri 13/3/20	Sat 14/3/20						4		
70 17.7.8.10.1	tomporary but a bribaration of bon	1 day	Fri 13/3/20	Fri 13/3/20						h		
71 17.7.8.10.1		1 day	Sat 14/3/20	Sat 14/3/20						ή		
72 17.7.8.10.2	0.030 =	2 days	Mon 16/3/20	Tue 17/3/20						1		
73 17.7.8.10.2	, , , , , , , , , , , , , , , , , , , ,	1 day	Mon 16/3/20	Mon 16/3/20						ħ.		
17.4 17.7.8.10.2	F	1 day	Tue 17/3/20	Tue 17/3/20						h h		
75 17.7.8.10.3	3	2 days	Wed 18/3/20	Thu 19/3/20						14		
76 17.7.8.10.3		1 day	Wed 18/3/20	Wed 18/3/20						h h		
17.7.8.10.3	p	1 day	Thu 19/3/20	Thu 19/3/20						ř.		
378 17.7.8.11	biodegradable erosion control mat with hydroseeding & shrub planting	12 days	Fri 20/3/20	Thu 2/4/20						*		
79 17.7.9	Slopeworks: - 3NW-C/C224 (ch1040-1120N/B)		Tue 31/3/20	Sat 22/8/20		1						
04 17.7.10	Slopeworks: - 3NW-C/C225 (ch1300-1376N/B)		Tue 3/12/19	Wed 3/2/21					j —			
38 17.7.11	Slopeworks: - 3NW-C/C231 (ch1220-1240N/B)	-	Thu 12/9/19	Wed 3/2/21								
05 18	Planned Completion for section 2 of the works	0 days	Wed 3/2/21	Wed 3/2/21							***	,
506 19	Completion Date for section 2 of the works	0 days	Wed 3/2/21	Wed 3/2/21							+ + +	
507 20	section 3 of the works - Completion of all works within Parts D and E of the Site		Thu 31/5/18	Wed 3/2/21								
508 20.1	Parts D		Mon 26/11/18				-					
509 20.1.1	access date for section 3 (Parts D) - not more than 180 days after the starting date	0 days	Mon 26/11/18	Mon 26/11/18			*					
510 20.1.2	seek specialist for design, supply and installation of the covered walkway	59 days	Tue 27/11/18	Thu 24/1/19								
511 20.1.3	acceptance of specialist		Thu 14/2/19	Thu 14/2/19			*	4				
512 20,1,4	design for approval for lighting system for the	150 days	Fri 15/2/19	Sun 14/7/19					■ j			
513 20.1.5	covered walkway submit for approval for lighting system for the	0 days	Sun 14/7/19	Sun 14/7/19					<u>.</u>			
514 20.1.6	covered walkway acceptance of lighting system for the covered walkway	0 days	Sun 4/8/19	Sun 4/8/19					*			
515 20.1.7	Coordination with CLP to obtain the electricity supply for the street lighting system (Design for Road B, Road E, Road F(part), Lin Ma Hang Road and Sheung Shui Landmark PTI & Lighting system for	y 168 days	Mon 5/8/19	Sun 19/1/20								
516 20.1.8	the covered walkway) design for glazing system of the proposed covered walkway at Fanling Station Road	150 days	Fri 15/2/19	Sun 14/7/19			٢		_			
517 20.1.9	submission of glazing system	0 davs	Sun 14/7/19	Sun 14/7/19		H			<u>+</u>			
518 20.1.10	acceptance of glazing system and fall arrest system		Sun 4/8/19	Sun 4/8/19					*			
519 20.1.11	by Project Manager design for fall arrest system of the proposed covered walkway at Fanling Station Road	1 150 days	Fri 15/2/19	Sun 14/7/19			-		■ ∏			
520 20.1.12	submission of fall arrest system	0 days	Sun 14/7/19	Sun 14/7/19					*			
21 20,1.13	acceptance of fall arrest system by Project Manager		Sun 4/8/19	Sun 4/8/19					*			
22 20.1.14	Liaison with MTRC for the works arrangement	30 days		Tue 3/9/19					-			
523 20.1.15	general site clearance		Wed 4/9/19	Wed 18/9/19					*			
524 20.1.16	initial survey	12 days	Thu 19/9/19	Thu 3/10/19					*			
	utility detection and submit reports	8 days	Fri 4/10/19	Mon 14/10/19					*			
525 20.1.17 526 20.1.18 527 20.1.19	Fabrication of Steelworks & glass panel delivery steelworks & glass panel to site	100 days	Mon 5/8/19 Tue 3/12/19	Mon 2/12/19 Sat 18/1/20					*			

Sang Hing Civil Contractors Company Limited

3 month rolling programme 20211126(26 Nov 21-25 Feb 22)

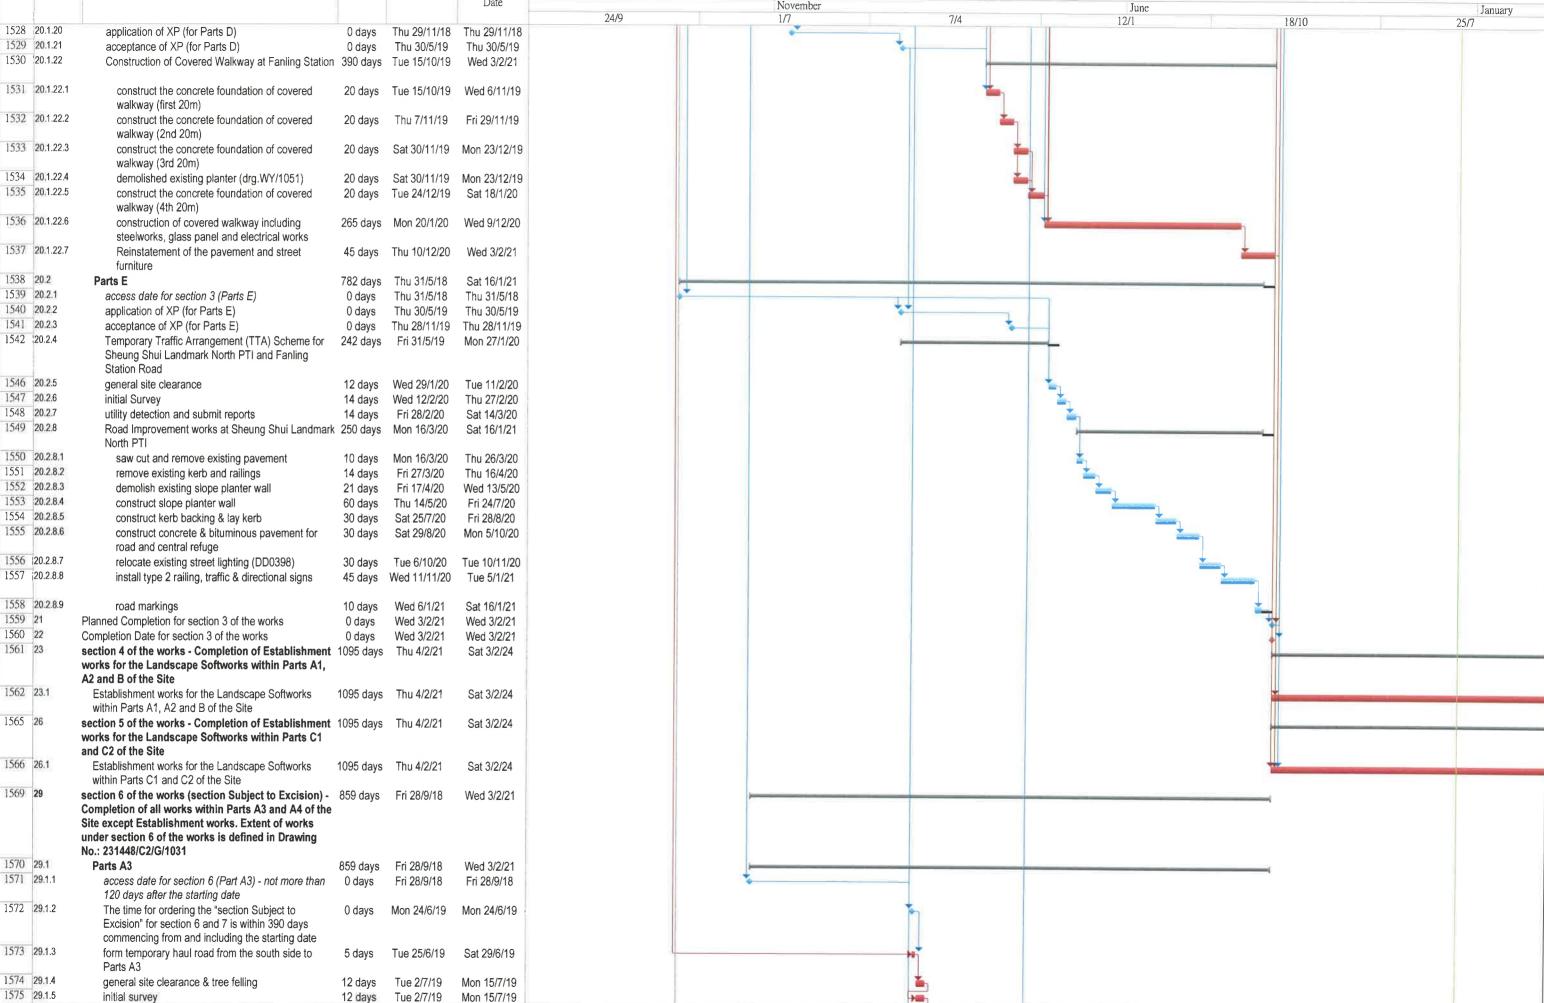

Page 7/9

Contract No. CV/2017/02 Development of Columbarium at Sandy Ridge Cemetery - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

3 Month Rolling Programme (from 26/11/2021 to 25/2/2022)

Accepted Initial Works Programme (06)

WBS	Task Name	Duration	Start Date	Completion			COLUMN	Qtr 4, 2019				
11.130	* 1000 / THING	Dat WOLL	our Date	Date			ember		June			January
76 0010		44.1	M. 45 P/40	T 00 7/10	24/9	1/7		7/4	12/1		18/10	25/7
76 29.1.6	construction of temporary drainage		Mon 15/7/19	Tue 30/7/19				-				
77 29.1.7	Construction of Retaining Wall RW14 (Bay 1-Bay			Sat 22/8/20						4		
02 29.1.8	backfilling works behind Retaining Wall RW14 (bay1	90 days	Sat 22/8/20	Tue 15/12/20					9			
	to 6) (include SRT tests)											
03 29.1.9	Construction of Retaining Wall RW14 Bay 7	27 days	Wed 30/9/20	Mon 9/11/20						Second 1		
13 29.1.10	backfilling works behind RW14 (bay 7) (include SRT											
	tests)	oo dayo	140 10/11/20	100 10/12/20								
14 29,1.11	install instrument for RW14	E dove	Fri 11/12/20	Mod 16/10/00								
										u ₁		
15 29.1.12	construct 300U channel & catchpit in front of RW14		Fri 11/12/20	Sat 19/12/20	,					1		
16 29.1.13	site formation works for fill slope FS19 and FS20	90 days	Sat 22/8/20	Tue 15/12/20	,	(Į.	- Carrier - Carr		
	(including in "backfilling works behind Retaining Wall				,	(
	RW14 (bay1 to 6)")				,	(
17 29.1.14	300U channel & stepped channel for FS19 & 20	3 days	Wed 16/12/20	Fri 18/12/20	,	(**		
18 29,1.15	install instrument for FS19 & FS20		Wed 16/12/20		,	(
19 29.1.16	minor site formation works for cut slope CS25		Wed 16/12/20		,					1		
19 23.1.10	minor site formation works for cut slope C525	i day	Wed 10/12/20	Wed 10/12/20	1					H		
20 004.47		0 1	T) 47/10/00	0	1							II.
20 29.1.17	minor site formation works for cut slope CS26	3 days	Thu 17/12/20	Sat 19/12/20	,	(· ·		
					1							1
21 29.1.18	install instruments for CS25 & CS26	5 days	Mon 21/12/20	Mon 28/12/20						*		
22 29.1.19	waterworks at Road E	12 days	Mon 21/12/20	Wed 6/1/21	,					-		1
	<u>-</u>	,-	, _, _ 3		,					and a		
23 29.1.20	drainage works at Road E	10 dave	Thu 31/12/20	Tue 12/1/21	,						•	
1	drainago works at Nodu L	io days	1114 01/12/20	146 12/1/21						-	1	
24 29.1.21	Li channola at Baset F	7 4	Tue 5/4/04	Tue 40/4/04							L	
	U channels at Road E	7 days	Tue 5/1/21	Tue 12/1/21								
25 29.1.22	Roadworks of Road E (ch20-60)		Wed 13/1/21	Wed 3/2/21	/					V		
26 29.1.22.1	kerbing & sub-base & cross road ducts for UU	11 days		Mon 25/1/21						7		
27 29.1.22.2	ducting for road lighting & construction of	4 days	Thu 21/1/21	Mon 25/1/21	9						*	
	irrigation system	,			/						1	
28 29.1.22.3	concrete pavement	10 days	Fri 22/1/21	Tue 2/2/21	/						+	
29 29.1.22.4	street lighting (Drg/RD/2091)	4 days	Sat 30/1/21	Wed 3/2/21	/	1						
30 29.1.22.5					1						•	
29.1.22.3	traffic signs, directional signs, emergency crash	10 days	Sat 23/1/21	Wed 3/2/21	/							
22	gate, type 2 railing & footpath							1				
31 29.1.23	Site Formation works for Cut Slope CS24 (include	4 days	Tue 17/9/19	Frì 20/9/19				F)				
	temporary cutting from top of RW12 to toe of CS24)											
	(for RW12 bays 1-3)											
32 29.1.24	install instrument for CS24	5 days	Mon 23/9/19	Fri 27/9/19				*				
33 29.1.25	temporary soil nails between CS20 & RW12 (for					(1				
	RW12 bays 1-3)	oo days	1011 20/0/10	141011 47 1 17 13		ĺ						
34 29.1.26	Construction of Retaining Wall RW12 CH 0-20	67 days	Tuo E/11/10	Fri 24/1/20		1						ľ
57 29.1.27			Tue 5/11/19			1						
29.1.27	backfilling along Retaining Wall RW12	40 days	Thu 4/6/20	Wed 22/7/20	,	1						

58 29.1.28	Completion of Site Formation works for Cut Slope 25	2 days	Tue 21/7/20	Wed 22/7/20					M			
					-							
59 29.1.29	Waterworks at Road F	24 days	Thu 23/7/20	Wed 19/8/20					*			
		,										
50 29.1.30	Drainage works at Road F	25 days	Thu 20/8/20	Thu 17/9/20					nit			
	Diamago Homo actional	Lo days	1114 20/0/20	1110 1770/20								
61 96 4 94	wheels well for Dood E and Dood E's Burn AC	40 4-	E=: 40/0/00	0-4-0/40/00		l						
61 29.1.31	planter wall for Road E and Road F in Parts A3		Fri 18/9/20	Sat 3/10/20						a		
52 29.1.32	UU-Arrange Town Gas & PCCW to lay across Road	14 days	Mon 5/10/20	Thu 22/10/20						*		
	F (not yet agree)											
53 29.1.33	Roadworks of Road F (60m)	55 days	Fri 23/10/20	Mon 4/1/21								
64 29.1.33.1	kerbing and cross road duct (RD/2061, 2081)		Fri 23/10/20	Fri 6/11/20						*		
	more and stood road date (10/2001)	. o dajo	20/10/20	, ,, 0, 1, 1, 20								
55 29.1.33.2	ducting for road lighting & construction of	12 days	Mon 9/11/20	Mon 23/11/20	1					-		
E. 011.00.2		12 uays	WOII 3/ I 1/20	WUII 23/ 1 1/20						1000		
66 004000	irrigation system	40.1	T 04444100									
66 29.1.33.3	bituminous pavement			Mon 7/12/20								
57 29.1.33.4	traffic signs, directional signs, type 2 railing &	21 days	Tue 8/12/20	Mon 4/1/21	1							
	footpath	-			1							
58 29.1.34	street lighting (Drg/ RD/2091)	6 days	Tue 5/1/21	Mon 11/1/21	1					*		
69 29.1.35	landscaping (hydroseeding)		Tue 12/1/21	Thu 21/1/21						1		
70 29.1.36				Wed 3/2/21	1						1	
71 29.2	landscaping (shrub planting)									1	•	
	Parts A4		Mon 24/6/19	Wed 3/2/21								
	access date for section 6 (Parts A4) - not more than	0 days	Tue 31/12/19	Tue 31/12/19								
2 29.2.1	580 days after the starting date	•					The second secon					

Contract No. CV/2017/02
Development of Columbarium at Sandy Ridge Cemetery
- Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

3 Month Rolling Programme (from 26/11/2021 to 25/2/2022)

Accepted Initial Works Programme (06)

	rai vvorks at Man Kam To Road and Lin Ma Hang Road	a			(11011)	20/11/2021 (0 25/2/2022)				
) WBS	Task Name	Duration	Start Date	Completion			Qtr 4, 2019			
				Date		November		June		January
					24/9	1/7	7/4	12/1	18/10	25/7
1673 29.2.2	The time for ordering the "section Subject to Excision" for section 6 and 7 is within 390 days commencing from and including the starting date	0 days	Mon 24/6/19	Mon 24/6/19			*			
1674 29.2.3	general site clearance	15 days	Thu 2/1/20	Sat 18/1/20	11		i i			
1675 29.2.4	initial survey	11 days	Sat 11/1/20	Thu 23/1/20				*		
1676 29.2.5	construction of temporary drainage	15 days	Thu 16/1/20	Wed 5/2/20				*	1	
1677 29.2.6	Site Formation works for Cut Slope CS24 (include temporary cutting from top of RW12 to toe of CS24) (for RW12 bays 4-6)	7 days	Wed 29/1/20	Wed 5/2/20						
1678 29.2.7	install instrument for CS24	3 days	Thu 6/2/20	Sat 8/2/20				*		
1679 29.2.8	temporary soil nails between CS20 & RW12 (for RW12 bays 4-6)	35 days		Tue 17/3/20				4		
680 29.2.9	Construction of Retaining Wall RW12 CH 21-40	58 days	Wed 18/3/20	Wed 3/6/20				-		
1703 29.2.10	Site Formation works for Cut Slope CS20		Mon 1/6/20	Tue 3/11/20						
1737 29.2.11	Site Formation works for Cut Slope CS26 (A4)	8 days	Tue 13/10/20							
738 29.2.12	Site Formation works for Cut Slope CS25 (A4)	9 days	Fri 23/10/20	Thu 5/11/20				*		
739 29.2.13	complete the construction of U channel at CS 25 and 26	15 days	Wed 4/11/20	Mon 23/11/20						
740 29.2.14	planter wall	10 days	Wed 18/11/20	Sat 28/11/20					<u></u>	
741 29.2.15	Waterworks at Road B	8 days	Tue 24/11/20						₽.	
1000000	Waterworks at result B	o dayo	140 2-11 11/20	***CG Z/12/20						
742 29.2.16	Sewerage works at Road B	7 days	Fri 27/11/20	Fri 4/12/20					↓	
	•	•								
743 29,2.17	Drainage works at Road B	7 days	Mon 30/11/20	Mon 7/12/20						
1744 29.2.18	UU - Arrange Town Gas & PCCW to lay cables (not	14 days	Tue 8/12/20	Wed 23/12/20					*	
745 00040	agreed yet)	00.1	141 1 00140/00	044404						
745 29.2.19	Roadworks of Road B (A4-ch90-130)		Wed 23/12/20						i	
746 29.2.19.		4 days	Wed 23/12/20	Tue 29/12/20					ř.	
747 29.2.19.2	2081)	A dava	T 00/40/00	0-4-0/4/04					1	
747 29.2.19.	3 3 3	4 days	Tue 29/12/20	Sat 2/1/21						
748 29.2.19.3	irrigation system	7 days	0-4-014-104	C=+ 0/4/04					1.	
749 29.2.19.4		7 days	Sat 2/1/21	Sat 9/1/21					<u> </u>	
149 23.2.13.	traffic signs, directional signs, type 2 railing & footpath	12 days	Fri 8/1/21	Thu 21/1/21					<u> </u>	
750 29.2.20	street lighting (Drg/ RD/2091)	4 days	Thu 21/1/21	Mon 25/1/21					1	
751 29.2.21	5 5 7		Mon 25/1/21	Mon 1/2/21					1	
752 29.2.22	landscaping (shrub planting)	7 days							-	
753 30		5 days	Fri 29/1/21	Wed 3/2/21					•]	
754 31	Planned Completion for section 6 of the works	0 days	Wed 3/2/21	Wed 3/2/21					•	
755 32	Completion Date for section 6 of the works	0 days	Wed 3/2/21	Wed 3/2/21					•	
133 3Z	section 7 of the works (section Subject to Excision) - Completion of Establishment works for the	TUBD days	Thu 4/2/21	Sat 3/2/24					}	
	Landscape Softworks within Parts A3 and A4 of the									
1756 32.1	Establishment works for the Landscape Softworks	1005 days	Thu 4/2/21	Sat 3/2/24						
A. A. HESSELL MARKET	within Parts A3 and A4 of the Site	1050 days	111u 4 /2/21	Oat 3/2/24						





Appendix D


Monitoring Locations



Air Quality Monitoring Location

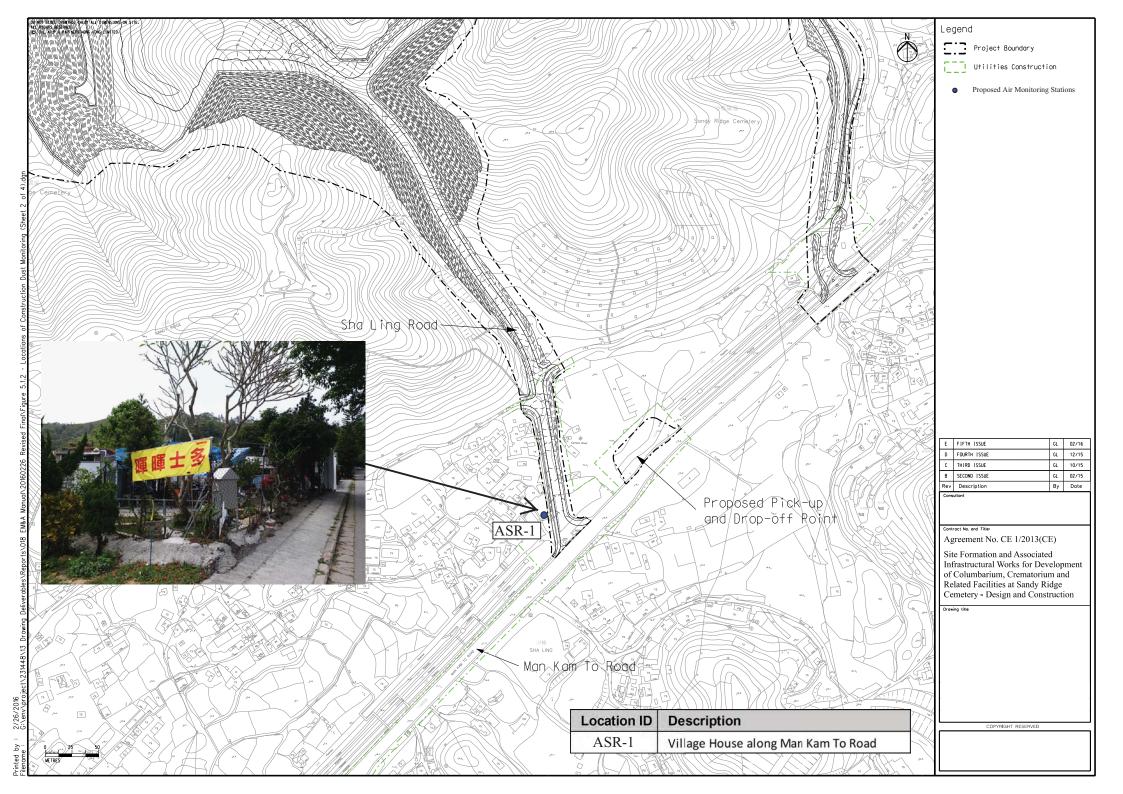

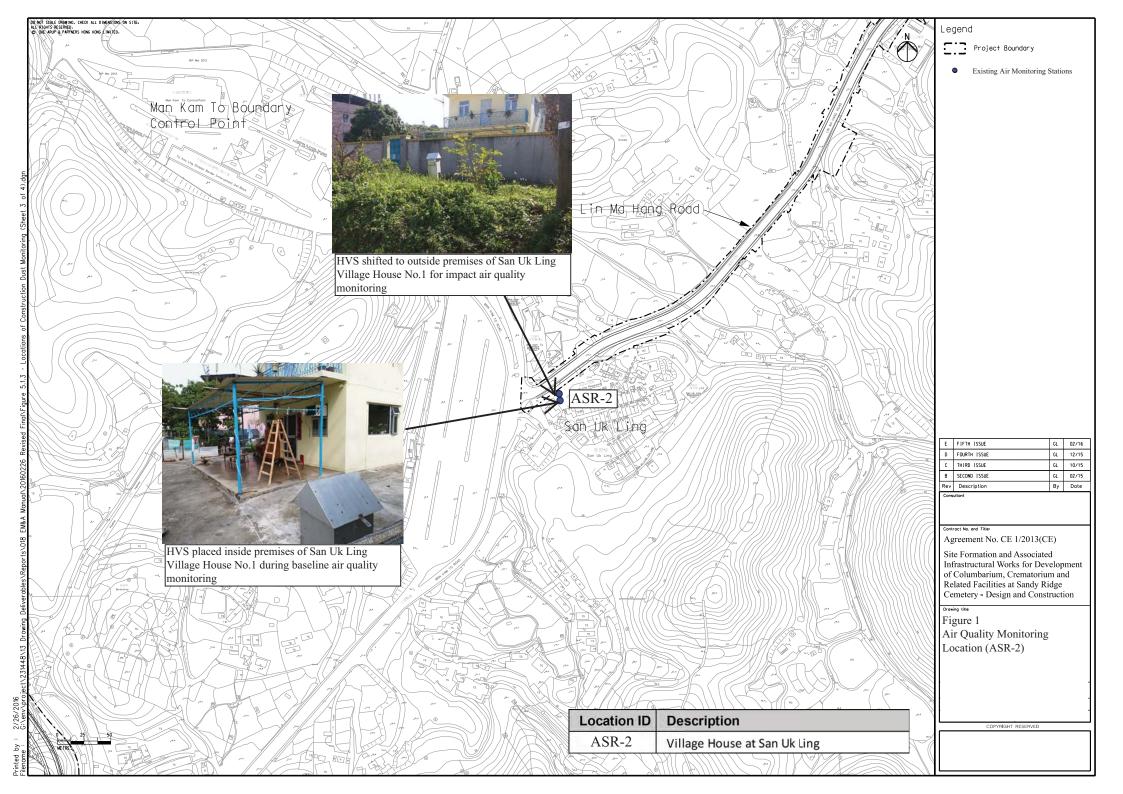

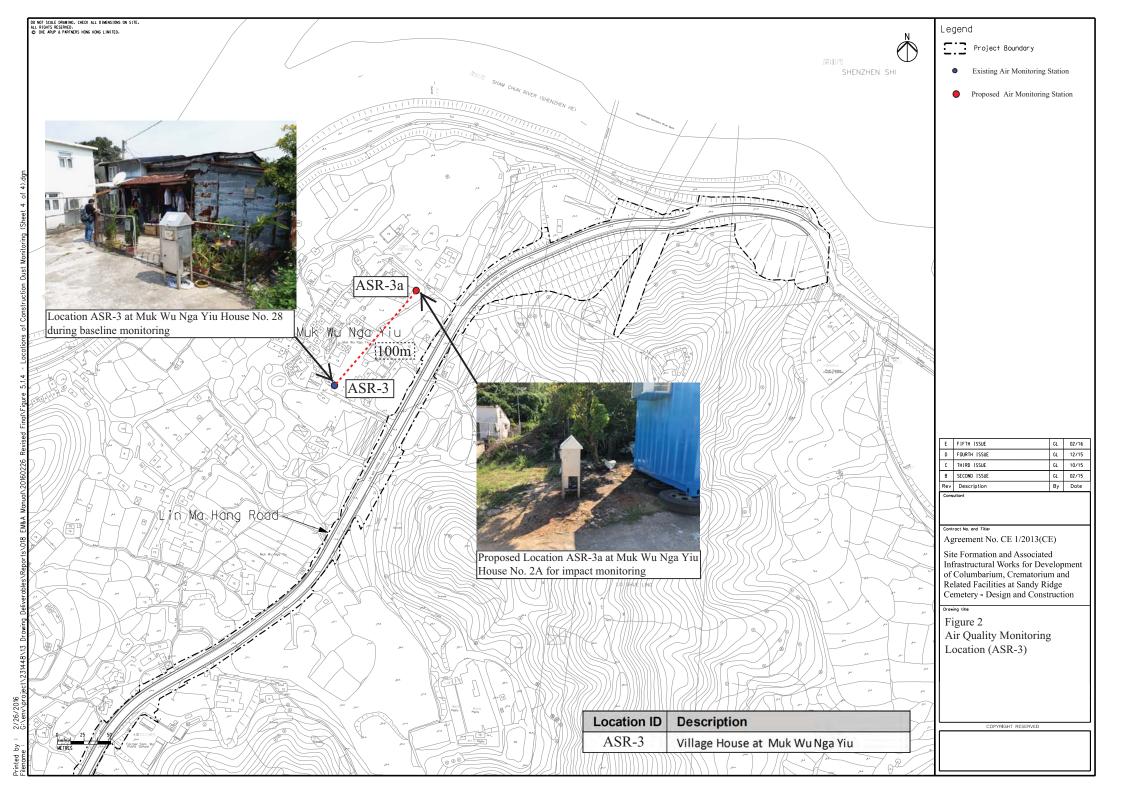




Noise Monitoring Location






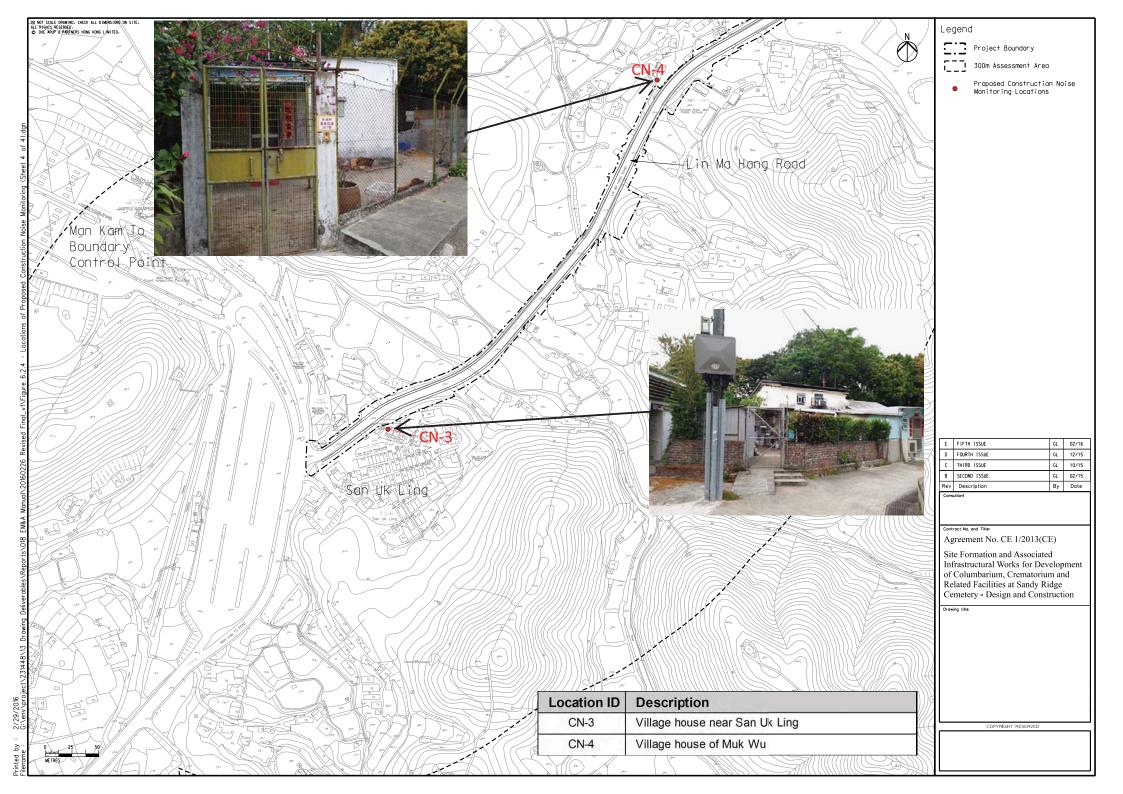



Water Quality Monitoring Station

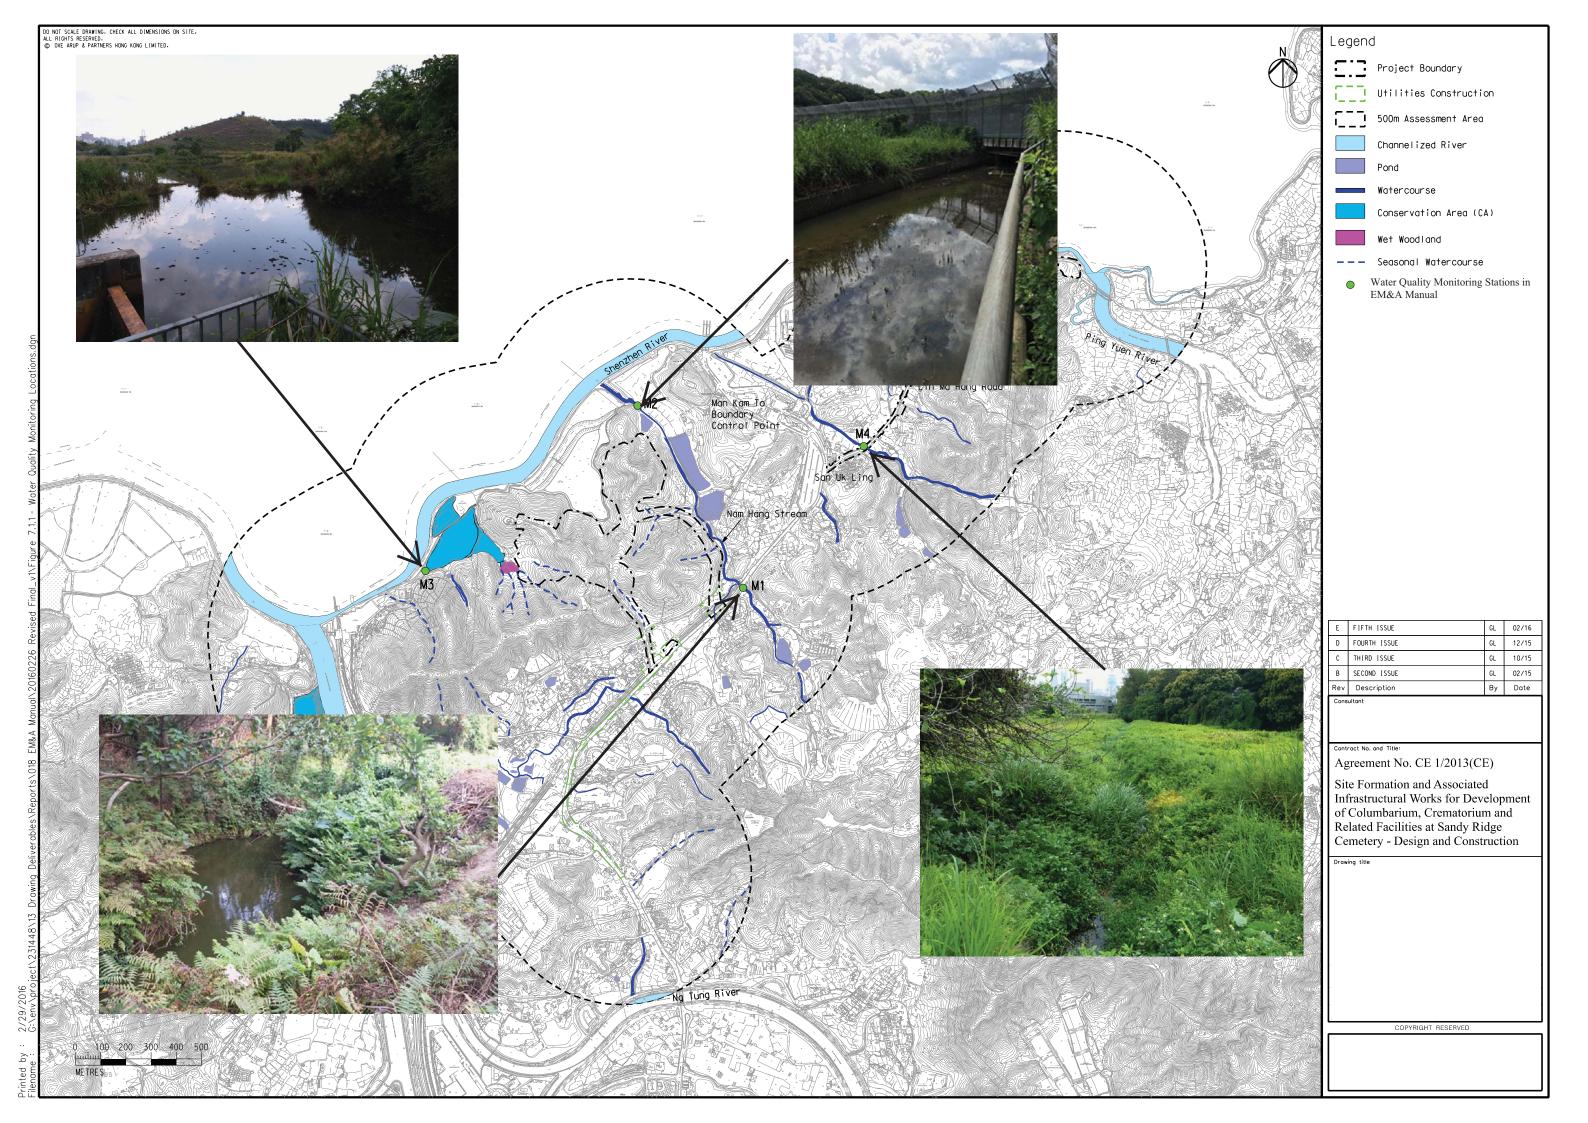



Appendix E

Calibration Certificate of Monitoring Equipment and Laboratory Certificate



CALIBRATION CERTIFICATES FOR MONITORING EQUIPMENT USED IN THE REPORTING MONTH

Items	Aspect	Description of Equipment	Date of Calibration	Date of Next Calibration
1		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-1	23 Oct 21	6 Nov 21
1a		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-1	10 Nov 21	24 Nov 21
1b		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-1	27 Nov 21	11 Dec 21
2		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-2	23 Oct 21	6 Nov 21
2a		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-2	10 Nov 21	24 Nov 21
2b		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-2	27 Nov 21	11 Dec 21
3		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-3a	23 Oct 21	6 Nov 21
3a	Air	TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-3a	10 Nov 21	24 Nov 21
3b		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-3a	27 Nov 21	11 Dec 21
4		Calibration Kit TISCH Model TE-5025A Orifice ID 1941 and Rootsmeter S/N 438320	19 Jan 21	19 Jan 22
5		Laser Dust Monitor, Model AM510 (Serial No. 11008017) – EQ102	8 Jan 21	8 Jan 22
6		Laser Dust Monitor, Model LD-3B (Serial No. 2X6145) – EQ105	8 Jan 21	8 Jan 22
7		Laser Dust Monitor, Model LD-3B (Serial No. 366410) – EQ110	8 Jan 21	8 Jan 22
8		Laser Dust Monitor, Model LD-3B (Serial No. 3Y6503) – EQ112	8 Jan 21	8 Jan 22
9		Rion NL- 52 Sound Level Meter (Serial No. 00410221) – EQ067	21 Jan 21	21 Jan 22
10	Noise	Rion NL- 52 Sound Level Meter (Serial No. 00921191) – EQ015	10 Sep 21	10 Sep 22
11		Rion NC - 75 Acoustical Calibrator (Serial No. 34680623) – EQ089	20 Jan 21	20 Jan 22
12	Water	YSI Professional DSS (Serial No.15H103928)	14 Sep 21	14 Dec 21
13	vv ater	Global Water FP211 Flow Meter (Serial No. 1449006330)	1 Sep 21	1 Sep 22

Location: Sha Ling Village House No.6

Location ID: ASR-1

Date of Calibration: 20-Sep-21 Next Calibration Date: 4-Oct-21

Name and Model: TISCH HVS Model TE-5170

Technician: Leung Ka Wai

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1010.4 29.3 Corrected Pressure (mm Hg)
Temperature (K)

757.8 302

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1941

Qstd Slope -> Qstd Intercept ->

2.10574 -0.00985

CALIBRATION

L								
	Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
l	No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
	18	6.60	6.60	13.2	1.715	54	53.15	Slope = 29.3698
	13	5.20	5.20	10.4	1.523	47	46.26	Intercept = 2.3250
	10	3.90	3.90	7.8	1.320	42	41.34	Corr. coeff. = 0.9990
	7	2.50	2.50	5.0	1.057	34	33.47	
	5	1.40	1.40	2.8	0.793	26	25.59	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart response

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tay = daily average temperature

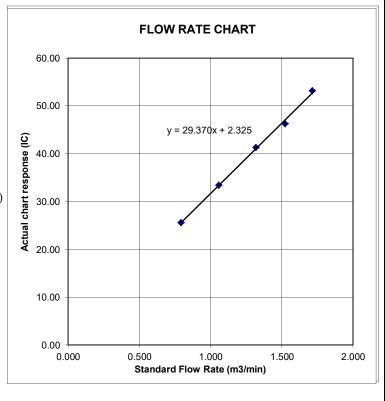

Location: San Uk Ling Village House No.1

Location ID : ASR-2

-2 Next Calibration Date: 4-Oct-21

Name and Model: TISCH HVS Model TE-5170

Technician: Leung Ka Wai

Date of Calibration: 20-Sep-21

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C)

1010.4
29.3

Corrected Pressure (mm Hg)
Temperature (K)

757.8 302

CALIBRATION ORIFICE

Make->	TISCH
Model->	5025A
Serial # ->	1941

Qstd Slope -> Qstd Intercept ->

2.10574 -0.00985

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.50	6.50	13.0	1.702	53	52.17	Slope = 31.1446
13	5.20	5.20	10.4	1.523	46	45.28	Intercept = -1.2959
10	4.00	4.00	8.0	1.336	41	40.36	Corr. coeff. = 0.9980
7	2.50	2.50	5.0	1.057	33	32.48	
5	1.60	1.60	3.2	0.847	25	24.61	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

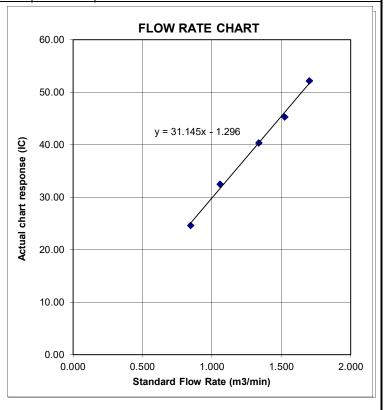

Location: Muk Wu Nga Yiu House No.2A

Location ID: ASR-3a

Next Calibration: 20-Sep-21

Name and Model: TISCH HVS Model TE-5170

Date of Calibration: 20-Sep-21

Next Calibration Date: 4-Oct-21

Technician: Leung Ka Wai

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1010.4 29.3

Corrected Pressure (mm Hg)
Temperature (K)

757.8 302

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1941

Qstd Slope -> Qstd Intercept -> 2.10574

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Ostd	Ţ	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
INO.	(111)	(111)	(111)	(1111/1/1111)	_ `	Corrected	
18	6.20	6.20	12.4	1.663	53	52.17	Slope = 35.0617
13	4.70	4.70	9.4	1.448	45	44.30	Intercept = -6.6359
10	4.00	4.00	8.0	1.336	40	39.37	Corr. coeff. = 0.9985
7	2.70	2.70	5.4	1.099	32	31.50	
5	1.60	1.60	3.2	0.847	24	23.62	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Ostd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)
Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:


1/m((I)[Sgrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

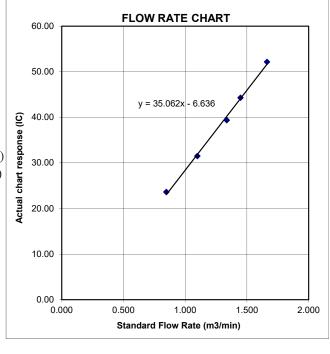

Location: Sha Ling Village House No.6

Location ID: ASR-1

Date of Calibration: 10-Nov-21 Next Calibration Date: 24-Nov-21

Name and Model: TISCH HVS Model TE-5170

Technician: Leung Ka Wai

CONDITIONS

Sea Level Pressure (hPa)
Temperature (°C)

1018.7 20.5

Corrected Pressure (mm Hg)
Temperature (K)

764.025 294

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1941

Qstd Slope -> Qstd Intercept ->

2.10574 -0.00985

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.10	6.10	12.2	1.680	53	53.95	Slope = 35.6406
13	4.80	4.80	9.6	1.491	47	47.85	Intercept = -6.2154
10	4.10	4.10	8.2	1.379	41	41.74	Corr. coeff. = 0.9968
7	2.40	2.40	4.8	1.056	30	30.54	
5	1.50	1.50	3.0	0.836	24	24.43	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tay = daily average temperature

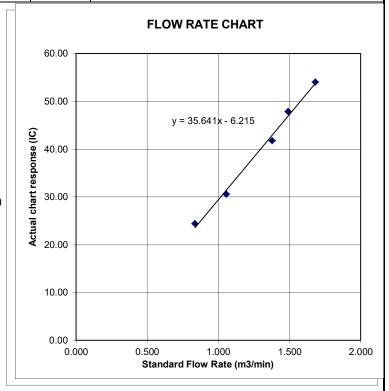

Location: San Uk Ling Village House No.1

Location ID: ASR-2

Name and Model: TISCH HVS Model TE-5170

Date of Calibration: 10-Nov-21 Next Calibration Date: 24-Nov-21

Technician: Leung Ka Wai

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1018.7 20.5

Corrected Pressure (mm Hg)
Temperature (K)

764.025 294

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1941

Qstd Slope -> Qstd Intercept -> 2.10574 -0.00985

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	Ι	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.50	6.50	13.0	1.735	53	53.95	Slope = 31.9331
13	5.30	5.30	10.6	1.567	47	47.85	Intercept = -2.1276
10	4.20	4.20	8.4	1.395	41	41.74	Corr. coeff. = 0.9982
7	2.50	2.50	5.0	1.078	31	31.56	
5	1.40	1.40	2.8	0.808	24	24.43	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

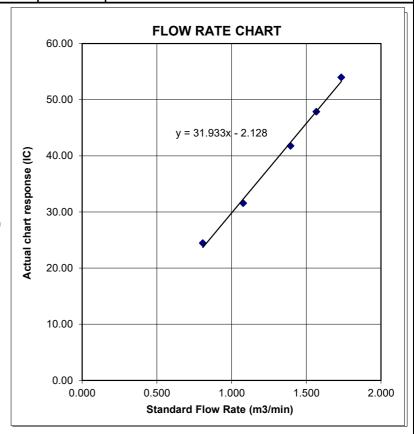

Location: Muk Wu Nga Yiu House No.2A

Date of Calibration: 10-Nov-21

Location ID: ASR-3a

Next Calibration Date: 24-Nov-21

Name and Model: TISCH HVS Model TE-5170

Technician: Leung Ka Wai

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1018.7 20.5

Corrected Pressure (mm Hg)
Temperature (K)

764.025 294

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1941

Qstd Slope -> Qstd Intercept -> 2.10574 -0.00985

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.10	6.10	12.2	1.680	53	53.95	Slope = 35.3918
13	5.10	5.10	10.2	1.537	46	46.83	Intercept = -6.8264
10	3.90	3.90	7.8	1.345	39	39.70	Corr. coeff. = 0.9963
7	2.70	2.70	5.4	1.120	32	32.58	
5	1.60	1.60	3.2	0.863	24	24.43	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Ostd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)
Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:


1/m((I)[Sgrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

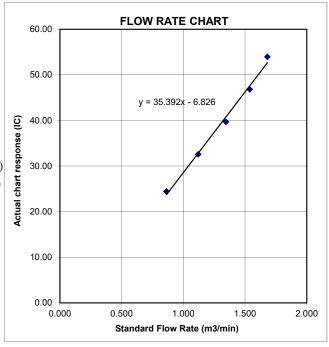

Location: Sha Ling Village House No.6

Location ID: ASR-1

Next Calibration Date: 11-Dec-21

Name and Model: TISCH HVS Model TE-5170

Technician: Leung Ka Wai

Date of Calibration: 27-Nov-21

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1020.1 21.2

Corrected Pressure (mm Hg)
Temperature (K)

765.075 294

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1941

Qstd Slope -> Qstd Intercept ->

2.10574 -0.00985

CALIBRATION

	Plate	H20 (L)H2O (R)		H20	Qstd	I	IC	LINEAR
	No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
	18	6.40	6.40	12.8	1.720	58	58.94	Slope = 28.9558
	13	5.00	5.00	10.0	1.521	52	52.85	Intercept = 8.2749
	10	4.00	4.00	8.0	1.361	46	46.75	Corr. coeff. = 0.9961
	7	2.60	2.60	5.2	1.098	38	38.62	
	5	1.50	0.00	1.5	0.592	26	26.42	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tay = daily average temperature

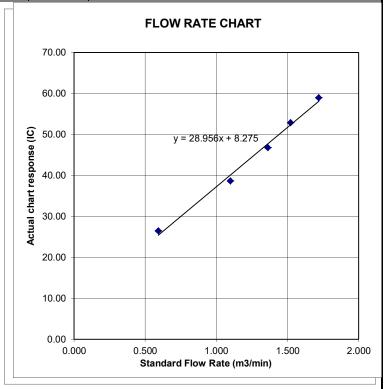

Location: San Uk Ling Village House No.1

Location ID: ASR-2

Date of Calibration: 27-Nov-21 Next Calibration Date: 11-Dec-21

Name and Model: TISCH HVS Model TE-5170

Technician: Leung Ka Wai

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C)

1020.1

Corrected Pressure (mm Hg) Temperature (K)

765.075

CALIBRATION ORIFICE

Make-> TISCH Model-> 5025A Serial # -> 1941

Qstd Slope -> Qstd Intercept -> 2.10574 -0.00985

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	Ι	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.30	6.30	12.6	1.707	53	53.86	Slope = 36.5615
13	4.90	4.90	9.8	1.506	47	47.77	Intercept = -8.2993
10	4.00	4.00	8.0	1.361	41	41.67	Corr. coeff. = 0.9941
7	2.70	2.70	5.4	1.119	30	30.49	
5	1.60	1.60	3.2	0.863	24	24.39	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tay = daily average temperature

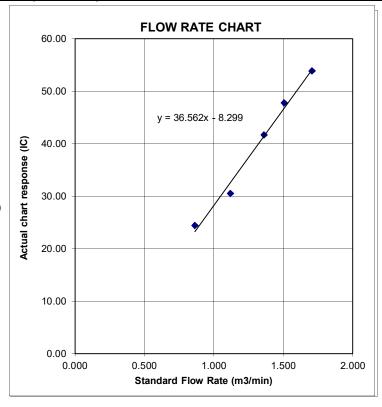

Location: Muk Wu Nga Yiu House No.2A

Location ID: ASR-3a

Next Calibration: 27-Nov-21

Name and Model: TISCH HVS Model TE-5170

Date of Calibration: 27-Nov-21

Next Calibration Date: 11-Dec-21

Technician: Leung Ka Wai

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1020.1 21.2

Corrected Pressure (mm Hg)
Temperature (K)

765.075 294

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1941

Qstd Slope -> Qstd Intercept -> 2.10574 -0.00985

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.40	6.40	12.8	1.720	58	58.94	Slope = 38.1748
13	5.10	5.10	10.2	1.536	51	51.83	Intercept = -6.3568
10	4.10	4.10	8.2	1.378	47	47.77	Corr. coeff. = 0.9976
7	2.80	2.80	5.6	1.139	36	36.59	
5	1.70	1.70	3.4	0.889	27	27.44	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Ostd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)
Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:


1/m((I)[Sgrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

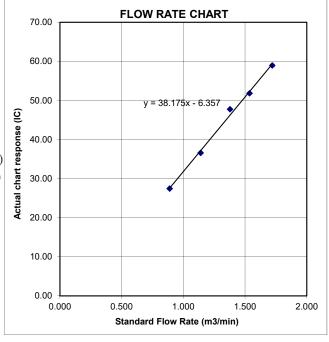



RECALIBRATION DUE DATE:

January 19, 2022

Certificate of Calibration

Calibration Certification Information

Cal. Date: January 19, 2021

Rootsmeter S/N: 438320

Ta: 294
Pa: 755.1

°K

Operator: Jim Tisch

Calibration Model #:

TE-5025A

Calibrator S/N: 1941

mm Hg

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4830	3.2	2.00
2	3	4	1	1.0420	6.4	4.00
3	5	6	1	0.9290	8.0	5.00
4	7	8	1	0.8840	8.8	5.50
5	9	10	1	0.7340	12.9	8.00

	Data Tabulation										
Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right) \left(\frac{Tstd}{Ta}\right)}$		Qa	$\sqrt{\Delta H (Ta/Pa)}$						
(m3)	(x-axis)	(y-axis)	Va	(x-axis)	(y-axis)						
1.0029	0.6762	1.4192	0.9958	0.6715	0.8824						
0.9986	0.9583	2.0071	0.9915	0.9516	1.2479						
0.9965	1.0726	2.2440	0.9894	1.0650	1.3952						
0.9954	1.1260	2.3535	0.9883	1.1180	1.4633						
0.9899	1.3487	2.8385	0.9829	1.3391	1.7648						
	m=	2.10574		m=	1.31858						
QSTD	b=	-0.00985	QA	b=	-0.00612						
-	r=	0.99992	,	r=	0.99992						

Calculations									
Vstd= ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	Va= ΔVol((Pa-ΔP)/Pa)								
Qstd= Vstd/∆Time	Qa= Va/ΔTime								
For subsequent flow ra	ate calculations:								
Qstd= $1/m \left(\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	$\mathbf{Qa} = 1/m \left(\left(\sqrt{\Delta H \left(Ta/Pa \right)} \right) - b \right)$								

Standard Conditions							
Tstd: 298.15 °K							
Pstd:	760 mm Hg						
	Key						
ΔH: calibrate	or manometer reading (in H2O)						
	ter manometer reading (mm Hg)						
	solute temperature (°K)						
Pa: actual barometric pressure (mm Hg)							
b: intercept							
m: slope							

RECALIBRATION

US EPA recommends annual recalibration per 1998
40 Code of Federal Regulations Part 50 to 51,
Appendix B to Part 50, Reference Method for the
Determination of Suspended Particulate Matter in
the Atmosphere, 9.2.17, page 30

FAX: (513)467-9009

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES



SUB-CONTRACTING REPORT

HK2102490 : MR BEN TAM WORK ORDER CONTACT

CLIENT : ACTION UNITED ENVIRONMENT

SERVICES AND CONSULTING

: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 **ADDRESS** SUB-BATCH

> DATE RECEIVED : 15-JAN-2021 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG DATE OF ISSUE : 26-JAN-2021

KONG

PROJECT NO. OF SAMPLES: 1

CLIENT ORDER

General Comments

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Calibration was subcontracted to and analysed by Action United Environmental Services & Consulting.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Sianatories Position

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

: HK2102490 WORK ORDER

SUB-BATCH

: 1 : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING CLIENT

PROJECT



ALS Lab Client's Sample ID		Sample	Sample Date	External Lab Report No.	
ID		Туре			
HK2102490-001	S/N: 2X6145	AIR	15-Jan-2021	S/N: 2X6145	

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor

Manufacturer: Sibata LD-3B

Serial No. 2X6145

Equipment Ref: EQ105

Job Order HK2102490

Standard Equipment:

Standard Equipment: Higher Volume Sampler

Location & Location ID: AUES office (calibration room)

Equipment Ref: HVS 018

Last Calibration Date: 8 October 2020

Equipment Verification Results:

Testing Date: 31 December 2020

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr01min	09:16 ~ 11:17	10.9	1027.0	0.058	3107	25.6
2hr01min	11:19 ~ 11:20	10.9	1027.0	0.027	1724	14.2
2hr01min	11:22 ~ 13:23	10.9	1027.0	0.026	1300	10.8

Sensitivity Adjustment Scale Setting (Before Calibration) 586
Sensitivity Adjustment Scale Setting (After Calibration) 586

Linear Regression of Y or X

Slope (K-factor): 0.0022

Correlation Coefficient 0.9926

Date of Issue 8 January 2021

Remarks:

1. **Strong** Correlation (R>0.8)

2. Factor 0.0022 should be apply for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment

0.07 0.06 0.05 0.04 0.03 0.02 y = 0.0022x - 0.0003 $R^2 = 0.9853$ 0.01 0 5 10 15 20 25 30

(CPM)

(CPM)

Operator : ______ Fai So____ Signature : ______ Date : ____ 8 January 2021

QC Reviewer : ______ Ben Tam ____ Signature : ________ Date : _____ 8 January 2021

Location: Gold King Industrial Building, Kwai Chung Date of Calibration: 8-Oct-20
Location ID: Calibration Room Next Calibration Date: 8-Jan-21

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1015.2 25.5

Corrected Pressure (mm Hg)
Temperature (K)

761.4 299

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Calibration Date-> 7-Feb-20

Qstd Slope -> Qstd Intercept -> Expiry Date-> 2.03014 -0.04616 7-Feb-21

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	Ι	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.4	6.4	12.8	1.785	56	56.00	Slope = 38.0056
13	5.1	5.1	10.2	1.596	49	49.00	Intercept = -11.6655
10	4	4	8.0	1.416	42	42.00	Corr. coeff. = 0.9991
8	2.5	2.5	5.0	1.124	32	32.00	
5	1.5	1.5	3.0	0.876	21	21.00	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart response

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

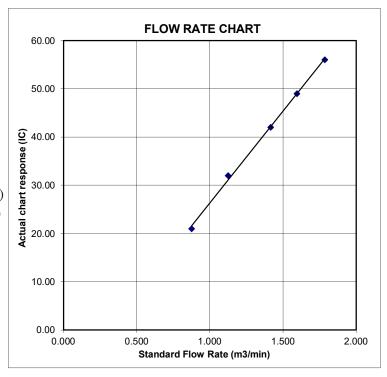



RECALIBRATION DUE DATE:

February 7, 2021

Certificate of Calibration

Calibration Certification Information

Cal. Date: February 7, 2020 Rootsmeter S/N: 438320

Ta: 295 °K

Operator: Jim Tisch **Pa:** 745.5 mm Hg

Calibration Model #: TE-5025A Calibrator S/N: 1612

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.3730	3.2	2.00
2	3	4	1	0.9820	6.4	4.00
3	5	6	1	0.8780	8.0	5.00
4	7	8	1	0.8340	8.8	5.50
5	9	10	1	0.6900	12.8	8.00

	Data Tabulation										
Vstd Qstd		$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right) \left(\frac{Tstd}{Ta}\right)}$		Qa	√∆H(Ta/Pa)						
(m3)	(x-axis)	(y-axis)	Va	(x-axis)	(y-axis)						
0.9866	0.7186	1.4078	0.9957	0.7252	0.8896						
0.9824	1.0004	1.9909	0.9914	1.0096	1.2581						
0.9802	1.1165	2.2259	0.9893	1.1267	1.4066						
0.9792	1.1741	2.3345	0.9882	1.1849	1.4753						
0.9739	1.4114	2.8155	0.9828	1.4244	1.7792						
	m=	2.03014		m=	1.27124						
QSTD	b=	-0.04616	QA	b=	-0.02917						
	r=	0.99995		r=	0.99995						

Calculations						
Vstd=	ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	Va=	ΔVol((Pa-ΔP)/Pa)			
Qstd=	Vstd/∆Time	Qa=	Va/ΔTime			
For subsequent flow rate calculations:						
Qstd=	$1/m\left(\left(\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}\right)-b\right)$	Qa=	$1/m\left(\left(\sqrt{\Delta H\left(Ta/Pa\right)}\right)-b\right)$			

Standard Conditions					
Tstd:	298.15 °K				
Pstd:	760 mm Hg				
Key					
ΔH: calibrator manometer reading (in H2O)					
ΔP: rootsmeter manometer reading (mm Hg)					
Ta: actual absolute temperature (°K)					
Pa: actual barometric pressure (mm Hg)					
b: intercept					
m: slone					

RECALIBRATION

US EPA recommends annual recalibration per 1998
40 Code of Federal Regulations Part 50 to 51,
Appendix B to Part 50, Reference Method for the
Determination of Suspended Particulate Matter in
the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc. 145 South Miami Avenue Village of Cleves, OH 45002 www.tisch-env.com

TOLL FREE: (877)263-7610 FAX: (513)467-9009

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES



SUB-CONTRACTING REPORT

HK2102509 : MR BEN TAM WORK ORDER CONTACT

CLIENT : ACTION UNITED ENVIRONMENT

SERVICES AND CONSULTING

: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 **ADDRESS** SUB-BATCH : 1

> DATE RECEIVED : 15-JAN-2021 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG DATE OF ISSUE : 26-JAN-2021

KONG

PROJECT NO. OF SAMPLES: 1

CLIENT ORDER

General Comments

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Calibration was subcontracted to and analysed by Action United Environmental Services & Consulting.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Sianatories Position

Richard Fung Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

: HK2102509 WORK ORDER

SUB-BATCH

: 1 : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING CLIENT

PROJECT



ALS Lab	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2102509-001	S/N: 11008017	AIR	18-Jan-2021	S/N: 11008017

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor

Manufacturer: TSI AM510

Serial No. 11008017

Equipment Ref: EQ102

Work Order: HK2102509

Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)

Location & Location ID: AUES Office (Calibration Room)

Equipment Ref: HVS 018

Last Calibration Date: 8 October 2020

Equipment Verification Results:

Verification Date: 31 December 2020

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m³ (Standard Equipment)	Concentration in mg/m³ (Calibrated Equipment)	Tolerance (mg/m³)
2hr01min	09:16 ~ 11:17	10.9	1027.0	0.058	0.097	+0.039
2hr01min	11:19 ~ 11:20	10.9	1027.0	0.027	0.058	+0.031
2hr01min	11:22 ~ 13:23	10.9	1027.0	0.026	0.053	+0.027

Linear Regression of Y or X

Slope (factor): 0.5842


Correlation Coefficient (R) 0.9876

Date of Issue 8 January 2021

Remarks:

- 1. **Strong** Correlation (R>0.8)
- 2. Factor 0.5842 should be apply for TSP monitoring

^{*}If R<0.5, repair or re-verification is required for the equipment



Operator : _____ Fai So ___ Signature : _____/ Date : ____ 8 January 2021

QC Reviewer: Ben Tam Signature: Date: 8 January 2021

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location: Gold King Industrial Building, Kwai Chung Date of Calibration: 8-Oct-20
Location ID: Calibration Room Next Calibration Date: 8-Jan-21

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1015.2 25.5 Corrected Pressure (mm Hg)
Temperature (K)

761.4 299

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Calibration Date-> 7-Feb-20

Qstd Slope -> Qstd Intercept -> Expiry Date-> 2.03014 -0.04616 7-Feb-21

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.4	6.4	12.8	1.785	56	56.00	Slope = 38.0056
13	5.1	5.1	10.2	1.596	49	49.00	Intercept = -11.6655
10	4	4	8.0	1.416	42	42.00	Corr. coeff. = 0.9991
8	2.5	2.5	5.0	1.124	32	32.00	
5	1.5	1.5	3.0	0.876	21	21.00	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart response

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

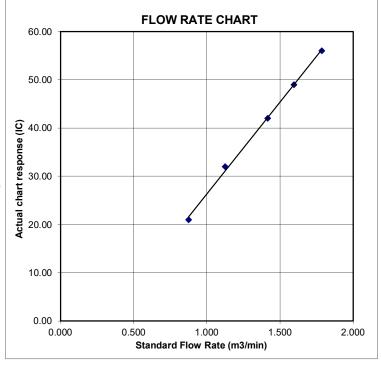



RECALIBRATION DUE DATE:

February 7, 2021

Certificate of Calibration

Calibration Certification Information

Cal. Date: February 7, 2020 Rootsmeter S/N: 438320

Ta: 295 °K

Operator: Jim Tisch **Pa:** 745.5 mm Hg

Calibration Model #: TE-5025A Calibrator S/N: 1612

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.3730	3.2	2.00
2	3	4	1	0.9820	6.4	4.00
3	5	6	1	0.8780	8.0	5.00
4	7	8	1	0.8340	8.8	5.50
5	9	10	1	0.6900	12.8	8.00

	Data Tabulation						
Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right) \left(\frac{Tstd}{Ta}\right)}$		Qa	√∆H(Ta/Pa)		
(m3)	(x-axis)	(y-axis)	Va	(x-axis)	(y-axis)		
0.9866	0.7186	1.4078	0.9957	0.7252	0.8896		
0.9824	1.0004	1.9909	0.9914	1.0096	1.2581		
0.9802	1.1165	2.2259	0.9893	1.1267	1.4066		
0.9792	1.1741	2.3345	0.9882	1.1849	1.4753		
0.9739	1.4114	2.8155	0.9828	1.4244	1.7792		
	m=	2.03014		m=	1.27124		
QSTD	b=	-0.04616	QA	b=	-0.02917		
	r=	0.99995		r=	0.99995		

	Calculations					
Vstd=	ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	Va=	ΔVol((Pa-ΔP)/Pa)			
Qstd=	Vstd/∆Time	Qa=	Va/ΔTime			
	For subsequent flow rate calculations:					
Qstd=	$1/m\left(\left(\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}\right)-b\right)$	Qa=	$1/m\left(\left(\sqrt{\Delta H\left(Ta/Pa\right)}\right)-b\right)$			

Standard Conditions					
Tstd: 298.15 °K					
Pstd:	Pstd: 760 mm Hg				
	Key				
ΔH: calibrator manometer reading (in H2O)					
ΔP: rootsmeter manometer reading (mm Hg)					
Ta: actual absolute temperature (°K)					
Pa: actual barometric pressure (mm Hg)					
b: intercept					
m: slone					

RECALIBRATION

US EPA recommends annual recalibration per 1998
40 Code of Federal Regulations Part 50 to 51,
Appendix B to Part 50, Reference Method for the
Determination of Suspended Particulate Matter in
the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc. 145 South Miami Avenue Village of Cleves, OH 45002 www.tisch-env.com

TOLL FREE: (877)263-7610 FAX: (513)467-9009

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES



SUB-CONTRACTING REPORT

CONTACT : MR BEN TAM WORK ORDER : HK2102511

CLIENT : ACTION UNITED ENVIRONMENT

SERVICES AND CONSULTING

ADDRESS : RM A 20/F., GOLD KING IND BLDG, NO. 35-41 SUB-BATCH :

TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG

DATE RECEIVED : 15-JAN-2021

DATE OF ISSUE : 26-JAN-2021

KONG

PROJECT : NO. OF SAMPLES : 1

CLIENT ORDER :---

General Comments

 Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Calibration was subcontracted to and analysed by Action United Environmental Services & Consulting.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories Position

_...

Richard Fung Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

: HK2102511 WORK ORDER

SUB-BATCH

: 1 : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING CLIENT

PROJECT



ALS Lab	Client's Sample ID	Sample	Sample Date	External Lab Report No.
ID		Туре		
HK2102511-001	S/N: 3Y6503	AIR	15-Jan-2021	S/N: 3Y6503

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor

Manufacturer: Sibata LD-3B

Serial No. 3Y6503

Equipment Ref: EQ112

Job Order HK2102511

Standard Equipment:

Standard Equipment: Higher Volume Sampler

Location & Location ID: AUES office (calibration room)

Equipment Ref: HVS 018

Last Calibration Date: 8 October 2020

Equipment Verification Results:

Testing Date: 31 December 2020

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr01min	09:16 ~ 11:17	10.9	1027.0	0.058	3127	25.8
2hr01min	11:19 ~ 11:20	10.9	1027.0	0.027	1347	11.1
2hr01min	11:22 ~ 13:23	10.9	1027.0	0.026	1298	10.8

(CPM)

(CPM)

15

y = 0.0022x + 0.0013

25

20

0.07

0.06

0.05

0.04

0.02

Sensitivity Adjustment Scale Setting (Before Calibration) 655

Sensitivity Adjustment Scale Setting (After Calibration) 655

Linear Regression of Y or X

Slope (K-factor): 0.0022

Correlation Coefficient 0.9985

Date of Issue 8 January 2021

Remarks:

1. **Strong** Correlation (R>0.8)

2. Factor 0.0022 should be apply for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment

Operator : Fai So Signature : Date : 8 January 2021

QC Reviewer : Ben Tam Signature : Date : 8 January 2021

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location: Gold King Industrial Building, Kwai Chung Date of Calibration: 8-Oct-20
Location ID: Calibration Room Next Calibration Date: 8-Jan-21

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1015.2 25.5 Corrected Pressure (mm Hg)
Temperature (K)

761.4 299

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Calibration Date-> 7-Feb-20

Qstd Slope -> Qstd Intercept -> Expiry Date-> 2.03014 -0.04616 7-Feb-21

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.4	6.4	12.8	1.785	56	56.00	Slope = 38.0056
13	5.1	5.1	10.2	1.596	49	49.00	Intercept = -11.6655
10	4	4	8.0	1.416	42	42.00	Corr. coeff. = 0.9991
8	2.5	2.5	5.0	1.124	32	32.00	
5	1.5	1.5	3.0	0.876	21	21.00	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart response

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

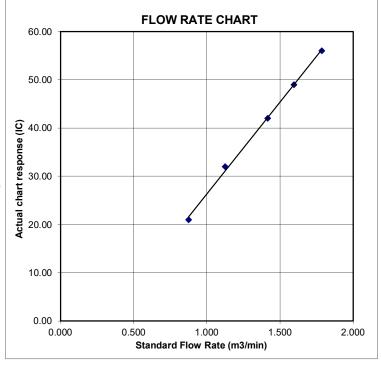



RECALIBRATION DUE DATE:

February 7, 2021

Certificate of Calibration

Calibration Certification Information

Cal. Date: February 7, 2020 Rootsmeter S/N: 438320

Ta: 295 °K

Operator: Jim Tisch **Pa:** 745.5 mm Hg

Calibration Model #: TE-5025A Calibrator S/N: 1612

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.3730	3.2	2.00
2	3	4	1	0.9820	6.4	4.00
3	5	6	1	0.8780	8.0	5.00
4	7	8	1	0.8340	8.8	5.50
5	9	10	1	0.6900	12.8	8.00

	Data Tabulation						
Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right) \left(\frac{Tstd}{Ta}\right)}$		Qa	√∆H(Ta/Pa)		
(m3)	(x-axis)	(y-axis)	Va	(x-axis)	(y-axis)		
0.9866	0.7186	1.4078	0.9957	0.7252	0.8896		
0.9824	1.0004	1.9909	0.9914	1.0096	1.2581		
0.9802	1.1165	2.2259	0.9893	1.1267	1.4066		
0.9792	1.1741	2.3345	0.9882	1.1849	1.4753		
0.9739	1.4114	2.8155	0.9828	1.4244	1.7792		
	m=	2.03014		m=	1.27124		
QSTD	b=	-0.04616	QA	b=	-0.02917		
	r=	0.99995		r=	0.99995		

	Calculations					
Vstd=	ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	Va=	ΔVol((Pa-ΔP)/Pa)			
Qstd=	Vstd/∆Time	Qa=	Va/ΔTime			
	For subsequent flow rate calculations:					
Qstd=	$1/m\left(\left(\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}\right)-b\right)$	Qa=	$1/m\left(\left(\sqrt{\Delta H\left(Ta/Pa\right)}\right)-b\right)$			

Standard Conditions					
Tstd: 298.15 °K					
Pstd:	Pstd: 760 mm Hg				
	Key				
ΔH: calibrator manometer reading (in H2O)					
ΔP: rootsmeter manometer reading (mm Hg)					
Ta: actual absolute temperature (°K)					
Pa: actual barometric pressure (mm Hg)					
b: intercept					
m: slone					

RECALIBRATION

US EPA recommends annual recalibration per 1998
40 Code of Federal Regulations Part 50 to 51,
Appendix B to Part 50, Reference Method for the
Determination of Suspended Particulate Matter in
the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc. 145 South Miami Avenue Village of Cleves, OH 45002 www.tisch-env.com

TOLL FREE: (877)263-7610 FAX: (513)467-9009

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES



SUB-CONTRACTING REPORT

CONTACT : MR BEN TAM WORK ORDER : HK2102507

CLIENT : ACTION UNITED ENVIRONMENT

SERVICES AND CONSULTING

ADDRESS : RM A 20/F., GOLD KING IND BLDG, NO. 35-41 SUB-BATCH : 1

TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG

DATE RECEIVED : 15-JAN-2021

DATE OF ISSUE : 26-JAN-2021

KONG

PROJECT : NO. OF SAMPLES : 1

CLIENT ORDER :---

General Comments

 Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

• Calibration was subcontracted to and analysed by Action United Environmental Services & Consulting.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories Position

Richard Fung Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

: HK2102507 WORK ORDER

SUB-BATCH

: 1 : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING CLIENT

PROJECT



ALS Lab	S Lab Client's Sample ID		Sample Date	External Lab Report No.
ID		Туре		
HK2102507-001	S/N: 366410	AIR	15-Jan-2021	S/N: 366410

Equipment Verification Report (TSP)

Equipment Calibrated:

Laser Dust monitor Type:

Manufacturer: Sibata LD-3B

366410 Serial No.

Equipment Ref: EQ110

Job Order HK2102507

Standard Equipment:

Standard Equipment: Higher Volume Sampler

Location & Location ID: AUES office (calibration room)

Equipment Ref: HVS 018

Last Calibration Date: 8 October 2020

Equipment Verification Results:

Testing Date: 31 December 2020

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr01min	09:16 ~ 11:17	10.9	1027.0	0.058	3158	26.1
2hr01min	11:19 ~ 11:20	10.9	1027.0	0.027	1608	13.3
2hr01min	11:22 ~ 13:23	10.9	1027.0	0.026	1107	9.2

Sensitivity Adjustment Scale Setting (Before Calibration) 674 (CPM) Sensitivity Adjustment Scale Setting (After Calibration) 674 (CPM)

Linear Regression of Y or X

Slope (K-factor): 0.0022 **Correlation Coefficient** 0.9895

Date of Issue 8 January 2021

Remarks:

- 1. Strong Correlation (R>0.8)
- 2. Factor 0.0022 should be apply for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment

0.07						
0.06					*	
0.05						
0.04				/		
0.03		• /	/			
0.02		——			22x + 0.00 = 0.9791	016
0.01	$-\!\!/$					
0		-		-	-	
0	5	10	15	20	25	30

Date : 8 January 2021

Date : 8 January 2021 Operator : _____Fai So Signature:

Ben Tam

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location: Gold King Industrial Building, Kwai Chung Date of Calibration: 8-Oct-20
Location ID: Calibration Room Next Calibration Date: 8-Jan-21

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1015.2 25.5 Corrected Pressure (mm Hg)
Temperature (K)

761.4 299

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Calibration Date-> 7-Feb-20

Qstd Slope -> Qstd Intercept -> Expiry Date-> 2.03014 -0.04616 7-Feb-21

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.4	6.4	12.8	1.785	56	56.00	Slope = 38.0056
13	5.1	5.1	10.2	1.596	49	49.00	Intercept = -11.6655
10	4	4	8.0	1.416	42	42.00	Corr. coeff. = 0.9991
8	2.5	2.5	5.0	1.124	32	32.00	
5	1.5	1.5	3.0	0.876	21	21.00	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart response

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

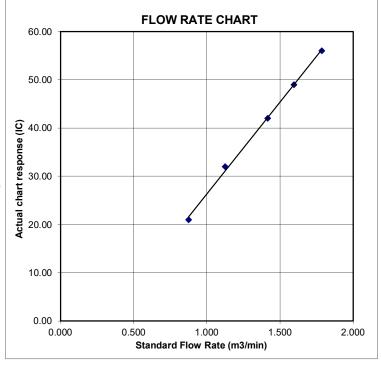



RECALIBRATION DUE DATE:

February 7, 2021

Certificate of Calibration

Calibration Certification Information

Cal. Date: February 7, 2020 Rootsmeter S/N: 438320

Ta: 295 °K

Operator: Jim Tisch **Pa:** 745.5 mm Hg

Calibration Model #: TE-5025A Calibrator S/N: 1612

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.3730	3.2	2.00
2	3	4	1	0.9820	6.4	4.00
3	5	6	1	0.8780	8.0	5.00
4	7	8	1	0.8340	8.8	5.50
5	9	10	1	0.6900	12.8	8.00

	Data Tabulation								
Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right) \left(\frac{Tstd}{Ta}\right)}$		Qa	√∆H(Ta/Pa)				
(m3)	(x-axis)	(y-axis)	Va	(x-axis)	(y-axis)				
0.9866	0.7186	1.4078	0.9957	0.7252	0.8896				
0.9824	1.0004	1.9909	0.9914	1.0096	1.2581				
0.9802	1.1165	2.2259	0.9893	1.1267	1.4066				
0.9792	1.1741	2.3345	0.9882	1.1849	1.4753				
0.9739	1.4114	2.8155	0.9828	1.4244	1.7792				
	m=	2.03014		m=	1.27124				
QSTD	b=	-0.04616	QA	b=	-0.02917				
	r=	0.99995		r=	0.99995				

Calculations						
$Vstd = \Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta) $ $Va = \Delta Vol((Pa-\Delta P)/Pa)$						
Qstd=	Vstd/∆Time	Qa= Va/ΔTime				
For subsequent flow rate calculations:						
Qstd=	$1/m\left(\left(\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}\right)-b\right)$	Qa=	$1/m\left(\left(\sqrt{\Delta H\left(Ta/Pa\right)}\right)-b\right)$			


Standard Conditions						
Tstd:	298.15 °K					
Pstd:	760 mm Hg					
	Key					
ΔH: calibrator manometer reading (in H2O)						
ΔP: rootsme	ter manometer reading (mm Hg)					
Ta: actual ab	solute temperature (°K)					
Pa: actual barometric pressure (mm Hg)						
b: intercept						
m: slope						

RECALIBRATION

US EPA recommends annual recalibration per 1998
40 Code of Federal Regulations Part 50 to 51,
Appendix B to Part 50, Reference Method for the
Determination of Suspended Particulate Matter in
the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc. 145 South Miami Avenue Village of Cleves, OH 45002 www.tisch-env.com

TOLL FREE: (877)263-7610 FAX: (513)467-9009



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C210403

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC20-1324)

Date of Receipt / 收件日期: 19 January 2021

Description / 儀器名稱

Sound Level Meter (EQ067)

Manufacturer / 製造商

Rion NL-31

Model No. / 型號 Serial No. / 編號

00410221

Supplied By / 委託者

Action-United Environmental Services and Consulting

Unit A, 20/F., Gold King Industrial Building, 35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 温度 :

Relative Humidity / 相對濕度 : $(50 \pm 25)\%$

Line Voltage / 電壓

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

21 January 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By 測試

K P Cheuk

Assistant Engineer

Certified By 核證

K C Lee Engineer Date of Issue 簽發日期

21 January 2021

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laborator

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所 c/o 香港新界屯門興安里一號四樓



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C210403

證書編號

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm 1. up for over 10 minutes before the commencement of the test.

2. Self-calibration was performed before the test.

The results presented are the mean of 3 measurements at each calibration point. 3.

4. Test equipment:

Equipment ID CL280

CL281

Description

40 MHz Arbitrary Waveform Generator Multifunction Acoustic Calibrator

Certificate No. C210084

CDK1806821

Test procedure: MA101N. 5.

6. Results:

Sound Pressure Level 6.1

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied	Value	UUT	IEC 61672 Class 1
Range	Mode	Frequency	Time	Level	Freq.	Reading	Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 120	L _A	A	Fast	94.00	1	94.0	± 1.1

6.1.2 Linearity

•	UUT Setting				Value	UUT
Range	Mode	Frequency	Time	Level	Freq.	Reading
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)
30 - 120	L_A	A	Fast	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		114.0

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting			Applied	Value	UUT	IEC 61672 Class 1	
Range	Mode	Frequency	Time	Level	Freq.	Reading	Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 120	L_{A}	A	Fast	94.00	1	94.0	Ref.
			Slow			93.9	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所 c/o 香港新界屯門興安里一號四樓



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C210403

證書編號

Frequency Weighting

6.3.1 A-Weighting

11- Weighting	5						
	UUT Setting			Appl	ied Value	UUT	IEC 61672 Class 1
Range	Mode	Frequency	Time	Level	Freq.	Reading	Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
30 - 120	L_{A}	A	Fast	94.00	63 Hz	67.7	-26.2 ± 1.5
					125 Hz	77.8	-16.1 ± 1.5
					250 Hz	85.3	-8.6 ± 1.4
					500 Hz	90.7	-3.2 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	95.2	$+1.2 \pm 1.6$
					4 kHz	95.1	$+1.0 \pm 1.6$
					8 kHz	93.0	-1.1 (+2.1; -3.1)
					12.5 kHz	90.1	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

		T Setting		Appl	ied Value	UUT	IEC 61672 Class 1
Range	Mode	Frequency	Time	Level	Freq.	Reading	Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
30 - 120	L_{C}	С	Fast	94.00	63 Hz	93.1	-0.8 ± 1.5
					125 Hz	93.8	-0.2 ± 1.5
					250 Hz	93.9	0.0 ± 1.4
					500 Hz	94.0	0.0 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	93.9	-0.2 ± 1.6
					4 kHz	93.3	-0.8 ± 1.6
					8 kHz	91.1	-3.0 (+2.1; -3.1)
					12.5 kHz	88.3	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory. 本證書所載校正用之測試器材均可溯源至國際標準。 局部複印本證書需先獲本實驗所書面批准。



Certificate of Calibration 校正證書

Certificate No.: C210403

證書編號

Remarks: - UUT Microphone Model No.: UC-53A & S/N: 322551

- Mfr's Spec. : IEC 61672 Class 1

: 63 Hz - 125 Hz : \pm 0.35 dB - Uncertainties of Applied Value: 94 dB

> 250 Hz - 500 Hz : \pm 0.30 dB $\pm 0.20 \text{ dB}$ 1 kHz 2 kHz - 4 kHz : $\pm 0.35 \text{ dB}$ 8 kHz $\pm 0.45 \text{ dB}$

12.5 kHz $\pm 0.70 \text{ dB}$

104 dB : 1 kHz $\pm 0.10 \text{ dB (Ref. 94 dB)}$ 114 dB : 1 kHz $\pm 0.10 \text{ dB (Ref. 94 dB)}$

- The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C215420

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC21-1765)

Date of Receipt / 收件日期: 26 August 2021

Description / 儀器名稱

Sound Level Meter (EQ013)

Manufacturer / 製造商

Rion

Model No. / 型號 Serial No. / 編號 NL-52 00921191

Supplied By / 委託者

Action-United Environmental Services and Consulting

Unit A, 20/F., Gold King Industrial Building, 35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 温度 :

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 (50 ± 25) %

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST/測試日期

10 September 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By 測試

K P Cheuk

Project Engineer

Certified By 核證

K C Lee Engineer Date of Issue

13 September 2021

Lee 簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration

Certificate No.:

C215420

證書編號

仪止起音

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

2. Self-calibration was performed before the test.

3. The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment:

Equipment ID

Description

Certificate No.

CL280

40 MHz Arbitrary Waveform Generator

C210084

CL281

Multifunction Acoustic Calibrator

AV210017

5. Test procedure: MA101N.

6. Results:

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

	UUT	Setting		Applied	d Value	UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	L _A	A	Fast	94.00	1	94.2	± 1.1

6.1.2 Linearity

-	UU'	Γ Setting		Applied	d Value	UUT
Range	Function	Frequency	Time	Level	Freq.	Reading
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)
30 - 130	L_A	A	Fast	94.00	1	94.2 (Ref.)
	1 5000)			104.00		104.2
				114.00		114.1

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

6.2 Time Weighting

	UUT	Setting		Applie	d Value	UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	L _A	A	Fast	94.00	1	94.2	Ref.
			Slow			94.2	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C215420

證書編號

6.3 Frequency Weighting

A-Weighting 6.3.1

11- Weighting	x-weighting						
	UUT Setting			Applied Value		UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
30 - 130	L_A	A	Fast	94.00	63 Hz	67.9	-26.2 ± 1.5
					125 Hz	78.0	-16.1 ± 1.5
					250 Hz	85.5	-8.6 ± 1.4
					500 Hz	91.0	-3.2 ± 1.4
					1 kHz	94.2	Ref.
					2 kHz	95.4	$+1.2 \pm 1.6$
					4 kHz	95.2	$+1.0 \pm 1.6$
					8 kHz	93.2	-1.1 (+2.1; -3.1)
					16 kHz	86.2	-6.6 (+3.5 ; -17.0)

6.3.2 C-Weighting

C Weighting	UUT Setting			Applied Value		UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
30 - 130	L_{C}	С	Fast	94.00	63 Hz	93.3	-0.8 ± 1.5
					125 Hz	94.0	-0.2 ± 1.5
					250 Hz	94.2	0.0 ± 1.4
					500 Hz	94.2	0.0 ± 1.4
					1 kHz	94.2	Ref.
					2 kHz	94.0	-0.2 ± 1.6
					4 kHz	93.4	-0.8 ± 1.6
					8 kHz	91.3	-3.0 (+2.1 ; -3.1)
					16 kHz	84.3	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C215420

證書編號

Remarks: - UUT Microphone Model No.: UC-59 & S/N: 12910

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz : \pm 0.35 dB

 $\begin{array}{lll} 250 \ Hz - 500 \ Hz & : \pm 0.30 \ dB \\ 1 \ kHz & : \pm 0.20 \ dB \\ 2 \ kHz - 4 \ kHz & : \pm 0.35 \ dB \\ 8 \ kHz & : \pm 0.45 \ dB \\ 16 \ kHz & : \pm 0.70 \ dB \end{array}$

104 dB : 1 kHz : \pm 0.10 dB (Ref. 94 dB) 114 dB : 1 kHz : \pm 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C210388

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC21-0122)

Date of Receipt / 收件日期: 19 January 2021

Description / 儀器名稱

Sound Calibrator (EQ089)

Manufacturer / 製造商

Rion

Model No. / 型號 Serial No./編號

NC-75 34680623

Supplied By / 委託者

Action-United Environmental Services and Consulting

Unit A, 20/F., Gold King Industrial Building, 35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 :

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$

Line Voltage / 電壓

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

20 January 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By 測試

K P Cheuk

Assistant Engineer

Certified By 核證

K C Lee Engineer Date of Issue 簽發日期

20 January 2021

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

Certificate of Calibration 校正證書

Certificate No.: C210388

證書編號

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement 1. of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

> Equipment ID CL130 CL281 TST150A

Description Universal Counter Multifunction Acoustic Calibrator Measuring Amplifier

Certificate No. C203952 CDK1806821 C201309

4. Test procedure: MA100N.

5. Results:

Sound Level Accuracy 5.1

UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz	94.0	± 0.25	± 0.2

Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value
(kHz)	(kHz)	Spec.	(Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory



ALS Technichem (HK) Pty Ltd

11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street, Kwai Chung N.T., Hong Kong

T: +852 2610 1044 | F: +852 2610 2021

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:

MR BEN TAM

CLIENT:

ACTION UNITED ENVIRONMENT SERVICES AND

CONSULTING

ADDRESS:

RM A 20/F., GOLD KING IND BLDG,

NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG WORK ORDER: HK2135790

SUB-BATCH:

0

LABORATORY:

HONG KONG

DATE RECEIVED: DATE OF ISSUE:

02-Sep-2021 10-Sep-2021

SPECIFIC COMMENTS

The calibration of flow rate performed by AUES staff on 02 September 2020.

Scope of Test:

Flow rate

Equipment Type:

Flow Meter

Brand Name:

Global Water

Model No.:

FP211

Serial No.:

1449006330

Equipment No.:

314

Calibration Factor:

Date of Calibration: 01 September, 2021

GENERAL COMMENTS

This is the Final Report and supersedes any preliminary report with this batch number.

Mr. Fung Lim Chee, Richard Managing Director, Life Sciences

Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

Page 1 of 2

ALS

Work Order:

HK2135790

Sub-batch:

0

Date of Issue:

10-Sep-2021

Client:

ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Reference Equipment:

Model:

SonTek IQ Standard

Serial Number:

IQ1217004

Equipment to be calibrated:

Equipment Type:

Flow Meter

Brand Name:

Global Water

Model No.:

FP211

Serial No.:

1449006330

Equipment No.:

to commission to the

Calibration Factor:

314

Cumbration : actor.

314

Date of Calibration: 01 September, 2021

Parameters:

The calibration of flow meter is verified with standard flow meter on site by AUES Staff.

Flow rate

Tidal	Reading of Reference Equipment (m/s)	Reading of Equipment to be calibrated (m/s)
Trial	SonTek IQ Standard Serial No: IQ1217004	Global Water FP211 Serial No. 1449006330
	Scharno. 1Q1217661	
1	0.10	0.1
2	0.19	0.2
3	0.41	0.4
4	0.78	0.8
5	1.02	1.0
6	1.11	1.1

Mr. Fung Lim Chee, Richard Managing Director, Life Sciences Hong Kong

Page 2 of 2



ALS Technichem (HK) Pty Ltd

11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street, Kwai Chung N.T., Hong Kong

T: +852 2610 1044 | F: +852 2610 2021

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR BEN TAM

CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND

CONSULTING

ADDRESS: RM A 20/F., GOLD KING IND BLDG,

> NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG

SUB-BATCH:

WORK ORDER:

LABORATORY:

HONG KONG

HK2136941

DATE RECEIVED: 09-Sep-2021 DATE OF ISSUE:

15-Sep-2021

SPECIFIC COMMENTS

Equipment information (Brand name, Model No., Serial No. and Equipment No.) is provided by client.

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the laboratory or quoted from relevant international standards.

The validity of equipment/ meter performance only applies to the result(s) stated in the report.

Equipment Type: Multifunctional Meter Service Nature: Performance Check

Conductivity, Dissolved Oxygen, pH Value, Turbidity, Salinity and Temperature Scope:

Brand Name/ Model No.: [YSI]/ [Professional DSS]

Serial No./ Equipment No.: [20J101862/15H103928]/[EQW018]

Date of Calibration: 14-September-2021

GENERAL COMMENTS

This is the Final Report and supersedes any preliminary report with this batch number.

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganic

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

WORK ORDER: HK2136941

SUB-BATCH: (

DATE OF ISSUE: 15-Sep-2021

CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[YSI]/ [Professional DSS]

Serial No./ Equipment No.:

[20J101862/15H103928]/[EQW018]

Date of Calibration: 14-September-2021 Date of Next Calibration: 14-December-2021

PARAMETERS:

Conductivity Method Ref: APHA (21st edition), 2510B

Expected Reading (µS/cm)	Displayed Reading (µS/cm)	Tolerance (%)
146.9	153.8	+4.7
6667	6903	+3.5
12890	13790	+7.0
58670	61979	+5.6
	Tolerance Limit (%)	±10.0

Dissolved Oxygen

Method Ref: APHA (21st edition), 45000: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.76	3.62	-0.14
5.31	5.36	+0.05
7.66	7.74	+0.08
	Tolerance Limit (mg/L)	±0.20

pH Value Method Ref: APHA (21st edition), 4500H: B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)
4.0	3.92	-0.08
7.0	6.96	-0.04
10.0	9.98	-0.02
	Tolerance Limit (pH unit)	±0.20

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganic

WORK ORDER: HK2136941

SUB-BATCH: 0

DATE OF ISSUE: 15-Sep-2021

CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[YSI]/ [Professional DSS]

Serial No./ Equipment No.: [20J101862/15H103928]/ [EQW018]

Date of Calibration: 14-September-2021 Date of Next Calibration: 14-December-2021

PARAMETERS:

Turbidity Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.78	
4	4.09	+2.3
40	39.37	-1.6
80	78.96	-1.3
400	394.01	-1.5
800	787.92	-1.5
	Tolerance Limit (%)	±10.0

Salinity Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.00	
10	10.06	+0.6
20	20.24	+1.2
30	29.53	-1.6
	Tolerance Limit (%)	±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganic

WORK ORDER: HK2136941

SUB-BATCH: 0

DATE OF ISSUE: 15-Sep-2021

CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[YSI]/ [Professional DSS]

Serial No./ Equipment No.: [20J101862/15H103928]/ [EQW018]

Date of Calibration: 14-September-2021 Date of Next Calibration: 14-December-2021

PARAMETERS:

Temperature Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
10.5	10.8	+0.3
21.0	21.4	+0.4
39.5	39.3	-0.2
	Tolerance Limit (°C)	±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

16:3

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganic



Hong Kong Accreditation Service 香港認可處

Certificate of Accreditation

認可證書

This is to certify that 特此證明

ALS TECHNICHEM (HK) PTY LIMITED

11/F, Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong 香港新界葵涌永業街1-3號忠信針織中心11樓

is accredited by the Hong Kong Accreditation Service (HKAS) to ISO/IEC 17025:2017 for performing specific laboratory activities as listed in the scope of accreditation within the test category of 獲香港認可處根據ISO/IEC 17025:2017認可 進行載於認可範圍內下述測試類別中的指定實驗所活動

Environmental Testing

環境測試

This accreditation to ISO/IEC 17025:2017 demonstrates technical competence for a defined scope and the implementation of a management system relevant to laboratory operation (see joint IAF-ILAC-ISO Communiqué).

此項 ISO/IEC 17025:2017 的認可資格證明此實驗所具備指定範疇內所須的技術能力並 實施一套與實驗所運作相關的管理體系 (見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of HKAS is affixed hereto by the authority of the HKAS Executive 現經香港認可處執行機關授權在此蓋上香港認可處的印章

SHUM Wai-leung, Executive Administrator

執行幹事 沈偉良

Issue Date: 28 February 2020

簽發日期:二零二零年二月二十八日

Registration Number: HOKLAS 066

註冊號碼:



Date of First Registration: 15 September 1995 首次註冊日期:一九九五年九月十五日



Appendix F

Event and Action Plan of Air Quality, Noise and Water Quality



Event and Action Plan for air quality

E 4	Action				
Event	ET	IEC	ER	Contractor	
Action level exceedance for one sample	I. Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER; Repeat measurement to confirm finding; Increase monitoring frequency to daily.	Check monitoring data submitted by ET; Check Contractor's working method.	1. Notify Contractor	Rectify any unacceptable practice; Amend working methods if appropriate.	
Action level exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring.	Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; Supervise Implementation of remedial measures.	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented.	Submit proposals for remedial to ER within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate.	
Limit level exceedance for one sample	I. Identify source, investigate the causes of exceedance and propose remedial measures; Inform ER, Contractor and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ER on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. 	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented.	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate.	
Limit level exceedance for two or more consecutive samples	Notify IEC, ER, Contractor and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring.	Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.	

Note: ET – Environmental Team IEC – Independent Environmental Checker ER – Engineer's Representative



Event and Action Plan for Construction Noise

Event	Action			
Event	ET	IEC	ER	Contractor
Action Level Exceedance	1. Notify IEC, ER and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness.	1.Review the analyzed results submitted by the ET; 2.Review the proposed remedial measures by the Contractor and advise the ER accordingly;	remedial measures for the analyzed	Submit noise mitigation proposals to IEC and ER; Implement noise mitigation proposals
Limit Level Exceedance	formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness 1. Identify source; 2. Inform IEC, ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be 3. Supervise the implementation of remedial measures. 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures.		1.Confirm receipt of notification of failure in writing; 2.Notify Contractor; 3.Require Contractor to propose remedial measures for the analyzed noise problem; 4.Ensure remedial measures properly	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Note:

ET – Environmental Team

IEC – Independent Environmental Checker

ER – Engineer's Representative



Event and Action Plan for Water Quality

Event	Action			
Event	ET	IEC	ER	Contractor
Action level exceedance for one sampling day	Inform IEC, Contractor and ER; Check monitoring data, all plant, equipment and Contractor's working methods; and Discuss remedial measures with IEC and Contractor and ER.	Discuss with ET, ER and Contractor on the implemented mitigation measures; Review proposals on remedial measures submitted by Contractor and advise the ER accordingly; and Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.	Discuss with IEC, ET and Contractor on the implemented mitigation measures; Make agreement on the remedial measures to be implemented; Supervise the implementation of agreed remedial measures.	I. Identify source(s) of impact; Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ER, ET and IEC and purpose remedial measures to IEC and ER; and Implement the agreed mitigation measures.
Action level exceedance for more than one consecutive sampling days	Repeat in-situ measurement on next day of exceedance to confirm findings; Inform IEC, contractor and ER; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss remedial measures with IEC, contractor and ER Ensure remedial measures are implemented	Discuss with ET, Contractor and ER on the implemented mitigation measures; Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.	Discuss with ET, IEC and Contractor on the proposed mitigation measures; Make agreement on the remedial measures to be implemented; and Discuss with ET, IEC and Contractor on the effectiveness of the implemented remedial measures.	I. Identify source(s) of impact; Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment and consider changes of working methods; Discuss with ET, IEC and ER and submit proposal of remedial measures to ER and IEC within 3 working days of notification; and Implement the agreed mitigation measures.
Limit level exceedance for one sampling day	Repeat measurement on next day of exceedance to confirm findings; Inform IEC, contractor and ER; Rectify unacceptable practice; Check monitoring data, all plant, equipment and Contractor's working methods; Consider changes of working methods; Discuss mitigation measures with IEC, ER and Contractor; and Ensure the agreed remedial measures are implemented	 Discuss with ET, Contractor and ER on the implemented mitigation measures; Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and Review and advise the ET and ER on the effectiveness of the implemented mitigation measures. 	Discuss with ET, IEC and Contractor on the implemented remedial measures; Request Contractor to critically review the working methods; Make agreement on the remedial measures to be implemented; and Discuss with ET, IEC and Contractor on the effectiveness of the implemented remedial measures.	 Identify source(s) of impact; Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment and consider changes of working methods; Discuss with ET, IEC and ER and submit proposal of additional mitigation measures to ER and IEC within 3 working days of notification; and Implement the agreed remedial measures.
Limit level exceedance for more than one consecutive sampling days	1. Inform IEC, contractor and ER; 2. Check monitoring data, all plant, equipment and Contractor's working methods; 3. Discuss mitigation measures with IEC, ER and Contractor; 4. Ensure mitigation measures are implemented; and 5. Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days	Discuss with ET, Contractor and ER on the implemented mitigation measures; Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.	Discuss with ET, IEC and Contractor on the implemented remedial measures; Request Contractor to critically review the working methods; Make agreement on the remedial measures to be implemented; Discuss with ET and IEC on the effectiveness of the implemented mitigation measures; and Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level.	1. Identify source(s) of impact; 2. Inform the ER and confirm notification of the non-compliance in writing; 3. Rectify unacceptable practice; 4. Check all plant and equipment and consider changes of working methods; 5. Discuss with ET, IEC and ER and submit proposal of additional mitigation measures to ER and IEC within 3 working days of notification; and 6. Implement the agreed remedial measures; and 7. As directed by the ER, to slow down or stop all or part of the construction activities until no exceedance of Limit level.

Note: ET – Environmental Team IEC – Independent Environmental Checker ER – Engineer's Representative Each step of actions required shall be implemented within 1 working day unless otherwise specified or agreed with EPD.



Appendix G

Monitoring Schedules of the Reporting Month and Coming Month



<u>Impact Monitoring Schedule of Air Quality, Noise and Water Quality – November 2021</u>

	Dete	NI-to- NI-o-th-o-to-	Air Quality	Monitoring	Water Oalit
	Date	Noise Monitoring	1-Hour TSP	24-Hour TSP	Water Quality
Mon	1-Nov-21				✓
Tue	2-Nov-21	✓	✓		
Wed	3-Nov-21				✓
Thu	4-Nov-21				
Fri	5-Nov-21			✓	✓
Sat	6-Nov-21				
Sun	7-Nov-21				
Mon	8-Nov-21	✓	✓		✓
Tue	9-Nov-21				
Wed	10-Nov-21				✓
Thu	11-Nov-21			✓	
Fri	12-Nov-21				✓
Sat	13-Nov-21		✓		
Sun	14-Nov-21				
Mon	15-Nov-21				✓
Tue	16-Nov-21				
Wed	17-Nov-21			✓	✓
Thu	18-Nov-21				
Fri	19-Nov-21	✓	✓		✓
Sat	20-Nov-21				
Sun	21-Nov-21				
Mon	22-Nov-21				✓
Tue	23-Nov-21			✓	
Wed	24-Nov-21				✓
Thu	25-Nov-21	✓	✓		
Fri	26-Nov-21				✓
Sat	27-Nov-21				
Sun	28-Nov-21				
Mon	29-Nov-21			✓	✓
Tue	30-Nov-21				

✓	Monitoring Day
	Sunday or Public Holiday



<u>Impact Monitoring Schedule of Air Quality, Noise and Water Quality – December 2021</u>

	D-4-	Noise Monitoring Air Quality Monitoring			Water Quality
	Date	1-Hour TSP	1-Hour TSP	24-Hour TSP	water Quanty
Wed	1-Dec-21	✓	✓		✓
Thu	2-Dec-21				
Fri	3-Dec-21				✓
Sat	4-Dec-21			✓	
Sun	5-Dec-21				
Mon	6-Dec-21				✓
Tue	7-Dec-21	✓	✓		
Wed	8-Dec-21				✓
Thu	9-Dec-21				
Fri	10-Dec-21			✓	✓
Sat	11-Dec-21				
Sun	12-Dec-21				
Mon	13-Dec-21	✓	✓		✓
Tue	14-Dec-21				
Wed	15-Dec-21				✓
Thu	16-Dec-21			✓	
Fri	17-Dec-21				✓
Sat	18-Dec-21		✓		
Sun	19-Dec-21				
Mon	20-Dec-21				✓
Tue	21-Dec-21				
Wed	22-Dec-21			✓	✓
Thu	23-Dec-21	✓	✓		
Fri	24-Dec-21				✓
Sat	25-Dec-21				
Sun	26-Dec-21				
Mon	27-Dec-21				
Tue	28-Dec-21			✓	
Wed	29-Dec-21	✓	✓		✓
Thu	30-Dec-21				
Fri	31-Dec-21				✓

✓	Monitoring Day
	Sunday or Public Holiday



Appendix H

Monitoring Data

- 24-hour TSP Air Quality
- Noise
- Water Quality



Air Quality (24-hour TSP)



						24-H	our TSI	P Monitor	ring Data f	or ASR-1					
DATE	SAMPLE NUMBER		APSED TI	ME	CHAI	RT REA	DING	AVG TEMP	AVG AIR PRESS	HI ()W/	AIR VOLUME	FILTER V	.)	DUST WEIGHT COLLECTED	24-Hr TSP (μg/m³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG	(°C)	(hPa)	(m³/min)	(std m ³)	INITIAL	FINAL	(g)	,, ,
5-Nov-21	27632	24742.70	24766.70	1440.00	38	39	38.5	25.6	1012.5	1.27	1826	2.6833	2.8275	0.1442	79
11-Nov-21	27651	24766.70	24790.70	1440.00	38	38	38.0	21.5	1017.7	1.25	1799	2.7045	2.8431	0.1386	77
17-Nov-21	27525	24790.70	24814.70	1440.00	40	40	40.0	23.5	1017.1	1.30	1874	2.7181	2.7884	0.0703	38
23-Nov-21	27658	24814.70	24838.70	1440.00	41	41	41.0	16.1	1021.1	1.35	1939	2.7121	2.9834	0.2713	140
29-Nov-21	27694	24838.70	24862.70	1440.00	40	41	40.5	20.5	1018.4	1.13	1623	2.7139	2.9359	0.2220	137

						24-H	our TSI	P Monito	ring Data f	or ASR-2					
\mathbf{I}	SAMPLE NUMBER		APSED TI	ME	СНАБ	RT REA	DING	AVG TEMP	AVG AIR PRESS	HI ()W/	AIR VOLUME	FILTER V	ď	DUST WEIGHT COLLECTED	24-Hr TSP (μg/m³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG	(°C)	(hPa)	(m³/min)	(std m ³)	INITIAL	FINAL	(g)	
5-Nov-21	27631	22157.35	22181.35	1440.00	35	36	35.5	25.6	1012.5	1.19	1711	2.6798	2.7090	0.0292	17
11-Nov-21	27640	22181.35	22205.35	1440.00	37	38	37.5	21.5	1017.7	1.25	1801	2.6655	2.7087	0.0432	24
17-Nov-21	27659	22205.35	22229.35	1440.00	39	40	39.5	23.5	1017.1	1.31	1885	2.7148	2.7706	0.0558	30
23-Nov-21	27678	22229.35	22253.35	1440.00	43	43	43.0	16.1	1021.1	1.44	2072	2.7072	2.7764	0.0692	33
29-Nov-21	27693	22253.35	22277.35	1440.00	37	38	37.5	20.5	1018.4	1.26	1819	2.7024	2.7361	0.0337	19

						24-Но	our TSP	Monitor	ing Data fo	or ASR-3a					
DATE	SAMPLE NUMBER		APSED TI	ME	СНА	RT REA	DING	AVG TEMP	AVG AIR PRESS	H(() \ \ \ /	AIR VOLUME	FILTER V		DUST WEIGHT COLLECTED	24-Hr TSP (μg/m³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG	(℃)	(hPa)	(m ³ /min)	(std m ³)	INITIAL	FINAL	(g)	
5-Nov-21	27629	15925.07	15949.07	1440.00	32	32	32.0	25.6	1012.5	1.10	1580	2.6819	2.7053	0.0234	15
11-Nov-21	27639	15949.07	15973.07	1440.00	37	38	37.5	21.5	1017.7	1.26	1816	2.6493	2.7066	0.0573	32
17-Nov-21	27660	15973.07	15997.07	1440.00	38	39	38.5	23.5	1017.1	1.29	1851	2.7015	2.8345	0.1330	72
23-Nov-21	27677	15997.07	16021.07	1440.00	40	40	40.0	16.1	1021.1	1.34	1936	2.7139	2.7972	0.0833	43
29-Nov-21	27689	16021.07	16045.07	1440.00	38	39	38.5	20.5	1018.4	1.19	1707	2.7180	2.7911	0.0731	43



Noise



								Nois	e Measu	rement	Results ((dB(A))	of CN-1								
Date	Start Time	$\begin{array}{c} 1^{st} \\ Leq_{5min} \end{array}$	L10	L90	$\begin{array}{c} 2^{nd} \\ Leq_{5min} \end{array}$	L10	L90	3 nd Leq _{5min}	L10	L90	4 th Leq _{5min}	L10	L90	5 th Leq _{5min}	L10	L90	6 th Leq _{5min}	L10	L90	Leq ₃₀	Façade Correction (*)
2-Nov-21	13:00	57.5	58.1	55.2	62.1	63.8	56.1	61.8	60.3	57	66.1	70.1	56.1	59.2	61.8	55.5	71.8	58.6	55.1	66	69
8-Nov-21	10:15	63.8	65.6	60.8	61.7	62.9	59.8	64.2	66.5	61.4	65.4	67.2	62.8	62.8	64.6	60	63.5	65.2	60.3	64	67
19-Nov-21	9:25	63.6	60.5	57	61.2	61.7	57.7	60.6	60.6	57	64.6	61.9	58.5	61.5	62.9	58.6	63.5	63.8	59.6	63	66
25-Nov-21	13:00	60.3	62.1	56.6	59.5	61.8	55.8	60.4	61.6	57.2	57.9	61	55.1	57.6	58.8	55.5	58.5	60.5	56.1	59	62

^(*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

								Nois	e Measu	rement	Results ((dB(A))	of CN-2	ļ							
Date	Start Time	1 st Leq _{5min}	L10	L90	2 nd Leq _{5min}	L10	L90	3 nd Leq _{5min}	L10	L90	4 th Leq _{5min}	L10	L90	5 th Leq _{5min}	L10	L90	6 th Leq _{5min}	L10	L90	Leq ₃₀	Façade Correction (*)
2-Nov-21	13:33	62.9	55.2	47.4	49.7	51.4	46.8	48.9	50.3	45.6	51.3	54.5	46.3	48.9	50.4	45.9	55.8	52.4	46.5	57	60
8-Nov-21	10:55	62.1	63.6	58.9	58.7	60.5	55.7	59.2	61.4	56.5	60.4	62.1	57.5	57.6	60.2	54.8	59.9	61.3	57.2	60	63
19-Nov-21	11:39	61.9	65.9	46.5	58.6	63.8	44.8	60.5	65.9	45.9	61.7	65.8	47.8	61.2	66.8	45.7	60.2	64.1	46.5	61	64
25-Nov-21	13:36	59.6	59.7	49.3	51.3	52.4	46.7	54.7	54.3	48.7	56.6	57.7	48.8	63	67.7	49.5	59.2	63.6	48.9	59	62

^(*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

								Nois	e Measu	rement	Results ((dB(A))	of CN-3								
Date	Start Time	1 st Leq _{5min}	L10	L90	$\begin{array}{c} 2^{nd} \\ Leq_{5min} \end{array}$	L10	L90	$\begin{matrix} 3^{nd} \\ Leq_{5min} \end{matrix}$	L10	L90	4 th Leq _{5min}	L10	L90	5 th Leq _{5min}	L10	L90	6 th Leq _{5min}	L10	L90	Leq ₃₀	Façade Correction (*)
2-Nov-21	14:06	50.6	48.6	42.1	43.1	45.3	40.7	43.8	45.9	40.7	45.4	47.6	41.2	47	47.2	41.4	44.6	46.3	40.6	47	50
8-Nov-21	13:00	52.2	55.5	48.6	51.5	53.4	45.7	54.6	57.8	52.1	53.4	56.8	49.7	51.7	54.6	46.4	52.8	54.2	47.5	53	56
19-Nov-21	15:15	52.8	56.4	47	52.5	54.8	48	54.3	56.9	48.5	56.5	58.8	49.1	56.3	60.8	49.7	53.3	57.7	49	55	58
25-Nov-21	14:11	49.2	50.8	46.3	52.6	55.4	46.4	50.8	50.7	45.7	51.5	53.5	45.3	49.7	54.1	45.3	54.7	57.2	46	52	55

^(*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

								Nois	e Measu	rement	Results	(dB(A))	of CN-4	ļ						
Date	Start Time	1 st Leq _{5min}	L10	L90	2 nd Leq _{5min}	L10	L90	3 nd Leq _{5min}	L10	L90	4 th Leq _{5min}	L10	L90	5 th Leq _{5min}	L10	L90	6 th Leq _{5min}	L10	L90	Leq _{30min}
2-Nov-21	14:41	58.6	60.4	54.6	57.9	59.8	54.7	58.1	60.2	55.3	57.7	59.8	53.7	57.5	59.3	54.5	57.1	59.9	51.8	58
8-Nov-21	13:45	60.8	62.5	58.6	59.9	61.3	57.4	61.5	63.6	60.1	58.8	60.2	56.6	59.4	60.8	57.2	60	62.3	59.9	60
19-Nov-21	15:52	58.8	62.4	44	58.5	57.8	44	57.3	60.9	44.5	58.5	62.8	44.1	60.3	65.8	44.7	56.3	59.7	43	58
25-Nov-21	14.47	72.8	60.5	55.4	57.6	58.6	55.8	62.4	64	56.5	62	60.6	57.2	66.4	70.2	56.4	59.4	61.8	55.7	67



Water Quality



Water Quality Impact Monitoring Result for M1

Date	1-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ty (NTU)	p	H	Sali	nity	SS(1	mg/L)
M1	9:30	0.14	22.1 22.1	22.1	<0.1	<0.1	7.8 7.75	7.78	97.5 96.8	97.2	3.24	3.3	7.45 7.45	7.5	0.06	0.06	4	4.0

Date	3-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (1	ng/L)	DO	(%)	Turbidi	ty (NTU)	р	H	Sali	nity	SS(1	mg/L)
M1	9:30	0.12	23.1	22.1	< 0.1	<0.1	7.74	7.74	97.1	07.0	2.78	2.7	7.91	7.9	0.06	0.06	4	4.0
IVII	9.30	0.13	23.1	23.1	< 0.1	<0.1	7.73	7.74	96.9	97.0	2.67	2.1	7.91	7.9	0.06	0.00	4	4.0

Date	5-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ty (NTU)	р	H	Sali	nity	SS(1	mg/L)
M1	10.10	0.12	23.6	22.6	< 0.1	ر <u>۱</u> د	7.69	7 60	97.4	97.2	2.48	2.4	7.64	7.6	0.06	0.06	5	15
IVII	10:10	0.13	23.6	23.0	< 0.1	< 0.1	7.66	7.68	97.0	91.2	2.37	2.4	7.64	7.0	0.06	0.06	4	4.3

Date	8-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ty (NTU)	p]	H	Sali	nity	SS(1	ng/L)
M1	10.20	0.12	21	21.0	< 0.1	۰0 1	7.87	7.07	94.8	04.9	2.92	2.0	8.10	0.1	0.06+	0.06	3	2.0
M1	10:20	0.13	21	21.0	< 0.1	<0.1	7.86	7.87	94.7	94.8	2.84	2.9	8.10	8.1	0.06	0.06	3	3.0

Date	10-Nov-21									
Location	Time	Depth (m)	Temp (oC)	Flow Velocity (m/s)	DO (mg/L)	DO (%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M1	14:00	0.13	19.2 19.2	<0.1 <0.1	8.21 8.14 8.18	98.3 97.5 97.9	0.58 0.6	7.25 7.25 7.3	0.06 0.06	4.0

Date	12-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (1	ng/L)	DO	(%)	Turbidi	ty (NTU)	pl	H	Sali	nity	SS(1	mg/L)
M1	10:05	0.13	18.7 18.7	18.7	<0.1	<0.1	7.85 7.81	7.83	94.1 93.7	93.9	1.22 1.23	1.2	6.93 6.93	6.9	0.04	0.04	4 3	3.5

Date	15-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ty (NTU)	р	H	Sali	nity	SS(1	mg/L)
M1	10.20	0.12	18.7	10.7	< 0.1	ر ۵ ر	8.07	9.04	94.7	04.2	2.84	2.0	8.11	0.1	0.06	0.06	4	2 5
M1	10:20	0.13	18.7	18.7	< 0.1	<0.1	8	8.04	93.9	94.3	2.85	2.8	8.11	8.1	0.06	0.06	3	3.3



Date	17-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (1	ng/L)	DO	(%)	Turbidi	ty (NTU)	р	H	Sali	nity	SS(1	mg/L)
M1	10:25	0.12	20.2	20.2	< 0.1	< 0.1	8.07	8.06	96.7	96.6	2.38	2.4	7.97	8 N	0.06	0.06	4	2.5
1V1 1	10:23	0.15	20.2	20.2	< 0.1	<0.1	8.05	0.00	96.4	90.0	2.42	2.4	7.97	8.0	0.06	0.00	3	3.3

Date	19-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (1	ng/L)	DO	(%)	Turbidi	ty (NTU)	p.	H	Sali	nity	SS(1	mg/L)
M1	9:40	0.13	20.3	20.3	<0.1	< 0.1	7.82 7.79	7.81	95.5 95.1	95.3	1.17	1.2	7.95 7.95	8.0	0.06	0.06	3	2.5

Date	22-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (1	ng/L)	DO	(%)	Turbidi	ty (NTU)	р	Н	Sali	nity	SS(1	mg/L)
M1	0.20	0.12	19.8	10.8	< 0.1	ر ۵ ر	7.93	7.02	95.3	05.1	2.31	2.2	8.27	0.2	0.06	0.06	3	2.5
IVII	9:30	0.13	19.8	19.8	< 0.1	< 0.1	7.9	7.92	94.8	95.1	2.27	2.3	8.27	8.3	0.06	0.06	4	3.3

Date	24-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (1	ng/L)	DO	(%)	Turbidi	ty (NTU)	р	H	Sali	nity	SS(1	mg/L)
M1	9:30	0.13	15.6 15.6	15.6	<0.1	< 0.1	8.3 8.24	8.27	93.9 93.0	93.5	1.9 1.91	1.9	7.91 7.91	7.9	0.06	0.06	4	3.5

Date	26-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ty (NTU)	p]	H	Sali	nity	SS(1	mg/L)
M1	11.45	0.12	17.6	17.6	< 0.1	ر <u>۱</u> د	8.33	0 22	93.6	03.4	2.16	2.1	7.16	7.2	0.03	0.02	<2	-2
M1	11:45	0.13	17.6	17.0	< 0.1	<0.1	8.3	8.32	93.2	93.4	2.11	2.1	7.16	1.2	0.03	0.03	<2	<2

Date	29-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (r	ng/L)	DO	(%)	Turbidi	ty (NTU)	p]	H	Sali	nity	SS(1	mg/L)
3.41	0.20	0.12	17.7	177	< 0.1	.0.1	8.26	0.25	95.2	05.1	2.96	2.0	7.81	7.0	0.06	0.06	<2	-0
M1	9:30	0.13	17.7	1/./	< 0.1	<0.1	8.24	8.25	94.9	95.1	3.12	3.0	7.81	7.8	0.06	0.06	<2	<2



Water Quality Impact Monitoring Result for M2

				<u>water Qu</u>	anty Impact M	omtoring Kes	uit 10f 1V12			
Date	1-Nov-21									
Location	Time	Depth (m)	Temp (oC)	Flow Velocity (m/s)	DO (mg/L)	DO (%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M2	10:30	0.02		<0.1 <0.1						
Date	3-Nov-21									
Location	Time	Depth (m)	Temp (oC)	Flow Velocity (m/s)	DO (mg/L)	DO (%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M2	10:15	0.02		<0.1 <0.1 <0.1						
Date	5-Nov-21									
Location	Time	Depth (m)	Temp (oC)	Flow Velocity (m/s)	DO (mg/L)	DO (%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M2	11:00	0.02		<0.1 <0.1						
Date	8-Nov-21									
Location	Time	Depth (m)	Temp (oC)	Flow Velocity (m/s)	DO (mg/L)	DO (%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M2	10:50	0.00								
Date	10-Nov-21									
Location	Time	Depth (m)	Temp (oC)	Flow Velocity (m/s)	DO (mg/L)	DO (%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M2	13:35	0.00								
Date	12-Nov-21									
Location	Time	Depth (m)	Temp (oC)	Flow Velocity (m/s)	DO (mg/L)	DO (%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M2	10:40	0.00								
Date	15-Nov-21									
Location	Time	Depth (m)	Temp (oC)	Flow Velocity (m/s)	DO (mg/L)	DO (%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M2	14:05	0.00								



Monthly Environmental Monitoring & Audit Report (No.40) – November 2021

			r	(= (= (= ()	11070111001 2021							
Doto	17-Nov-21											
Date		Donath (m)	Тата (а	C) Flores	Valacita (as/s)	DO (===/L)	DO	(0/)	Turbidity (NTU)	pН	Calinida	CC(/T_)
Location	Time	Depth (m)	Temp (o	C) Flow	Velocity (m/s)	DO (mg/L)	DO	(%)	Turblaity (NTO)	pn 	Salinity	SS(mg/L)
M2	11:10	0.00										
	10.37											
Date	19-Nov-21	<u> </u>		~ I				(0.1)			1 ~	
Location	Time	Depth (m)	Temp (o	C) Flow	Velocity (m/s)	DO (mg/L)	DO	(%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M2	10:20	0.00			_							
			<u>"</u>	· · · · · · · · · · · · · · · · · · ·	-\ <u>-</u>	<u>'</u>	l .			<u>'</u>	'	
Date	22-Nov-21											
Location	Time	Depth (m)	Temp (o	C) Flow	Velocity (m/s)	DO (mg/L)	DO	(%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M2	10:15	0.00			_							
			ı			l l		<u> </u>	<u>l</u>		l l	<u>l</u>
Date	24-Nov-21											
Location	Time	Depth (m)	Temp (o	C) Flow	Velocity (m/s)	DO (mg/L)	DO	(%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M2	10:20	0.00										
	<u>l</u>	<u>l</u>	J			<u> </u>	l		<u> </u>	<u> </u>		l
Date	26-Nov-21											
Location	Time	Depth (m)	Temp (o	C) Flow	Velocity (m/s)	DO (mg/L)	DO	(%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
M2	13:50	0.00										
			L			l l	I			L	J J	<u> </u>
Date	29-Nov-21											
Date Location	29-Nov-21 Time	Depth (m)	Temp (o	C) Flow	Velocity (m/s)	DO (mg/L)	DO	(%)	Turbidity (NTU)	pН	Salinity	SS(mg/L)
		Depth (m) 0.00	Temp (o	C) Flow	Velocity (m/s)	DO (mg/L)	DO	(%)	Turbidity (NTU)	рН	Salinity	SS(mg/L)



Water Quality Impact Monitoring Result for M3

Date	1-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ty (NTU)	p.	H	Sali	nity	SS(r	mg/L)
M3	10:45	2.45	23.7	23.7	<0.1	< 0.1	7.47 7.46	7.47	94.1 94.0	94.1	1.31	1.3	7.47 7.47	7.5	0.02	0.02	<2 <2	<2

Date	3-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (1	mg/L)	DO	(%)	Turbidi	ty (NTU)	p	H	Sali	nity	SS(1	mg/L)
M3	10:30	2.45	23.8 23.8	23.8	<0.1	<0.1	7.54 7.53	7.54	94.4 94.3	94.4	1.29	1.3	7.88 7.88	7.9	0.02	0.02	2 2	2.0

Date	5-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (1	mg/L)	DO	(%)	Turbidi	ty (NTU)	р	H	Sali	nity	SS(1	ng/L)
M3	11:10	2.45	24	24.0	< 0.1	< 0.1	7.47	7.47	94.4	94.4	0.87	0.9	7.65	77	0.02	0.02	<2	<2
IVIS	11.10	2.43	24	24.0	< 0.1	\0.1	7.46	7.47	94.3	77.7	0.88	0.7	7.65	/./	0.02	0.02	<2	\2

Date	8-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ty (NTU)	р	H	Sali	nity	SS(1	ng/L)
M2	11.05	2.45	21.5	21.5	< 0.1	ر ۵ ر	7.88	7.96	94.6	04.4	1.06	1.1	8.16	0.2	0.02	0.02	<2	-0
M3	11:05	2.45	21.5	21.5	< 0.1	<0.1	7.84	7.86	94.1	94.4	1.04	1.1	8.16	8.2	0.02	0.02	<2	<2

Date	10-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (ı	mg/L)	DO	(%)	Turbidi	ity (NTU)	p	H	Sali	nity	SS(1	mg/L)
M2	12.45	2.45	19.6	10.6	< 0.1	c0 1	7.97	7.95	96.0	05.7	0.57	0.6	7.28	7.2	0.02	0.02	<2	-2
M3	13:45	2.43	19.6	19.6	< 0.1	< 0.1	7.92	1.93	95.4	93.7	0.56	0.6	7.28	7.3	0.02	0.02	<2	<2

Date	12-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (1	ng/L)	DO	(%)	Turbidi	ity (NTU)	p]	H	Sali	nity	SS(1	mg/L)
M3	10:55	2.45	19.1	10 1	< 0.1	ر n 1	7.47	7.42	89.2	88.9	1.67	1.7	6.90	6.9	0.02	0.02	3	3.0
IVIS	10:55	2.43	19.1	19.1	< 0.1	< 0.1	7.39	7.43	88.5	88.9	1.65	1./	6.90	0.9	0.02	0.02	3	5.0

Date	15-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ty (NTU)	р	H	Sali	nity	SS(1	mg/L)
M3	14.15	2.45	18.9	18.9	< 0.1	ر n 1	7.91	7.85	93.1	02.4	2.1	2.1	8.08	0 1	0.02	0.02	2	2.0
WIS	14:15	2.45	18.9	18.9	< 0.1	<0.1	7.79	7.83	91.7	92.4	2.11	2.1	8.08	6.1	0.02	0.02	2	2.0



Date	17-Nov-21																	
Location	Time	Depth (m)	Temp	o (oC)	Flow V	elocity (m/s)	DO (1	mg/L)	DO	(%)	Turbidi	ty (NTU)	p.	H	Sali	nity	SS(1	mg/L)
M2	11.20	2.45	21.4	21.4	< 0.1	ر n 1	7.52	7.51	89.4	89.3	1.54	1.5	7.93	7.0	0.02	0.02	2	2.5
M3	11:20	2.45	21.4	21.4	< 0.1	<0.1	7.49	7.31	89.1	89.3	1.55	1.3	7.93	7.9	0.02	0.02	3	2.3

Date	19-Nov-21																	
Location	Time	Depth (m)	Temp	o (oC)	Flow V	elocity (m/s)	DO (1	mg/L)	DO	(%)	Turbidi	ty (NTU)	p	H	Sali	nity	SS(1	mg/L)
M3	10:30	2.45	21.5 21.5	21.5	<0.1 <0.1	<0.1	7.55 7.51	7.53	91.7 91.3	91.5	0.97	1.0	7.75 7.75	7.8	0.02	0.02	<2 <2	<2

Date	22-Nov-21																	
Location	Time	Depth (m)	Temp	o (oC)	Flow V	elocity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ty (NTU)	р	H	Sali	nity	SS(1	ng/L)
M3	10:30	2.45	20.1	20.1	< 0.1	c0 1	7.68	7 67	92.2	92.0	1.88	1.0	8.22	0.2	0.02	0.02	2	2.0
WI3	10:50	2.45	20.1	20.1	< 0.1	< 0.1	7.66	7.67	91.8	92.0	1.99	1.9	8.22	0.2	0.02	0.02	2	2.0

Date	24-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ty (NTU)	р	H	Sali	nity	SS(1	ng/L)
M3	10:30	2.45	16.3 16.3	16.3	<0.1	<0.1	7.69 7.66	7.68	87.3 87.0	87.2	1.43 1.42	1.4	7.73 7.73	7.7	0.02	0.02	2 2	2.0

Date	26-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow V	elocity (m/s)	DO (1	ng/L)	DO	(%)	Turbidi	ty (NTU)	p]	H	Sali	nity	SS(1	mg/L)
142	14.00	2.45	18.5	10.5	< 0.1	ە 1 م	8.06	0.02	89.5	90.0	2.11	2.1	7.36	7.4	0.02	0.02	<2	-2
M3	14:00	2.45	18.5	18.5	< 0.1	< 0.1	7.97	8.02	88.4	89.0	2.09	2.1	7.36	7.4	0.02	0.02	<2	<2

Date	29-Nov-21																	
Location	Time	Depth (m)	Temp	o (oC)	Flow V	elocity (m/s)	DO (1	ng/L)	DO	(%)	Turbidi	ty (NTU)	р	H	Sali	nity	SS(1	mg/L)
M2	10.20	2.45	18.7	10.7	< 0.1	ە 0.1	7.87	7.05	91.3	01 1	2.18	2.2	7.75	7.0	0.02	0.02	<2	-2
M3	10:20	2.45	18.7	18.7	< 0.1	< 0.1	7.83	7.85	90.8	91.1	2.19	2.2	7.75	7.8	0.02	0.02	<2	<2



Water Quality Impact Monitoring Result for M4

Date	1-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow Veloc	city (m/s)	DO (1	ng/L)	DO	(%)	Turbidi	ity (NTU)	р	H	Sali	nity	SS(1	ng/L)
M4	11:00	0.43	23.8 23.8	23.8	<0.1 <0.1	<0.1	7.96 7.97	7.97	99.3 99.4	99.4	4.4	4.4	7.80 7.80	7.8	0.05	0.05	3	3.5

Date	3-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow Veloc	eity (m/s)	DO (ı	ng/L)	DO	(%)	Turbid	ity (NTU)	р	H	Sali	nity	SS(1	mg/L)
M4	10:50	0.43	24 24	24.0	<0.1 <0.1	<0.1	7.88 7.87	7.88	98.7 98.6	98.7	2.1	2.1	7.51 7.51	7.5	0.04	0.04	<2 <2	<2

Date	5-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow Veloc	city (m/s)	DO (ı	ng/L)	DO	(%)	Turbid	ity (NTU)	р	Н	Sali	nity	SS(1	mg/L)
MA	11.20	0.44	24.1	24.1	< 0.1	ر n 1	7.85	7.84	98.9	98.9	1.6	1.6	7.31	7.2	0.04	0.04	<2	-2
M4	11:30	0.44	24.1	24.1	< 0.1	< 0.1	7.83	7.64	98.8	98.9	1.6	1.6	7.31	7.3	0.04	0.04	<2	<2

Date	8-Nov-21																	
Location	Time	Depth (m)	Temp	o (oC)	Flow Veloc	eity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ity (NTU)	р	Н	Sali	nity	SS(1	mg/L)
M4	11.25	0.44	21.8	21.0	< 0.1	c0 1	7.89	7.88	94.7	04.7	1.5	1 /	7.85	7.0	0.04	0.04	<2	-2
W14	11:23	0.44	21.8	21.8	< 0.1	< 0.1	7.86	7.00	94.6	94.7	1.4	1.4	7.85	7.9	0.04	0.04	<2	<2

Date	10-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow Veloc	city (m/s)	DO (1	mg/L)	DO	(%)	Turbid	ity (NTU)	р	Н	Sali	nity	SS(r	mg/L)
M4	14:15	0.44	19.8 19.8	19.8	<0.1 <0.1	<0.1	8.13 8.11	8.12	97.7 97.5	97.6	1.2	1.2	6.96 6.96	7.0	0.04	0.04	<2 <2	<2

Date	12-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow Veloc	city (m/s)	DO (1	ng/L)	DO	(%)	Turbid	ity (NTU)	p.	H	Sali	nity	SS(r	ng/L)
M4	11:10	0.43	19.3 19.3	19.3	<0.1 <0.1	<0.1	8.14 8.11	8.13	97.9 97.5	97.7	1.3	1.3	6.94 6.94	6.9	0.03	0.03	<2 <2	<2

Date	15-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow Veloc	eity (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ity (NTU)	р	Н	Sali	nity	SS(1	mg/L)
M4	14:35	0.41	18.8	100	< 0.1	<0.1	8.38	9 24	98.4	98.1	1.4	1.2	7.74	77	0.03	0.03	<2	-2
1014	14.33	0.41	18.8	10.0	< 0.1	<0.1	8.29	8.34	97.7	96.1	1.3	1.3	7.74	7.7	0.03	0.03	<2	<2



Date	17-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow Veloc	city (m/s)	DO (1	mg/L)	DO	(%)	Turbid	ity (NTU)	р	Н	Sali	nity	SS(1	mg/L)
MA	11.45	0.40	21.6	21.6	< 0.1	∠0.1	7.51	7.50	89.6	89.5	1.2	1.2	7.48	7.5	0.04	0.04	<2	-2
M4	11:45	0.40	21.6	21.0	< 0.1	<0.1	7.48	7.50	89.3	89.3	1.1	1.2	7.48	7.3	0.04	0.04	<2	<2

Date	19-Nov-21																	
Location	Time	Depth (m)	Temp	o (oC)	Flow Veloc	city (m/s)	DO (1	ng/L)	DO	(%)	Turbidi	ity (NTU)	p	Н	Sali	nity	SS(1	mg/L)
M4	10:45	0.40	21.6 21.6	21.6	<0.1 <0.1	<0.1	7.36 7.33	7.35	89.9 89.5	89.7	1.1	1.1	7.39 7.39	7.4	0.04	0.04	<2 <2	<2

Date	22-Nov-21																	
Location	Time	Depth (m)	Temp	o (oC)	Flow Veloc	city (m/s)	DO (ı	ng/L)	DO	(%)	Turbidi	ity (NTU)	p	Н	Sali	nity	SS(1	mg/L)
MA	10.50	0.42	20.3	20.2	< 0.1	c0 1	7.22	7.21	86.6	96.1	1.2	1.2	7.79	7.0	0.04	0.04	<2	-2
M4	10:50	0.43	20.3	20.3	< 0.1	< 0.1	7.19	7.21	86.2	86.4	1.2	1.2	7.79	7.8	0.04	0.04	<2	<2

Date	24-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow Veloc	city (m/s)	DO (ı	ng/L)	DO	(%)	Turbid	ity (NTU)	р	Н	Sali	nity	SS(1	mg/L)
M4	10:50	0.41	16.2	16.2	< 0.1	< 0.1	7.01	6.98	79.3	78.9	1.0	1.0	7.32	7.2	0.02	0.02	<2	/2
IVI4	10.30	0.41	16.2	10.2	< 0.1	<0.1	6.94	0.98	78.5	70.9	1.0	1.0	7.32	7.3	0.02	0.02	<2	<2

Date	26-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow Veloc	city (m/s)	DO (1	mg/L)	DO	(%)	Turbid	ity (NTU)	р	H	Sali	nity	SS(r	ng/L)
M4	11:30	0.40	18.6 18.6	18.6	<0.1 <0.1	<0.1	7.81 7.74	7.78	87.7 86.9	87.3	1.5 1.5	1.5	7.04 7.04	7.0	0.04	0.04	<2 <2	<2

Date	29-Nov-21																	
Location	Time	Depth (m)	Temp	(oC)	Flow Veloc	city (m/s)	DO (1	ng/L)	DO	(%)	Turbid	ity (NTU)	р	H	Sali	nity	SS(r	ng/L)
MA	10.40	0.42	18.9	10.0	< 0.1	∠0.1	8.54	0 5 5	98.3	98.4	0.9	0.0	8.24	0.2	0.04	0.04	<2	\sim
M4	10:40	0.42	18.9	18.9	< 0.1	<0.1	8.55	8.33	98.4	90.4	1.0	0.9	8.24	8.2	0.04	0.04	<2	<2





Appendix I


Graphical Plots of Air Quality, Noise and Water Quality



Air Quality Impact Monitoring – 1-hour TSP

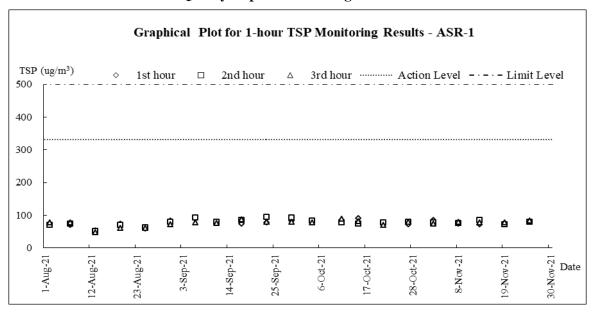


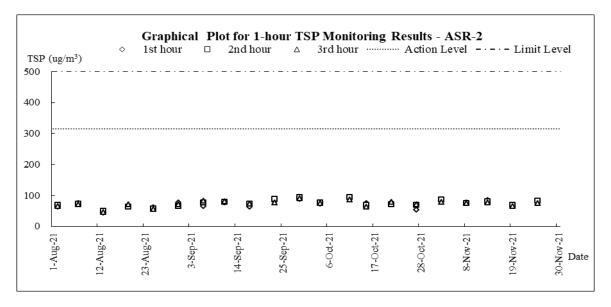


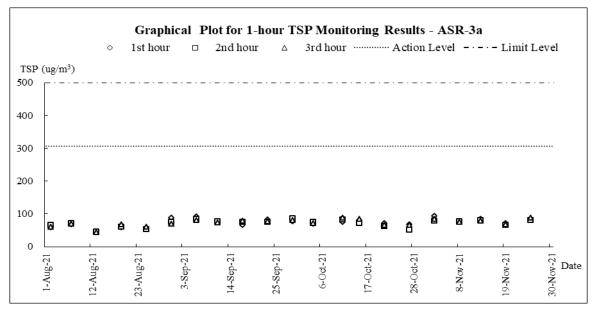




Air Quality Impact Monitoring – 24-hour TSP

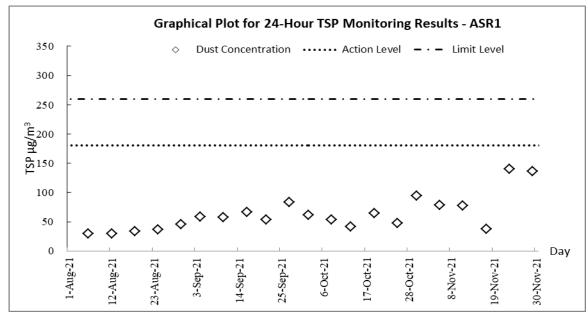


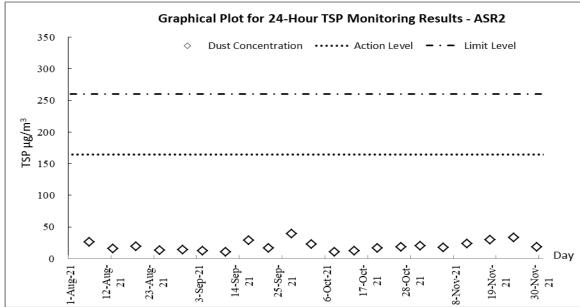


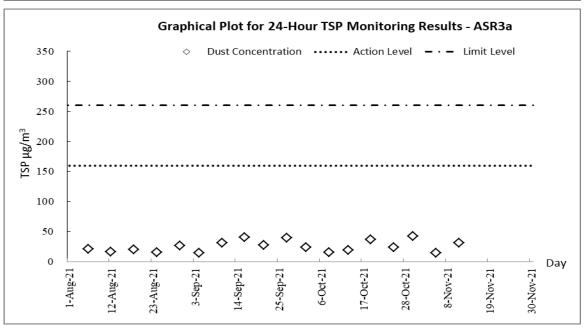





Construction Noise Impact Monitoring

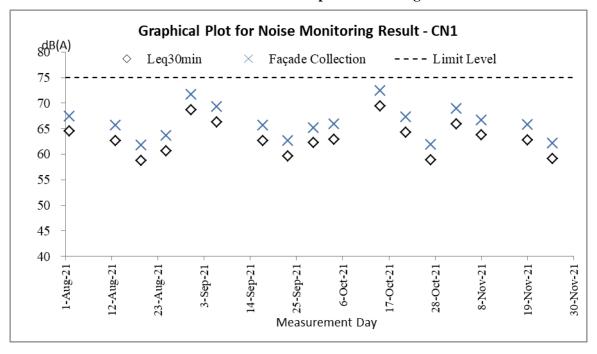

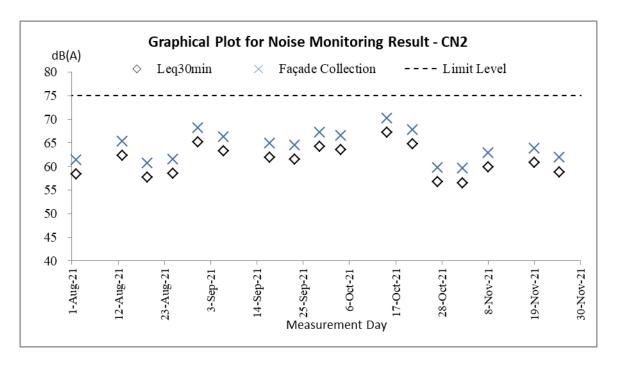




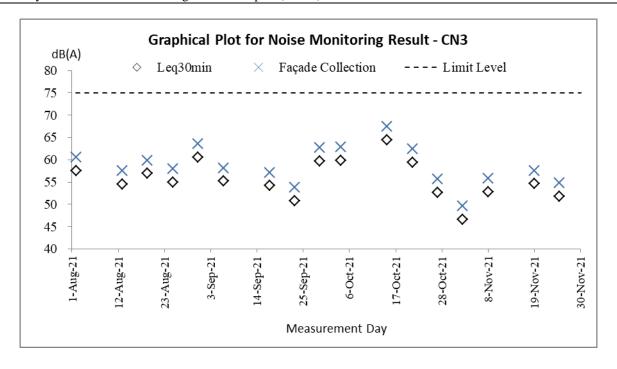


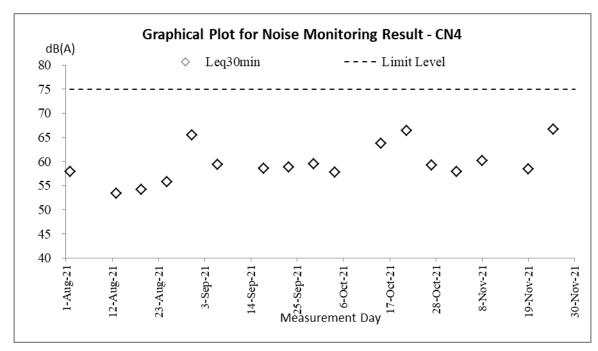





Water Quality Impact Monitoring

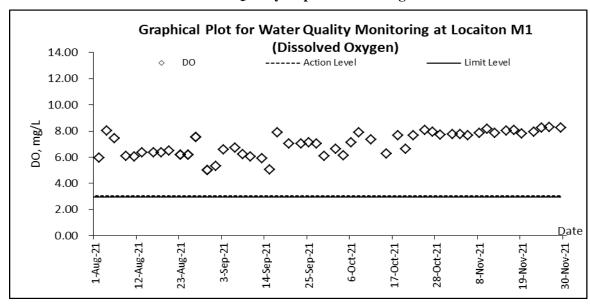


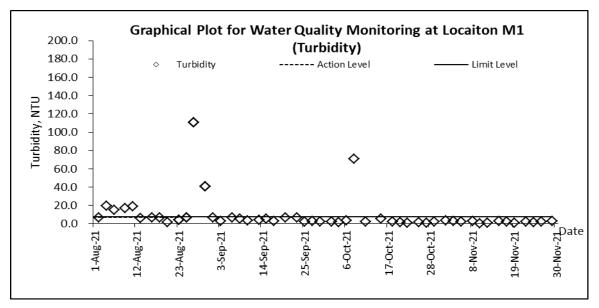


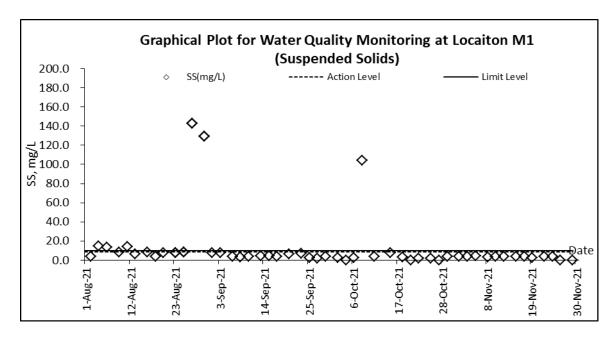




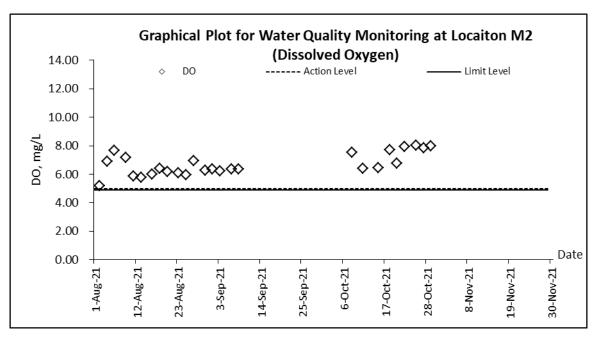


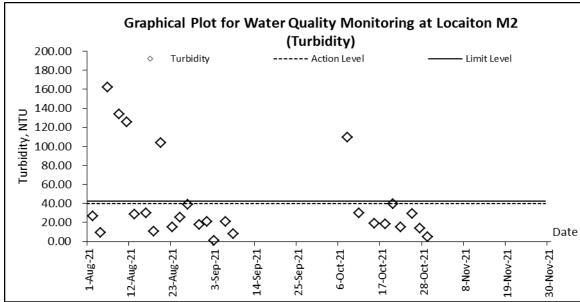


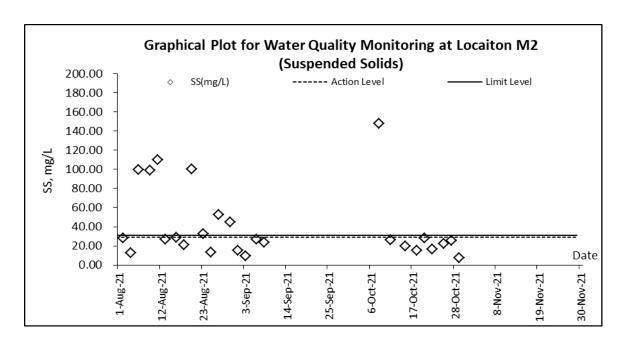




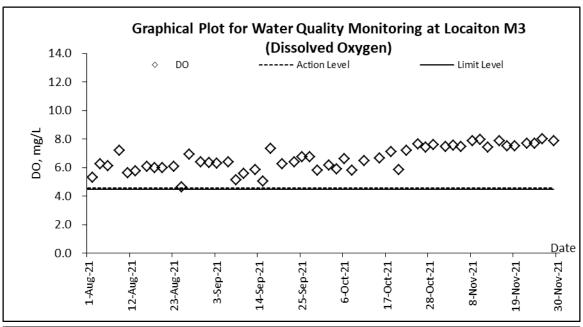


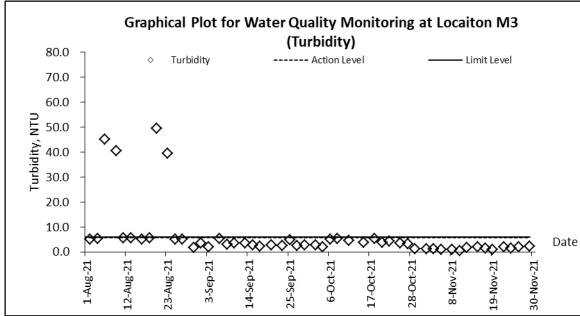


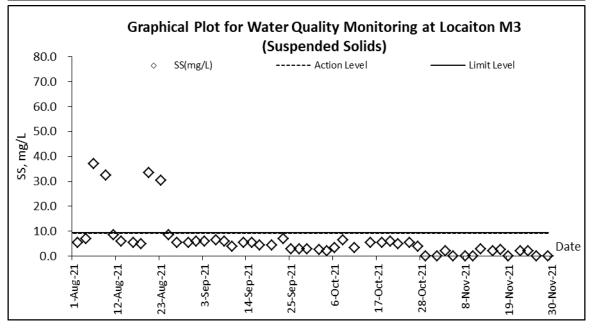



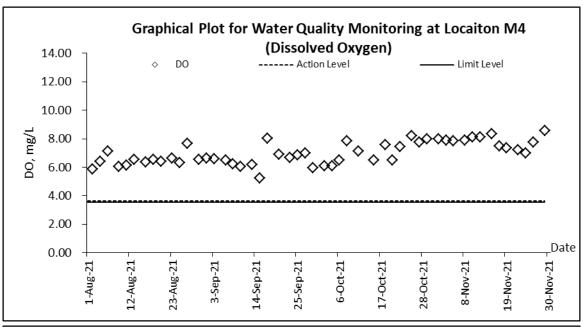

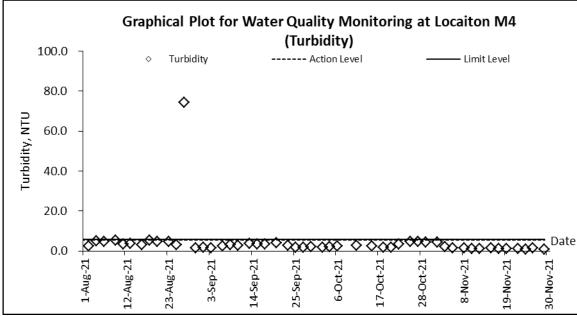

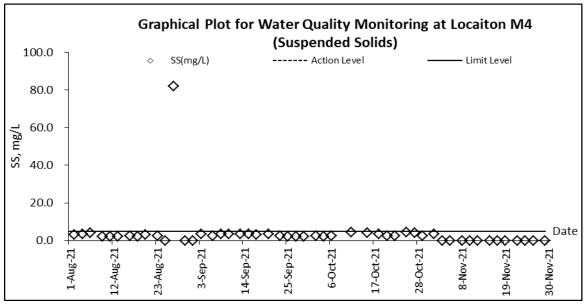



Appendix J

Meteorological Data of the Reporting Month



				Ta Kwu Ling Station				
Date		Weather	Total Rainfall (mm)	Mean Air Temp. (°C)	Wind Speed (km/h)	Mean Relative Humidity (%)	Wind Direction	
1-Nov-21	Mon	Light to moderate easterly winds.	Trace	24.3	8	77.2	Е	
2-Nov-21	Tue	Cloudy periods tonight.	Trace	25.3	7.5	79.5	E/SE	
3-Nov-21	Wed	Mainly fine in the afternoon.	Trace	25.1	7.5	76	E	
4-Nov-21	Thu	Mainly fine and rather warm tomorrow	0	26.3	7.5	75.5	E/SE	
5-Nov-21	Fri	Light to moderate easterly winds.	0	26.5	8	77.7	E	
6-Nov-21	Sat	Mainly fine in the afternoon.	0	26	10.5	75	E/SE	
7-Nov-21	Sun	Moderate northerly winds	0	25.1	9.2	78.2	E/SE	
8-Nov-21	Mon	Mainly fine and dry.	2	19.3	13.7	67.0	N/NE	
9-Nov-21	Tue	Mainly fine and very dry.	0	18.2	13.3	69.7	N	
10-Nov-21	Wed	Cloudy periods tonight.	0	18.3	12	48.5	N/NE	
11-Nov-21	Thu	Mainly fine and rather warm tomorrow	0	17.9	6	59.5	S/SE	
12-Nov-21	Fri	Light to moderate easterly winds.	0	20.2	7	59	N	
13-Nov-21	Sat	Mainly fine in the afternoon.	Trace	19.6	6	57	E/SE	
14-Nov-21	Sun	Mainly fine and dry.	0	18.9	5.5	63	E/SE	
15-Nov-21	Mon	Moderate east to northeasterly winds.	0	19.8	7	66	E/SE	
16-Nov-21	Tue	Mainly cloudy tonight.	0	21.3	5.5	71.5	N	
17-Nov-21	Wed	Sunny intervals in the afternoon.	0	22	7	77	Е	
18-Nov-21	Thu	Very dry in the afternoon.	0	21.7	7.5	71.7	N	
19-Nov-21	Fri	Moderate to fresh north to northeasterly winds	Trace	20.4	3.7	82.5	E/SE	
20-Nov-21	Sat	Cloudy periods tonight.	0.3	23.7	7.5	81	Е	
21-Nov-21	Sun	Moderate to fresh northerly winds	0	23.3	6.2	81.5	Е	
22-Nov-21	Mon	One or two rain patches at first.	0.5	14.1	13.5	79.2	N	
23-Nov-21	Tue	Light to moderate easterly winds.	Trace	14.1	15.7	61.5	N	
24-Nov-21	Wed	Mainly fine in the afternoon.	0	17.9	5	55	N	
25-Nov-21	Thu	Mainly fine and dry.	0	18.4	6.2	65	N/NW	
26-Nov-21	Fri	Fine. Very dry in the afternoon.	0	18.8	7.5	65	N	
27-Nov-21	Sat	Strong offshore and on high ground.	0	19	8.1	61	N	
28-Nov-21	Sun	Moderate to fresh northerly winds	0	19.1	6.2	68.5	N	
29-Nov-21	Mon	Fine and dry.	0	19.8	7.5	67.5	N	
30-Nov-21	Tue	It will become appreciably cooler tonight	0	19.4	11.2	69.5	N/NE	



Appendix K

Ecological Survey Report

Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery Monthly Environmental Monitoring & Audit Report (No.40) – November 2021



Ecological Survey Report for Contract CV/2016/10



Contract No. CV/2016/10

Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery

Monthly Report of Ecologically Sensitive Habitats Monitoring – November 2021

Revision Date of issue	0 06 Dec 2021	
Prepared by	Alan Lam	积
Reviewed by	Hoiki Leung	Make
Verified by	Mike Leung	A

1



Table of Contents

1	INT	RODUCTION	4
	1.1	BACKGROUND	4
	1.2	OBJECTIVE	4
2	ECC	DLOGICALLY SENSITIVE HABITATS	5
	2.1	DESCRIPTION OF HABITATS	5
	2.2	MONITORING MEASURES OF WETLAND HABITATS	6
	2.3	MONITORING MEASURES OF NON-WETLAND HABITATS	6
3	ME	THODOLOGY	7
	3.1	MAMMAL SURVEY	7
	3.2	BIRD SURVEY	7
	3.3	HERPETOFAUNA SURVEY	7
	3.4	DRAGONFLY SURVEY	7
	3.5	BUTTERFLY SURVEY	8
	3.6	AQUATIC FAUNA SURVEY	8
4	RES	ULT	9
5	DIS	CUSSION	14
Арр	endix l	- Transect Routes for Contract CV/2016/10	17



LIST OF TABLE	
Table 1	Action and Limit Levels and Responses to Evidence of Declines
	in Aquatic Fauna
Table 2	Action and Limit Levels and Responses to Evidence of Declines
	in Non-Aquatic Fauna
Table 3	Survey Schedule
Table 4	Result of mammal in survey
Table 5	Result of Avifauna in survey
Table 6	Result of reptile in survey
Table 7	Result of amphibian in survey
Table 8	Result of butterfly in survey
Table 9	Result of Odonate in survey
Table 10	Result of freshwater communities in survey

LIST OF APPENDIX					
Appendix I	Transect Routes for Contract CV/2016/10				

LIST OF FIGURE	E <u>S</u>
Figure 1	Bar chart showing the total species richness within site boundary
	from 2018 to 2021
Figure 2	Bar chart showing the total abundance within site boundary from
	2018 to 2021
Figure 3	Bar chart showing the species richness within site boundary by
	taxa from 2018 to 2021
Figure 4	Bar chart showing the species richness based on habitat type
	from 2018 to 2021
Figure 5	Bar chart showing the abundance based on habitat type from
	2018 to 2021



1 INTRODUCTION

1.1 BACKGROUND

- 1.1.1 The main objective of the proposed site formation and associated infrastructural works for development of columbarium, crematorium (C&C) and related facilities at Sandy Ridge Cemetery is to increase the public cremation services and supply of public niches to meet the future demand.
- 1.1.2 The project includes site formation and associated works for development of C&C facilities at the Sandy Ridge Cemetery, road works within Sandy Ridge Cemetery, widening a section of Lin Ma Hang Road (from 6.5m to 7.3m), provision of off-site pick-up/drop-off points for shuttle buses as well as barging point at Siu Lam, Lok On Pai.
- 1.1.3 The Environmental Impact Assessment (EIA) report, including Environmental Monitoring and Audit Manual (EM&A Manual), was approved with conditions on 8 August 2016 (Register No.: AEIAR-198/2016). EPD issued an Environmental Permit (EP) for the Project (EP-534/2017) on 7 April 2017. A Further Environment Permit (FEP) for the Project (FEP-01/534/2017) was issued on 23 February 2018, variation of EP (EP-534/2017/A) and variation of FEP (FEP-01/534/2017/A) were issued on 24 December 2018.
- 1.1.4 According to Clause 3.1 of the FEP (FEP-01/534/2017/A), "The Permit Holder shall implement the EM&A programme in accordance with the procedures and requirements as set out in the EM&A Manual. Any changes to the programme shall be justified by the ET Leader and verified by the IEC as conforming to the information and requirements contained in the EM&A Manual before submission to the Director for approval".
- 1.1.5 This Ecologically Sensitive Habitats Monitoring Methodology articulates the protocol of monitoring the ecology of concerned habitats as specified in EM&A Manual.

1.2 OBJECTIVE

- 1.2.1 According to approved EIA report (AEIAR-198/2016), habitat types within project boundary comprise of watercourse, grassland, upland grassland, plantation, woodland and developed area. Natural habitats were of moderate ecological value in terms of species diversity, species rarity, species abundance, ecological linkage as well as nursery. Moreover, 0.3ha of wet woodland on the northern side of Sandy Ridge was deemed habitat with high ecological value. Four types of habitats were regarded as ecologically sensitive habitats, namely wet woodland, watercourses, upland grassland and woodland. Considering human disturbance in upcoming construction and operation phases, ecologically sensitive habitats shall be monitored in accordance with EM&A Manual.
- 1.2.2 The objective of ecologically sensitive habitats monitoring is to evaluate the effectiveness of measures to minimize impacts on concerned habitats from disturbance and pollution.



2 ECOLOGICALLY SENSITIVE HABITATS

2.1 DESCRIPTION OF HABITATS

2.1.1 In order to monitor the effectiveness of the measures to the minimise impact on ecologically sensitive habitats from disturbance and pollution, monthly monitoring during construction and operation phases is required as specified in EM&A Manual. Standard faunal transect and sampling surveys cover both wetland and non-wetland habitats:

Wetland habitats	Non-wetland habitats
Wet Woodland	Upland Grassland
Watercourses	Woodland

- 2.1.2 Wet woodland is small patch present on northwest of the project boundary, and is confined by the marsh area to the north and the secondary woodland to the east, south and south-west parts. A number of mature trees Cleistocalyx nervosum and Acronychia pedunculata form the tree canopy, with other self-sown shrubs (including Psychotria asiatica, Ligustrum sinense and Glochidion lanceolarium) and trees (Aporosa dioica and Litsea monopetala). Whilst botanically it comprises of naturally regenerated secondary woodland and ground level are a series of small braided streams and weep points which even during the dry season remain wet. This creates a rather uncommon habitat in Hong Kong offering suitable conditions for a good assemblage of common wetland species. The wet woodland provides a good assemblage of micro-habitats, which is relatively undisturbed and has good linkages to other natural habitats. Several species of conversation importance were recorded in EIA report from this habitat: East Asian Porcupine, Leopard Cat, Red Muntjac, Two-striped Grass Frog, Small Snakehead, Somanniathelphusa zanklon, Dancing Shadow-emerald.
- 2.1.3 Seasonal watercourse running west to east in the eastern part of the area inside the Project boundary is shallower in gradient than those running off the hillside. This seasonal watercourse is heavily vegetated with wetland-associated herbs including *Commelina diffusa*, *Polygonum chinense*, *Colocasia esculenta* and *Dracaena sanderiana*. A mature tree of *Aquilaria sinensis* was recorded at the bank of the seasonal watercourse to the west of the Sandy Ridge Cemetery Office. Seasonal watercourses are restricted to the steeper slopes within the project boundary and are characterised by being entirely dry for much of the dry season. However, endemic crab *S. zanklon* population is supported by ephemeral watercourses close to the project boundary.
- Upland grassland is the major habitat within the project boundary. The semi-natural habitat is dominated by typical upland grassland species: fern *Dicranopteris pedata*, grass *Neyraudia reynaudiana*, *Miscanthus floridulus*, climbing vines *Smilax china*, *Smilax glabra*, and shrubs such as *Rhodomyrtus tomentosa*, *Breynia fruticosa* and *Helicteres angustifolia*. Approximately 30 flowering spikes of two orchid species Bamboo Orchid and Toothed Habenaria were recorded near the hill top in the northern part of this upland grassland. Golden-headed Cisticola, which is considered as Local Concern by Fellowes *et al.* (2002), was also recorded in upland grassland on Sandy Ridge, including a proved breeding record of fledged young in September 2013. In addition, numerous species of conservation interest were recorded in EIA report, such as East Asian Porcupine, Leopard Cat, Red Muntjac, Great Swift, Tamil Grass Dart, Small Three-ring and Small Grass Yellow.



2.1.5 Scattered patches of woodland are present throughout the assessment area, with the largest contiguous block located immediately to the east of the project boundary. These woodlands are relatively young with single-layered of canopy dominants (~10 – 15m tall) including *A. dioica*, *Bridelia tomentosa*, *Cinnamomum burmannii*, *Daphniphyllum calycinum*, *Litsea glutinosa*, *Rhus succedanea*, and *Zanthoxylum avicennae*. Such areas comprise secondary woodland which is largely derived from natural regeneration and colonisation of trees as a result of seed dispersal by birds and/or bats. A mature tree of *A. sinensis* is located at the woodland edge at the central part of the Project according to EIA report.

2.2 MONITORING MEASURES OF WETLAND HABITATS

- 2.2.1 Wetland habitats include wet woodland and watercourses. Monitoring surveys using standardised quantitative methodology will be conducted at fixed points. For seasonal watercourse, survey shall be conducted whenever the habitat appears.
- 2.2.2 Measures to respond to decreases in numbers of aquatic fauna using the wetland habitats and action and limit levels to trigger these measures are detailed in Table 1.

Action Level	Response	Limit Level	Response		
Reduction in	Investigate cause and if	Reduction	Investigate cause and if		
taxa diversity	cause identified as related	in taxa	cause identified as related		
by 30%	to the project instigate	diversity	to the project instigate		
	remedial action to remove	by 50%	remedial action.		
	or reduce source of				
	disturbance.				

Table 1 Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna

2.3 MONITORING MEASURES OF NON-WETLAND HABITATS

- 2.3.1 Non-wetland habitats consist of upland grassland and woodland. Monthly quantitative surveys of non-aquatic fauna will be conducted using standard route transect counts.
- 2.3.2 Measures to respond to decreases in numbers of non-aquatic fauna using the non-wetland habitats and action and limit levels to trigger these measures are detailed in Table 2.

Action Level	Response	Limit Level	Response		
Reduction in	Investigate cause and if	Reduction	Investigate cause and if		
species diversity	cause identified as related	in species	cause identified as related		
by 30%	to the project instigate	diversity by	to the project instigate		
	remedial action to remove	50%	remedial action.		
	or reduce source of				
	disturbance.				

Table 2 Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna



3 METHODOLOGY

The ecological survey includes all taxa being investigated in EIA report. Table 3 summarizes schedule of faunal surveys.

Month	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Mammals	√	√	√	√	√	√	√	√	√	√	$\sqrt{}$	\checkmark
Birds (day)	√	√	√	√	√	√	√	√	√	√	$\sqrt{}$	\checkmark
Birds (night)				√	$\sqrt{}$	\checkmark	√	√	√	$\sqrt{}$		
Herpetofauna				√	√	$\sqrt{}$	√	√	√	√		
Dragonflies			√	√	√	√	√	√	√	√		
Butterflies			√	√	√	$\sqrt{}$	√	√	√	√		
Aquatic fauna	√	√	√	√	√	$\sqrt{}$	√	√	√	√	$\sqrt{}$	\checkmark

Table 3 Survey Schedule

3.1 MAMMAL SURVEY

3.1.1 Mammal surveys will be conducted along the transects shown in Appendix 1 during both daytime and night time periods. Along with direct observations, other field signs, such as scats and tracks, will be searched and recorded if present.

3.2 BIRD SURVEY

3.2.1 Bird surveys will be conducted along the transects shown in Appendix 1 during the surveys, species and their vocalizing individuals recorded will be enumerated and recorded according to the habitat(s) they are utilising.

3.3 HERPETOFAUNA SURVEY

3.3.1 Reptile and amphibian surveys will be conducted along transects shown in Appendix 1 during surveys careful searches of appropriate microhabitats and refugia for reptiles and their vocalizing individuals will be undertaken and all reptiles observed will be identified and counted.

3.4 DRAGONFLY SURVEY

3.4.1 Dragonfly surveys will be conducted along transects shown in Appendix 1 during surveys all dragonflies seen will be identified and counted as accurately as possible.



3.5 BUTTERFLY SURVEY

3.5.1 Butterfly surveys will be conducted along transects shown in Appendix 1 during surveys all butterflies seen will be identified and counted as accurately as possible.

3.6 AQUATIC FAUNA SURVEY

3.6.1 Freshwater fishes and macro-invertebrates will be recorded by direct observation. All species trapped/recorded will be enumerated and identified (to the lowest taxonomic level possible), and the species of conservation importance photographed.



4 RESULT

This monitoring survey started on 18th November 2021, a sunny day. The day survey covered wetland and non-wetland areas. The survey was conducted by transect and at fixed points. All species seen will be identified and counted as accurately as possible.

Mammal

There was no mammal recorded in the monitoring area.

■ Bird

There were a total of 24 bird individuals from 12 species recorded in the monitoring area. No Golden-headed Cisticola was observed during the bird survey. One species of conservation interests was recorded in the monitoring area: *Milvus migrans* Black Kite 黑鳶.

■ Herpetofauna

There was no reptile species recorded in the monitoring area.

There was no amphibian species recorded in the monitoring area.

■ Butterfly

There were a total of 12 butterfly individuals from 5 species recorded in the monitoring area.

Dragonfly

There were a total of 4 odonate individuals from 1 species recorded in the monitoring area.

Freshwater communities

There was no freshwater community recorded in the monitoring area.



Picture 1 Upland grassland in monitoring area.



Picture 2Parathyma sulpitia Five-dot Sergeant 殘鍔線蛺蝶





Table 4 Result of mammal in survey

				18/11/2021					
Scientific Name	Common Name	Chinese Name	Conservation Status		on- land	v	Vetlan	d	
				UG	WL	MA	ww	WC	
		N/A							

 $[*]UG: Upland \ Grassland \ | \ WL: \ Woodland \ | \ MA: \ Marsh \ | \ WW: \ Wet \ Woodland \ | \ WC: \ Watercourse$

Table 5 Result of Avifauna in survey

	Common Name		Conservation Status	18/11/2021					
Scientific Name		Chinese Name		Non- wetland		Wetland			
				UG	WL	MA	ww	WC	
Milvus migrans	Black Kite	黑鳶	Fellowes et al. (2002): RC; Appendix 2 of CITES	1					
Amaurornis phoenicurus	White-breasted Waterhen	白胸苦惡鳥			1				
Spilopelia chinensis	Spotted Dove	珠頸斑鳩		2					
Dicrurus macrocercus	Black Drongo	黑卷尾					1		
Parus cinereus	Cinereous Tit	蒼背山雀		2					
Pycnonotus jocosus	Red-whiskered Bulbul	紅耳鵯		4					
Phylloscopus inornatus	Yellow-browed Warbler	黃眉柳鶯		2					
Prinia flaviventris	Yellow-bellied Prinia	黃腹鷦鶯			2				
Prinia inornata	Plain Prinia	純色鷦鶯			1				
Orthotomus sutorius	Common Tailorbird	長尾縫葉鶯			2				
Garrulax perspicillatus	Masked Laughingthrush	黑臉噪鶥						4	
Motacilla alba	White Wagtail	白鶺鴒		2					

 $[*]UG: Upland \ Grassland \ | \ WL: \ Woodland \ | \ MA: \ Marsh \ | \ WW: \ Wet \ Woodland \ | \ WC: \ Watercourse$



Table 6 Result of reptile in survey

Scientific Name				18/11/2021					
	Common Name	Chinese Name	Conservation Status	Non- wetland		Wetland		ıd	
				UG	WL	MA	ww	WC	
		N/A							

^{*}UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

Table 7 Result of amphibian in survey

		Common Name Chinese Name		18/11/2021					
	Scientific Name			Conservatio n Status	Non- wetland		Wetland		d
					UG	WL	MA	ww	WC
			N/A						

^{*}UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

Table 8 Result of butterfly in survey

	Common Name	mmon Name	Conservatio n Status	18/11/2021					
Scientific Name				Non- wetland		Wetland			
				UG	WL	MA	ww	WC	
Jamides bochus	Dark Cerulean	雅灰蝶		4					
Rapala manea	Slate Flash	燕灰蝶		1					
Parathyma sulpitia	Five-dot Sergeant	殘鍔線蛺蝶		2					
Neptis hylas	Common Sailer	中環蛺蝶		3					
Abisara echerius	Plum Judy	蛇目褐蜆蝶		2					

^{*}UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

Table 9 Result of Odonate in survey

				18/11/2021					
Scientific Name	Common Name			Non- wetland		Wetland		d	
				UG	WL	MA	ww	WC	
Pantala flavescens	Wandering Glider	黄蜻		2				2	

^{*}UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse



Table 10 Result of freshwater communities in survey

				18/11/2021					
Scientific Name	Common Name	Chinese Name	Conservation Status		n- land	v	Vetlan	d	
				UG	WL	MA	ww	WC	
		N/A							

 $[*]UG: Upland \ Grassland \ | \ WL: \ Woodland \ | \ MA: \ Marsh \ | \ WW: \ Wet \ Woodland \ | \ WC: \ Watercourse$



5 DISCUSSION

Data analysis was carried out to compare with the biodiversity within the site boundary in the same month over years. General description of the ecological conditions is first revealed in terms of abundance as well as species richness, following by statistical analysis of the existing database. The result is considered as significant whenever the drop of diversity indexes exceeds the percentages mentioned in previous sections 2.2 and 2.3.

5.1 Total abundance and species richness in November over years were compared to show the trends. Figures 1 and 2 indicate the total species richness and total abundance within the site boundary respectively.

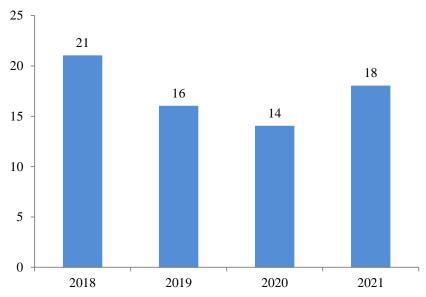


Figure 1: Bar chart showing the total species richness within site boundary from 2018 to 2021 (Actual quantity annotated at the top of each bar)

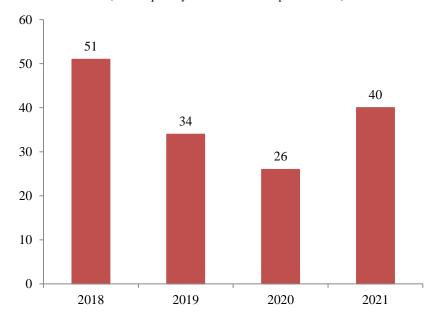


Figure 2: Bar chart showing the total abundance within site boundary from 2018 to 2021 (Actual quantity annotated at the top of each bar)



As results in section 4 were categorized by taxa, a detailed breakdown of each taxon is shown in figure 3 to further investigate the trend of specific taxa over contract period.

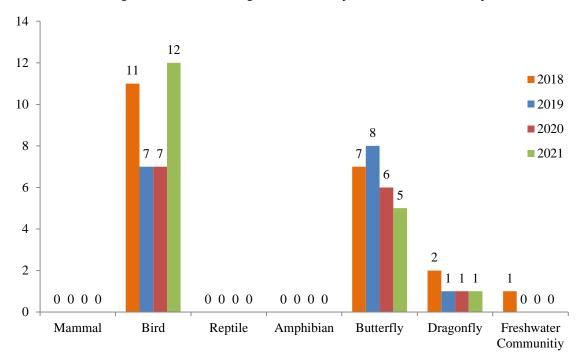


Figure 3: Bar chart showing the species richness within site boundary by taxa from 2018 to 2021 (Actual quantity annotated at the top of each bar)

5.3 According to EM&A Manual, monitoring measures was determined by the species diversity of types of sensitive habitats, i.e. non-wetland and wetland habitats. Abundance and species richness by habitat type in November over years were compared in Figures 4 and 5.

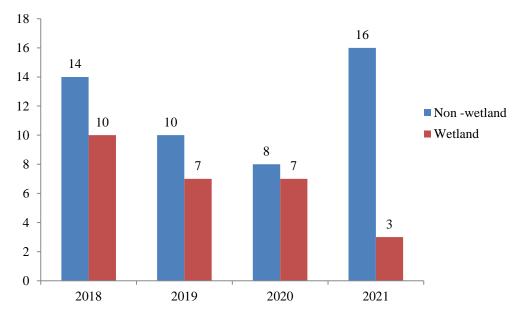


Figure 4: bar chart showing the species richness based on habitat type from 2018 to 2021 (Actual quantity annotated at the top of each bar)




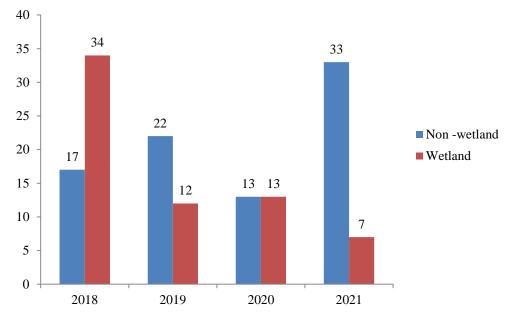


Figure 5: bar chart showing the abundance based on habitat type from 2018 to 2021 (Actual quantity annotated at the top of each bar)

After analysing survey results in November from 2018 to 2021, there were a slight decrease in abundance and a drop in species richness for wetland habitat. These reductions could be due to natural fluctuation. Yet, good site practice during construction, with reference to EM&A Manual, is required to prevent or alleviate environmental impacts. For instance, the size of work areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works. Unnecessary site clearance should be avoided as well. In addition, implementing proper waste disposal is necessary to reduce contamination to water and soil. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.



Appendix I – Transect Routes for Contract CV/2016/10

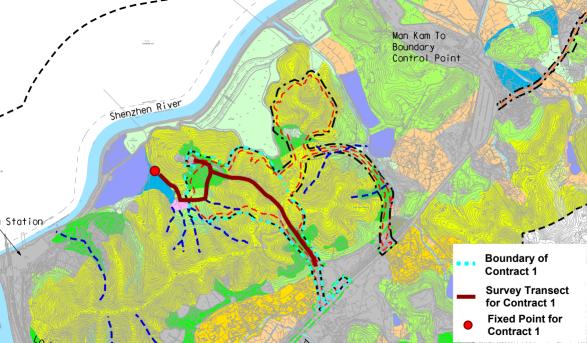

Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery Monthly Environmental Monitoring & Audit Report (No.40) – November 2021



Ecological Survey Report for Contract CV/2017/02



Contract No. CV/2017/02 Development of Columbarium at Sandy Ridge Cemetery – Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

Monthly Report of Ecologically Sensitive Habitats Monitoring – November 2021

Revision Date of issue	0 06 Dec 2021	
Prepared by	Alan Lam	积
Reviewed by	Hoiki Leung	Mark
Verified by	Mike Leung	

1



Table of Contents

1	INT	RODUCTION	4
	1.1	BACKGROUND	4
	1.2	OBJECTIVE	4
2	ECC	DLOGICALLY SENSITIVE HABITATS	5
	2.1	DESCRIPTION OF HABITATS	5
	2.2	MONITORING MEASURES OF WETLAND HABITATS	ϵ
	2.3	MONITORING MEASURES OF NON-WETLAND HABITATS	6
3	ME'	THODOLOGY	7
	3.1	MAMMAL SURVEY	7
	3.2	BIRD SURVEY	7
	3.3	HERPETOFAUNA SURVEY	7
	3.4	DRAGONFLY SURVEY	7
	3.5	BUTTERFLY SURVEY	8
	3.6	AQUATIC FAUNA SURVEY	8
4	RES	SULT	9
5	DIS	CUSSION	13
Арр	oendix l	I – Transect Routes for Contract CV/2017/02	16



LIST OF TABLE	
Table 1	Action and Limit Levels and Responses to Evidence of Declines
	in Aquatic Fauna
Table 2	Action and Limit Levels and Responses to Evidence of Declines
	in Non-Aquatic Fauna
Table 3	Survey Schedule
Table 4	Result of mammal in survey
Table 5	Result of Avifauna in survey
Table 6	Result of reptile in survey
Table 7	Result of amphibian in survey
Table 8	Result of butterfly in survey
Table 9	Result of Odonate in survey
Table 10	Result of freshwater communities in survey

LIST OF APPENDIX			
Appendix I	Transect Routes for Contract CV/2017/02		

LIST OF FIGURE	<u>ES</u>
Figure 1	Bar chart showing the total species richness within site boundary
	from 2018 to 2021
Figure 2	Bar chart showing the total abundance within site boundary from
	2018 to 2021
Figure 3	Bar chart showing the species richness within site boundary by
	taxa from 2018 to 2021
Figure 4	Bar chart showing the species richness based on habitat type
	from 2018 to 2021
Figure 5	Bar chart showing the abundance based on habitat type from
	2018 to 2021



1 INTRODUCTION

1.1 BACKGROUND

- 1.1.1 The main objective of the proposed site formation and associated infrastructural works for development of columbarium, crematorium (C&C) and related facilities at Sandy Ridge Cemetery is to increase the public cremation services and supply of public niches to meet the future demand.
- 1.1.2 The project includes site formation and associated works for development of C&C facilities at the Sandy Ridge Cemetery, road works within Sandy Ridge Cemetery, widening a section of Lin Ma Hang Road (from 6.5m to 7.3m), provision of off-site pick-up/drop-off points for shuttle buses as well as barging point at Siu Lam, Lok On Pai.
- 1.1.3 The Environmental Impact Assessment (EIA) report, including Environmental Monitoring and Audit Manual (EM&A Manual), was approved with conditions on 8 August 2016 (Register No.: AEIAR-198/2016). EPD issued an Environmental Permit (EP) for the Project (EP-534/2017) on 7 April 2017, variation of EP (EP-534/2017/A) were issued on 24 December 2018.
- 1.1.4 According to Clause 3.1 of the EP (EP-534/2017/A), "The Permit Holder shall implement the EM&A programme in accordance with the procedures and requirements as set out in the EM&A Manual. Any changes to the programme shall be justified by the ET Leader and verified by the IEC as conforming to the information and requirements contained in the EM&A Manual before submission to the Director for approval".
- 1.1.5 This Ecologically Sensitive Habitats Monitoring Methodology articulates the protocol of monitoring the ecology of concerned habitats as specified in EM&A Manual.

1.2 OBJECTIVE

- 1.2.1 According to approved EIA report (AEIAR-198/2016), habitat types within project boundary comprise of watercourse, grassland, upland grassland, plantation, woodland and developed area. Natural habitats were of moderate ecological value in terms of species diversity, species rarity, species abundance, ecological linkage as well as nursery. Moreover, 0.3ha of wet woodland on the northern side of Sandy Ridge was deemed habitat with high ecological value. Four types of habitats were regarded as ecologically sensitive habitats, namely wet woodland, watercourses, upland grassland and woodland. Considering human disturbance in upcoming construction and operation phases, ecologically sensitive habitats shall be monitored in accordance with EM&A Manual.
- 1.2.2 The objective of ecologically sensitive habitats monitoring is to evaluate the effectiveness of measures to minimize impacts on concerned habitats from disturbance and pollution.



2 ECOLOGICALLY SENSITIVE HABITATS

2.1 DESCRIPTION OF HABITATS

2.1.1 In order to monitor the effectiveness of the measures to the minimise impact on ecologically sensitive habitats from disturbance and pollution, monthly monitoring during construction and operation phases is required as specified in EM&A Manual. Standard faunal transect and sampling surveys cover both wetland and non-wetland habitats:

Wetland habitats	Non-wetland habitats
Wet Woodland	Upland Grassland
Watercourses	Woodland

- 2.1.2 Wet woodland is small patch present on northwest of the project boundary, and is confined by the marsh area to the north and the secondary woodland to the east, south and south-west parts. A number of mature trees Cleistocalyx nervosum and Acronychia pedunculata form the tree canopy, with other self-sown shrubs (including Psychotria asiatica, Ligustrum sinense and Glochidion lanceolarium) and trees (Aporosa dioica and Litsea monopetala). Whilst botanically it comprises of naturally regenerated secondary woodland and ground level are a series of small braided streams and weep points which even during the dry season remain wet. This creates a rather uncommon habitat in Hong Kong offering suitable conditions for a good assemblage of common wetland species. The wet woodland provides a good assemblage of micro-habitats, which is relatively undisturbed and has good linkages to other natural habitats. Several species of conversation importance were recorded in EIA report from this habitat: East Asian Porcupine, Leopard Cat, Red Muntjac, Two-striped Grass Frog, Small Snakehead, Somanniathelphusa zanklon, Dancing Shadow-emerald.
- 2.1.3 Seasonal watercourse running west to east in the eastern part of the area inside the Project boundary is shallower in gradient than those running off the hillside. This seasonal watercourse is heavily vegetated with wetland-associated herbs including *Commelina diffusa*, *Polygonum chinense*, *Colocasia esculenta* and *Dracaena sanderiana*. A mature tree of *Aquilaria sinensis* was recorded at the bank of the seasonal watercourse to the west of the Sandy Ridge Cemetery Office. Seasonal watercourses are restricted to the steeper slopes within the project boundary and are characterised by being entirely dry for much of the dry season. However, endemic crab *S. zanklon* population is supported by ephemeral watercourses close to the project boundary.
- Upland grassland is the major habitat within the project boundary. The semi-natural habitat is dominated by typical upland grassland species: fern *Dicranopteris pedata*, grass *Neyraudia reynaudiana*, *Miscanthus floridulus*, climbing vines *Smilax china*, *Smilax glabra*, and shrubs such as *Rhodomyrtus tomentosa*, *Breynia fruticosa* and *Helicteres angustifolia*. Approximately 30 flowering spikes of two orchid species Bamboo Orchid and Toothed Habenaria were recorded near the hill top in the northern part of this upland grassland. Golden-headed Cisticola, which is considered as Local Concern by Fellowes *et al.* (2002), was also recorded in upland grassland on Sandy Ridge, including a proved breeding record of fledged young in September 2013. In addition, numerous species of conservation interest were recorded in EIA report, such as East Asian Porcupine, Leopard Cat, Red Muntjac, Great Swift, Tamil Grass Dart, Small Three-ring and Small Grass Yellow.



2.1.5 Scattered patches of woodland are present throughout the assessment area, with the largest contiguous block located immediately to the east of the project boundary. These woodlands are relatively young with single-layered of canopy dominants (~10 – 15m tall) including *A. dioica*, *Bridelia tomentosa*, *Cinnamomum burmannii*, *Daphniphyllum calycinum*, *Litsea glutinosa*, *Rhus succedanea*, and *Zanthoxylum avicennae*. Such areas comprise secondary woodland which is largely derived from natural regeneration and colonisation of trees as a result of seed dispersal by birds and/or bats. A mature tree of *A. sinensis* is located at the woodland edge at the central part of the Project according to EIA report.

2.2 <u>MONITORING MEASURES OF WETLAND HABITATS</u>

- 2.2.1 Wetland habitats include wet woodland and watercourses. Monitoring surveys using standardised quantitative methodology will be conducted at fixed points. For seasonal watercourse, survey shall be conducted whenever the habitat appears.
- 2.2.2 Measures to respond to decreases in numbers of aquatic fauna using the wetland habitats and action and limit levels to trigger these measures are detailed in Table 1.

Action Level	Response	Limit Level	Response
Reduction in	Investigate cause and if	Reduction	Investigate cause and if
taxa diversity	cause identified as related	in taxa	cause identified as related
by 30%	to the project instigate	diversity	to the project instigate
	remedial action to remove	by 50%	remedial action.
	or reduce source of		
	disturbance.		

Table 1 Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna

2.3 MONITORING MEASURES OF NON-WETLAND HABITATS

- 2.3.1 Non-wetland habitats consist of upland grassland and woodland. Monthly quantitative surveys of non-aquatic fauna will be conducted using standard route transect counts.
- 2.3.2 Measures to respond to decreases in numbers of non-aquatic fauna using the non-wetland habitats and action and limit levels to trigger these measures are detailed in Table 2.

Action Level	Response	Limit Level	Response
Reduction in	Investigate cause and if	Reduction	Investigate cause and if
species diversity	cause identified as related	in species	cause identified as related
by 30%	to the project instigate	diversity by	to the project instigate
	remedial action to remove	50%	remedial action.
	or reduce source of		
	disturbance.		

Table 2 Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna



3 METHODOLOGY

The ecological survey includes all taxa being investigated in EIA report. Table 3 summarizes schedule of faunal surveys.

Month	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Mammals	$\sqrt{}$											
Birds (day)	√	√	√	√	√	$\sqrt{}$	√	√	√	√	$\sqrt{}$	\checkmark
Birds (night)				$\sqrt{}$								
Herpetofauna				$\sqrt{}$								
Dragonflies			$\sqrt{}$									
Butterflies			$\sqrt{}$	$\sqrt{}$	$\sqrt{}$	$\sqrt{}$	√	$\sqrt{}$	$\sqrt{}$	$\sqrt{}$		
Aquatic fauna	√	√	$\sqrt{}$	$\sqrt{}$	$\sqrt{}$	$\sqrt{}$	√	$\sqrt{}$	$\sqrt{}$	$\sqrt{}$	$\sqrt{}$	$\sqrt{}$

Table 3 Survey Schedule

3.1 MAMMAL SURVEY

3.1.1 Mammal surveys will be conducted along the transects shown in Appendix 1 during both daytime and night time periods. Along with direct observations, other field signs, such as scats and tracks, will be searched and recorded if present.

3.2 BIRD SURVEY

3.2.1 Bird surveys will be conducted along the transects shown in Appendix 1 during the surveys, species and their vocalizing individuals recorded will be enumerated and recorded according to the habitat(s) they are utilising.

3.3 HERPETOFAUNA SURVEY

3.3.1 Reptile and amphibian surveys will be conducted along transects shown in Appendix 1 during surveys careful searches of appropriate microhabitats and refugia for reptiles and their vocalizing individuals will be undertaken and all reptiles observed will be identified and counted.

3.4 DRAGONFLY SURVEY

3.4.1 Dragonfly surveys will be conducted along transects shown in Appendix 1 during surveys all dragonflies seen will be identified and counted as accurately as possible.



3.5 BUTTERFLY SURVEY

3.5.1 Butterfly surveys will be conducted along transects shown in Appendix 1 during surveys all butterflies seen will be identified and counted as accurately as possible.

3.6 AQUATIC FAUNA SURVEY

3.6.1 Freshwater fishes and macro-invertebrates will be recorded by direct observation. All species trapped/recorded will be enumerated and identified (to the lowest taxonomic level possible), and the species of conservation importance photographed.



4 RESULT

This monitoring survey started on 18th November 2021, a sunny day. The day survey covered wetland and non-wetland areas. The survey was conducted by transect and at fixed point. All species seen will be identified and counted as accurately as possible.

Mammal

There was no mammal recorded in the monitoring area.

■ Bird

There were total of 20 bird individuals from 6 species recorded in the monitoring area. No Golden-headed Cisticola was observed during the bird survey.

Herpetofauna

There was no reptile recorded in the monitoring area.

There was no amphibian recorded in the monitoring area.

Butterfly

There were a total of 7 butterfly individuals from 5 species recorded in the monitoring area.

■ Dragonfly

There were a total of 7 odonate individuals from 2 species recorded in the monitoring area.

Freshwater communities

There were 2 species of freshwater fish recorded in the monitoring area.



Picture 1
Watercourse in monitoring area.



Picture 2
The engineering site in monitoring area.





Table 4 Result of mammal in survey

Scientific Name	Common Name		Conservation Status		18/	18/11/2021				
				UG	WL	MA	ww	WC		
		N/A								

^{*}UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

Table 5 Result of Avifauna in survey

Scientific Name	Common Name Chinese Conservation Name Status			18/11/2021					
		UG	WL	MA	ww	WC			
Hypothymis azurea	Black-naped Monarch	黑枕王鶲		1					
Parus cinereus	Cinereous Tit	蒼背山雀		2					
Phylloscopus proregulus	Pallas's Leaf Warbler	黄腰柳鶯		1					
Phylloscopus inornatus	Yellow-browed Warbler	黄眉柳鶯		2			1		
Pycnonotus jocosus	Red-whiskered Bulbul	紅耳鵯		5			3		
Garrulax perspicillatus	Masked Laughingthrush	黑臉噪鶥			5				

^{*}UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

Table 6 Result of reptile in survey

Scientific Name	Common Name		Conservation Status	18/11/2021							
				UG	WL	MA	ww	WC			
		N/A						·			

 $[*]UG: Upland \ Grassland \ | \ WL: \ Woodland \ | \ MA: \ Marsh \ | \ WW: \ Wet \ Woodland \ | \ WC: \ Watercourse$

Table 7 Result of amphibian in survey

Scientific Name	Common Name	Chinese Conservation 18/11/2021 Name Status						
				UG	WL	MA	ww	WC
		N/A						

 $[*]UG: Upland\ Grassland\ |\ WL:\ Woodland\ |\ MA:\ Marsh\ |\ WW:\ Wet\ Woodland\ |\ WC:\ Watercourse$



Table 8 Result of butterfly in survey

Scientific Name	Common Name		Conservatio n Status	18/11/2021					
		1 (unic		UG	WL	MA	ww	WC	
Neptis hylas	Common Sailor	中環蛺蝶		1					
Mycalesis mineus	Dark Brand Bush Brown	小眉眼蝶					2		
Papilio polytes	Common Mormon	玉帶鳳蝶					1		
Delias pasithoe	Red-base Jezebel	報喜斑粉蝶		2					
Abisara echerius	Plum Judy	蛇目褐蜆蝶		1					

 $[*]UG: Upland\ Grassland\ |\ WL:\ Woodland\ |\ MA:\ Marsh\ |\ WW:\ Wet\ Woodland\ |\ WC:\ Watercourse$

Table 9 Result of Odonate in survey

Scientific Name	Common Name		Conservatio n Status	18/11/2021							
				UG	WL	MA	ww	WC			
Orthetrum pruinosum	Common Red Skimmer	赤褐灰蜻				1					
Pantala flavescens	Wandering Glider	黄蜻				6					

^{*}UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

Table 10 Result of freshwater communities in survey

Scientific Name	Common Name	Chinese Name	Conservatio n Status	18/11/2021					
				UG	WL	MA	ww	WC	
Gambusia affinis	Mosquito fish	食蚊魚						+	
Puntius semifasciolatus	Chinese Barb	五線無鬚鯉						+	

^{*}UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

⁺ Species appeared but uncountable



5 DISCUSSION

Data analysis was carried out to compare with the biodiversity within the site boundary in the same month over years. General description of the ecological conditions is first revealed in terms of abundance as well as species richness, following by statistical analysis of the existing database. The result is considered as significant whenever the drop of diversity indexes exceeds the percentages mentioned in previous sections 2.2 and 2.3.

5.1 Total abundance and species richness in November over years were compared to show the trends. Figures 1 and 2 indicate total species richness and total abundance within the site boundary respectively.

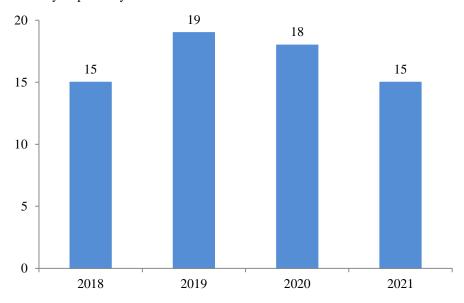


Figure 1: Bar chart showing the total species richness within site boundary from 2018 to 2021 (Actual quantity annotated at the top of each bar)

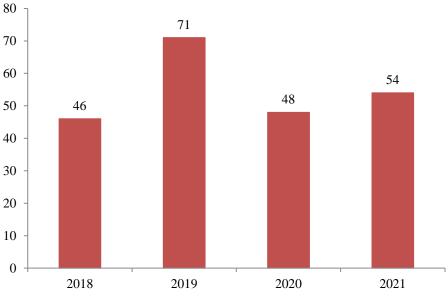


Figure 2: Bar chart showing the total abundance within site boundary from 2018 to 2021 (Actual quantity annotated at the top of each bar)



As results in section 4 were categorized by taxa, a detailed breakdown of each taxon is shown in figure 3 to further investigate the trend of specific taxa over contract period.

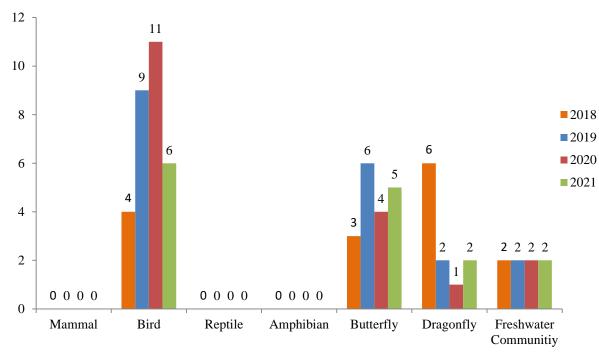


Figure 3: Bar chart showing the species richness within site boundary by taxa from 2018 to 2021 (Actual quantity annotated at the top of each bar)

5.3 According to EM&A Manual, monitoring measures was determined by the species diversity of types of sensitive habitats, i.e. non-wetland and wetland habitats. Abundance and species richness by habitat type in November over years were compared in figures 4 and 5.

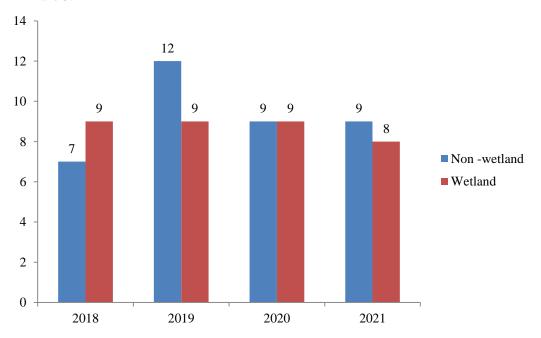


Figure 4: bar chart showing the species richness based on habitat type from 2018 to 2021 (Actual quantity annotated at the top of each bar)




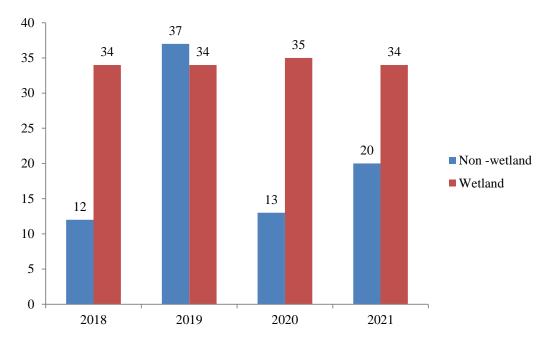


Figure 5: bar chart showing the abundance based on habitat type from 2018 to 2021 (Actual quantity annotated at the top of each bar)

5.4 After analysing survey results in November 2018 to 2021, no significant drop in species richness and abundance is observed for wetland and non-wetland habitats. Maintaining good site practice during construction, with reference to EM&A Manual, is still required to prevent or alleviate environmental impacts. For instance, the size of work areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works. Unnecessary site clearance should be avoided as well. In addition, implementing proper waste disposal is necessary to reduce contamination to water and soil. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.



Appendix I – Transect Routes for Contract CV/2017/02

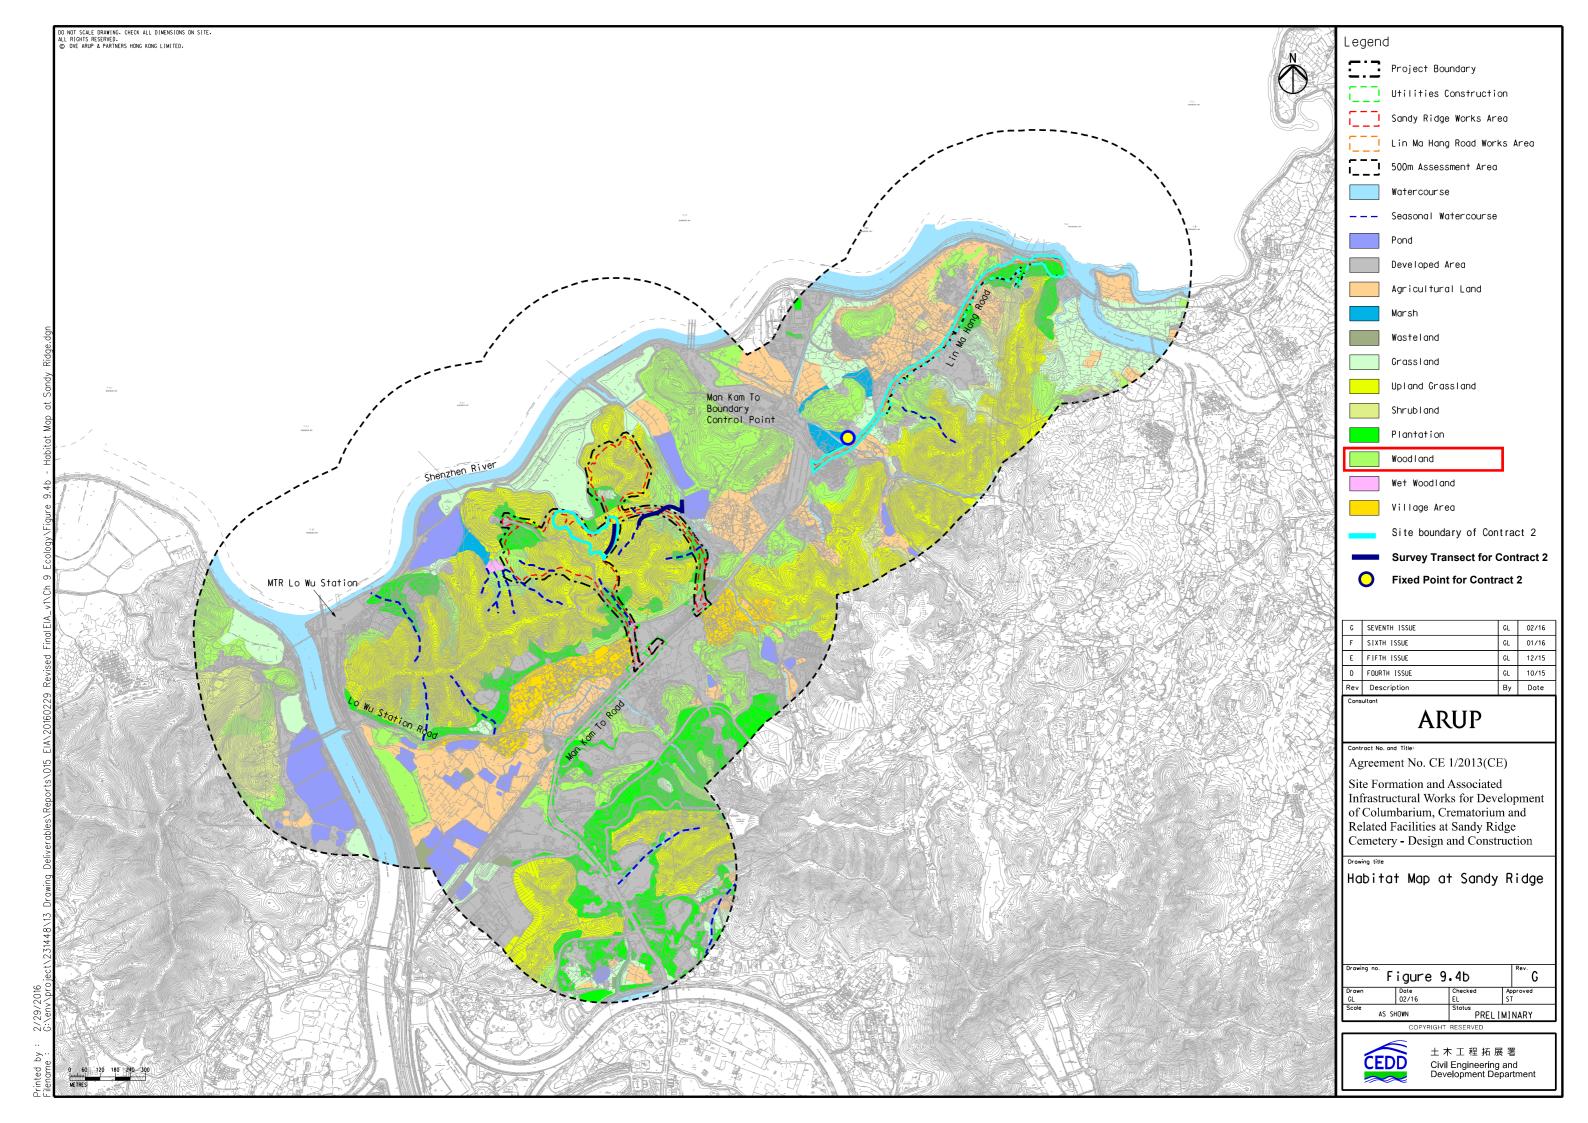



Appendix L

Landscape & Visual Inspection Checklist



Contract No. CV/2016/10

Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery

Landscape and Visual Impact Assessment Checklist for Site Audit

Date/ Time: 15/11/2021 15:00 Weather: Fine/ Overcast/ Rain/ Windy

Item	Mitigation Measures	Im	olemen	tation	Actions/ Remarks
		Yes	No	N/A	
1	Landscape and Visual				
1.1	Is the construction period become shortened?			✓	Under review.
1.2	Is the work site confined within site boundaries and without encroaching into the landscape resources offsite?	✓			
1.3	Is the site kept clean and tidy (E.g. storage of materials, location and appearance of site accommodation being well positioned)	✓			
1.4	Is the construction site screened properly by hoardings or noise barriers in visually unobstructed colours?	✓			
1.5	Is the erosion and dust control for exposed soil well performed during excavation work? (E.g. Exposed soil shall be covered or "camouflaged" and watered frequently. Areas that are expected to be left with bare soil for a long period of time should be hydro seeded and / or covered with suitable protective fabrics.)	✓			
1.6	Are the woodland, plantation and other vegetation being protected and preserved in accordance with DEVB TC(W) No. 07/2015(E.g. Set up Tree Protection Zone)?	✓			
1.7	Are the trees which are in direct conflict with the development proposal being transplanted as far as practical in accordance with and DEVB TC(W) No. 07/2015?	✓			
1.8	Are compensatory planting for trees being provided to compensate the trees felled in accordance with DEVB TC(W) No. 07/2015?	✓			
1.9	Are precautionary control measures to protect natural streams and rivers from adverse impact being implemented in accordance with ETWWB TCW No. 5/2005? (E.g. Construction debris and spoil should be covered up and properly disposed)	✓			
1.10	Is light and glare control such as hooding being implemented during construction and operation to minimize light pollution and night time glare? (E.g. All security floodlights for construction sites should be equipped with adjustable shield, frosted diffusers and reflective covers)	✓			

Summary / Remarks:



Follow up actions taken by Contractor for previous comments:

N/A

New observation:

N/A


Reminders:

- 1. Contractor is reminded to set up TPZ of proper size and with appropriate material around retain trees according to approved method statement.
- 2. Contractor is reminded to prevent the construction material pile within TPZ and ensure no works is allowed within the TPZ.
- 3. Transplanted trees T2465, T2468 and T2928 were in fair health condition with normal foliage color and density. Contractor is reminded to provide proper maintenance according to approved method statement.

Photo Record:

Fig A. Fig B.







General view (2)

Fig C. Fig D.



General view (3)



General view (4)





Transplanted tree (T-2465)



Transplanted tree (T-2468)



Transplanted tree (T-2928)



Contract No. CV/2017/02

Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery

Development of Columbarium at Sandy Ridge Cemetery –

Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

Date/ Time: 15/11/2021 16:00 Weather: Fine/ Overcast/ Rain/ Windy

Landscape and Visual Impact Assessment Checklist for Site Audit

Item	Mitigation Measures	Im	olemen	tation	Actions/ Remarks
		Yes	No	N/A	
1	Landscape and Visual				_
1.1	Is the construction period become shortened?			✓	Under review
1.2	Is the work site confined within site boundaries and without encroaching into the landscape resources offsite?	√			
1.3	Is the site kept clean and tidy (E.g. storage of materials, location and appearance of site accommodation being well positioned)	✓			
1.4	Is the construction site screened properly by hoardings or noise barriers in visually unobstructed colours?	✓			
1.5	Is the erosion and dust control for exposed soil well performed during excavation work? (E.g. Exposed soil shall be covered or "camouflaged" and watered frequently. Areas that are expected to be left with bare soil for a long period of time should be hydro seeded and / or covered with suitable protective fabrics.)	✓			
1.6	Are the woodland, plantation and other vegetation being protected and preserved in accordance with DEVB TC(W) No. 07/2015(E.g. Set up Tree Protection Zone)?	✓			
1.7	Are the trees which are in direct conflict with the development proposal being transplanted as far as practical in accordance with and DEVB TC(W) No. 07/2015?			✓	
1.8	Are compensatory planting for trees being provided to compensate the trees felled in accordance with DEVB TC(W) No. 07/2015?			✓	
1.9	Are precautionary control measures to protect natural streams and rivers from adverse impact being implemented in accordance with ETWWB TCW No. 5/2005? (E.g. Construction debris and spoil should be covered up and properly disposed)			✓	
1.10	Is light and glare control such as hooding being implemented during construction and operation to minimize light pollution and night time glare? (E.g. All security floodlights for construction sites should be equipped with adjustable shield, frosted diffusers and reflective covers)			✓	

Summary / Remarks:

Follow up actions taken by Contractor for previous comments:



N/A

New Observation:

N/A

Reminders:

1. Contractor is reminded to set up TPZ of proper size and with appropriate material around retain trees according to approved method statement. Contractor should prevent any construction material pile within TPZ and ensure no works is allowed within the TPZ.

Photo Record:

Fig A. Fig B.





General view (1)

General view (2)





General view (3)

General view (4)



Signature:

		Signature	Date
Recorded by	Registered Landscape Architect	STATE OF THE PROPERTY OF THE P	17 Nov 2021
Checked by	Environmental Team Leader	Am	7 Dec 2021
Checked by	Independent Environmental Checker		13 Dec 2021



Appendix M

Monthly Summary Waste Flow Table

Monthly Summary Waste Flow Table for August 2021

Department: Civil Engineering and Development Department Contract No.: CV/2016/10

Contract Title: Site Formation and Assoicated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery

Commencement Date: 15-Dec-2017 Estimated completion Date 22-Dec-2023 Estimated Contract Sum: 780M

Month	Actual Quantities of Inert C&D Materials Generated Monthly					Actual Quantities of C&D Wastes Generated Monthly					
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan	3.044	0.000	0.525	0.000	0.119	2.400	0.000	0.000	0.000	0.000	0.022
Feb	2.419	0.000	0.958	0.000	0.135	1.326	0.000	0.000	0.000	0.000	0.030
Mar	8.541	0.000	0.754	0.525	6.344	1.968	0.000	0.000	0.000	0.000	0.242
Apr	4.699	0.000	1.213	1.762	3.681	1.567	0.000	0.000	0.000	0.000	0.073
May	5.230	0.000	0.000	0.000	5.230	0.000	0.000	0.000	0.000	0.000	0.076
June	5.712	0.000	0.000	0.000	3.594	2.118	0.000	0.000	0.000	0.000	0.068
Sub-total	29.645	0.000	3.450	2.287	19.103	9.379	0.000	0.000	0.000	0.000	0.511
July	5.857	0.000	0.000	0.000	3.739	2.118	0.000	0.000	0.000	0.000	0.030
Aug	5.674	0.000	0.000	0.000	5.563	0.111	0.000	0.000	0.000	0.000	0.035
Sept	5.490	0.000	0.620	0.000	3.840	1.030	0.000	0.000	0.000	0.000	0.030
Oct	4.170	0.000	0.250	0.000	3.293	0.627	0.000	0.000	0.000	0.000	0.025
Nov	5.166	0.000	0.250	0.000	4.166	0.750	0.000	0.000	0.000	0.000	0.035
Dec											
Total	56.002	0.000	4.570	2.287	39.704	14.015	0.000	0.000	0.000	0.000	0.666

Notes: (1) The waste flow table should cover the whole construction period of the Contract.

- (2) The original estimates of the C&D materials should be the estimates at contract commencement and should not be altered during construction.
- (3) Inert C&D materials that are specified in the Contract to be imported for use at the Site shall be separately indicated.
- (4) The yearly estimates of the C&D materials should be updated as appropriate taking into account the latest works programme etc.
- (5) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
- (6) Broken concrete for recycling into aggregates.

Name of Department: CEDD

Monthly Summary Waste Flow Table for 2021

	A	ctual Quantities	of Inert C&D M	Iaterials Gener	ated Monthl	у	Actual Q	uantities of C	C&D Wastes	Generated	l Monthly
Month	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in Litre)	(in '000kg)
JAN	741.560	0.000	0.000	0.000	741.56	0.000	0.000	0.000	0.000	0.000	8.770
FEB	672.150	0.000	0.000	0.000	672.15	0.000	0.000	0.000	0.000	0.000	4.700
MAR	1512.670	0.000	0.000	0.000	1512.67	0.000	0.000	0.000	0.000	0.000	9.380
APRIL	1467.270	0.000	0.000	0.000	1467.27	0.000	0.000	0.000	0.000	0.000	27.700
MAY	1136.740	0.000	0.000	0.000	1136.74	0.000	0.000	0.000	0.000	0.000	13.170
JUN	901.090	0.000	0.000	0.000	901.09	0.000	0.000	0.000	0.000	200.000	8.040
Sub Total	6431.480	0.000	0.000	0.000	6431.480	0.000	0.000	0.000	0.000	200.000	71.760
JUL	1042.940	0.000	0.000	0.000	1042.94	0.000	0.000	0.107	0.000	0.000	4.730
AUG	2258.880	0.000	0.000	0.000	2258.88	0.000	0.000	0.000	0.000	0.000	9.340
SEP	1192.890	0.000	0.000	0.000	1192.89	0.000	0.000	0.000	0.000	0.000	8.200
ОСТ	1020.530	0.000	0.000	0.000	1020.53	0.000	0.000	0.000	0.000	0.000	4.580
NOV	547.910	0.000	0.000	0.000	547.91	0.000	0.000	0.090	0.000	0.000	8.240
DEC											
Total	12494.630	0.000	0.000	0.000	12494.630	0.000	0.000	0.197	0.000	200.000	106.850

Notes: * estimated quantity (pending from EPD NENT (soil) to update the actual quantity)

Name of Department: CEDD

	Fore	cast of Total Qu	antities of C&	D Materials	to be Generat	ed from the	Contract (see	Note 4)		
Total Quantity Generated	Hard Rocks and Large Broken Concrete	Reused in the Contract	Reused in Other Projects	Disposed as Public Fill	Imported Fill	Metal	Paper / cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
0	0	0	0	0	0	0	0	0	1	0

Notes:

- (1) The performance targets are given in PS clause 6(14) above.
- (2) The waste flow table shall also include C&D materials that are specified in the Contractor to be imported for use at the Site.
- (3) Plastic refer to plastic bottles/containers, plastic sheets/foam from packaging material.
- (4) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature
- Hard Rocks and Large Broken Concrete = Cannot be defined at this stage
- Imported Fill = Estimated by the Contractor
- Metal = Estimated by the Contractor
- Paper/cardboard packaging = Estimated by the Contractor
- Plastics = Estimated by the Contractor
- Chemical Waste = Estimated by the Contractor (Spent lubricating oil, assume density 0.9kg/L)
- Other, e.g. general refuse = Estimated by the Contractor



Appendix N

Complaint Log



Complaint Log for Contract 1

Log ref.	Date of complaint	Complaint route	Reference no.	Complaint nature	Investigation fining	Status
1	15-Apr-21	EPD	EPD Ref.: EP3/N07/RN/8770-21	Air Quality	Non-project related	Interim IR was submitted to EPD on 22 April 2021 and included in EM&A Report – Apr 2021

Complaint Log for Contract 2

Log ref.	Date of complaint	Complaint route	Reference no.	Complaint nature	Investigation fining	Status
1	4-Sep-20	EPD	EPD Ref.: EP/RN/419300	Water quality	Non-project related	Interim IR was submitted to EPD on 14 Sep 2020 Included in EM&A Report – Sep 2020
2	15-Apr-21	EPD	EPD Ref.: EP3/N07/RN/8770-21	Air Quality	Non-project related	Interim IR was submitted to EPD on 22 April 2021 and



Appendix O

Implementation Schedule for Environmental Mitigation Measures

Environmental Mitigation Implementation Schedule – Sandy Ridge

EIA Dof	Pagamandad Mitigation Magazana			Leastion /		Dogwinomonta	Implementation
EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended	Implementation	Location / Timing	Implementation	Requirements and / or standards to	Implementation status and remark*
		Measures & Main	Agent	Tilling	Stage	be achieved	status and remark*
		Concerns to address				be acmeved	
Common N	 Iitigation Measures (Applicable to ALL Project Components, including DPs and Non-D.						
	on Dust Impact						
\$4.4.5.2	The contractor shall follow the procedures and requirements given in the Air Pollution	Minimise dust impact	Contractor	All	Construction	• APCO	Implemented.
34.4.3.2	Control (Construction Dust) Regulation	at the nearby sensitive	Contractor	construction	phase	• To control the dust	implemented.
	Control (Construction Dust) Regulation	receivers		sites	phase	impact to meet	
		receivers		Sites		HKAQO and	
						TM-EIAO	
						criteria	
S4.4.5.3	Water spraying every hour for all active works area.	Minimise dust impact	Contractor	All	Construction	• APCO	Implemented.
	1 1 2 2 1 1	at the nearby sensitive		construction	phase	To control the dust	*2 nos. of water
		receivers		sites	1	impact to meet	truck were running
						HKAQO and	on haul road for
						TM-EIAO	sufficient water
						criteria	spraying
S4.4.5.2	Any excavated or stockpile of dusty material should be covered entirely by	Minimise dust impact	Contractor	All	Construction	• APCO	Implemented.
	impervious sheeting or sprayed with water to maintain the entire surface wet and	at the nearby sensitive		construction	phase	To control the dust	
	then removed or backfilled or reinstated where practicable within 24 hours of the	receivers		sites		impact to meet	
	excavation or unloading;					HKAQO and	
	Any dusty materials remaining after a stockpile is removed should be wetted with					TM-EIAO	Implemented
	water and cleared from the surface of roads;					criteria	
	A stockpile of dusty material should not be extended beyond the pedestrian						Implemented
	barriers, fencing or traffic cones;						
	The load of dusty materials on a vehicle leaving a construction site should be						Implemented
	covered entirely by impervious sheeting to ensure that the dusty materials do not						
	leak from the vehicle;						
	Vehicle wheel washing facilities should be provided at each construction site exit.						Implemented
	Immediately before leaving the construction site, every vehicle should be washed						
	to remove any dusty materials from its body and wheels;						
	• When there are open excavation and reinstatement works, hoarding of not less						Implemented
	than 2.4m high should be provided as far as practicable along the site boundary.						
	Good site practice shall also be adopted by the Contractor to ensure the conditions						
	of the hoardings are properly maintained throughout the construction period;						
	• The portion of any road leading only to construction site that is within 30m of a						Invalence 1
	vehicle entrance or exit should be kept clear of dusty materials;						Implemented
	Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other machanical breaking appendict takes place about the ground with water or						Implements 1
	other mechanical breaking operation takes place should be sprayed with water or						Implemented
	a dust suppression chemical continuously; Any area that involves demolition estivities should be enroyed with water or a						
	Any area that involves demolition activities should be sprayed with water or a			1			

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
	dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet; • Any skip hoist for material transport should be totally enclosed by impervious						Implemented
	 sheeting; Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) 						Implemented
	should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;						Implemented
	 Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system; Exposed earth should be properly treated by compaction, turfing, hydroseeding, 						Implemented
	vegetation planting or sealing with latex, vinyl, bitumen, shortcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.						Implemented
S4.4.5.1	Implement regular dust monitoring under EM&A programme during the construction stage.	Monitoring of dust impact	Contractor	Selected representative dust monitoring station	Construction phase	• TM-EIAO	Implemented. 3 dust monitoring stations were Implemented.
S4.4.5.3	 All road surface within the barging facilities will be paved. Dust enclosures will be provided for the loading ramp, installation of 3- sided screen with top cover and the provision of water sprays at the discharge point would be provided. Vehicles will be required to pass through designated wheel wash facilities. Continuous water spray at the loading point. 	Minimise dust impact at the nearby sensitive receivers	Contractor	Barging point at Siu Lam	Construction phase	• TM-EIAO	No Applicable. * Barging point at Siu Lam is not in used.
Construction			l .		<u> </u>		
S5.5.5.3	Implement the following good site management practices: only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme; machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs;	Control construction noise	Contractor	All construction sites	Construction phase	• Annex 5, TM-EIAO	Implemented Implemented Implemented
	 silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works; mobile plant should be sited as far away from NSRs as possible and practicable; material stockpiles, mobile container site office and other structures should be effectively utilised, where practicable, to screen noise from onsite construction 						Implemented Implemented Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
	activities.						
S5.5.5.5	Adopt quiet plants during the construction of viaduct, widening of Sha Ling Road, construction of platform for crematorium and widening of Lin Ma Hang Road. The quiet plants should be made reference to the PME listed in the TM or the QPME/ other commonly used PME listed in EPD web pages or taken from BS5228: Part 1: 2009 Noise Control on Construction and Open Sites as far as possible.	Reduce the noise levels of plant items	Contractor	Works area for construction of viaduct, widening of Sha Ling Road, construction of platform for crematorium and widening of Lin Ma Hang Road	Construction phase	• Annex 5, TM-EIAO	Implemented * Quiet plants were in used.
\$5.5.5.6	Install temporary noise barriers (in the form of site hoardings, approx. 2.4m high) located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level zone of NSRs through partial screening.	Contractor	All construction sites where practicable	Construction phase	Annex 5, TM-EIAO	Implemented where necessary. * Temporary noise barriers are not practicable due to site constraint.
\$5.5.5.7 - \$5.5.5.12	Install movable noise barriers (typical design is wooden framed barrier with a small-cantilevered upper portion of superficial density no less than 7kg/m2 on a skid footing with 25mm thick internal sound absorptive lining), acoustic mat or full enclosure, screen the noisy plants including air compressors, generators etc.	Screen the noisy plant items to be used at all construction sites	Contractor	All construction sites where practicable	Construction phase	Annex 5, TM-EIAO	Implemented where necessary. * Movable noise barriers are not practicable due to site constraint.
\$5.5.5.13	Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction noise	Contractor	All construction sites where practicable	Construction phase	Annex 5, TM-EIAO	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S13.2.1.1 - S13.4.1.2	Implement a noise monitoring under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected representative noise monitoring station	Construction phase	TM-EIAO	Implemented. * 4 noise monitoring stations were Implemented.
Operation	l nl Noise (Road Traffic Noise)						L
S5.6.6.4	Provide a series of noise mitigation measures including absorptive noise barriers and low noise road surfacing materials along Lin Ma Hang Road and Sha Ling Road before operation of the proposed project for existing and planned representative NSRs. Locations of noise mitigation measures are stated as following: For existing representative NSRs Approx. 12m of absorptive noise barrier 2.5m above road level along Sha Ling Road (MM1); Approx. 92m of absorptive noise barrier 3m above road level along Sha Ling Road (MM2); Approx. 28m of absorptive noise barrier 3m above road level along Project Road near Sha Ling Road (MM3); Approx. 51m of absorptive noise barrier 3m above road level along Project Road near Sha Ling Road (MM4); Approx. 25m of absorptive noise barrier 4m above road level along Lin Ma Hang Road near San Uk Ling (MM5); Approx. 21m of absorptive noise barrier 4m above road level along Lin Ma Hang Road near San Uk Ling (MM6); Approx. 14m of absorptive noise barrier 4m above road level along Lin Ma Hang Road near San Uk Ling (MM7); Approx. 18m of absorptive noise barrier 3m above road level along Lin Ma Hang Road near San Uk Ling (MM8); Approx. 42m of absorptive noise barrier 3m above road level along Lin Ma Hang Road near San Uk Ling (MM8); Approx. 93m of absorptive noise barrier 3m above road level along Lin Ma Hang Road opposite San Uk Ling (MM10); Approx. 185m of low noise surfacing materials along Lin Ma Hang Road near San Uk Ling (MM10); For planned representative NSRs Approx. 36m of absorptive noise barrier 5m above road level along Lin Ma Hang Road near Muk Wu Nga Yiu (MM12);	Reduce operation noise from road traffic	Contractor	Refer to Figures 5.6.9 - 5.6.13 of the EIA Report	Prior to operation of the Project for existing representative NSRs. While for barriers to protect planned representative NSRs, it should constructed before intake of planned representative NSRs.	• TM-EIAO	Shall be implemented Prior to operation of the Project.

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
	 Road near Muk Wu Nga Yiu (MM13); Approx. 31m of absorptive noise barrier 5m above road level along Lin Ma Hang Road near Muk Wu Nga Yiu (MM14); Approx. 31m of absorptive noise barrier 5m above road level along Lin Ma Hang Road near Muk Wu Nga Yiu (MM15); Approx. 41m of absorptive noise barrier 5m above road level along Lin Ma Hang Road near Muk Wu Nga Yiu (MM16); Approx. 340m of low noise surfacing materials along Lin Ma Hang Road near Muk Wu Nga Yiu (MM17). 						
Water Qua	lity (Construction Phase)						
S6.4.4.1 - S6.4.4.3	 In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN1/94), construction phase mitigation measures shall include the following: General Site Operation At the start of site establishment, perimeter cut-off drains to direct offsite water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction; Diversion of natural stormwater should be avoided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimise polluted runoff. Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m³ capacities are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs 	To minimise water quality impact from construction site runoff and general construction activities	Contractor	All construction sites where applicable	Construction phase	Water Pollution Control Ordinance ProPECC PN1/94 TM-EIAO TM-DSS	Implemented
	from a variety of sources and suited to applications where the influent is pumped; • The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a site/sediment trap. The sediment/silt traps should be incorporated in the						Implemented
	 permanent drainage channels to enhance deposition rates; The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94. The detailed design of the sand/silt traps 						Implemented
	shall be undertaken by the contractor prior to the commencement of construction; Construction works should be programmed to minimise surface excavation works during the rainy seasons (April to September). All exposed earth areas should be						Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
	completed and vegetated as soon as possible after earthworks have been						
	completed. If excavation of soil cannot be avoided during the rainy season, or at						
	any time of year when rainstorms are likely, exposed slope surfaces should be						
	covered by tarpaulin or other means;						
	 If the excavation of trenches in wet periods is necessary, it should be dug and 						Implemented
	backfilled in short sections wherever practicable. Water pumped out from						
	trenches or foundation excavations should be discharged into storm drains via silt						
	removal facilities;						
	 All drainage facilities and erosion and sediment control structures should be 						Implemented
	regularly inspected and maintained to ensure proper and efficient operation at all						
	times and particularly following rainstorms. Deposited silt and grit should be						
	removed regularly and disposed of by spreading evenly over stable, vegetated						
	areas;						
	 All open stockpiles of construction materials (for example, aggregates, sand and 						
	fill material) of more than 50m3 should be covered with tarpaulin or similar fabric						Implemented
	during rainstorms. Measures should be taken to prevent the washing away of						
	construction materials, soil, silt or debris into any drainage system;						
	 Manholes (including newly constructed ones) should always be covered and 						
	temporarily sealed so as to prevent silt, construction materials or debris being						Implemented
	washed into the drainage system and storm runoff being directed into foul						
	sewers;						
	• Precautions be taken at any time of year when rainstorms are likely, actions to be						
	taken when a rainstorm is imminent or forecasted, and actions to be taken during						Implemented
	or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94.						
	Particular attention should be paid to the control of silty surface runoff during						
	storm events, especially for areas located near steep slopes;						
	All vehicles and plant should be cleaned before leaving a construction site to						
	ensure no earth, mud, debris and the like is deposited by them on roads. An						Implemented
	adequately designed and sited wheel washing facilities should be provided at						
	every construction site exit where practicable.						
	• Wash-water should have sand and silt settled out and removed at least on a						
	weekly basis to ensure the continued efficiency of the process. The section of						Implemented
	access road leading to, and exiting from, the wheel-wash bay to the public road						
	should be paved with sufficient backfall toward the wheel-wash bay to prevent						
	vehicle tracking of soil and silty water to public roads and drains;						
	Oil interceptors should be provided in the drainage system downstream of any						
	oil/fuel pollution sources. The oil interceptors should be emptied and cleaned						Implemented
	regularly to prevent the release of oil and grease into the storm water drainage						
	system after accidental spillage. A bypass should be provided for the oil						
	interceptors to prevent flushing during heavy rain;						

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
	 Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts; All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby; 						Implemented Implemented
	 Regular environmental audit on the construction site should be carried out in order to prevent any malpractices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the water bodies, marsh and ponds; Adopt best management practices. 						Implemented
S6.4.4.4 - S6.4.4.5	Sewage from workforce Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance; Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project; Regular environmental audit on the construction site should be conducted in order to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site.	To minimise water quality from sewage effluent	Contractor	All construction sites where practicable	Construction phase	Water Pollution Control Ordinance TM-DSS	Implemented Implemented Implemented
S6.4.4.6	 Operation of Barging Point at Siu Lam All barges should be fitted with tight bottom seals to prevent leakage of materials during transport; Barges or hoppers should not be filled to a level that will cause overflow of materials or polluted water during loading or transportation; All vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; and Loading of barges and hoppers should be controlled to prevent splashing of material into the surrounding water. Mitigation measures for land-based activities as outlined in Section 6.4.4 should be applied to minimise water quality impacts from site runoff and open stockpile spoils at the proposed barging facilities where appropriate. 	To minimise water quality from operation of barging point at Siu Lam	Contractor	All construction sites where practicable	Construction phase	Water Pollution Control Ordinance TM-DSS	No Applicable. * Barging point at Siu Lam is not in used.

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S6.5.4.1 - S6.5.4.6	The following mitigation measures during operational phase are recommended: Sewage and wastewater discharge should be connected to foul sewerage system; Proper drainage systems with silt traps and oil interceptors should be installed; The design of road gullies with silt traps should be incorporated especially for the catchment leading to the existing wet woodland area located at the north of the site; The silt traps and oil interceptors should be cleaned and maintained regularly, especially before peak seasons of the visitors in Ching Ming Festival and Chung Yeung Festival; Energy dissipaters should be installed at the seasonally wet watercourses to reduce the magnitude of the first flush in order to minimise the erosion impact to the wet woodland. agement (Construction Waste)	To minimise the road runoff, wastewater discharge and erosion of seasonal watercourse during the operational phase	Highways Department /Contractors	Whole alignment	Construction / Operational Phase	Water Pollution Control Ordinance TM-DSS	For Operational phase
\$7.3.3.8	Construction & Demolition Material Management Plan (C&DMMP) • A C&DMMP shall be submitted to the Public Fill Committee for approval in the case of C&D materials disposal exceeding 50,000m3.	To enhance the management of construction and demolition (C&D) material including rock in public works projects	Contractor	All construction sites	Construction phase	Project Administrative Handbook for Civil Engineering Works, 2012 Edition	
S7.3.4.2	 Good Site Practice The following good site practices are recommended throughout the construction activities: nomination of an approved personnel, such as a site manager, to be responsible for the implementation of good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; training of site personnel in site cleanliness, appropriate waste management procedures and concepts of waste reduction, reuse and recycling; provision of sufficient waste disposal points and regular collection for disposal; appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; a Waste Management Plan (WMP) should be prepared by the contractor and submitted to the Engineer for approval. 	Minimise waste generation during construction	Contractor	All construction sites	Construction phase	• Waste Disposal Ordinance	Implemented Implemented Implemented Implemented Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
\$7.3.4.3	Waste Reduction Measures Waste reduction is best achieved at the planning and design phase, as well as by ensuring the implementation of good site practices. The following recommendations are proposed to achieve reduction: • segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling of materials and their proper disposal; • proper storage and site practices to minimise the potential for damage and contamination of construction materials; • plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste; • sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable portions (i.e. soil, broken concrete metal etc.); • provide training to workers on the importance of appropriate waste management	Reduce waste generation	Contractor	All construction sites	Construction phase	Waste Disposal Ordinance	Implemented Implemented Implemented Implemented Implemented
S7.3.4.5	procedures, including waste reduction, reuse and recycling. Storage of Waste The following recommendation should be implemented to minimise the impacts: non-inert C&D materials such as soil should be handled and stored well to ensure secure containment; stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; different locations should be designated to stockpile each material to enhance reuse;	Good site practice to minimise the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction phase	• Land (Miscellaneous Provisions) Ordinance • Waste Disposal Ordinance • ETWB TCW No. 19/2005	Implemented Implemented Implemented
\$7.3.4.6	Collection and Transportation of Waste The following recommendation should be implemented to minimise the impacts: • remove waste in timely manner; • employ the trucks with cover or enclosed containers for waste transportation; • obtain relevant waste disposal permits from the appropriate authorities; and • disposal of waste should be done at licensed waste disposal facilities.	Minimise waste impacts from storage	Contractor	All construction sites	Construction phase	Waste Disposal Ordinance	Implemented Implemented Implemented Implemented
S7.3.4.8 - S7.3.4.15	Excavated and C&D Materials Wherever practicable, C&D materials should be segregated from other wastes to avoid contamination and ensure acceptability at public filling areas or reclamation sites. The following mitigation measures should be implemented in handling the excavated and C&D materials: • maintain temporary stockpiles and reuse excavated fill material for backfilling; • carry out on-site sorting; • make provisions in the Contract documents to allow and promote the	Minimise waste impacts from excavated and C&D materials	Contractor	All construction sites	Construction phase	Land (Miscellaneous Provisions) Ordinance Waste Disposal Ordinance	Implemented Implemented Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
\$7.3,4.17	 use of recycled aggregates where appropriate; and implement a recording system for the amount of waste generated, recycled and disposed of for checking. The recommended C&D materials handling should include: On-site sorting of C&D materials; Reuse of C&D materials; and Use of Standard Formwork and Planning of Construction Material purchasing. Chemical Waste 	Control the chemical	Contractor	All	Construction	• Waste Disposal	Implemented Implemented Implemented Implemented Implemented Implemented Implemented Implemented Implemented
S7.3.4.18	If chemical wastes are produced at the construction site, the Contractors should register with EPD as chemical waste producer. Chemical wastes should be stored in appropriate containers and collected by a licensed chemical waste Contractor. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	waste and ensure proper storage, handling and disposal.		construction	phase	(Chemical Waste) General) Regulation • Code of Practice on the Packaging, Labelling and Storage of Chemical Waste	
\$7.3.4.19	 General Refuse General refuse should be stored in enclosed bins separately from construction and chemical wastes. Recycling bins should also be placed to encourage recycling. Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should also be implemented to keep areas clean. A reputable waste collector should be employed to remove general refuse on a daily basis. 	Minimise production of the general refuse and avoid odour, pest and litter impacts	Contractor	All construction sites	Construction phase	Waste Disposal Ordinance	Implemented Implemented Implemented
\$7.3.4.20	The WMP should document the locations and number of portable chemical toilets depending on the number of workers, land availability, site condition and activities. Regularly collection by licensed collectors should be arranged to minimise potential environmental impacts.	Minimise production of sewage impacts	Contractor	All construction sites	Construction phase	Waste Disposal Ordinance	Implemented Implemented
Waste Man	agement (Operational Waste)						
\$7.4.4.1	General Refuse A reputable waste collector should be employed to remove general refuse on a daily basis.	Remove general refuse during routine road cleaning activities on the roads network and avoid odour, pest and litter impacts	Highways Department /Contractor	Roads network for the C&C facilities and Lin Ma Hang Road	Operational phase	Waste Disposal Ordinance	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
Land Cont	amination						
S8.9.1.1	Re-appraisal of the potentially contaminated site (SRC-1)	Identify any hot spots for SI within the southeast and western portions of SRC-1	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	Once the works area for the Project is confirmed and site access is available (e.g. after land resumption)	Annex 19 of the TM-EIAO, Guidelines for Assessment of Impact On Sites of Cultural Heritage and Other Impacts (Section 3 :Potential Contaminated Land Issues); Guidance Manual for Use of Risk-Based Remediation Goals (RBRGs) for Contaminated Land Management; Guidance Notes for Contaminated Land Assessment and Remediation; and Practice Guide for Investigation and Remediation of Contaminated Land Recommendations in Health Risk Assessment	Implemented
S8.11.1.1	Preparation and submission of Contamination Assessment Plan (CAP) to EPD for review and approval, if required	Present the findings of the reappraisal and strategy of the recommended SI, if required	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	After land resumption and prior to the construction phase	Ditto	Implemented
S8.11.1.2	Preparation and submission of Contamination Assessment Report (CAR) to EPD for review and approval, if required	Present the findings of SI, if any, and evaluate the level and extent of potential contamination	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	Prior to the construction phase	Ditto	Implemented
S8.11.1.2	Preparation and submission of Remediation Action Plan (RAP) to EPD for review and approval if contamination is identified	Recommend appropriate mitigation	Project Proponent	Potentially contaminated	Prior to the construction	Ditto	Not required as no contamination is

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
		measures for the contaminated soil and groundwater identified in the assessment if	Detailed Design Consultant	site (SRC-1)	phase		identified.
S8.11.1.2	Preparation and submission of Remediation Report (RR) to EPD for review and approval following the completion of any necessary remediation works	remediation is required Demonstrate that the decontamination work is adequate and is carried out in accordance with the endorsed CAR and RAP	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	Prior to the construction phase	Ditto	Not required as no contamination is identified.
Ecology (Construction Phase)						
S9.7.2.3	Preparation and submission of Upland Grassland Reinstatement Plan to EPD for agreement.	An Upland Grassland Reinstatement Plan will be prepared by a qualified ecologist/botanist with full details of the findings of a baseline grassland survey, the practical details and methodology of the physical excavation, transport and storage or turves/topsoil and their subsequent reinstatement once the receptor sites have been established, along with an implementation programme of reinstatement, post- reinstatement monitoring and maintenance programme.	Project Proponent/ Detailed Design Consultant (qualified ecologist/ botanist) for Upland Grassland Reinstatement Plan	Engineered slopes Of Crematorium Indicative locations for Grassland Reinstatement should be referred to Figure 9.11 of the EIA Report	Prior to construction phase	Reinstatement and establishment requirements to be detailed in Upland Grassland Reinstatement Plan TM-EIAO	Implemented *Upland Grassland Reinstatement Plan was submitted to EPD.

EIA Ref.	Recommended Mitigation Measures	Objectives of the	Implementation	Location /	Implementation	Requirements	Implementation
		Recommended	Agent	Timing	Stage	and / or standards to	status and remark*
		Measures & Main				be achieved	
		Concerns to address					
		should be proposed in					
		the Grassland					
		Reinstatement Plan so					
		as to describe the					
		action and limit					
		levels and the action					
		plan if certain					
		performance criteria					
		(such as area of					
		preferred habitat) are					
		not met during the					
		monitoring and					
		maintenance period.					
S9.7.2.5	Preparation and submission of a Vegetation Survey Report and	The Vegetation Survey	Project Proponent/	Within the	Prior to	 Survey findings and 	Implemented
-	Transplantation Proposal (if needed as concluded in the Vegetation Survey Report) to	will report the	Detailed Design	Project	construction	transplantation	* Vegetation Survey
S9.7.2.6	EPD for agreement.	presence, as well as	Consultant	Area where	phase	methodology to be	Report and
		update the conditions,	(qualified	applicable		detailed in Vegetation	Transplantation
		number, locations and	ecologist/			Survey Report and	Proposals for
		habitat types of any	botanist) for			Transplantation Plan	Contract 1 and
		identified floral	Vegetation Survey			respectively.	Contract 2 were
		species of	Report and			• TM-EIAO.	submitted to EPD.
		conservation	Transplantation				
		importance to be	Proposal.				
		impacted by the					
		development, and					
		evaluate suitability					
		and/or practicality of					
		transplantation.					
		The Transplantation					
		Proposal will					
		recommend locations					
		of the receptor site(s),					
		transplantation					
		methodology,					
		implementation					
		programme of					
		transplantation and					
		post-transplantation					
		monitoring					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address and maintenance programme.	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
\$9.7.5.3 - \$9.7.5.5, \$9.8.1.6	Preparation and submission of Enhancement Woodland Proposal to EPD for agreement.	Recommend appropriate enhancement planting programme, planting and post-transplantation monitoring methodology, action plan for monitoring the enhancement planting and maintenance programme.	Project Proponent/ Detailed Design Consultant (qualified ecologist/ botanist) for Wooded Area Proposal.	Filled slope west of the platform, and north west of the platform in the valley below MacIntosh Fort Indicative locations for Enhancement Woodland should be referred to Figure 9.11 of the EIA Report	Prior to construction phase	Enhancement planting and establishment requirements to be detailed in Wooded Enhancement Proposal. TM-EIAO	Implemented *Woodland compensation plan was submitted to EPD.
\$9.7.3.1 - \$9.7.3.3	Indirect impacts due to potential changes in water quality, hydrology and sedimentation could occur to a series of downstream watercourses and wetland systems (including the wet woodland, marsh and mitigation ponds) during both the construction (for the Platform and LMHR widening works) and operational stages. Generally, indirect water impact to any aquatic fauna during the construction phase should easily be avoided by implementing water control measures (ETWB TCW No. 5/2005) to avoid direct or indirect impacts any watercourses and good site practices (further details are discussed in Section 6 of the EIA Report). In addition, construction phase impacts on the watercourses, riparian corridor and fauna using these areas will be minimised by erection of a 2m high, solid, dull green site boundary fence on the edge of any active works area, 30m from the watercourse. Where this is not practicable due to site constraints, demarcation fencing will need to be erected to prevent unauthorised encroachment into the riparian corridor by constructions works and traffic. Detailed mitigation measures will be designed at the detailed design stage.	Minimise the indirect impacts to Water Quality and Hydrology	Contractor /detailed design consultant.	On the edge of any active works area, 30m from The watercourse	Prior to commencement and during construction phase	• ETWB TCW No. 5/2005 • TM-EIAO	Implemented.

EIA Ref.	Recommended Mitigation Measures	Objectives of the	Implementation	Location /	Implementation	Requirements	Implementation
LIII KCI.	Recommended Printigation Predicties	Recommended	Agent	Timing	Stage	and / or standards to	status and remark*
		Measures & Main	ngem .	Timing	Stage	be achieved	status and Temark
		Concerns to address				be deme ved	
S9.7.3.4	Mitigation for noise disturbance (details refer to \$5.5.5 to \$5.6.6 of this table). Site	The construction work	Contractor	All	Prior to	• TM-EIAO.	
_	formation and construction are tentatively proposed to cover a 65-month period from	and site formation will	Project Proponent	construction	commencement	TWI EINO.	
S9.7.3.6	mid 2017 to late 2022.	be phased in order to	1 Toject 1 Toponent	sites	and		
57.7.3.0	mid 2017 to face 2022.	reduce overall noise		Sites	during		
	As a precautionary approach, consideration should be given at the detailed design stage	disturbance impacts in			construction		
	to avoid the use of highly reflective materials in the design and implementing the use	particular areas.			phase		
	of opaque materials, fritting, breaking up external reflections with stickers or plastic	Collisions usually			phase		
	wrap and/or any other birdfriendly design for noise barriers.	occurs as a result of					
	with and of any other oraniently design for noise ourners.	birds perceiving a					
	Works will be restricted to daytime and any construction lighting should	clear path through an					
	be designed and positioned as to not impact on adjacent ecologically sensitive areas.	object that is					
	to designed and positioned as to not impact on adjacent ecologically sensitive areas.	transparent or appears					
		to be transparent at					
		some distance, or if					
		the noise barrier is					
		highly reflective which					
		would appear to be					
		composed of the					
		adjacent natural					
		vegetation.					
		Furthermore,					
		mitigation measures to					
		control noise					
		disturbance during this					
		phase will involve the					
		selection of					
		quieter plant, use of					
		movable noise barriers					
		and erection of					
		hoarding and fencing					
		to demarcate the site					
		boundary					
.9.7.3.7	In order to demonstrate ecological awareness and to minimise the risk of indirect	Minimise impacts on	Contractor	All	Prior to	• TM-EIAO.	
.,.,.,	impacts from water pollution and hill fires, a series of good site practices should be	hydrological condition	Contractor	construction	commencement	1111 21110.	
	adopted by site staff throughout the construction phase at each works site. These are as	and water quality of		sites	and		
	follows:	hillside watercourses		3100	during		
	Put up signs to alert site staff about any locations which are ecologically sensitive	and reduce chances of			construction		Implemented
	and measures to prevent accidental impacts;	hillfires.			phase		Implemented
	Erection of temporary geotextile silt or sediment fences/oil traps around any	mmics.			Pilase		Implemented
	earth-moving works to trap any sediments and prevent them from entering						Implemented
L	carm-moving works to trap any seminents and prevent them from entering		1	L		1	

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S.9.7.3.9	watercourses; Prohibition of soil storage against trees or close to waterbodies; Delineation of works site to prevent encroachment onto adjacent habitats and fence off areas which have some ecological value; No smoking, hot works or sources of fire close to upland grassland; No on-site burning of waste; and Waste and refuse in appropriate receptacles. Precautionary checks by a suitably experienced ecologist of the vegetation for the presence of nesting birds should be carried out in the breeding season (February to July) before vegetation clearance. These impacts can be avoided by conducting vegetation clearance during the non-breeding season (tentatively August-January) and	Minimise the impacts to breeding birds within the works areas.	Contractor	All construction sites	Prior to site clearance	• TM-EIAO • WAPO	Implemented Implemented Implemented Implemented Implemented Implemented Implemented during breeding season.
Ecology (C	phased through the project period to minimise impacts. **Department of the project period to minimise impacts.** **Department of the project period to minim			<u> </u>			
S9.7.2	Establishment, maintenance and monitoring of a Upland Grassland Reinstatement Area	Reinstatement of upland grassland and to maintain connectivity in Sandy Ridge.	Project Proponent/ Contractor / Maintenance Authority	Engineered slopes of Crematorium Indicative locations for Grassland Reinstatement should be referred to Figure 9.11 of the EIA Report	Operational phase	Monitoring methodology and successfulness of survival of upland grassland should follow Upland Grassland Reinstatement Plan. TM-EIAO.	Upland Grassland Reinstatement Area will be implemented by other contract.
\$9.7.5.3 - \$9.7.5.6	Establishment, maintenance and monitoring of an enhancement woodland	Recommend appropriate enhancement planting programme, planting and post-transplantation monitoring methodology, action plan for monitoring the enhancement planting and	Project Proponent/ Detailed Design Consultant (qualified ecologist/ botanist) for Wooded Area Proposal.	Filled slope west of the platform, and north west of the platform in the valley below MacIntosh Fort	Operational phase	Enhancement planting and establishment requirements to be detailed in Wooded Area Proposal. TM-EIAO.	

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
		maintenance		Indicative			
		programme.		locations for			
				Enhancement			
				Woodland			
				should			
				be referred to			
				Figure 9.11			
				of the			
				EIA Report			
S9.7.4.1	Mitigation for Impacts to Water Quality and Hydrology (Operational	Specific mitigation	Detailed Design	Wet	Detailed Design	• TM-EIAO	Implemented before
-	<u>Phase</u>)	measures will be	Consultant	woodland	phase/Operational		Operational phase
S9.7.4.5	• Stormwater drainage system will be further developed in detailed design stage to	implemented to		(and further	phase		
	collect dusty materials from water collected from the platform and associated road	prevent indirect		down			
	system. Silt traps will be installed to ensure removal of dusty materials. Regular	impacts wetland		the marsh and			
	cleaning will be conducted to avoid debris entering downstream rivers during first	habitats and fauna.		mitigation			
	flush; and	Mitigation measures		ponds)			
	The proposed small diameter bore pile system at the foundation of	are to be further		and the			
	the proposed platform structure.	developed in the		seasonal			
		detailed design stage		watercourse			
		to address any water		to the			
		quality impacts due to		east of the			
		the drainage from the		Project			
		proposed platform, and any erosion issues		boundary			
		due to the drainage					
		from the proposed					
		platform.					
		The surface runoff					
		collected on the					
		platform will be					
		captured by a					
		stormwater drainage					
		system, which will be					
		further developed					
		at the detailed design					
		stage.					
		The proposed small					
		diameter bore					
		pile system at the					
		foundation of the					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
\$9.7.4.6 - \$9.7.4.7	Minimise the potential indirect light disturbance on the Street Lighting on fireflies surrounding the Project Site during operational phase It is considered that at the detailed design stage, street lighting of similar lux/light intensity as to what is currently present is utilised. Furthermore, as a precautionary measure, it is suggested that deflectors are fixed to	proposed platform structure would allow a notional free area of about 87 – 91% for groundwater to pass through. Reduce light pollution and impact on the nearby habitats and their associated wildlife groups,	Detailed Design/ Consultant/ Operator	The whole Project area	Detailed Design phase/Operational phase	• TM-EIAO	Implemented before Operational phase
S9.7.4.9 - S9.7.4.9	the back of the street lights to prevent additional light reaching the marsh and causing adverse impacts to fireflies. The increase in visitors to the columbarium allows greater public access to the upland grassland of Sandy Ridge and in turn, the potential for hill fires is also increased. Fires may emanate from discarded cigarettes and from specific practices during festivals or	particularly nocturnal fireflies. Minimise the risk of hill fires.	Detailed Design/ Consultant/ Operator	The whole Project area	Detailed Design phase/Operational phase	• TM-EIAO	Implemented before Operational phase
	In order to reduce the risk of hill fires, sufficient educational signage should be displayed throughout the columbarium warning people of the risks of fire and strictly prohibits practices that could cause hill fires. This will require input in the detailed design phase.						
Fisheries							
\$10.5.1.1	No loss of fish ponds is anticipated and no <i>in situ</i> mitigation is required. However, mitigation measures for water quality (S6.4.4 – S6.5.4 in this table) proposed are also pertinent in ensuring that fisheries impacts of the Project do not occur downstream of the Project area either locally or in Inner Deep Bay.	-	-	-	-	-	Not applicable
Landscape	& Visual			•			
S11.8.1.3 , Table 11.9	CM1 – The construction area and contractor's temporary works areas should be minimised to avoid impacts on adjacent landscape, and the reliance on off-site construction.	Minimise landscape impact and visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-	Implemented.

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S11.8.1.3 , Table 11.9	CM3 – Screening of construction works by hoardings/noise barriers around works area in visually unobtrusive colours and to screen construction works. It is proposed that screening be compatible with the surrounding environment and non-reflective, recessive colours be used. Hoarding should be taken down at the end of the construction period.	Minimise visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-	Implemented.
S11.8.1.3 , Table 11.9	CM4 – Dust and Erosion Control for Exposed Soil - Excavation works anddemolition of existing building blocks shall be well planned with precautions to suppress dust. Exposed soil shall be covered or watered often. Areas that are expected to be left with bare soil for a long period of time after excavation shall be properly covered with suitable protective fabric. Suitable drainage shall be provided around construction sites to avoid discharge of contaminants and sediments into sensitive water-based habitat.	Minimise indirect landscape impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-	Implemented.
S11.8.1.3 , Table 11.9	CM5 – Control night-time lighting and glare by hooding all lights.	Minimise visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-	Implemented.
11.8.1.3, Table 11.9	CM6 – Tree Protection and Preservation – Woodland, plantation and other vegetation within the Study Area will be protected and preserved as far as possible in accordance with ETWB TCW No. 29/2004 - Registration of Old and Valuable Trees, and Guidelines for their Preservation and DEVB TCW No.07/2015 – Tree Preservation. Detailed Design Considerations are made to avoid impacts to trees, e.g. proper viaduct/ bridge design routing to avoid majority of the woodland, locating the columbarium buildings in areas with less trees and ensuring design of the buildings has as small a footprint as practical.	Minimise landscape impact and visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	DEVB TC(W) 07/2015 Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DevB	Implemented.
S11.8.1.3 , Table 11.9	CM7 – Tree Transplantation – Tree(s) will be affected according to the Tree Preservation and Removal Proposal to be carried out in a later stage. Established trees of value are to be re-located where practically feasible.	Minimise landscape and visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Design and Construction phase	• 'Guidelines for Tree Risk Management And Assessment Arrangement on an Area Basis and on a Tree Basis', issued January 2011, Greening, Landscape and Tree Management	Implemented.

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S11.8.1.3 , Table 11.9	CM8 - Implementing precautionary control measures during construction stage accordingly to ETWB TCW No. 5/2005 – Protection of natural streams/rivers from adverse impacts arising from construction works to avoid direct or indirect impacts any	Minimize landscape impact	Funded by CEDD and implemented by	Work site/ during construction	Design and Construction phase	(GLTM) Section, DevB • Latest recommended horticultural practices from GLTM Section, DevB • ETWB TCW No. 5/2005 – Protection of natural	Implemented.
	watercourses and good site practices.	Composed the loss	Contractor	Wishin	·	streams/rivers from adverse impacts arising from construction works	Implemented
\$11.8.1.3 , Table 11.9	OM1 – Compensatory Woodland Planting - The arrangement of compensatory planting (e.g. areas of woodland to be compensated and space to be allowed within the Project Site) will be subject to detailed engineering design, landscape design and planting plan, and is recommended to be implemented prior to the construction activities as far as practical.	Compensate the loss of landscape greenery and enhance the overall visual value of the site.	Funded by CEDD and implemented by Contractor	Within Project Site	Prior to Construction phase	DEVB TC(W) 07/2015 – Tree Preservation Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DevB DEVB TCW No. 06/2015 – Maintenance of Vegetation and Hard Landscape Features	Implemented
S11.8.1.3 , Table 11.9	OM2 – Compensatory Tree Planting for Plantation and Other Vegetated Areas - Compensatory planting should be provided in accordance with DEVB TCW No. 07/2015 to compensate for those trees felled. According to the preliminary design, compensatory trees will be planted on the cut/fill slopes, along new roads and in car parks. The selection of planting species shall be made with reference to the species identified in the future Detailed Tree Survey and be native to Hong Kong or the South China region.	Compensate the loss of landscape greenery and enhance the overall visual value of the site.	Funded by CEDD and implemented by Contractor	Within Project Site	Construction phase	DEVB TC(W) 07/2015 – Tree Preservation Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DevB DEVB TCW No. 06/2015 –	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
						Maintenance of Vegetation and Hard Landscape Features	
S11.8.1.3 , Table 11.9	OM3 – Amenity Planting and aesthetic streetscape design of hard landscaping for Pedestrian Walkway, Roadside - Roadside amenity planting should be provided along Sha Ling Road, Lin Ma Hang Road, as well as the internal road within Sandy Ridge columbarium and crematorium site; to enhance the landscape quality of the existing and proposed transport routes. Climbers are proposed to cover vertical, hard surfaces of the piers of the proposed viaducts, and also the newly formed retaining wall within the site. Shade tolerant plants will be planted, where light is sufficient, to improve aesthetic value of areas under viaducts.	Minimise visual impact and also enhance landscape.	Funded by CEDD and implemented by Contractor	Within Project Site	Construction phase	 Guidelines on Greening of Noise Barriers, issued April 2012, GLTMS, DevB DEVB TCW No. 06/2015 – Maintenance of Vegetation and Hard Landscape Features 	Implemented
S11.8.1.3 , Table 11.9	OM4 – Greening Works and Contour Grading Works on Cut/ Fill Slopes - Greening works such as hydroseeding/ terraces of shrub or tree planting will be provided where slope gradient allows, according to Geotechnical Engineering Office (GEO) Publication No.1/2011 Technical Guidelines on Landscape Treatment for Slopes.	Minimise landscape and visual impact	Funded by CEDD and implemented by Contractor	Within Project Site	Construction phase	Geotechnical Engineering Office (GEO) Publication No.1/2011 Technical Guidelines on Landscape Treatment for Slopes.	Implemented
S11.8.1.3 , Table 11.9	OM5 – Landscape design treatment to be provided by relevant government department.	Mitigate the loss of greenery and enhance the overall landscape and visual value	Funded by FEHD and implemented by Contractor	Within Project Site	After handover to the relevant department	-	Implemented after handover to the relevant department
S11.8.1.3 , Table 11.9	OM6 – Architectural and chromatic treatment of the hard architectural and engineering structures and facilities.	Mitigate the loss of greenery and enhance the overall landscape and visual value	Funded by FEHD and implemented by Contractor	Within Project Site	After handover to the relevant department	-	Implemented after handover to the relevant department
S11.8.1.3 , Table 11.9	OM7 – Aesthetic design of the proposed noise barriers.	Mitigate the visual impact	Funded by CEDD and implemented by Contractor	Along Sha Ling Road and Lin Ma Hang Road	Construction phase	• WBTC No. 36/2004 - ACABAS - submission is required to ACABAS for approval of any bridges and associated structures within the public highway	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the	Implementation	Location /	Implementation	Requirements	Implementation
		Recommended	Agent	Timing	Stage	and / or standards to	status and remark*
		Measures & Main				be achieved	
		Concerns to address					
						system.	
S11.8.1.3	OM8 - Silt traps should also be incorporated into design of road gullies for the natural	Minimise the	Funded by CEDD	Within	Construction		Implemented
, Table	water stream(s).	landscape impact	and implemented	Project Site	Phase		
11.9		on natural stream	by				
			Contractor				

Notes:

- (a) A detailed Tree Survey Report showing all identified valuable trees and OVT will be undertaken in a separate Tree Preservation and Removal Proposal.
- (b) Wood resulting from tree removal should be recycled as mulch or soil conditioner for re-use within the Project or in other projects as far as possible e.g. for the construction of soft landscape work, were practical.
- (c) Contractor is responsible for landscaping during the agreed establishment and maintenance period. Other designated management and maintenance agents to take up maintenance and management of landscaping after end of agreed period
- (d) Highways Department (HyD) is responsible for maintenance and management of landscaping of public road side slope, Leisure and Cultural Services Department (LCSD) is responsible for the management and maintenance of soft landscapes along non-expressway public roads outside Country Park and Food and Environmental Hygiene Department (FEHD) is responsible for maintenance and management of landscaping of other areas allocated to FEHD.
- (e) The landscape mitigation treatment of the future development site shall follow the below frameworks:
 - Buffer planting shall be provided to soften the edge of the site.
 - Aesthetic landscape treatment including both soft and hard landscape features shall be provided.
 - Vertical greening shall be provided as far as practicable.
 - At-grade tree planting shall be provided as far as possible while planting space is allowed, to enhance the overall environment.
 - Architectural design shall blend in with the surrounding environment.
 - Overall greening ratio shall comply with TC(W) No.3/2012 Site coverage of Greenery for Government Building Projects.

EIA Ref.	Recommended Mitigation Measures	Objectives of the	Implementation	Location /	Implementation	Requirements	Implementation
		Recommended	Agent	Timing	Stage	and / or	status and remark*
		Measures & Main				standards to be	
		Concerns to address				achieved	

The compensatory woodland planting shall be included woodland mixed whips, seeding, and shrubs. The principle of the location shall be the extension of the existing woodland, as well as the original lost woodland location. The proposal will be agreed with AFCD, the woodland enhancement planting shall refer to Chapter 9.

EM&A Project							
S13.1.1.1	An Independent Environmental Checker needs to be employed as per the EM&A	Control EM&	A Highways	All	Construction	EIAO Guidance	Implemented
,	Manual.	Performance	Department	construction	phase	Note No.4/2010	
S13.2.1.2				sites		• TM-EIAO	
S13.2.1.1	1) An Environmental Team needs to be employed as per the EM&A Manual.	Perform	Highways	All	Construction	EIAO Guidance	Implemented
_	2) Prepare a systematic Environmental Management Plan to ensure effective	environmental	Department	construction	phase	Note No.4/2010	
S13.4.1.2	implementation of the mitigation measures.	monitoring & auditin	g / Contractor	sites		• TM-EIAO	
	3) An environmental impact monitoring needs to be implementing by the						
	Environmental Team to ensure all the requirements given in the EM&A Manual are						
	fully complied with.						



Appendix P

Illustrations of Site Activities

